PROJECT: NIHON UNIVERSITY NEWCASTLE CAMPUS

Monthly Project Control Group Report

Date Issued	30.07.2021
Report No.	19
Status	☐ Draft ☒ Approved
Prepared By	Ben Moss (Built Pty Ltd)

TEMPLATE OWNER: ENTERPRISE PROJECT CAPABILITY (v 12 DEC 10)

Table of Contents

Document Control **3**

1. Introduction **5**

2. Project Details **5**

3. Report **6**

3.1 HSE Overview 6
3.2 Community Liaison Overview 7
3.3 Audits & Monitoring 8
3.3.1 Internal Audits & Monitoring *8*
3.3.2 External Audits & Monitoring *9*
3.4 Contract Programme Status 10
3.4.1 Construction Progress Update *10*
3.4.2 Upcoming Construction Activities (August 2021) *11*
3.4.3 Potential Issues *12*
3.4.4 Statused Contract Programme *12*
3.4.5 Four Weekly Look Ahead *12*
3.5 Progress Photos 12
3.6 Design Update 13
3.6.1 Architectural *13*
3.6.2 Structural & Civil *13*
3.6.3 Hydraulic Services *13*
3.6.4 Electrical Services *13*
3.6.5 Mechanical Services *13*
3.6.6 Fire Services *13*
3.6.7 Fire Engineering *13*
3.6.8 Green Star *13*
3.6.9 Shop Drawings *13*
3.7 Authorities & Approvals 14
3.7.1 NSW Dept. Planning & Environment *14*
3.7.2 City of Newcastle *14*
3.7.3 Ausgrid *14*
3.7.4 Jemena *14*
3.7.5 Hunter Water *14*
3.7.6 Communications (NBN & Other Service Providers) *14*
3.7.7 SANSW *14*
3.7.8 Principal Certifying Authority *14*
3.8 Outstanding RFIs 15
3.9 Cost & Time 21
3.9.1 Head Contract Progress Claim Schedule *21*
3.9.2 Project Variation Register *22*
3.9.3 Provisional Sum Adjustments *25*
3.9.4 Notice of Delay & Extension of Time Register *26*
3.9.5 Inclement Weather (Programme Contingency) *26*
3.10 Recycling Records 27

4. Appendices **28**

Document Control

Revision History

Version	Author	Issue Date	Changes
Draft A	Ben Moss	16.01.2020	Draft Report
Rev 1	Ben Moss	20.01.2020	Approved
PCG Report 01	Ben Moss	31.01.2020	January 2020
PCG Report 02	Ben Moss	28.02.2020	February 2020
PCG Report 03	Ben Moss	27.03.2020	March 2020
PCG Report 04	Ben Moss	29.04.2020	April 2020
PCG Report 05	Ben Moss	29.05.2020	May 2020
PCG Report 06	Ben Moss	26.06.2020	June 2020
PCG Report 07	Ben Moss	31.07.2020	July 2020
PCG Report 08	Ben Moss	29.08.2020	August 2020
PCG Report 09	Ben Moss	25.09.2020	September 2020
PCG Report 10	Ben Moss / Rob McLaughlin	30.10.2020	October 2020
PCG Report 11	Ben Moss	27.11.2020	November 2020
PCG Report 12	Ben Moss / Rob McLaughlin	11.01.2021	December 2020
PCG Report 13	Ben Moss	29.01.2021	January 2021
PCG Report 14	Ben Moss	26.02.2021	February 2021
PCG Report 15	Ben Moss	26.03.2021	March 2021
PCG Report 16	Ben Moss	30.04.2021	April 2021
PCG Report 17	Ben Moss	28.05.2021	May 2021
PCG Report 18	Ben Moss	25.06.2021	June 2021
PCG Report 19	Ben Moss	30.07.2021	July 2021

Distribution List

Name	Title	Company	Email
Jun Yokobori	Lead Architect	Azusa Sekkei	Yokobori1482@azusasekkei.co.jp
Ed Clode	Architect	dwp Australia Pty Ltd	Edward.c@dwp.com
Katherine Daunt	Architect	dwp Australia Pty Ltd	Katherine.d@dwp.com
Christian Barkowski	Architect	dwp Australia Pty Ltd	Christian.b@dwp.com
Rod O'Neill	General Manager	Built NSW Pty Ltd	rodoneill@built.com.au
Rob McLaughlin	Construction Manager	Built NSW Pty Ltd	robertmclaughlin@built.com.au
Benjamin Moss	Project Manager	Built NSW Pty Ltd	benmoss@built.com.au
Slafco Gavriloski	Senior Contracts Administrator	Built NSW Pty Ltd	slafcogavriloski@built.com.au
Sita Vasanthakumar	Design Manager	Built NSW Pty Ltd	sita@built.com.au
Ben Bates	Site Manager	Built NSW Pty Ltd	benbates@built.com.au

1. Introduction

Built NSW Pty Ltd has been engaged by Nihon Daigaku Australia Newcastle Pty Ltd, c\o Azusa Sekkei & dwp Australia Pty Ltd to undertake the project and works associated with the redevelopment of the existing heritage-listed Newcastle Courthouse site for the new Nihon University Newcastle Campus located at 9 Church Street, Newcastle NSW Australia.

Built NSW has been engaged under a Design & Construct (D&C) Contract for the Services and Structural (excluding Heritage Building) packages whilst all other packages are Construct Only.

The project consists of the complete demolition of two existing three-story buildings, site remediation (including the management of any resultant contamination, mine workings and/or archaeological findings), the restoration and refurbishment of the retained and state heritage listed Newcastle Courthouse building, and the construction of two new four-story buildings comprising student accommodation in the eastern building and teaching space\carpark in the western building.

2. Project Details

Date of Site Report: 30th July 2021

Prepared by Company: Built Pty Ltd

Address: Level 1, 155-157 Lambton Rd, Broadmeadow, NSW 2290

Contact: Rob McLaughlin

Phone: 02 4077 5906 **Email: robertmclaughlin@built.com.au**

Project No: 201229

Project Name: Nihon University Newcastle Campus

Address: 9 Church Street, Newcastle, NSW 2300

Client: Nihon Daigaku Australia C/O Azusa Sekkei

Architect / Head Contract Administration: dwp Australia Pty Ltd

Superintendent's Address: 16 Telford Street, Newcastle East, NSW 2300

Contact: Ed Clode

Phone: 02 4926 5222 **Email: Edward.c@dwp.com**

3. Report

3.1 HSE Overview

All site personnel demonstrated excellent communication and coordination throughout this reporting period in controlling high-risk works including working on/around mobile plant and traffic, working at heights, live services, and falling objects along Church Street and the building facades.

Built worked closely with City of Newcastle and adjacent property owners to complete S.138 works including new stormwater pits, kerbs, and gutters that required engineered temporary works and strict traffic and pedestrian management.

As project completion approaches next month, Built will continue to consult with stakeholders to identify and appropriately control HSE risks to finish safely.

A summary of HSE incidents for the reporting period is outlined in Table 1 below.

The HSE Incident Register is attached in **Appendix A.**

Table 1: HSE Incident Summary

DATE OF ISSUE	BRIEF SUMMARY OF ISSUE	CORRECTIVE ACTIONS COMPLETED
13/07/2021	Lost Time Injury Worker traversing a ladder slipped on third rung and injured their knee.	- Worker was provided first aid and referred for medical treatment.

3.2 Community Liaison Overview

In accordance with SSD-9787 Conditions of Consent and BUILT's Community Liaison Plan, BUILT has liaised with nearby residents, businesses, and organisations. BUILT intends to work closely with our neighbours for the duration of the Nihon University project by regularly updating and consulting stakeholders on upcoming works and overall construction progress.

BUILT has also established a Community Liaison email account (nihon@built.com.au) that is monitored by the Community Liaison Officers daily and a 24-hour contact number is present on project signage located on Church Street access gates.

BUILT maintains a register of all community complaints, notices, and queries received to ensure compliance with SSD conditions and reporting requirements.

A summary of community liaison for the reporting period is outlined in Table 2 below.

The Community Liaison Register is attached in **Appendix B**.

Table 2: Community Liaison Summary

DATE OF ISSUE	BRIEF SUMMARY OF ISSUE	RESPONSE / ACTIONS COMPLETED
07.07.2021	Community Notice (REF: 2107-CN040) Consultation meeting with the Grand Hotel regarding Section 138 works adjacent to their property including seeking permission for the installation of temporary propping to enable excavation works.	- Nil issues. Stakeholder provided written permission to commence works.
12.07.2021	Community Notice (REF: 2107-CN041) Site meeting with City of Newcastle infrastructure representatives to discuss extent and timing of road restoration works.	- CoN advised they wished to coordinate public infrastructure works with Built's to minimise disruption to the community. - CoN confirmed they will proceed with road restoration works in line with Built's construction programme.
13.07.2021	Community Notice (REF: 2107-CN036) Notice issued to community regarding a footpath closure and commencement of Section 138 works adjacent to the Grand Hotel.	- No responses received.
30.07.2021	Community Complaint (REF: 2107-CC026) Complaint received from James Fletcher Hospital in relation to safety concerns raised by staff regarding location of the skip bin and the impact on safe vision when exiting the Hospital.	- Built PM responded by both phone and email advising that the skip bin has been removed from site. - No further issues raised

3.3 Audits & Monitoring

Throughout the Nihon University Newcastle Campus project, Health, Safety, Environmental & Quality (HSEQ) Audits will be undertaken internally by Built and externally by an Independent Third-Party Auditor (GHD Group Pty Ltd Newcastle) in compliance with both Built Management Systems (AS/NZS ISO 14001 & AS/NZS ISO 9001:2016 accredited) and SSD-9787 Development Consent Conditions.

Built has engaged a qualified and experienced Acoustic Consultant, RAPT Consulting (RAPT) to conduct noise and vibration monitoring throughout the project as required by the Construction Noise and Vibration Management Sub-Plan. Built's Project HSE Officer also conducts noise level spot checks on current construction activities, plant, and equipment.

A summary of these audit and monitoring activities is outlined in Sections 3.3.1 & 3.3.2 below.

Copies of the key monitoring and inspection records as required under SSD-9787 are attached in **Appendix C.**

3.3.1 Internal Audits & Monitoring

Table 3 below outlines the total number of activities completed by Built during the reporting period. All activities are completed and recorded electronically using the Built.Safe software platform.

Table 3: Monthly Record of Internal HSE Activities Completed

ACTIVITY	DESCRIPTION	COMPLETED	ACTIONS
Site Inspection	Inspection of the site or specific work areas to identify potential HSE hazards and verify the implementation and effectiveness of management measures.	4	4
Plant Inspection	Inspection of plant and equipment to check it is fit for use prior to being permitted to use onsite or to re-inspect after a significant breakdown, damage, or expiry of a plant induction sticker.	9	0
Monitoring	Used to monitor construction activities compliant with the processes outlined in the Project HSE Management Plans and requirements of development approvals and permits.	13	0
BSMS Review	Review of the implementation and effectiveness of the Built Safe Mandatory Standards (controls) in relation to process risks such as electrical, scaffolding, temporary works, demolition, FRP concrete, and asbestos.	1	0
Noise Level Spot Check	Used to monitor noise levels at sensitive receiver locations, specific work areas, construction activities, and plant/equipment.	0	0
Audit – Internal HSE Plan	Used to monitor and measure the implementation of the HSE Plan by the project.	0	0
	TOTAL	**27**	**4**

Key activities completed (including related corrective actions) are summarised in Table 4 below.

Table 4: Summary of Key Internal Activities

DATE OF ACTIVITY	BRIEF SUMMARY OF ACTIVITY	CORRECTIVE ACTIONS COMPLETED
30.06.2021	Site inspection of all site areas identified crane lift in accordance with lifting plan, traffic & pedestrian management measures implemented, project & statutory signage in place, perimeter fencing in good condition, and road / footpath clean. Issues identified included worker standing on paint drum, extension leads piggy backed, poorly established exclusion zone around civil works, and plant with no induction sticker or signed logbook.	• Worker stopped and instructed to use ladder. • Worker stopped and instructed to use RCD box for extension lead. • Workers stopped and exclusion zone correctly established. • Plant found to be inducted (new sticker provided) and logbook signed.
06.07.2021	Monitoring of S.138 excavation works on Church Street identified spotters and exclusion zone in place, and pre-start logbook completed.	• Nil
12.07.2021	Monitoring of S.138 works on Church Street identified spotters in place, dust control measures implemented, and traffic management compliance.	• Nil
27.07.2021	Site inspection of Church Street and Work Zone found compliance with SSD conditions and Environmental Management Plans.	• Nil

3.3.2 External Audits & Monitoring

The Independent Environmental Audit 3 by GHD was completed on the 27th July 2021, consisting of interviews and a site inspection with dwp Newcastle and Built project personnel. The audit identified the following minor non-conformances:

- **Condition A2**
  - Administrative condition triggered due to the non-compliance with Condition D9.
- **Condition D9**
  - A non-compliance was raised due to City of Newcastle complaint on 24/05/2021 regarding the work zone extension on Church Street without approval. It was noted by GHD that no further actions are required as Built resolved the issue within 24 hours and gained approval from City of Newcastle for the extension.

The draft report is due for submission by GHD on 10th August 2021.

3.4 Contract Programme Status

3.4.1 Construction Progress Update

The updated statused contract programme provides detail on current progress however summary outlined below:

Building A – Education

- Render and painting to Level 1 external elevations – complete
- Level 2 Advert Room fit out – complete
- Lotus operable walls - complete
- FFE delivery & installation – complete

Building B – Heritage

- Internal linings & cornices on Levels 2 to 4 – complete
- Internal repairs and painting to walls and ceilings on Levels 2 to 4 – complete
- Services fit off to Levels 2 to 4 – complete
- Joinery installs – complete
- External render repairs and painting to Level 1 elevations – complete
- FFE delivery & installation – complete

Building C – Residential

- Render & painting to Level 1 elevations – complete
- Alpolic cladding install – complete
- Level 4 plant louvre screens – complete
- Civil works and FRP Northern service driveway – complete
- Atrium roof skylight, flashings, and roof plumbing – complete
- Atrium Levels 1 & 2 ceiling framing, sheeting, and painting – complete
- Atrium services fit off – complete
- Aluminium façade screens – complete

External Works:

- Palisade boundary fence installed – complete

3.4.2 Upcoming Construction Activities (August 2021)

The statused contract programme provides detail on upcoming activities for the next 4 weeks however summary outlined below:

Building A – Education

- Plant louvre screens to Level 4 Terrace – ongoing
- Aluminium façade screens – ongoing
- Services testing and commissioning – ongoing
- Level 1 Carpark fit out – ongoing
- Signage – ongoing
- Defects – ongoing
- Final clean - commencing

Building B – Heritage

- Services testing and commissioning – ongoing
- Signage – ongoing
- Defects - ongoing
- Final clean - commencing

Building C – Residential

- Services testing & commissioning – ongoing
- Atrium tiling – ongoing
- Atrium balustrade & glazing - ongoing
- FFE delivery & installation – ongoing
- Signage - ongoing
- Final clean - commencing
- DDA Lift install – commencing
- Monarch sectional doors to Atrium – commencing

External Works

- Section 138 public domain works – ongoing
- Landscaping – ongoing
- NBN site connection – commencing

3.4.3 Potential Issues

BUILT regularly reviews the construction programme to identify current or unresolved issues that have the potential to impact the time, cost, and quality aspects of the project. The following issues have been flagged for attention:

a) COVID-19 pandemic Sydney outbreak and related NSW Government Health Order restrictions causing delay to construction activities (refer to EOT #6).
b) Registration of Stormwater Easement.
c) Delays to the Atrium and Monarch Renlita operable doors (refer to EOT #5).
d) Client driven design changes due to the current stage of works.
e) Delays to the signing of completion documentation required for Occupation Certificate.

3.4.4 Statused Contract Programme

A copy of the statused Contract Programme for July 2021 is attached in **Appendix D.**

Built issued the updated construction programme as per Extension of Time 6 (EOT#6) reflecting delays caused by NSW Government COVID-19 Public Health Orders showing an adjusted completion date of 27th August 2021. At this stage, Built are proceeding with the works in accordance with this updated programme.

3.4.5 Four Weekly Look Ahead

A Four Week Programme for August 2021 is attached in **Appendix E**.

This programme shows both incomplete work and upcoming activities commencing prior to the end of August 2021.

3.5 Progress Photos

Progress photos were taken throughout July 2021 and are attached in **Appendix F.**

3.6 Design Update

3.6.1 Architectural

- Architectural drawings continue to be updated following minor amendments and onsite issues.
- Master keying schedule resolved.
- AV installation and cabinet concealment resolved.
- Signage shop drawings and sample reviews ongoing.
- Gas and water meter clash with swept path to be resolved.
- Vandal proof enclosure for gas meter to be resolved. Built has submitted the Jemena Network Operator Rules to dwp for review.

3.6.2 Structural & Civil

- No updates this period.

3.6.3 Hydraulic Services

- No updates this period.

3.6.4 Electrical Services

- Testing of the high-level heritage ball lights is to be completed within the Courtrooms once the LED lamps arrive onsite. ETA is 6th August.

3.6.5 Mechanical Services

- No updates this period.

3.6.6 Fire Services

- No updates this period.

3.6.7 Fire Engineering

- The revised FER has been received. It has triggered an amended CC and was required to be submitted to FRNSW.
- The amended CC application and documentation has been submitted to the PCA though cannot be finalised until FRNSW have reviewed the FER and provided their comments.

3.6.8 Green Star

- Green Star records and reports are being collected and collated for submission to Woods & Grieve.

3.6.9 Shop Drawings

- Shop drawing reviews and approvals are progressing through Aconex Workflow. A status of the workflows that are completed and in progress is attached in **Appendix G**.

3.7 Authorities & Approvals

3.7.1 NSW Dept. Planning & Environment.

- A statused version of the SSD-9787 Conditions Matrix has been attached in **Appendix H.**
- The current matrix identifies actions and responsibilities for Occupation Certificate. Built, dwp, and Azusa have commenced actioning these items.

3.7.2 City of Newcastle

- City of Newcastle and Built held discussions onsite where it was agreed that Council would re-surface both lanes of Church Street between Newcomen and Watt Street in conjunction with Built's S.138 asphalting works.

3.7.3 Ausgrid

- No updates this period.

3.7.4 Jemena

- Jemena signoff cannot be received until the vandal proof enclosure is resolved.

3.7.5 Hunter Water

- Metiri completed their site inspection and issued a list of completion documentation required for the Section 50 certificate. The hydraulics subcontractor is currently collating all documents for submission.

3.7.6 Communications (NBN & Other Service Providers)

- NBN advised site connection works will be completed in October 2021. This does not affect project completion.

3.7.7 SANSW

- No updates this period.

3.7.8 Principal Certifying Authority

- The PCA completed their initial OC inspection on 23rd July and will issue report shortly.
- Azusa and Nihon University to sign the ASE (Fire Monitoring) Form, Final Fire Safety Certificate, and OC Application Form so Built can submit to Surescope (PCA).
- Nihon University to sign the drafted letter for Commercial Kitchen operations.
- PCA to advise of NSWFB response to amended FER once review is complete.

3.8 Outstanding RFIs

(Generated from Aconex)

RFI Sent

Project Name: Nihon University

Date Generated: Jul 31, 2021



Definitions:
Overdue: RFI passed beyond response required date but not responded by the recipient
Outstanding: RFI that is awaiting response and within the response required date
Responded: RFI that has been responded by the recipient
Closed Out: RFI that has been responded and closed by the sender

Mail No	Subject	Sent Date	Due	Days Late	From Name	Recipients	To Organization	Status
BUILT-RFI-001271	Building B Courthouse - existing heritage gate stays	Jul 27, 2021	Jul 28, 2021	3	Mr Robert McLaughlin	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001269	Re: Paint colour of block signage wall	Jul 21, 2021	Jul 21, 2021		Slafco Gavriloski	Mr Ed Clode, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001268	Re: Condition E29 | Operational Waste Management Report - Rev E	Jul 21, 2021	Jul 23, 2021		Mrs Olivia Ryan	Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001267	Civil Pavement Type 9 & 10 Details	Jul 21, 2021	Jul 21, 2021		Mr Jack Garland	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Responded

Mail No	Subject	Sent Date	Due	Days Late	From Name	Recipients	To Organization	Status
BUILT-RFI-001266	Braille Exit Signs Clash	Jul 21, 2021	Jul 21, 2021		Ms Sita Vasanthakumar	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001265	Fwd: Window Decal Sample Submission	Jul 21, 2021	Jul 21, 2021		Mr Jack Garland	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001254	Signage Queries	Jul 16, 2021	Jul 19, 2021		Mr Jack Garland	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001252	Building B Heritage Courthouse - existing hardware	Jul 16, 2021	Jul 20, 2021	11	Mr Robert McLaughlin	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001248	Atrium L2 Landing - BAL03 Compliance Issue	Jul 14, 2021	Jul 15, 2021		Mr Benjamin Moss	Mr Ed Clode, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001244	atrium lower wall tag	Jul 13, 2021	Jul 14, 2021		Robbie Clydesdale	Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001243	Room designation for spare materials	Jul 13, 2021	Jul 16, 2021	15	Mr Robert McLaughlin	Mr Ed Clode, Mr Christian Barkowski	dwp	Overdue
BUILT-RFI-001242	8B OPERATIONAL WASTE	Jul 13, 2021	Jul 16, 2021		Mrs Olivia Ryan	Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001241	Fwd: Atrium Cladding	Jul 12, 2021	Jul 14, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001236	Residential Building - interface between vertical Alpolic and painted \ rendered wall	Jul 8, 2021	Jul 9, 2021		Mr Robert McLaughlin	Mr Ed Clode, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001235	Jemena Gas Meter Enclosure	Jul 8, 2021	Jul 12, 2021	19	Mr Benjamin Moss	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Overdue
BUILT-RFI-001234	EV charge location to be included on GA's & line marking to be different colour	Jul 8, 2021	Jul 13, 2021		Mrs Olivia Ryan	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001233	Fwd: Website, Brochure, Courthouse Timeline Text and Blockplan and Linework	Jul 8, 2021	Jul 8, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001227	Fwd: Projecting Signs -	Jul 6, 2021	Jul 7, 2021		Ms Sita Vasanthakumar	Mr Christian Barkowski, Mr	dwp	Responded

Mail No	Subject	Sent Date	Due	Days Late	From Name	Recipients	To Organization	Status
	Installation Notes					Ed Clode, Ms Katherine Daunt		
BUILT-RFI-001226	G.23 L2 lift lobby / corridor 7 link bridge - skirting type	Jul 6, 2021	Jul 7, 2021	24	Slafco Gavriloski	Mr Ed Clode, Mr Christian Barkowski	dwp	Overdue
BUILT-RFI-001221	Re: Final (WF-000133) Signage	Jul 1, 2021	Jul 2, 2021		Ms Sita Vasanthakumar	Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001220	Education Projector Setout Clash	Jul 1, 2021	Jul 2, 2021		Mr Jack Garland	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001219	Fwd: Nihon University. Re: Type LG light Fitting Location	Jun 30, 2021	Jun 30, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001218	Signage Mounting Queries	Jun 30, 2021	Jun 30, 2021		Ms Sita Vasanthakumar	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001207	Heritage Fence and Pillars - Further Set Out	Jun 24, 2021	Jun 25, 2021		Mr Robert McLaughlin	Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001206	Re: Master key system schedule - Nihon to complete	Jun 23, 2021	Jun 30, 2021	31	Ms Sita Vasanthakumar	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001205	Retained heritage water bubbler - set out	Jun 23, 2021	Jun 25, 2021		Mr Robert McLaughlin	Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001200	Building A Level 2 External Pathway - Epoxy Coating System	Jun 17, 2021	Jun 18, 2021		Mr Benjamin Moss	Mr Ed Clode, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001199	Fieldwire Training Session	Jun 17, 2021	Jun 18, 2021		Mr Benjamin Moss	Mr Christian Barkowski, Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001193	Client & Superintendent Witness Testing	Jun 4, 2021	Jun 7, 2021	54	Mr Benjamin Moss	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001177	Fwd: Controllers for Blinds	May 31, 2021	May 31, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001162	Draft Operational Landscape Management Plan	May 21, 2021	May 21, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded

Mail No	Subject	Sent Date	Due	Days Late	From Name	Recipients	To Organization	Status
BUILT-RFI-001158	Final Draft Operational Management Plan	May 21, 2021	May 21, 2021	71	Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Overdue
BUILT-RFI-001145	Heritage Building B - Rising Damp Concerns	May 13, 2021	May 20, 2021	72	Mr Robert McLaughlin	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001139	Provisional Sum Make Good - Sand & Stain Existing Timber Elements	May 12, 2021	May 14, 2021	78	Slafco Gavriloski	Mr Ed Clode	dwp	Overdue
BUILT-RFI-001050	Education/Heritage Link Window Fixing	Mar 19, 2021	Mar 19, 2021		Ms Sita Vasanthakumar	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Responded
BUILT-RFI-001046	L1 Laundry Nib Wall and Bulkhead	Mar 16, 2021	Mar 18, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001029	Nihon Contact Details	Mar 10, 2021	Mar 12, 2021	141	Mr Jake McIlhatton	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Overdue
BUILT-RFI-001024	Master key system schedule - Nihon to complete	Mar 9, 2021	Mar 23, 2021		Slafco Gavriloski	Mr Ed Clode, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-001011	Re: Non Sanitary FFE Items - Samples Brochure	Mar 4, 2021	Mar 5, 2021		Mr Jake McIlhatton	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-000949	Education_Grille Clash on Northern Facade	Feb 15, 2021	Feb 16, 2021		Ms Sita Vasanthakumar	Mr Ed Clode, Ms Katherine Daunt, Mr Christian Barkowski	dwp	Responded
BUILT-RFI-000941	Fwd: ASE Application Form	Feb 10, 2021	Feb 10, 2021	171	Ms Sita Vasanthakumar	Mr Christian Barkowski, Mr Ed Clode, Ms Katherine Daunt	dwp	Overdue

Filters: "Sent Date" within range "Past 180 days" AND "Status" equals "Outstanding,Overdue,Responded" AND "To Organization" equals "dwp".

Mail No	Subject	Sent Date	Due	Days Late	From	Recipients	To Organization	Status
dwp AU-RFI-000282	Costs to relocate "V" Crestron Panels	Apr 20, 2021	Apr 22, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Slafco Gavriloski, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000279	Marline Construction Inspection April 2021	Apr 13, 2021	Apr 15, 2021		Mr Christian Barkowski	Ms Sita Vasanthakumar, Mr Jack Garland, Mr Rod O'Neill, Mr Leif Aleksic, Mr Jake McIlhatton, Mr Benjamin Moss, Slafco Gavriloski, Mrs Olivia Ryan, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000278	Re: Landscape Construction Documentation Rev L	Apr 12, 2021	Apr 14, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000272	Moir Critical Landscape Inspections and Hold Points	Mar 22, 2021	Mar 25, 2021	128	Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Overdue

Filters: "Sent Date" within range "Past 180 days" AND "Status" equals "Outstanding,Overdue,Responded" AND "From Organization Name" equals "dwp".

RFI Received

Project Name: Nihon University

Date Generated: Jul 31, 2021



Definitions:
Overdue: RFI passed beyond response required date but not responded by the recipient
Outstanding: RFI that is awaiting response and within the response required date
Responded: RFI that has been responded by the recipient
Closed Out: RFI that has been responded and closed by the sender

Mail No	Subject	Sent Date	Due	Days Late	From	Recipients	To Organization	Status
dwp AU-RFI-000301	Confirmation of Imported Soil for Landscaping	Jul 29, 2021	Jul 30, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000300	Non compliance notification - D9 Construction Traffic	Jul 27, 2021	Jul 28, 2021		Ms Katherine Daunt	Mr Benjamin Moss	Built Pty Ltd	Responded
dwp AU-RFI-000299	Tile detail at Monarch Renlita doors	Jul 21, 2021	Jul 22, 2021		Mr Christian Barkowski	Ms Sita Vasanthakumar, Robbie Clydesdale, Ben Bates, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000298	Re: Gas and Water meters in Vehicle Swept Path	Jul 20, 2021	Jul 20, 2021		Mr Christian Barkowski	Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000297	Gas and Water meters in Vehicle Swept Path	Jul 13, 2021	Jul 13, 2021		Mr Christian Barkowski	Ms Sita Vasanthakumar, Robbie Clydesdale, Ben Bates, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000294	17-0347 Nihon University | Smoke Detection Heritage Courthouse	Jun 11, 2021	Jun 15, 2021		Mr Ed Clode	Ms Sita Vasanthakumar	Built Pty Ltd	Responded
dwp AU-RFI-000290	Civil Inspections and Reports until completion	Jun 3, 2021	Jun 7, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Leif Aleksic, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000289	Outstanding Management Plans for review	Jun 1, 2021	Jun 3, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000287	17-0347 Nihon University | Male Toilet G.11B	May 20, 2021	May 25, 2021	67	Mr Ed Clode	Ms Sita Vasanthakumar	Built Pty Ltd	Overdue
dwp AU-RFI-000285	Room Signage Changes	May 5, 2021	May 11, 2021	81	Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Slafco Gavriloski, Mr Robert McLaughlin	Built Pty Ltd	Overdue

Mail No	Subject	Sent Date	Due	Days Late	From	Recipients	To Organization	Status
dwp AU-RFI-000282	Costs to relocate "V" Crestron Panels	Apr 20, 2021	Apr 22, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Slafco Gavriloski, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000279	Marline Construction Inspection April 2021	Apr 13, 2021	Apr 15, 2021		Mr Christian Barkowski	Ms Sita Vasanthakumar, Mr Jack Garland, Mr Rod O'Neill, Mr Leif Aleksic, Mr Jake McIlhatton, Mr Benjamin Moss, Slafco Gavriloski, Mrs Olivia Ryan, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000278	Re: Landscape Construction Documentation Rev L	Apr 12, 2021	Apr 14, 2021		Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Responded
dwp AU-RFI-000272	Moir Critical Landscape Inspections and Hold Points	Mar 22, 2021	Mar 25, 2021	128	Ms Katherine Daunt	Ms Sita Vasanthakumar, Mr Benjamin Moss, Mr Robert McLaughlin	Built Pty Ltd	Overdue

Filters: "Sent Date" within range "Past 180 days" AND "Status" equals "Outstanding,Overdue,Responded" AND "From Organization Name" equals "dwp".

3.10 Recycling Records

Built has engaged Central Waste Station to handle all the construction waste from demolition through to project completion. Central Waste has a resource recovery centre in Kurri Kurri where they sort, and recycle materials on-site, or send on to speciality recyclers, with a minimum amount of waste that is unable to be recycled then disposed of in licenced landfill sites. Built and CWS are targeting a 90% materials recovery rate of all waste collected.

Central Waste submit monthly Waste Recovery Reports to Built specifically for the Nihon University Newcastle Campus project. These reports are **attached in Appendix I**.

For July 2021, the Waste Recovery Percentage is **90.59%**

4. Appendices

Appendix A – Monthly HSE Incident Register

Appendix B – Community Liaison Register

Appendix C – Audit Records

Appendix D – Statused Contract Programme

Appendix E – Four Week Programme

Appendix F – Monthly Progress Photos

Appendix G – Workflow Status

Appendix H – Statused SSD-9787 Conditions Matrix

Appendix I – Monthly Waste Recovery Reports

Appendix A – Monthly HSE Incident Register

Monthly HSE Incident Register

Project: Nihon University

Jul-21

Month	Labour Hours	First Aid Incident	Medical Treatment Incident	Lost Time Incident	Near Miss Incident	Notifiable Dangerous Incident	Environmental Incident *Includes complaints
Jan-20	2180	0	0	0	0	0	1*
Feb-20	6500	0	0	0	1	0	1*
Mar-20	5930	0	1	0	0	0	3*
Apr-20	5070	0	0	0	0	0	9*
May-20	7700	0	0	0	1	0	1*
Jun-20	7100	3	0	0	0	0	0
Jul-20	10820	0	0	0	0	0	0
Aug-20	11180	0	0	0	0	0	1*
Sep-20	11850	1	1	0	0	1	0
Oct-20	11440	0	1	0	0	0	1*
Nov-20	13924	1	0	0	1	0	1*
Dec-20	18400	0	1	0	0	0	0
Jan-21	24200	1	0	0	0	0	3*
Feb-21	25600	1	0	0	1	0	0
Mar-21	21300	0	0	0	0	1	1*
Apr-21	26400	0	1	0	1	0	0
May-21	22200	1	0	0	0	0	3*
Jun-21	22880	0	0	0	0	0	0
Jul-21	19580	0	0	1	0	0	1
TOTALS:	**274254**	**8**	**5**	**1**	**5**	**2**	**26***

Appendix B – Community Liaison Register

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2001-CC001	21/01/2020 1:20pm	TW (JFH Employee)	Concerned about removal of trees at Southern Boundary & wildlife. Works at James Fletcher Hospital.	22/01/2020 9:00am	BM	Phoned TW to disuss her concerns and assure precautions were taken and removal is in accordance with SSD-9787. Followed up with email containing project information and NSW Planning Portal.	Y
2002-CC002	27/02/2020 4:20pm	TL (Resident)	Notified Built via email of cracks appearing within his property that were previously not noted. Believes demolition works occurring the past couple of days and vibration are the cause.	27/02/2020 5:06pm	BM	Phoned TL to further discuss the issue raised. An inspection of the property has been arranged for 3:00pm 28/02/2020 with TL, Built Project Manager and Structural Engineer who completed initial Pre-Construction Dilapidation Report. Follow up email sent to TL at 5:26pm confirming details of phone complaint and inspection. Inspection Report submitted to TL on 02/03/20 showing cracks identified and not worsened. Vibration monitor results received on 03/03/20 show compliance with structural levels.	Y
2003-CC003	9/03/2020 1:50pm	JL (Resident)	Noise complaint received via phone call to Construction Manager RM regarding noise prior to approved construction hours.	09/03/2020 1:58pm	BM	Built contacted JL on her mobile number to discuss the issue. JL stated that there was noisy vehicles and concerns of "loading of bricks and things in the morning" approximately between 4:30am to 6:30am. Upon review of CCTV footage, a large skip bin garbage truck and other heavy vehicle was seen on Bolton Street between 5-6:00am and not related to the Nihon Project. Built also spoke with JL's neighbour MH, who confirmed the workers were related to a project on Bolton Street as he had confronted them that morning.	Y
2003-CC004	10/03/2020 4:06pm	TL (Resident)	Tony lodged an additional complaint via email related to demolition works causing existing cracks to "enlarge" within his residence.	10/03/2020 4:23pm	BM	Built responded via email advising that vibration monitoring to date has shown compliant levels. It was requested that the Resident submits photos of enlarged cracks for review by Structural Engineer prior to another inspection as it was found that all cracks were existing after his initial complaint. Built conducted 7 days of monitoring at the residence between 13/03/2020 & 20/03/2020. Built issued Vibration Monitoring Report to the Resident on 26/03/2020 showing that vibration results were well under the limits for both structural damage and human comfort.	Y

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2003-CC005	19/03/2020 4:05pm	James Fletcher Hospital (JFH)	Architect/Superintedent notified Built of noise complaint lodged directly to DPIE regarding demolition works.	19/03/2020 4:40pm	BM	Built contacted JFH main contact, NH (Corporate Services Manager - Hunter New England Health) to discuss the complaint. NH advised that she was unaware of the issue and had received no internal complaints. Built conducted immediate spot check of demolition noise which showed works were within permissable noise limits. Built engaged acoustic consultant to conduct internal noise monitoring within JFH on 20/03/2020. Results came back compliant with construction noise limits & report was submitted to JFH for their records on 25/03/2020.	Y
2004-CC006	01/04/2020 12:59pm	JB & CG (Resident)	Lodged complaint by email to Nihon community liaison address regarding vibration causing discomfort	02/04/2020 2:11pm	BM	Response email sent noting concerns and advising of Built monitoring activities to maintain compliance with vibration criteria and minimise disruptions. Advised the resident to contact if there are any further concerns or structural changes noted.	Y
2004-CC007	03/04/2020 9:24am	JB & CG (Resident)	Lodged complaint by email to Nihon community liaison address regarding workers being spotted onsite without Hard Hats and not maintaining social distancing.	03/04/2020 10:22am	BM	Response email sent advising that Built takes HSE and social distancing measures seriously and that this concern has been immediately addressed with workers onsite. It must be noted that the workers were completing a pre-start talk and were outdoors in open space.	Y
2004-CC008	03/04/2020 1:16pm	JB & CG (Resident)	Lodged complaint in relation to 2004-CN009 Extended Working Hours advising of the Environmental Planning and Assessment (COVID-19 Development – Construction Work Days) Order 2020 being implemented onsite.	06/04/2020 3:05pm	BM	Response sent by email noting concerns and frustration. Also advised that Built is continuing to follow Government advice in response to COVID-19, will continue to monitor the situation and implement required measures. - Refer also to Community Notice (2004-CN010) sent on 06/04/2020	Y
2004-CC009	03/04/2020 3:15pm	KD (Resident)	Lodged complaint in relation to 2004-CN009 Extended Working Hours advising of the Environmental Planning and Assessment (COVID-19 Development – Construction Work Days) Order 2020 being implemented onsite.	6/04/2020	BM	Refer to Community Notice (2004-CN010) sent on 06/04/2020.	Y
2004-CC010	03/04/2020 9:13pm	CT (Resident)	Lodged complaint in relation to 2004-CN009 Extended Working Hours advising of the Environmental Planning and Assessment (COVID-19 Development – Construction Work Days) Order 2020 being implemented onsite.	6/04/2020	BM	Refer to Community Notice (2004-CN010) sent on 06/04/2020.	Y

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2004-CC011	6/04/2020 10:04am	JB & CG (Resident)	Lodged complaint in relation to alleged cracking of their property caused by groundworks onsite.	06/04/2020 12:20pm	BM	Built arranged for an inspection of the property to assess claim against conditions noted within Pre-Construction Dilapidation Report. Inspection completed by Structural Engineer on 08/04/2020 Inspection Report issued to the Resident on 09/04/2020 advising that in the Engineer's opinion, the cracks identified by the Resident were noted within the Pre-Construction Dilapidation Report and had not worsened. Resident disputed the findings of one of the identified cracks. Built responded that vibration monitoring of an adjacent property during the same period had demonstrated compliance with vibration criteria and that any disputes will be addressed after the completion and findings of the Final Dilapidation Reports required under the Development Consent Conditions. No further response received.	Y
2004-CC012	06/04/2020 1:40pm	KD (Resident)	Lodged complaint by email regarding extended working hours, social distancing, and a traffic management issue on 04/04/2020 (Saturday).	06/04/2020 4:13pm	BM	Referred the Resident to Community Notice (2004-CN010) for response to concerns regarding social distancing. Advised that the traffic management issue had been issued to the Site Team and Subcontractors for urgent action. Also requested that for any future issues, the Resident should contact Built PM or SM immediately to ensure matters are actioned quickly. Email received from City of Newcastle Councillor thanking Built for responding to the concerns of residents.	Y
2004-CC013	8/04/2020 9:48am	MW (Employee - Newcastle Chambers)	Lodged complaint by email regarding noise caused by grinding activities onsite.	08/04/2020 11:58am	BM	Response stated Built's intention to minimise noise and conduct ongoing monitoring during construction, however, elimination of noise is not possible. Advised that structural demolition is nearing completion on the portion of site near his office. Note: Works were a short term activity located behind 2.4m plywood hoarding. No further response received	Y

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2004-CC014	28/04/2020 2:42pm	NH (HNE)	Email correspondence received from HNE advising of internal complaints related to vibration causing activities and requesting information on construction monitoring activities and methodology mentioned within Community Notice (2004-CN011) Construction Progress Update 02.	28/04/2020 3:53pm	BM	Built responded via email advising of the current site activities and their expected completion date of 1st May and that previous monitoring had demonstrated compliance. Built also advised that vibration monitors had been collected on 28/04/20 and that the monitoring report would be submitted to HNE for transparency and their records. Built submitted the monitoring report to HNE on 01/05/2020 showing that the acceptable vibration dose levels for intermittent vibration related to human comfort had not been exceeded. No further issues raised.	Y
2005-CC015	21/05/2020 5:52am	BC (Resident)	Email sent to Built Design Manager regarding noise when site personnel are arriving to site in the morning around 6:30am to 7:00am. Complaint specifically mentions noise generated by individuals talking as walking past the residence.	22/05/2020 3:38pm	BM	Email response sent advising of construction hours commencing at 7:00am and that Built would reinforce the need to be mindful of neighbours when arriving onsite of a morning. Resident responded with no further issues.	Y
2008-CC016	25/08/2020	HNE JFH	Received email from HNE JFH Corporate Services Manager regarding update on works currently occurring onsite due to receiving internal correspondence the previous week regarding jackhammering.	25/08/2020	BM	Built PM provided update of construction progress and advised that hand-held jackhammers were being intermittently used during construction of foundations. Works were expected to be completed by 28/08/2020. HNE responded advising of no further issues.	Y
2010-CC017	17/10/2020 6:38am	CG (Resident)	Received noise complaint from resident via text message and email on 17/10/2020 in relation to being woken by a worker opening the site access gate for personnel arriving to work.	19/10/2020	BM	Built PM provided apology and advised that whilst no construction activities or material deliveries were occurring at the time (in compliance with consent conditions), personnel would be reminded to be mindful of neighbours and noise when arriving to site of a morning. No further response received.	Y
2011-CC018	23/11/2020	Resident (Unknown) / SafeWork NSW	Safework Inspector attended site to follow up on a complaint received last week. Complaint received was around loads being lifted over the road in front of the works zone. The inspector reviewed the traffic management and traffic control plans, SWMS, crane crew and traffic controller competencies, road permits. No issues raised from documentation. Toolbox will be undertaken with crane crew and traffic control to reinforce controls around lifting from the works zone. All observed lifts have been completed in accordance with required controls and traffic stopped. NOTE: No complaint was received on this matter.	23/11/2020	ML	Nil	Y

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2101-CC019	20/01/2021	CG (Resident)	Complaint received via email regarding construction noise at 6:52am.	20/01/2021	BM	Site personnel addressed on construction working hours and apology issued to the resident.	Y
2101-CC020	21/01/2021	CG (Resident)	Complaint received via email regarding construction noise at 6:50am.	22/01/2021	BM	Site personnel responsible were specifically tool boxed on construction working hours and apology issued to the resident.	Y
2101-CC021	29/01/2021	HNE JFH	Complaint received via email from HNEH regarding unauthorised parking in hospital driveway and staff being subject to abuse when directions were given to remove vehicle. Initial details cannot confirm whether person(s) involved were related to the project.	1/02/2021	BM	Built Project Manager contacted HNEH Corporate Services Manager by phone to discuss the incident and offer assistance in identifying those responsible. Investigations ongoing. Subcontractor identified and immediately removed from site. HNE advised of no further issues.	Y
2103-CC022	26/03/2021 6:13am	CG (Resident)	Complaint received via email from Resident regarding works in relation to the tower crane removal commencing prior to 7:00am.	26/03/2021 8:00am	BM	Email response to the resident with apologies and an explanation that the tower crane removal involved a full road closure and significant amount of high risk activity including major plant travelling from Wollongong. This major operation within a busy street/business district requires the implementation of all necessary control measures and traffic management to be in place to prior to works commencing to ensure the safety of the public and site personnel. Further to this, with several delays due to recent inclement weather and ongoing unpredictable forecasts, we required the works to proceed this morning in the interest of safety. We are aiming to complete these works safely and ASAP to minimise further disruptions across the entire weekend and leading up to Easter. Project Superintendent notified DPIE who acknowledged the incident with no further action necessary.	Y
2105-CC023	8/05/2021 9:53am	CG (Resident)	Complaint received regarding noise and vibration from vehicle ('sucker truck') being operated onsite to conduct non-destructive service locating for Service Authority works along Church Street footpath. Resident also complained about the use of pressure hoses to clean footpath and work zone due to wastage of water resources.	10/05/2021 10:31am	BM	Response provided to Resident explaining that the vehicle involved was completing non-destructive testing near live services to mitigate safety and infrastructure damage risks as per industry standard, and that these works were within approved construction working hours. Built also advised that trigger nozzle high-pressure hoses have greater water efficiency than normal garden hoses as suggested by the Resident. No further response received.	Y

Community Liaison Register

Built.

Project: Nihon University	Complaints Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2105-CC024	13/05/2021 9:15am	Newcastle Chambers (Business)	Complaint received regarding construction vehicles parking in Work Zone established by the business outside of their premises for upcoming refurbishment works.	13/05/2021 10:01am	BM	Built PM responded with advice that subcontractors had been notified of the work zone and instructed to immediately remove vehicles. Subcontractors were also reminded that parking along Church Street is prohibited. Response received thanking Built and advising that refurbishment of their property commences the following week. No further issues.	Y
2105-CC025	24/05/2021 3:08pm	City of Newcastle	Advice received from City of Newcastle that Built's work zone on Church Street exceeded the approved length. Option to reduce work zone or pay additional fees.	25/05/2021 8:27am	OR	Built provided apology and agreed to additional fees for extension. No further issues. Note: Work zone was extended due to assumption that it was permitted between boundaries.	Y
2107-CC026	30/07/2021 8:50am	HNEH James Fletcher Hospital	Complaint received from James Fletcher Hospital in relation to safety concerns rasied by staff regarding location of the skip bin and the impact on safe vision when exiting the Hospital.	30/07/2021 8:58am	BM	Built PM responded by both phone and email advising that the skip bin has been removed from site. No further issues.	Y

Community Liaison Register

Built.

Project: Nihon University				Notices Register		Last Updated: 30/07/2021	
REF ID	DATE ISSUED	ISSUED TO	ISSUED BY	METHOD	DESCRIPTION	RESPONSES RECEIVED / DETAILS	CLOSED (Y / N)
1911-CN001	5/11/2019	ALL	SV	LETTER	Dilapidation Report request to nearby stakeholders - residents, businesses, etc.	Responses received from majority of stakeholders. Dilap reports completed by Engineer and submitted.	Y
1912-CN002	13/12/2019	James Fletcher Hospital	SV	MEETING	Consultation meeting with Hunter New England Health Management to discuss upcoming commencement of works, general scope, temporary fencing, boundary, etc.	Response received post-meeting that HNE Health would like the opportunity for NSW Dept. Public Works to review the works.	Y
1912-CN003	19/12/2019	ALL	BM	LETTER	Notice of commencement of works	NIL	Y
2001-CN004	21/01/2020	ALL	BM	EMAIL / LETTER	Notice of commencement of Asbestos removal	NIL	Y
2002-CN005	4/02/2020	Newcastle Police Station	BM / LA	MEETING	Meeting with Sgt Darren Holmes (Station Manager) to discuss shared lighting circuit requiring disconnection, noise mitigation & upcoming Work Zone Installation.	2002-CQ001	Y
2002-CN006	5/02/2020	NGS	BM	MEETING	Consultation meeting with Newcastle Grammar School Deputy Head of School & Director of Operations to discuss potential impacts and concerns regarding relocation of pedestrian crossing and proposed construction zone along Church Street site frontage.	Initial response was positive due to concerns around student & staff safety traversing past live site. Built issued additional information for review and suggested additional meeting if required.	Y
2002-CN007	19/02/2020	Newcastle Police Station	BM	LETTER	Formal notice of work zone installation	NPS raised concerns on lack of solution for parking of Correctional Services vehicles. Requested Built facilitate talks with CoN. Built facilitated discussions with CoN on 20/02/2020 & long term solution was agreed.	Y
2002-CN008	20/02/2020	ALL	BM	EMAIL & LETTER	Construction progress update including completion of Stage 1 asbestos removal, commencement of structural demolition, installation of work zone & pedestrian crossing	Response from Newcastle Grammar School thanking Built for notification and advised they will communicate the information to their parent body.	Y
2003-CN009	2/03/2020	HNE	BM/OR	MEETING	Meeting arranged with HNE & NSW Public Works representatives to discuss heritage wall retention works and other construction activities potentially affecting HNE James Fletcher Hospital	HNE Engineer Jason Thomas was the only attendee. Discussed all works and items. Built issued meeting minutes & retention design to HNE on 04/03/2020 for review and comment Deadline for HNE response is 27/03/2020. Response received from HNE on 27/03/2020 with no objections.	Y

Community Liaison Register

Built.

Project: Nihon University				Notices Register		Last Updated: 30/07/2021	
REF ID	DATE ISSUED	ISSUED TO	ISSUED BY	METHOD	DESCRIPTION	RESPONSES RECEIVED / DETAILS	CLOSED (Y / N)
2004-CN009	3/04/2020	ALL	BM	EMAIL / LETTER	Extended Construction Hours: Notice issued to all surrounding residents, businesses, and organisations advising of the introduction of the Environmental Planning and Assessment (COVID-19 Development - Construction Working Days) Order 2020. The notice advised that Built intended to enact this Order at Nihon University until further advice/notice received from the NSW Dept. Planning, Industry and Environment	Community complaints received from Residents on Church Street. These are referenced below. 2004-CC007 2004-CC008 2004-CC009 2004-CC010 2004-CC012 In response to the community concerns, Built issued additional Community Notice (2004-CN010).	Y
2004-CN010	6/04/2020	ALL	BM	EMAIL / LETTER	Community Response to Extended Construction Hours: Notice issued to surrounding residents, businesses, and organisations advising that in response to community responses received related to 2004-CN009, Built will be extending working hours on Saturday's only in the short term and that any changes will be communicated in advance.	Additional responses were received, however, all were still in relation to extended working hours. Built has continued to implement the revised extended working hours on Saturday's and COVID-19 prevention measures onsite in accordance with Government advice.	Y
2004-CN011	22/04/2020	ALL	BM	EMAIL / LETTER	Construction Progress Update 02: - Noted establishment of Church Street Hoarding. - Advised of structural demolition progress - Advised of commencing piling / retention works in SW corner of the site on 27/04/2020. - Advised of piling method (CFA) to minimise noise and vibration. - Advised of planned Water Main Upgrade works commencing in late May 2020.	NIL	Y
2005-CN012	15/05/2020	HNE	BM	EMAIL	Notice to HNE James Fletcher Hospital regarding commencement of Temporary Ground Anchor Works to new retaining wall as discussed onsite with HNE, dwp, and Built in March 2020 (REF 2003-CN009) and per the design approved by NSW Public Works (reference email received from N. Halpin on 26/03/2020)	HNE response on 18/05/2020 ensuring HNE Engineering is aware of what is occurring on their property. Built (BM) contacted HNE for phone discussion to clarify and followed up with email on 18/05/2020. No outstanding issues.	Y
2006-CN013	4/06/2020	HWC	BM	MEETING	Pre-Commencement Meeting held onsite at Nihon University with Hunter Water, dwp Australia, Metiri Consultants, Built, and Murphy Plumbing to discuss the upcoming watermain upgrade works.	Hunter Water & Metiri Consultants advised of pre-commencement documentation to be submitted prior to commencing works. All actions closed and approval received.	Y

Community Liaison Register

Built.

Project: Nihon University				Notices Register			Last Updated: 30/07/2021
REF ID	DATE ISSUED	ISSUED TO	ISSUED BY	METHOD	DESCRIPTION	RESPONSES RECEIVED / DETAILS	CLOSED (Y / N)
2006-CN014	5/06/2020	NPS	BM	MEETING/EMAIL	Site Meeting held with Newcastle Police Station to advise of and discuss upcoming road / lane closures on Church Street during Hunter Water works and erection of Tower Crane. Post-meeting, Built submitted the TMPs to NPS for information and comment if required.	No additional feedback / comments received. No further action.	Y
2006-CN015	5/06/2020	ALL	BM	EMAIL	Additional Community Notice issued to residents and businesses advising of Hunter Water Upgrade & Crane Erection works commencing.	Received one query from a resident requesting additional information. Received query from HNE James Fletcher Hospital clarifying if their driveway access would be affected. Built issued a Staging Plan and additional information on the works. No further comments received. No further action.	Y
2006-CN016	24/06/2020	HNE	BM	MEETING	Site Meeting and inspection held with Hunter New England Health, dwp Australia, Built, and Murphy Plumbing to discuss upcoming Sewer Main Upgrade requiring access to HNE property.	HNE granted access permission and requested additional notice prior to commencing works.	Y
2007-CN017	28/07/2020	ALL	BM	EMAIL	Construction Progress Update 03 - General update on progress and upcoming works including concrete pours (and related lane closures) and the 21 day notice for water main connection works.	NIL	Y
2007-CN018	29/07/2020	HNE	AM	EMAIL	Email correspondence with HNE regarding upcoming water main connection and potential disruptions to HNE James Fletcher Hospital.	Ongoing coordination with HNE contacts to ensure water connection does not cause disruption to normal operations. No disruptions to HNE operations & no further issues.	Y
2009-CN019	3/09/2020	HNE	BM	EMAIL	Provided HNE with an As-Built documentation package for retention works completed on the adjoining heritage retaining wall along the southern boundary of Nihon University and HNE James Fletcher Hospital.	No additional feedback / comments received. No further action.	Y
2009-CN020	23/09/2020	ALL	BM	EMAIL	Construction progress update and advising of upcoming works including additional Hunter Water infrastructure works and road restoration on Church Street.	Response received regarding ongoing implementation of DPIE Extended Working Hours Order 2020. Built confirmed extended hours are still ongoing in accordance with the Order and that any changes will be communicated to the community.	Y
2010-CN021	27/10/2020	HNE	BM	EMAIL	Notice provided that a section of the chain link fence along the western boundary has been relocated further west to accommodate scaffold. Advised that fencing and scaffold is still within Nihon site boundary. Marked up plan was also attached for information.	Response received thanking for the notice. Nil actions.	Y

Community Liaison Register

Built.

Project: Nihon University				Notices Register		Last Updated: 30/07/2021	
REF ID	DATE ISSUED	ISSUED TO	ISSUED BY	METHOD	DESCRIPTION	RESPONSES RECEIVED / DETAILS	CLOSED (Y / N)
2011-CN022	18/11/2020	ALL	BM	EMAIL	Notice provided to community regarding scheduled road restoration works on Church Street as part of the Hunter Water Upgrade Works package.	Response received from resident regarding driveway access. Built advised access limited for a single day. No further issues. Newcastle Police contacted Built PM after works completed advising that no issues were rasied during the works.	Y
2012-CN023	9/12/2020	ALL	OR	EMAIL	Notice provided to community stakeholders advising of partial road closures on Church Street for scheduled concrete pours on 11th & 14th December.	Response received from Grand Hotel, NGS, and HNEH James Fletcher thanking Built for the notice. Nil actions.	Y
2012-CN024	9/12/2020	ALL	OR	EMAIL	Notice provided to community stakeholders advising of rescheduled partial road closure on Church Street for rescheduled concrete pour on 10th December due to inclement weather.	Response received from Grand Hotel, NGS, and HNEH James Fletcher thanking Built for the notice. Nil actions.	Y
2012-CN025	10/12/2020	ALL	OR	EMAIL	Notice provided to community stakeholders advising of partial road closures on Church Street for concrete pours scheduled between December 2020 to mid-January 2021.	No response received.	Y
2012-CN026	21/12/2020	ALL	BM	EMAIL	Construction progress update and advising of upcoming works in early 2021 including concrete pours and public domain works.	No response received.	Y
2101-CN027	22/01/2021	ALL	BM	EMAIL	Community notice advising of upcoming road and footpath closures to enable construction works.	No response received.	Y
2102-CN028	5/02/2021	ALL	BM	EMAIL	Community notice advising of amended dates for upcoming road and footpath closures to enable Hunter Water works.	No response received.	Y
2102-CN029	11/02/2021	Newcastle Police Station	BM	MEETING	Consultation meeting held onsite with Newcastle Police personnel to discuss upcoming cabling works.	No issues raised. Works will be coordinated with NPS to minimise any disruptions.	Y
2102-CN030	26/02/2021	ALL	BM	EMAIL	Community notice advising that the tower crane removal and road closure has been rescheduled to 12th & 13th March 2021.	No response received.	Y
2103-CN031	10/03/2021	ALL	BM	EMAIL	Community notice advising that the tower crane removal and road closure has been rescheduled to the 19th & 20th March 2021 due to forecast inclement weather.	No response received.	Y
2103-CN032	23/03/2021	ALL	BM	EMAIL	Community notice advising that the tower crane removal and road closure has been rescheduled to the 26th & 27th March 2021 due to forecast inclement weather.	No response received.	Y
2103-CN033	25/03/2021	ALL	BM	EMAIL	Update advising of upcoming road closures, Authority service works, commencement of s.138 works, and general construction progress.	No response received.	Y

Community Liaison Register

Built.

Project: Nihon University				Notices Register		Last Updated: 30/07/2021	
REF ID	DATE ISSUED	ISSUED TO	ISSUED BY	METHOD	DESCRIPTION	RESPONSES RECEIVED / DETAILS	CLOSED (Y / N)
2103-CN034	29.03.2021	City of Newcastle	BM	Site Meeting	Consultation meeting with City of Newcastle Public Works Coordinator to discuss upcoming Section 138 Public Domain Works.	Built to coordinate regular inspection with Council throughout the works as required by permit conditions.	Y
2104-CN035	01.04.2021	Newcastle Police Station	LA	Site Meeting	Consultation meeting with Newcastle Police Station regarding the full road closure on Church Street scheduled for 29.04.2021 to enable a farewell parade for a retiring senior Officer.	Built communicated road closure to site personnel and cooperated with Police requests to prevent disruptions to the parade.	Y
2104-CN036	02.04.2021	Grand Hotel	LA	Site Meeting	Consultation meeting with the Grand Hotel regarding Section 138 works adjacent to their property including seeking permission for the installation of temporary propping to enable excavation works.	Verbal permission received. Built has proceeded with planning the works and will continue to consult with the property owner. The temporary works design was submitted to the owner on 12/07/21 after further discussions.	Y
2106-CN037	17.06.2021	HNE James Fletcher Hospital	BM	EMAIL	Email correspondence sent to HNE stakeholders requesting access to their property for removal of temporary fencing and construction of new boundary fence.	Permission received. Subcontractors must sign in and complete induction prior to commencing.	Y
2106-CN038	21.06.2021	ALL	BM	EMAIL	Notice issued to the community in regard to partial road closure scheduled for 28.06.2021 to allow lifting and installation of glazing panels to roof skylight	No response received.	Y
2106-CN039	22.06.2021	ALL	BM	EMAIL	Notice issued to community regarding public authority works on Church Street requiring after hours work.	No response received.	Y
2107-CN040	07.07.2021	City of Newcastle	BM	Site Meeting	Site meeting with CoN infrastructure representatives to discuss extent and timing of road restoration works.	CoN advised they wished to coordinate public infrastructure works with Built's to minimise disruption to the community. Built provided the required information to CoN and now waiting for confirmation. CoN agreed to coordinating works in accordance with Built's construction programme.	Y
2107-CN041	12.07.2021	ALL	BM	EMAIL	Notice issued to community regarding a footpath closure and commencement of Section 138 works adjacent to the Grand Hotel.	No response received.	Y

Community Liaison Register

Built.

Project: Nihon University	Queries Register	Last Updated: 30/07/2021

REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2002-CQ001	4/02/2020	Newcastle Police Station	Request for sound baffling installed to L1, 2, 3 Balcony Windows due to meeting held on 03/02/2020	4/02/2020	BM	Confimed that BUILT can organise an inspection by Acoustic Consultant and provide an appropriate solution. Acoustic solution provided by Consultant is to install acoustic door seals.	Y
2002-CQ002	19/02/2020	Newcastle Police Station	Request for Built to facilitate talks with City of Newcastle regarding long term solution for Correctional Services vehicle parking	19/02/2020	BM	Built has scheduled onsite meeting with Newcastle Police Station & City of Newcastle for 20/02/2020 to discuss solutions. City of Newcastle agreed to provide permanent parking on Watt Street for required vehicles.	Y
2003-CQ003	03/03/2020 1:04pm	AR	Email received from AR. Spoke with Built Foreman onsite regarding blanked out pedestrian crossing and concerns around pedestrian safety due to lack of signage & physical barriers warning common users that the crossing is no longer in place. Forwarded email sent to City of Newcastle expressing same concerns plus stating that Built had traffic control personnel onsite directing pedestrians which was good to see. Advised Council that additional signage should be implemented	04/03/2020 10:35am	BM	Response email sent acknowledging concerns and advising that Built is working with Council to ensure signage is installed ASAP. City of Newcastle responded on 09/03/20 with additional requirements originally not requested during consultation. All actions closed out.	Y
2003-CQ004	26/03/2020 5:19pm	JS	Email sent to Structural Engineer responsible for completing Pre-Construction Dilapidation Report on the property requesting that vibration causing activities be noted for Post-Construction Dilapidation Inspection.	27/03/2020	BM	Noted by Built & Engineer. No further correspondence received.	Y
2004-CQ005	01/04/2020 12:21pm	JP	Email sent to Nihon community liaison address advising of vibration felt within their residence caused by a loaded vehicle entering site	02/04/2020 2:06pm	BM	Response email sent noting concerns and advising of Built monitoring activities to maintain compliance and minimise disruptions. Advised the resident to contact if there are any further concerns or structural changes noted. No further response received.	Y
2004-CQ006	01/04/2020 12:47pm	KD	Email sent to Nihon community liaison address advising that vibrations were felt at various times throughout the day.	02/04/2020 2:08pm	BM	Response email sent noting concerns and advising of Built monitoring activities to maintain compliance and minimise disruptions. Advised the resident to contact if there are any further concerns or structural changes noted. No further response received.	Y
2005-CQ008	18/05/2020	Newcastle Grammar School	Phone call to Built & follow up email notifying Built that construction vehicles (trucks) were standing in the school drop off/pick-up zone. Noted this was prior to school zone hours and requested an alert to be raised with Built & Subcontractors to ensure no issues moving forward.	19/05/2020 9:24am	OR	Built immediately instructed Subcontractors on 18/05/2020 not to use this zone at any time. Follow up email sent to NGS advising them of action taken and acknowledging concerns. NGS had no further issues.	Y

Community Liaison Register

Built.

Project: Nihon University			Queries Register				Last Updated: 30/07/2021
REF ID	DATE / TIME RECEIVED	RECEIVED FROM	DESCRIPTION	DATE / TIME RESPONDED	RESPONSE BY	DESCRIPTION	CLOSED (Y / N)
2008-CQ009	10/08/2020	JP	Emailed Engineer responsible for dilapidation report to note potential cosmetic issues related to 2004-CQ005. Engineer contacted Built PM to advise.	10/08/2020	BM	Built PM contacted the resident via phone call to enquire further and requested photos to forward to Engineer for preliminary review. Resident submitted photos via email on 24/08/2020. Built PM forwarded photos to Engineer and has requested an inspection of the property to investigate further. The engineer inspected the property on 09/09/20 and reviewed alleged damage against pre-existing condition, noting that the majority of items were existing, whilst the remaining were minor and not captured within the original report. Built advised that these issues have been noted and would be further assessed at the completion of the post-construction dilapidation survey. No further comment has been received from the resident.	Y
2010-CQ010	19/10/2020	NGS	Received email advising that students would be using the building opposite Nihon University as a temporary exam facility for the next three weeks. Provided key exam dates with request that noise is minimised where able.	20/10/2020	BM	Built PM responded with advice that key exam dates did not currently clash with major construction activities (subject to change). Advised that as a precaution, additional noise monitoring and measures would be implemented where practicable and reasonable to do so if required.	Y

Appendix C – Audit Records

Monitoring

Details

Form id	221818
Created at	06/07/2021 by Robbie Clydesdale
Completed at	06/07/2021
Last modified	06/07/2021 09:15:41 by Robbie Clydesdale
Status	Complete
Respondent	Robbie Clydesdale
Division	NSW
Business unit	Newcastle Fitout
Department	
Project	Nihon University Newcastle Campus
Subcontractor	WOODBURY CIVIL PTY LIMITED
Monitoring Activity	SWMS Monitoring
Outline of activity being monitored	excavating tree vaults on church street
Documents referenced during monitoring *This could include; SWMS, Permit, Traffic Management Plans, Methodology documents, Engineering advice, SOP/JSA. Where possible provide the exact name and version number of the document.*	Operating excavators
Summary of monitoring *Provide an outline of any positive observations or conversations, work practices being performed well, compliance with the documents reference or a brief outline.*	Spotter in place while benching down, operator has filled in pre start book Exclusion zone in place around machine.
Was work required to be stopped?	No

Built staff in attendance

Include the person who is logged in to the software in this section as well as the other attendees

Attendee name
Robbie Clydesdale

Others in attendance

This could include workers involved in the activity, the subcontractor supervisor or others

Subcontractor name	Persons name

Monitoring

Additional

Photos



CIVIL CONTRACTORS FEDERATION

Plant Daily Inspection – Fault Report

Company Name: Woodbury Civil Week commencing: 5.7.21

Project: Courthouse Site/Location: Newcastle

Plant Type: Stex Plant No: 66 Plant Rego No:

Plant Operator Daily Safety Checklist

Operators are required to check the following items before commencing work. These records form the basis of a plant maintenance procedure and will be subject to random inspection. Keep the record with you at all times.

Please mark the boxes: [✓] OK No obvious defect [X] Fault identified (Use Fault/Defect Report below) [NA] Item not Applicable to this Plant

	Mon	Tue	Wed	Thur	Fri	Sat	Sun
Before commencing operations check –							
Record Plant Hours/Kilometre Reading	234	239					
1. Brakes, steering, gauges, lights, warning devices	✓	✓					
2. Visibility – windscreen, wipers, washer, demister, mirrors, windows	✓	✓					
3. Cabin – access/egress, seating, seatbelts, loose objects, control levers	✓	✓					
4. Wheels, tyres, nuts, damage, wear, pressure (visual)	✓	✓					
5. Guards – in place, secure, warning signs – lights, alarms	✓	✓					
6. Hydraulics – rams, hoses, leaks, wear	✓	✓					
7. Excessive wear – hooks, chains, pins, pivots, tracks, ground engagement tools	✓	✓					
8. Oil and Coolant Levels	✓	✓					
Miscellaneous electrical, fire extinguisher, communications	✓	✓					
Operators Names (Please print)	B. Sanderman						
Operator's Signatures	M						
Supervisor's Signature – Random Check							

Plant Fault/Defect Report

To be used to report any fault or defect identified during daily plant safety checks or during work operations.

Reported by: Reported to:

Position: Position:

Date:

Method of reporting: Telephone ☐ In person ☐ Radio ☐

Details of fault/defect:

Does fault constitute a safety hazard? Yes/No

Does machine require immediate repair? Yes/No

If **YES** to either, **PARK MACHINE UP**, contact the Plant Manager or Supervisor.

Machine **SHALL NOT BE USED** until Plant Manager or his delegate gives clearance for use.

If **NO**, indicate when machine requires attention and send this form in with daily report.

Requires attention in next few days. Yes/No Requires attention at next service. Yes/No

Signature: Date:

© Civil Contractors Federation Victoria

Distribution: White copy (client), Yellow copy (plant file), Blue copy (book)

Revision: September 2014



Attachments

- *No file attachments*

Actions

Monitoring

ID	First name	Last name	Due date	Date closed	Action description	Status	Last Comment

Actions

Monitoring

Details

Form id	223441
Created at	12/07/2021 by Jack Garland
Completed at	15/07/2021
Last modified	15/07/2021 09:38:02 by Jack Garland
Status	Complete
Respondent	Jack Garland
Division	NSW
Business unit	Newcastle Fitout
Department	
Project	Nihon University Newcastle Campus
Subcontractor	WOODBURY CIVIL PTY LIMITED
Monitoring Activity	SWMS Monitoring
Outline of activity being monitored	Replacing road base to kerb and gutter
Documents referenced during monitoring *This could include; SWMS, Permit, Traffic Management Plans, Methodology documents, Engineering advice, SOP/JSA. Where possible provide the exact name and version number of the document.*	Woodbury's swms
Summary of monitoring *Provide an outline of any positive observations or conversations, work practices being performed well, compliance with the documents reference or a brief outline.*	Working near road zone - spotter in place - watering done road base to prevent dust - traffic controllers in place - workers are all wearing high vis
Was work required to be stopped?	No

High Potential Hazard Reporting

High Potential ***Select from the drop down list those which apply. Use the Add button to add one line per issue***	**Trade/process** ***State the trade who has been identified as being responsible for the hazard. If unknown please state 'Unknown'***	**Comments** ***Describe the situation that is classified as High Potential***

Built staff in attendance

Include the person who is logged in to the software in this section as well as the other attendees

Attendee name
Jack Garland

Others in attendance

This could include workers involved in the activity, the subcontractor supervisor or others

Subcontractor name	**Persons name**

Monitoring

Additional


Photos

Monitoring



Monitoring



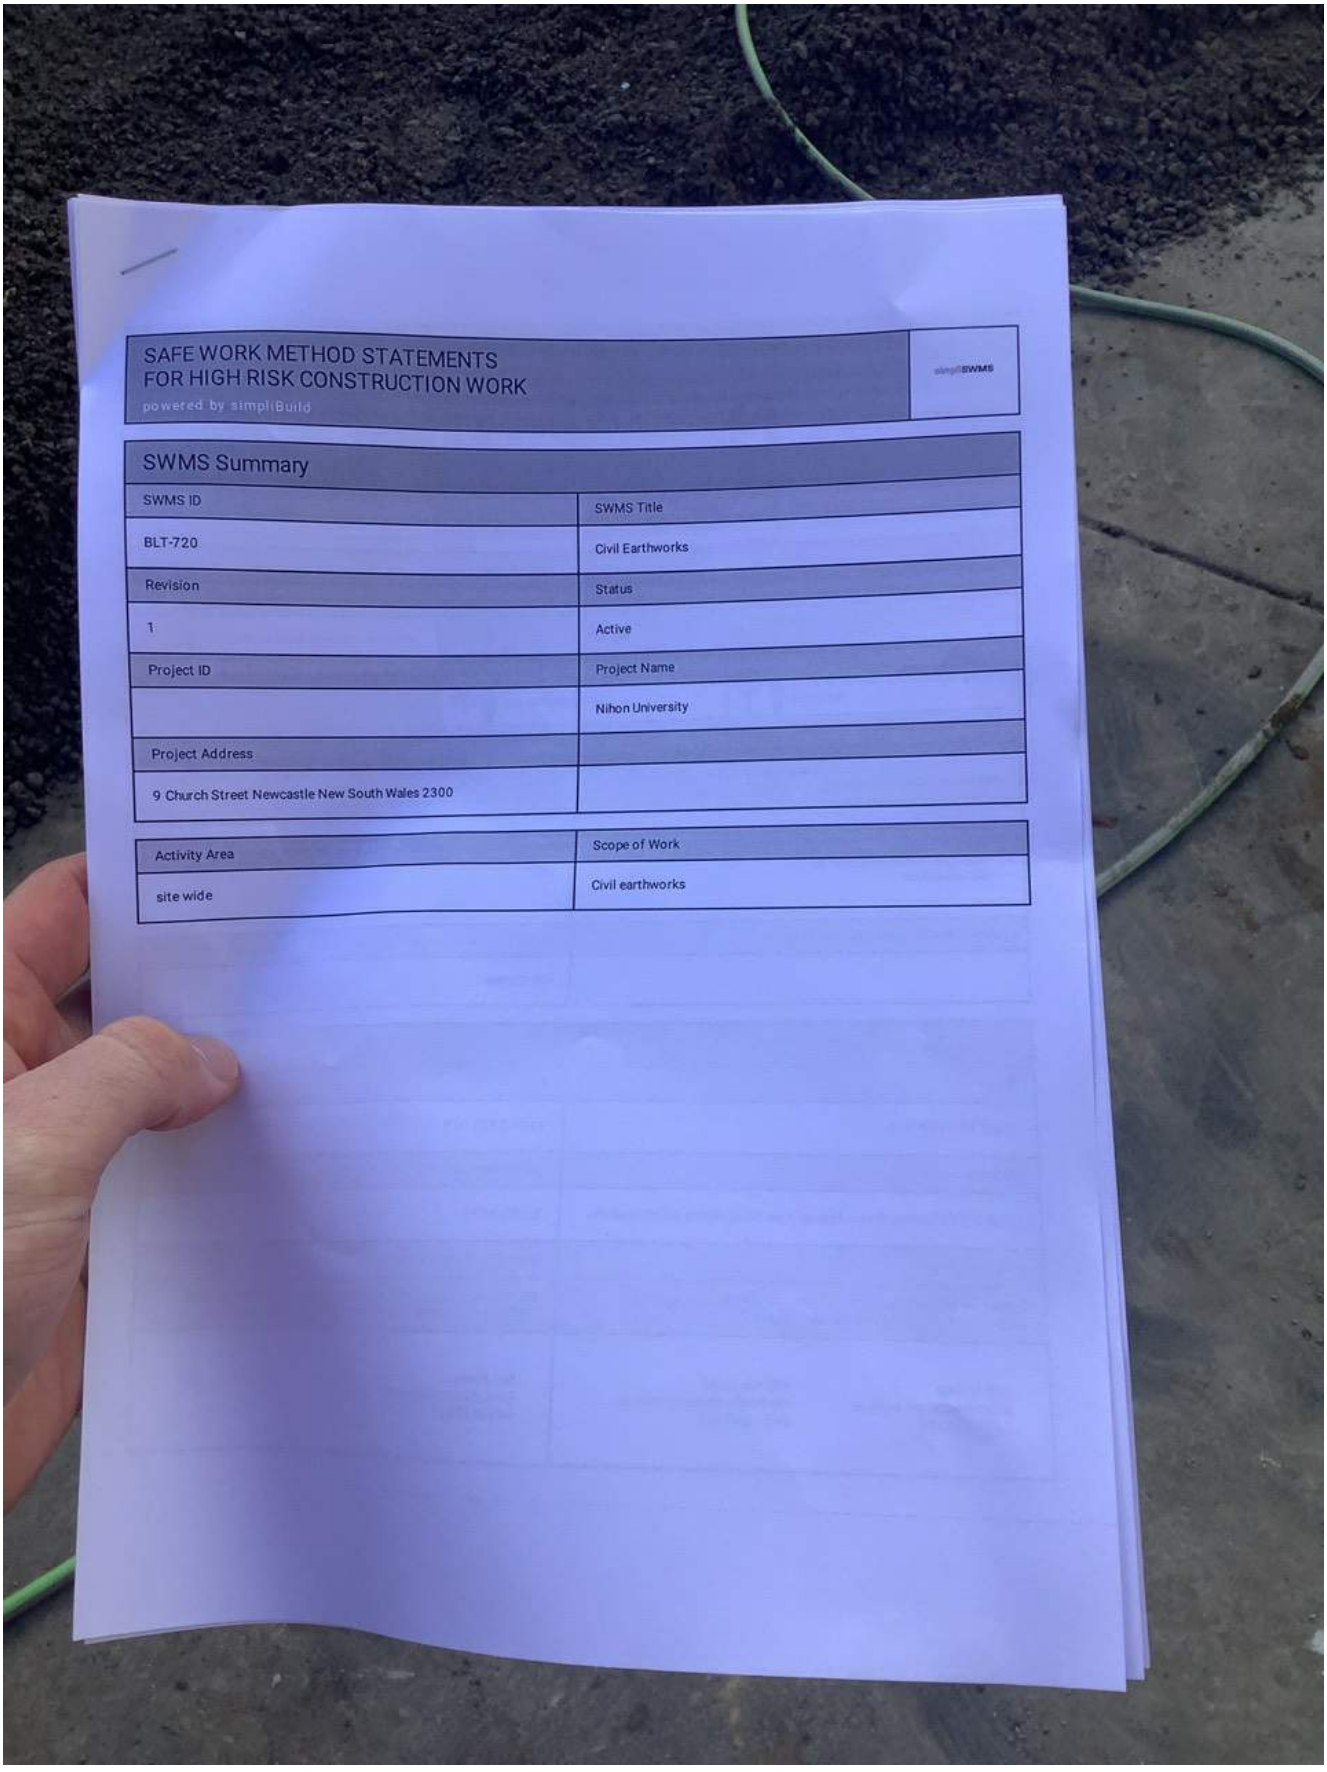

Attachments

- *No file attachments*

Actions

Monitoring

ID	First name	Last name	Due date	Date closed	Action description	Status	Last Comment

Actions

Site Inspection

Details

Form id	226181
Created at	27/07/2021 by Benjamin Moss
Completed at	27/07/2021
Last modified	27/07/2021 08:49:02 by Benjamin Moss
Status	Complete
Respondent	Benjamin Moss
Division	NSW
Business unit	Newcastle Fitout
Department	
Project	Nihon University Newcastle Campus
Subcontractor	
Type of Site Inspection	Supervisor Inspection

Built Attendance

Include the person who is logged in as well.

Name
Benjamin Moss

Others in attendance

Subcontractor Name	Persons Name

Areas or Locations Inspected *Identify the area/s reviewed during the inspection. The may include; whole of project, certain levels or certain locations.*	Site frontage
Summary of inspection *This may include; common checks, activities or items reviewed, good practices observed or general commentary of the inspection.* *Note; all actions need to be registered in the "Actions" area at the bottom of this page.*	- signage in place - traffic & pedestrian control in place incl. signage - sediment control in place - plant log books signed - COVID signage & QR code's at entrance - fencing in place, in good condition and with dust screens - dust control in place (exposed surfaces being lightly wetted) - waste management good / skip bins available

High Potential Hazard Reporting

High Potential Classification ***Select from the drop down list those which apply. Use the Add button to add one line per issue***	Trade/Process ***State the trade who has been identified as being responsible for the hazard. If unknown please state 'Unknown'***	Comments ***Describe the situation that is classified as High Potential***


Site Inspection

Additional

Photos


Nihon University Project
9 Church Street, Newcastle
Built.
RENT A FENCE
0411 554 479



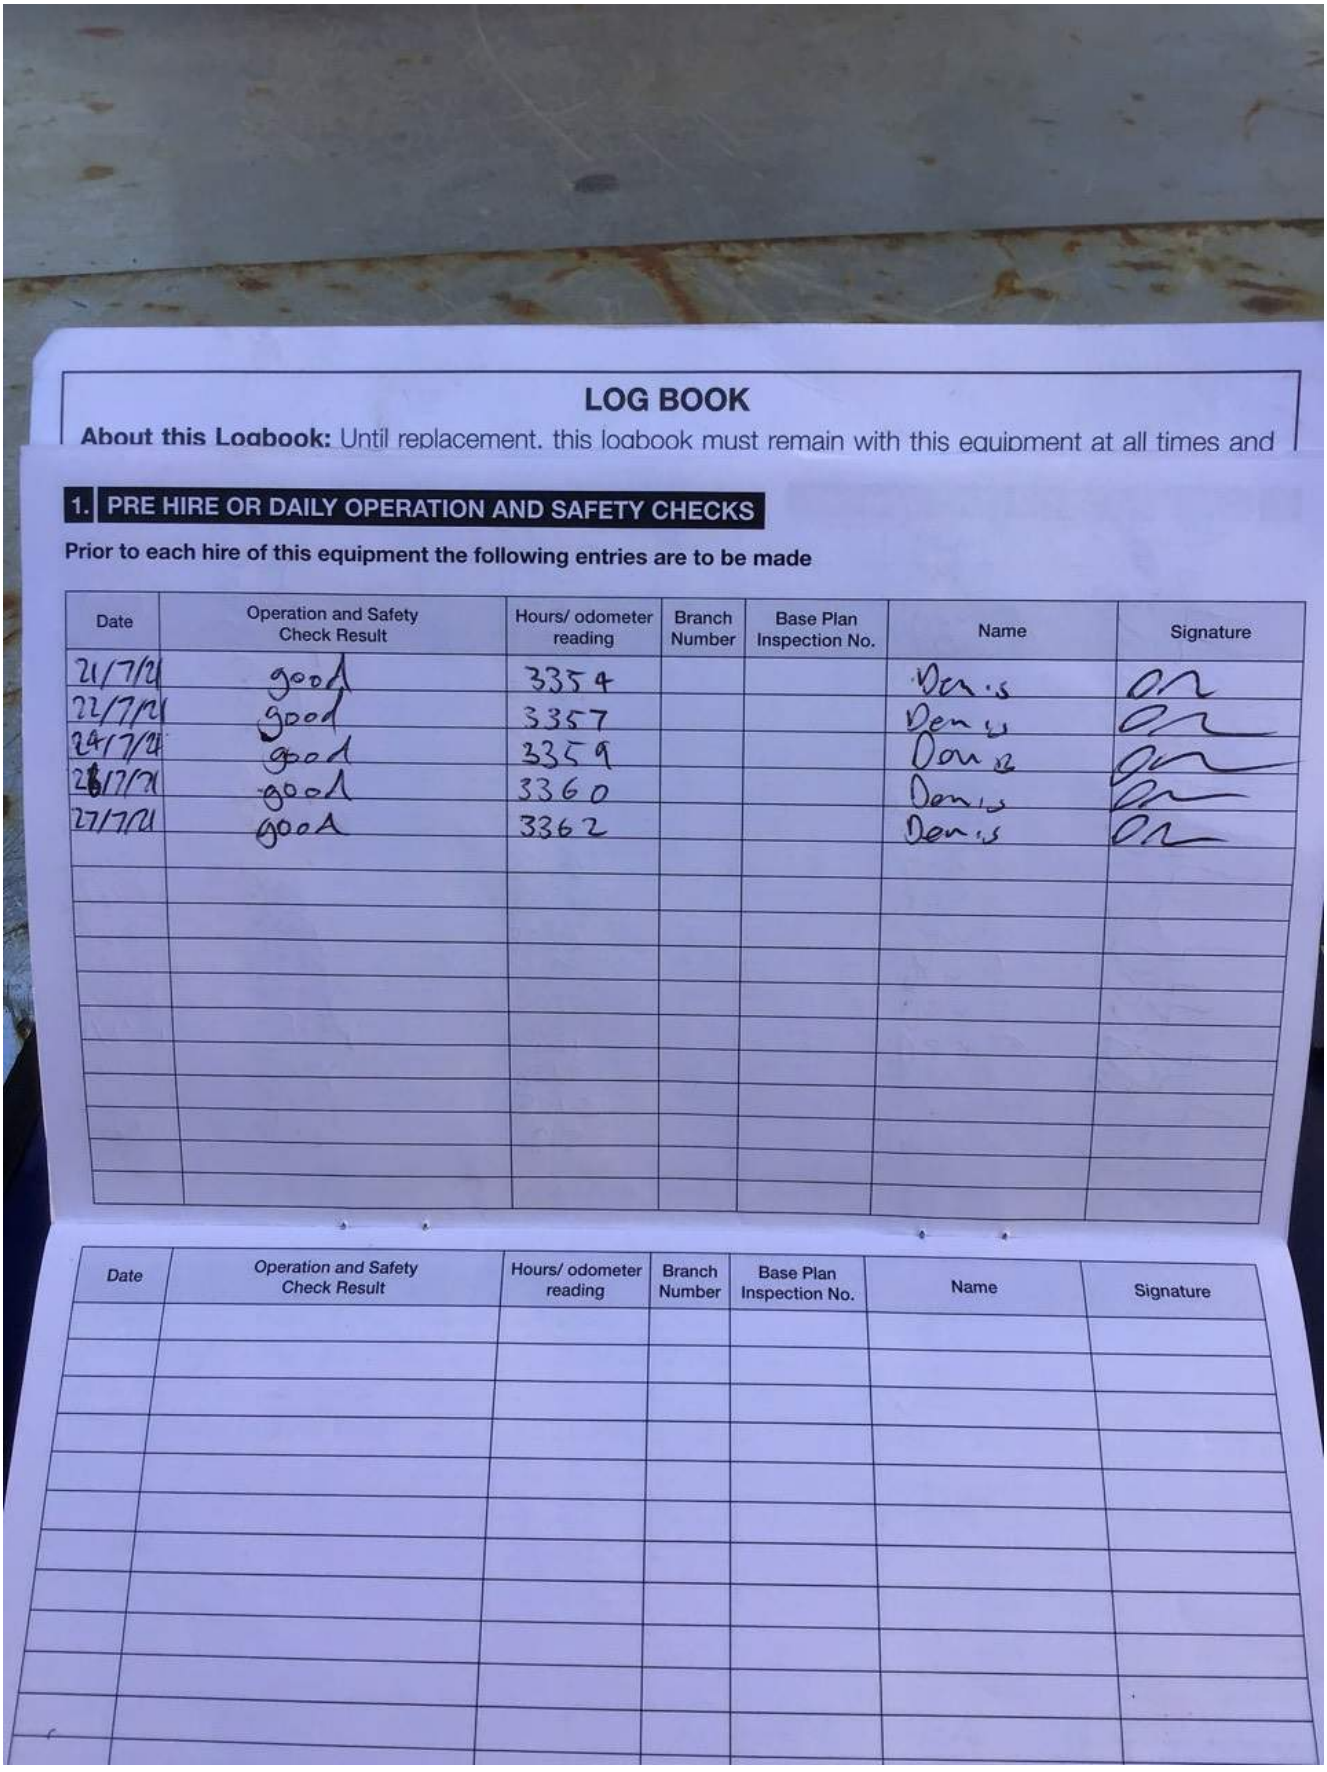

LOG BOOK

About this Logbook: Until replacement, this logbook must remain with this equipment at all times and


1. PRE HIRE OR DAILY OPERATION AND SAFETY CHECKS

Prior to each hire of this equipment the following entries are to be made

Date	Operation and Safety Check Result	Hours/ odometer reading	Branch Number	Base Plan Inspection No.	Name	Signature
21/7/21	good	3354			Denis	
22/7/21	good	3357			Denis	
24/7/21	good	3359			Denis	
26/7/21	good	3360			Denis	
27/7/21	good	3362			Denis	

Date	Operation and Safety Check Result	Hours/ odometer reading	Branch Number	Base Plan Inspection No.	Name	Signature


4000
CESS
e.net

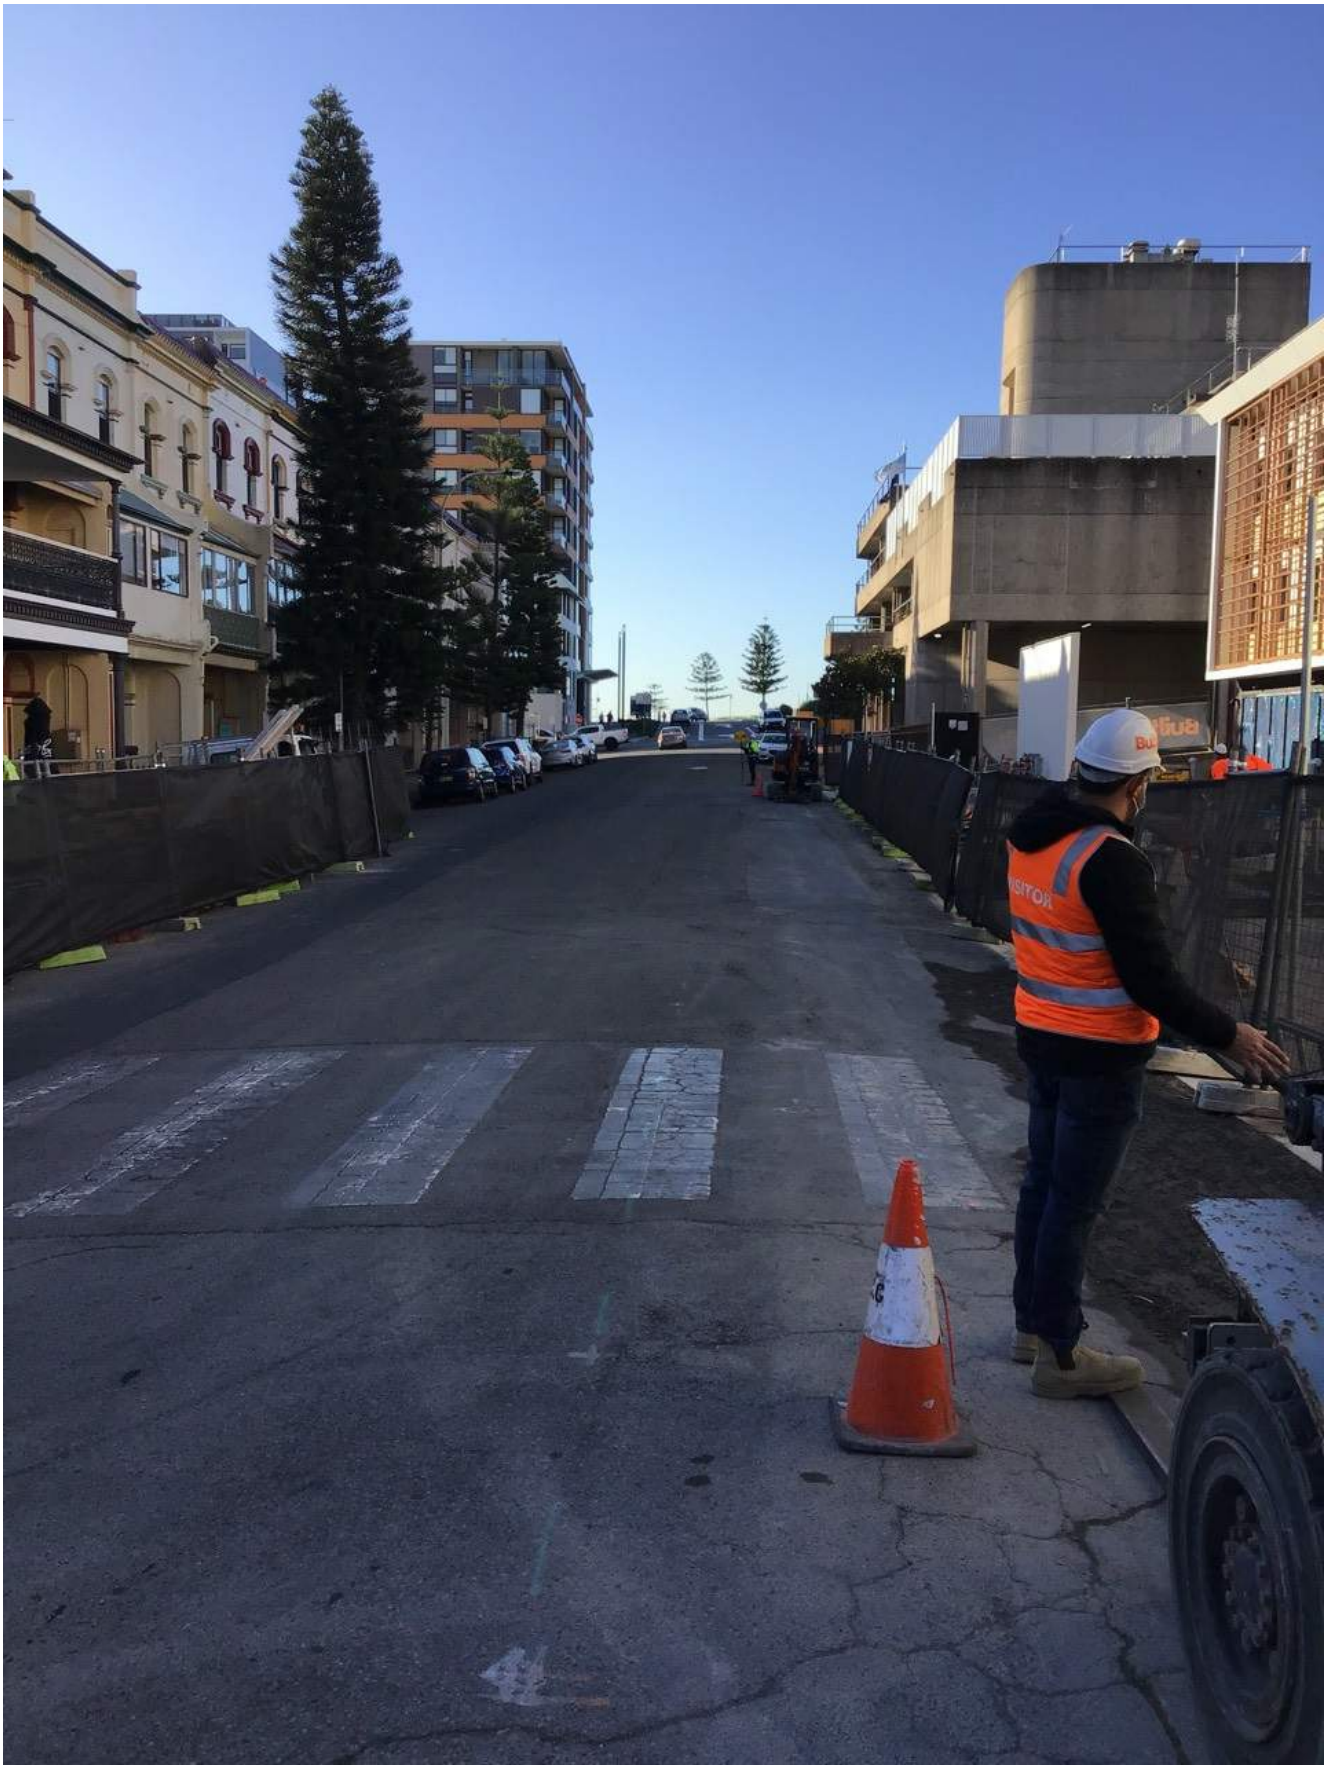


surescope
BUILDING CERTIFIERS
BUILDING CERTIFYING AUTHORITY
• CONSTRUCTION APPROVALS
• BUILDING CERTIFICATION
• BCA COMPLIANCE REPORTING
• FIRE SAFETY AUDITS
P 02 4940 0355
Suite 4C 250 Pacific Hwy Charlestown NSW 2290
office@scopecert.com.au www.surescope.com.au ABN 77 611 724 693
Built.
No unauthorised entry
Personal protective equipment & clothing must be worn on this site
All personnel must complete site & industry induction before starting work on site
All electrical equipment must have a current inspection tag & be in good working order
All visitors must report to site office
Vehicle access for deliveries by appointment only, contact Site Manager for access
All high risk construction works must have a specific SWMS
All mobile plant must be inducted to site before use
Nihon University
Project address
9 Church St
Newcastle
Office address
Level 1
155 – 157 Lambton Rd
Broadmeadow
24hr Contacts
Site Manager
BEN BATES
Built Office
02 4077 5900
Security
Secom
1300 360 535


Covid Safe Check In
Nihon University
NSW
1. Please scan the QR Code with your smart phone camera or QR Code reader
2. Follow the prompts on the ServiceNSW app
3. Show a Built person once complete
Speak with a Built supervisor for any assistance
Built.
All workers from the Greater Sydney region, inclusive of the Central Coast, must present a weekly Covid 19 Test to Built.
Built.
WEAR A FACE MASK
Face masks are required in all indoor and outdoor areas
Built.


PEDESTRIANS
Built.




DO NOT LOAD ABOVE SIDES
NO FIBRO
CENTRAL
WASTE SKIPS
1800 180





Attachments

- *No file attachments*

Actions

Site Inspection

ID	First name	Last name	Due date	Date closed	Action description	Status	Last Comment

Actions

Site Inspection

Details

Form id	219829
Created at	30/06/2021 by Benjamin Moss
Completed at	30/06/2021
Last modified	30/06/2021 09:35:01 by Benjamin Moss
Status	Complete
Respondent	Benjamin Moss
Division	NSW
Business unit	Newcastle Fitout
Department	
Project	Nihon University Newcastle Campus
Subcontractor	
Type of Site Inspection	Supervisor Inspection

Built Attendance

Include the person who is logged in as well.

Name
Benjamin Moss
Michael Louis
Jack Garland

Others in attendance

Subcontractor Name	Persons Name

Areas or Locations Inspected *Identify the area/s reviewed during the inspection. The may include; whole of project, certain levels or certain locations.*	Site
Summary of inspection *This may include; common checks, activities or items reviewed, good practices observed or general commentary of the inspection.* *Note; all actions need to be registered in the "Actions" area at the bottom of this page.*	- Painter in BLD B Level 2 standing on paint drum. Stopped and instructed to use ladder. - Bricklayer stopped from working due to leads piggy backed. RCD box used instead. - Exclusion zone, signage, and spotters in place for crane lift. - crane set up as per lift plan. - Traffic control personnel and signage in place. - Project and statutory signage in place on fence. - Temp fence and mesh screens in good condition. No sign of damage/graffiti. - Footpath and road clean & clear. - Poorly set up exclusion zone in place around civil works. Subcontractor rectified. - Civil plant (drum roller) found with no induction sticker. Log book not signed. - Cited plumbers hot works permit.
High Potential Hazard Reporting	

Site Inspection


High Potential Classification *Select from the drop down list those which apply. Use the Add button to add one line per issue*	Trade/Process *State the trade who has been identified as being responsible for the hazard. If unknown please state 'Unknown'*	Comments *Describe the situation that is classified as High Potential*

Additional

Photos




Built.
CERTIS
SECURITY

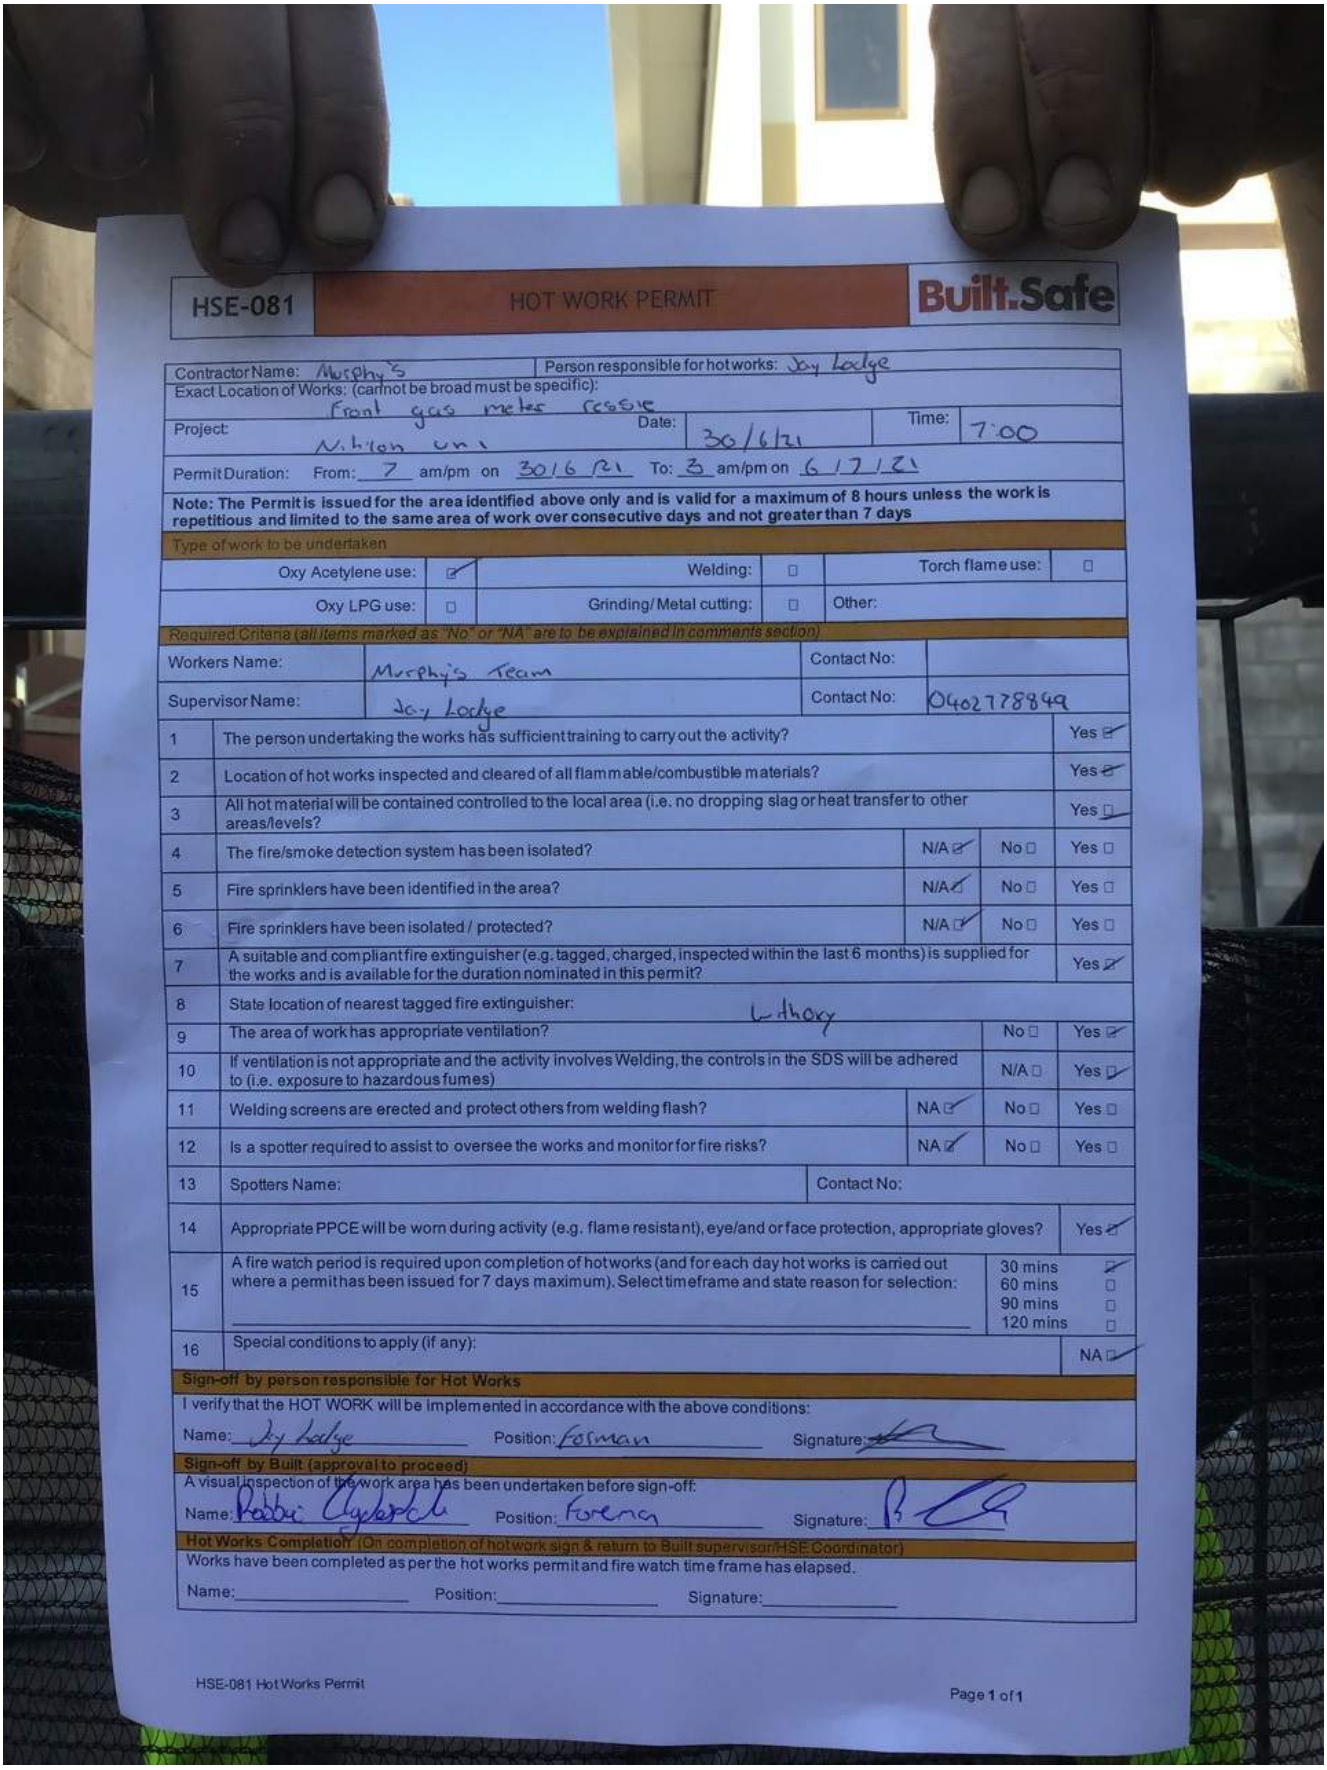

HSE-081 | HOT WORK PERMIT | Built.Safe

Contractor Name: Murphy's | Person responsible for hot works: Jay Lodge

Exact Location of Works: (cannot be broad must be specific): Front gas meter recess

Project: Nihon uni | Date: 30/6/21 | Time: 7:00

Permit Duration: From: 7 am/pm on 30/6/21 To: 3 am/pm on 6/7/21

Note: The Permit is issued for the area identified above only and is valid for a maximum of 8 hours unless the work is repetitious and limited to the same area of work over consecutive days and not greater than 7 days

Type of work to be undertaken

Oxy Acetylene use:	☑	Welding:	☐	Torch flame use:	☐
Oxy LPG use:	☐	Grinding/ Metal cutting:	☐	Other:	

Required Criteria (*all items marked as "No" or "NA" are to be explained in comments section*)

Workers Name:	Murphy's Team	Contact No:	
Supervisor Name:	Jay Lodge	Contact No:	0402778849

1	The person undertaking the works has sufficient training to carry out the activity?			Yes ☑
2	Location of hot works inspected and cleared of all flammable/combustible materials?			Yes ☑
3	All hot material will be contained controlled to the local area (i.e. no dropping slag or heat transfer to other areas/levels?			Yes ☐
4	The fire/smoke detection system has been isolated?	N/A ☑	No ☐	Yes ☐
5	Fire sprinklers have been identified in the area?	N/A ☑	No ☐	Yes ☐
6	Fire sprinklers have been isolated / protected?	N/A ☑	No ☐	Yes ☐
7	A suitable and compliant fire extinguisher (e.g. tagged, charged, inspected within the last 6 months) is supplied for the works and is available for the duration nominated in this permit?			Yes ☑
8	State location of nearest tagged fire extinguisher: Ute			
9	The area of work has appropriate ventilation?		No ☐	Yes ☑
10	If ventilation is not appropriate and the activity involves Welding, the controls in the SDS will be adhered to (i.e. exposure to hazardous fumes)		N/A ☐	Yes ☑
11	Welding screens are erected and protect others from welding flash?	NA ☑	No ☐	Yes ☐
12	Is a spotter required to assist to oversee the works and monitor for fire risks?	NA ☑	No ☐	Yes ☐
13	Spotters Name:	Contact No:		
14	Appropriate PPCE will be worn during activity (e.g. flame resistant), eye/and or face protection, appropriate gloves?			Yes ☑
15	A fire watch period is required upon completion of hot works (and for each day hot works is carried out where a permit has been issued for 7 days maximum). Select timeframe and state reason for selection: _____			30 mins ☑ 60 mins ☐ 90 mins ☐ 120 mins ☐
16	Special conditions to apply (if any):			NA ☑

Sign-off by person responsible for Hot Works

I verify that the HOT WORK will be implemented in accordance with the above conditions:

Name: Jay Lodge Position: Forman Signature:

Sign-off by Built (approval to proceed)

A visual inspection of the work area has been undertaken before sign-off:

Name: Robbie Aylward Position: Foreman Signature:

Hot Works Completion (On completion of hot work sign & return to Built supervisor/HSE Coordinator)

Works have been completed as per the hot works permit and fire watch time frame has elapsed.

Name: Position: Signature:

HSE-081 Hot Works Permit

Page 1 of 1


Built.
Nihon University
Project address
9 Church St
Newcastle
Site office address
On site
24hr Contacts
Site Manager
Leif Aldrich
0439 913 387
Project Manager
Den Moss
Security
Newcastle Security
0447 678 180


Built.
00178
Plant item: DRUM ROLLER
Serial No: 9407 18 04
Contractor: WOODBURY
Contact Name: JDE
Date: 30.06.21
Contact No:
Project No: 201229
Plant Registration No (where applicable): 78508.D
Plant Induction Expiry Date: 30.08.21

Site Inspection





Attachments

- *No file attachments*

Actions

Site Inspection

ID	First name	Last name	Due date	Date closed	Action description	Status	Last Comment

Actions


Appendix D – Statused Contract Programme

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
0	**NIHON UNIVERSITY NEWCASTLE NSW AUSTRALIA**	**527 d**	**Wed 18/09/19**	**Fri 27/08/21**	**98%**
1	**KEY PROJECT MILESTONES**	**508 d**	**Mon 21/10/19**	**Fri 27/08/21**	**99%**
2	Built announced as preferred contractor	0 d	Mon 21/10/19	Mon 21/10/19	*100%*
3	Letter of Intent Issued	0 d	Wed 23/10/19	Wed 23/10/19	*100%*
4	Built Ready to Begin Works	0 d	Thu 24/10/19	Thu 24/10/19	*100%*
5	*Hoarding Permit Approved*	*0 d*	*Sat 9/11/19*	*Sat 9/11/19*	*100%*
6	Work Zone Permit Approved	10 d	Tue 4/02/20	Sat 15/02/20	100%
7	Design Approved to Progress to CC	0 d	Sat 7/12/19	Sat 7/12/19	*100%*
8	*PCA Approval for Demolition Works to Commence*	*0 d*	*Tue 17/12/19*	*Tue 17/12/19*	*100%*
9	*CC#1 for SW Corner Shoring Works*	*0 d*	*Fri 17/04/20*	*Fri 17/04/20*	*100%*
10	*CC#2 for Superstructure, Façade, Finishes & Services_Residential Approved*	*0 d*	*Tue 26/05/20*	*Tue 26/05/20*	*100%*
11	*CC#3 for Superstructure, Façade, Finishes & Services_Education Approved*	*0 d*	*Mon 20/07/20*	*Mon 20/07/20*	*100%*
12	Site Established Construction Works Begin	0 d	Tue 14/01/20	Tue 14/01/20	*100%*
13	Demolition Approval - Construction Works Can Begin	0 d	Tue 17/12/19	Tue 17/12/19	*100%*
14	*Demolition Complete*	*0 d*	*Thu 25/06/20*	*Thu 25/06/20*	*100%*
15	*Structure Complete Traditional Topping Off Ceremony*	*0 d*	*Fri 12/02/21*	*Fri 12/02/21*	*100%*
16	*Tower Crane Removed*	*0 d*	*Mon 29/03/21*	*Mon 29/03/21*	*100%*
17	*Heritage Building Finishes Complete*	*0 d*	*Thu 29/07/21*	*Thu 29/07/21*	*0%*
18	*Residential Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
19	*Education Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
20	*Occupation Certificate Issued*	*0 d*	*Wed 18/08/21*	*Wed 18/08/21*	*0%*
21	*DWP Issue Practical Completion*	*0 d*	*Wed 18/08/21*	*Wed 18/08/21*	*0%*
22	*Built Project Complete*	*0 d*	*Fri 27/08/21*	*Fri 27/08/21*	*0%*
23	**TENDERING AND CONTRACT AWARD**	**29 d**	**Wed 18/09/19**	**Thu 24/10/19**	**100%**
31	**DESIGN, AUTHORITIES, & PROCUREMENT**	**419 d**	**Mon 21/10/19**	**Tue 4/05/21**	**100%**
185	**SITE ESTABLISHMENT, CRANES, HOISTS ETC**	**419 d**	**Tue 29/10/19**	**Fri 14/05/21**	**100%**
186	**INVESTIGATIONS AND SITE ESTABLISHMENTS**	**58 d**	**Tue 29/10/19**	**Wed 29/01/20**	**100%**
197	**SCAFFOLD AND HOARDINGS**	**366 d**	**Tue 21/01/20**	**Fri 14/05/21**	**100%**
198	Erect Demolition Scaffold to Administration Building	10 d	Tue 21/01/20	Tue 4/02/20	100%
199	Erect Demolition Scaffold to Supreme Courts Building	10 d	Wed 5/02/20	Sat 15/02/20	100%
200	Erect B Class Hoardings to Church Street	10 d	Fri 28/02/20	Tue 10/03/20	100%
201	*Remove B Class Hoarding*	*0 d*	*Mon 8/02/21*	*Mon 8/02/21*	*100%*
202	Scaffold Erection to Heritage Public Building (HPB)	33 d	Thu 24/09/20	Wed 4/11/20	100%
203	Scaffold Erection to Residential Building (RB) - 1st Lift & Set Out	6 d	Fri 7/08/20	Thu 13/08/20	100%
204	Scaffold RB Lvl 2 - 3	6 d	Tue 1/09/20	Mon 7/09/20	100%
205	Scaffold RB Lvl 3 - 4	3 d	Tue 22/09/20	Thu 24/09/20	100%
206	Scaffold RB Lvl 4 - Roof	2 d	Thu 15/10/20	Fri 16/10/20	100%
207	Scaffold Erection to Education Building (EB) - 1st Lift & Set Out	10 d	Tue 20/10/20	Fri 30/10/20	100%
208	Scaffold EB Lvl 2 - 3	3 d	Sat 31/10/20	Tue 3/11/20	100%
209	Scaffold EB Lvl 3 - 4	3 d	Sat 21/11/20	Tue 24/11/20	100%
210	Scaffold EB Lvl 4 - Roof	6 d	Wed 25/11/20	Tue 1/12/20	100%
211	Remove Scaffold to Residential Building (RB)	25 d	Sat 27/02/21	Wed 31/03/21	100%
212	Remove Scaffold to Heritage Public Building (HPB)	6 d	Thu 25/03/21	Thu 1/04/21	100%
213	Remove Scaffold to Education Building (EB)	6 d	Fri 7/05/21	Fri 14/05/21	100%
214	**PRELIMS ITEMS - CRANES, HOISTS ETC**	**279 d**	**Fri 8/05/20**	**Tue 11/05/21**	**100%**
215	Design & Engineering Crane and Base including Signage	10 d	Fri 8/05/20	Tue 19/05/20	100%
216	Erect & Commission Tower Crane on Stair Raft Residential Building	2 d	Fri 26/06/20	Sat 27/06/20	100%
217	Tower Crane Decommission & Remove Tower Crane	2 d	Fri 26/03/21	Mon 29/03/21	100%
218	Erect Materials Hoist No.1 Residential Building (RB)	3 d	Wed 7/10/20	Fri 9/10/20	100%
219	Erect Materials Hoist No.2 Educational Building (EB)	3 d	Sat 12/12/20	Tue 15/12/20	100%
220	Dismantle Hoist No.1 Residential Building (RB)	2 d	Tue 30/03/21	Wed 31/03/21	100%
221	Dismantle Hoist No.2 Educational Building (EB)	2 d	Mon 10/05/21	Tue 11/05/21	100%
222	**CONSTRUCTION WORKS**	**456 d**	**Tue 17/12/19**	**Fri 27/08/21**	**98%**
223	Demolition CC Received Works Can Begin	0 d	Tue 17/12/19	Tue 17/12/19	*100%*
224	**DEMOLITION WORKS**	**122 d**	**Tue 21/01/20**	**Thu 25/06/20**	**100%**
248	**CIVIL, PILING & RETENTION WORKS**	**143.5 d**	**Mon 9/03/20**	**Thu 3/09/20**	**100%**
281	**STRUCTURE WORKS**	**267 d**	**Wed 3/06/20**	**Tue 25/05/21**	**100%**
461	**FAÇADE**	**253 d**	**Wed 26/08/20**	**Wed 11/08/21**	**97%**
462	**FAÇADE RESIDENTIAL BUILDING (1,820m2)**	**220 d**	**Wed 7/10/20**	**Wed 11/08/21**	**99%**
463	**Level 1**	**42 d**	**Wed 7/10/20**	**Tue 24/11/20**	**100%**
464	External Stud Framing & Sarking	6 d	Wed 7/10/20	Tue 13/10/20	100%
465	L1-L2 Blockwork	10 d	Mon 12/10/20	Thu 22/10/20	100%
466	Subframes & Site Measure	6 d	Fri 30/10/20	Thu 5/11/20	100%
467	Install Windows	6 d	Wed 18/11/20	Tue 24/11/20	100%
468	**Level 2**	**27 d**	**Sat 31/10/20**	**Tue 1/12/20**	**100%**
469	External Stud Framing & Sarking	6 d	Sat 31/10/20	Fri 6/11/20	100%
470	L2-L3 Blockwork	6 d	Tue 3/11/20	Mon 9/11/20	100%
471	Subframes & Site Measure	6 d	Tue 10/11/20	Mon 16/11/20	100%
472	Install Windows	6 d	Wed 25/11/20	Tue 1/12/20	100%
473	**Level 3**	**40 d**	**Sat 7/11/20**	**Thu 7/01/21**	**100%**
474	External Stud Framing & Sarking	8 d	Sat 7/11/20	Mon 16/11/20	100%
475	L3-L4 Blockwork	6 d	Thu 12/11/20	Wed 18/11/20	100%
476	Subframes & Site Measure	6 d	Fri 4/12/20	Mon 14/12/20	100%
477	Install Windows	6 d	Mon 21/12/20	Thu 7/01/21	100%
478	**Level 4**	**49 d**	**Tue 17/11/20**	**Sat 30/01/21**	**100%**
479	External Stud Framing & Sarking	6 d	Tue 17/11/20	Mon 23/11/20	100%
480	L4-Roof Blockwork	12 d	Thu 19/11/20	Wed 2/12/20	100%
481	Subframes & Site Measure	4 d	Fri 4/12/20	Fri 11/12/20	100%
482	Install Windows	17 d	Fri 8/01/21	Sat 30/01/21	100%
483	**Render**	**85 d**	**Fri 8/01/21**	**Wed 5/05/21**	**100%**
484	L5-L2 Render External Walls - Western Elevation	8 d	Fri 8/01/21	Sat 16/01/21	100%
485	L5-L2 Render External Walls - Southern Elevation	8 d	Mon 18/01/21	Fri 29/01/21	100%
486	L5-L2 Render External Walls - Northern Elevation	8 d	Sat 30/01/21	Mon 8/02/21	100%
487	L5-L2 Render External Walls - Eastern Elevation	8 d	Tue 9/02/21	Wed 17/02/21	100%
488	L1 Render External Walls - All Elevations	20 d	Thu 1/04/21	Wed 5/05/21	100%
489	**Painting**	**79 d**	**Mon 18/01/21**	**Fri 7/05/21**	**100%**
490	L5-L1 Paint External Walls - Western Elevation	4 d	Mon 18/01/21	Thu 21/01/21	100%
491	L5-L1 Paint External Walls - Southern Elevation	6 d	Sat 30/01/21	Fri 5/02/21	100%
492	L5-L2 Paint External Walls - Northern Elevation	8 d	Tue 9/02/21	Wed 17/02/21	100%
493	L5-L2 Paint External Walls - Eastern Elevation	8 d	Thu 18/02/21	Fri 26/02/21	100%
494	L1 Paint External Walls Post Scaffold Strip	5 d	Mon 3/05/21	Fri 7/05/21	100%
495	**Equitone Cladding (Eastern Elevation)**	**90 d**	**Wed 6/01/21**	**Mon 10/05/21**	**100%**
496	Nvelepe Façade System Incl. Siniat Weather Defence Board	10 d	Wed 6/01/21	Sat 16/01/21	100%

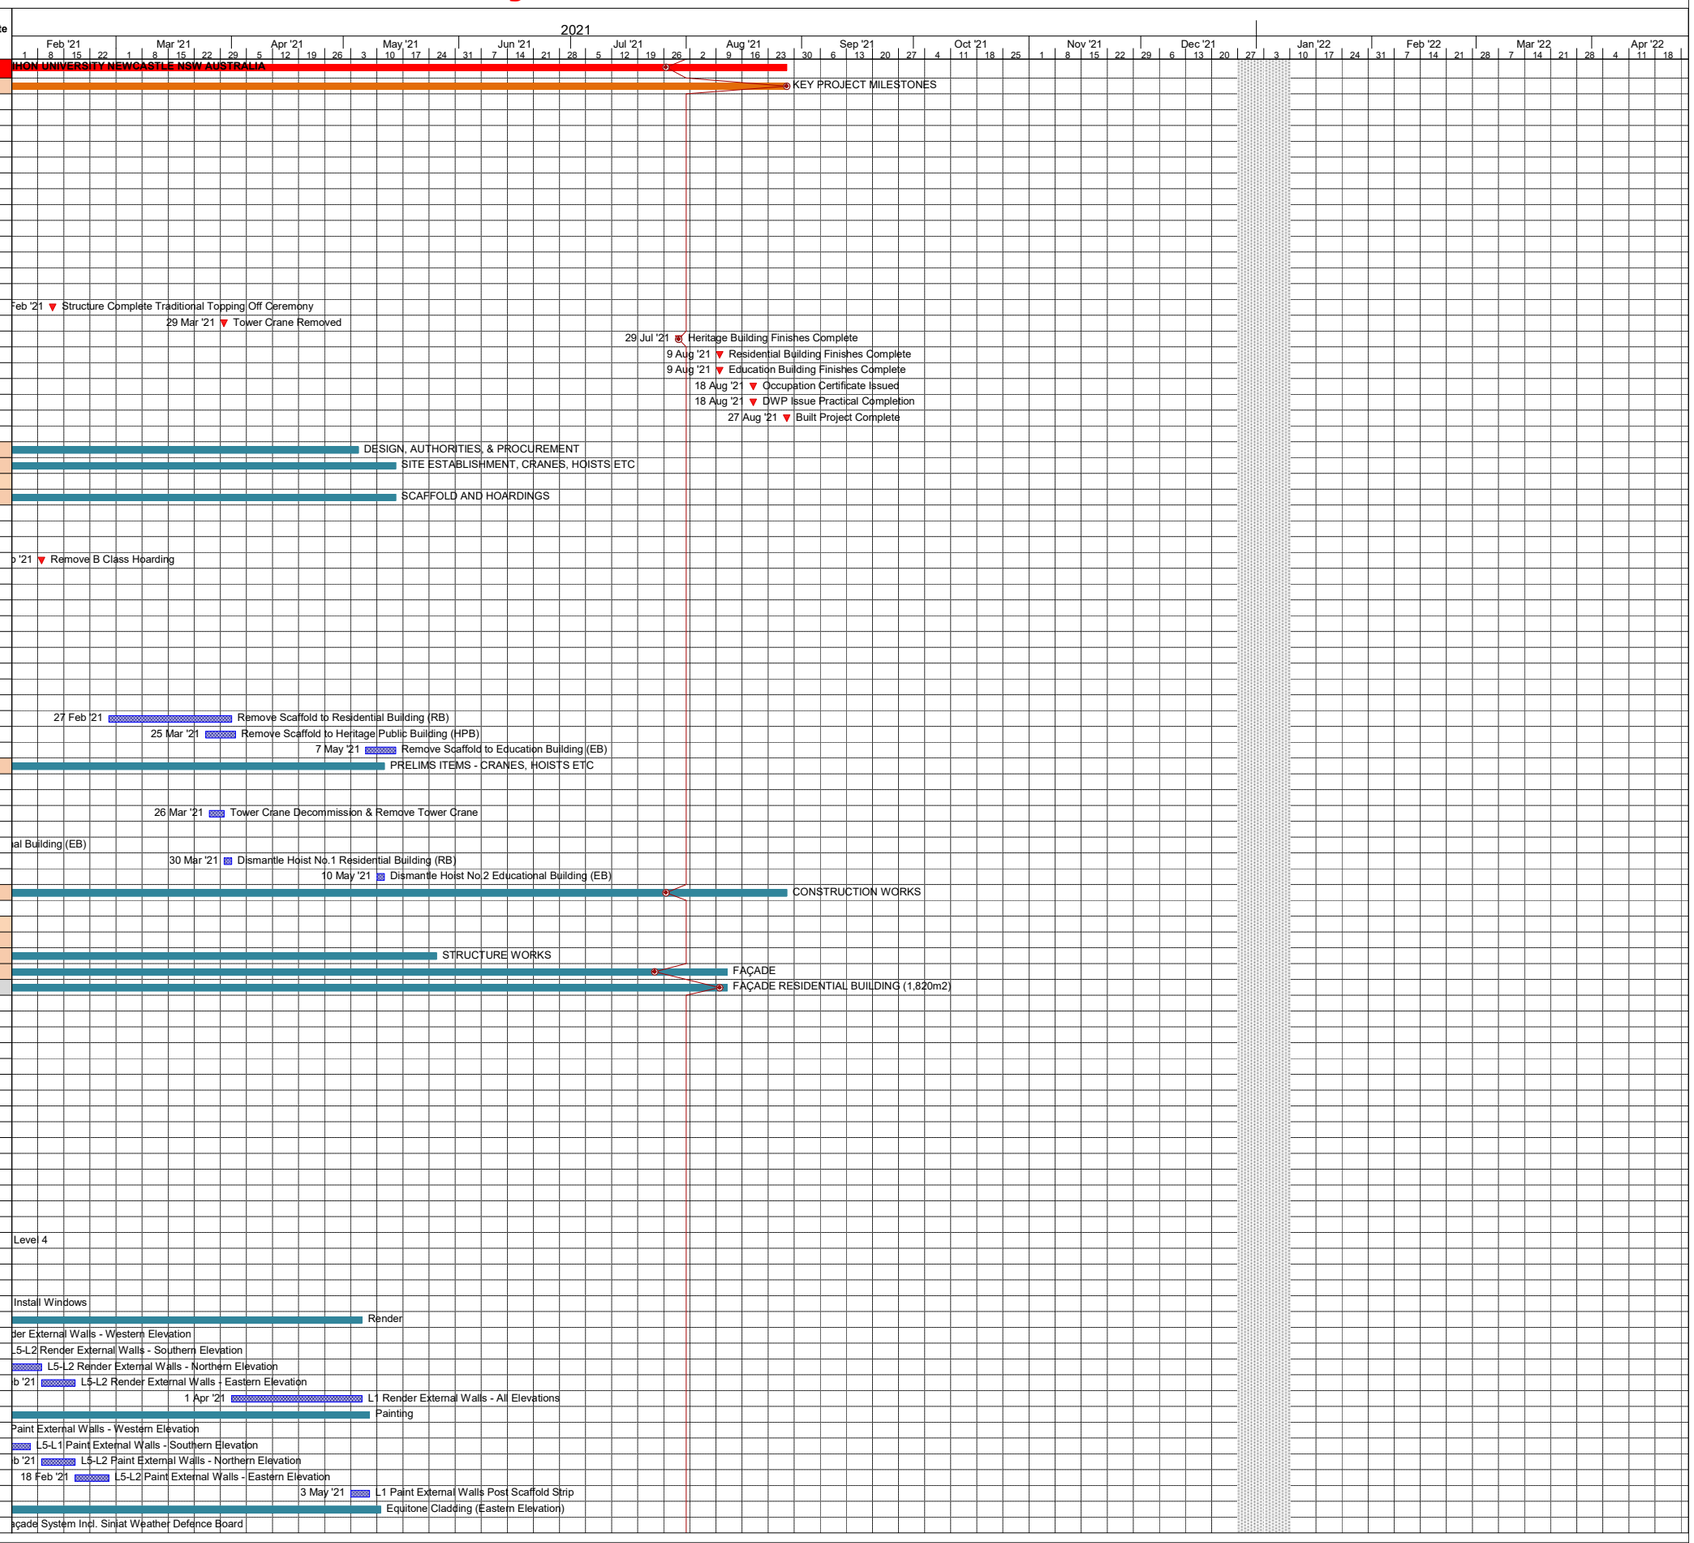


Critical Task — Non-critical — Milestone — Project Summary — Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
497	Equitone Rainscreen Cladding (from EWP's)	6 d	Mon 3/05/21	Mon 10/05/21	100%
498	**ACP Cassette Feature Band**	**44 d**	**Mon 3/05/21**	**Mon 5/07/21**	**100%**
499	Framing For ACP Cassette (from EWP's)	5 d	Mon 3/05/21	Fri 7/05/21	100%
500	Alpolic Cladding of Feature Band (from EWP's)	6 d	Mon 28/06/21	Mon 5/07/21	100%
501	**Aluminium Screens - Arcadia**	**7 d**	**Tue 13/07/21**	**Wed 21/07/21**	**100%**
502	Install Screening (From EWP's)	7 d	Tue 13/07/21	Wed 21/07/21	100%
503	**Builders Clean of Façade Elevations**	**2 d**	**Tue 10/08/21**	**Wed 11/08/21**	**0%**
504	Pressure Cleaning Façade Elevations	2 d	Tue 10/08/21	Wed 11/08/21	0%
505	**L1-2 Shop Front Framing & Glazing**	**1 d**	**Tue 23/02/21**	**Tue 23/02/21**	**100%**
506	L1-2 Install Shop Fronts	1 d	Tue 23/02/21	Tue 23/02/21	100%
507	**Atrium Works**	**52 d**	**Fri 21/05/21**	**Wed 4/08/21**	**90%**
508	**Structure & Envelope**	**30 d**	**Fri 21/05/21**	**Mon 5/07/21**	**100%**
509	Structural Steel Install	4 d	Fri 21/05/21	Wed 26/05/21	100%
510	Purlins & Sub-Framing	2 d	Thu 27/05/21	Fri 28/05/21	100%
511	Sarking & Insulation	2 d	Mon 31/05/21	Tue 1/06/21	100%
512	Roof Sheeting	3 d	Wed 2/06/21	Fri 4/06/21	100%
513	Skylights Installation	4 d	Wed 30/06/21	Mon 5/07/21	100%
514	Roof Safety Anchor System	1 d	Fri 2/07/21	Fri 2/07/21	100%
515	Flashings & Roof Plumbing	3 d	Thu 1/07/21	Mon 5/07/21	100%
516	**Monarch Renlita Doors**	**42 d**	**Mon 31/05/21**	**Thu 29/07/21**	**20%**
517	Temporary Weather Proofing to Mitigate Delay	1 d	Mon 31/05/21	Mon 31/05/21	100%
518	Installation of Doors	4 d	Mon 26/07/21	Thu 29/07/21	0%
519	**Finishes & Services**	**36 d**	**Wed 16/06/21**	**Wed 4/08/21**	**93%**
520	**Level 2**	**26 d**	**Wed 16/06/21**	**Wed 21/07/21**	**100%**
521	High Level Rough-in Services	4 d	Wed 16/06/21	Mon 21/06/21	100%
522	Ceiling Framing	4 d	Tue 22/06/21	Fri 25/06/21	100%
523	Sheet Plasterboard Ceiling	5 d	Mon 28/06/21	Fri 2/07/21	100%
524	Set & Sand Plasterboard Ceiling	3 d	Fri 2/07/21	Tue 6/07/21	100%
525	Paint - 1st Coat	2 d	Wed 7/07/21	Thu 8/07/21	100%
526	Paint - 2nd Coat	2 d	Fri 9/07/21	Mon 12/07/21	100%
527	Paint - 3rd Coat	2 d	Tue 13/07/21	Wed 14/07/21	100%
528	Fitoff Services	2 d	Thu 15/07/21	Fri 16/07/21	100%
529	Decorative Timber Ceiling (Armstrong Battens)	5 d	Thu 15/07/21	Wed 21/07/21	100%
530	**Level 1**	**13 d**	**Mon 19/07/21**	**Wed 4/08/21**	**83%**
531	Frame Ceilings (Level 2 Link Bridge)	1 d	Mon 19/07/21	Mon 19/07/21	100%
532	Sheet Plasterboard Ceiling (Level 2 Link Bridge)	1 d	Tue 20/07/21	Tue 20/07/21	100%
533	Set & Sand Plasterboard Ceiling (Level 2 Link Bridge)	3 d	Wed 21/07/21	Fri 23/07/21	100%
534	Paint - 1st Coat	1 d	Mon 26/07/21	Mon 26/07/21	100%
535	Paint - 2nd Coat	1 d	Tue 27/07/21	Tue 27/07/21	100%
536	Paint - 3rd Coat	1 d	Wed 28/07/21	Wed 28/07/21	0%
537	Fitoff Services	1 d	Thu 29/07/21	Thu 29/07/21	100%
538	Floor Preparation	2 d	Fri 23/07/21	Mon 26/07/21	100%
539	Balustrade Base Plates & Posts	2 d	Mon 19/07/21	Tue 20/07/21	100%
540	Tile Floor Finishes	6 d	Tue 27/07/21	Tue 3/08/21	75%
541	Balustrade Handrails & Glazed Panels	2 d	Tue 3/08/21	Wed 4/08/21	50%
542	**FAÇADE EDUCATIONAL BUILDING (1,820m2)**	**252 d**	**Wed 26/08/20**	**Tue 10/08/21**	**96%**
543	L1 - 2 External Blockwork	15 d	Wed 26/08/20	Fri 11/09/20	100%
544	**Level 2**	**75 d**	**Mon 18/01/21**	**Mon 3/05/21**	**100%**
545	L2-L3 Install Secondary Structural Steel	25 d	Mon 18/01/21	Thu 18/02/21	100%
546	External Stud Framing & Sarking	4 d	Fri 19/02/21	Tue 23/02/21	100%
547	L2-L3 Blockwork Infill Panels	6 d	Wed 24/02/21	Tue 2/03/21	100%
548	Subframes & Site Measure	5 d	Thu 25/03/21	Wed 31/03/21	100%
549	Install Windows	13 d	Tue 13/04/21	Mon 3/05/21	100%
550	**Level 3**	**65 d**	**Mon 8/02/21**	**Mon 10/05/21**	**100%**
551	L3-L4 Install Secondary Structural Steel	18 d	Mon 8/02/21	Sat 27/02/21	100%
552	External Stud Framing & Sarking	7 d	Tue 23/02/21	Tue 2/03/21	100%
553	L3-L4 Blockwork - Infill Panels	6 d	Wed 3/03/21	Tue 9/03/21	100%
554	Subframes & Site Measure	5 d	Thu 25/03/21	Wed 31/03/21	100%
555	Install Windows	5 d	Tue 4/05/21	Mon 10/05/21	100%
556	**Level 4**	**51 d**	**Sat 27/02/21**	**Thu 13/05/21**	**100%**
557	L4-Roof Install Secondary Structural Steel	3 d	Mon 1/03/21	Wed 3/03/21	100%
558	External Stud Framing & Sarking	4 d	Sat 27/02/21	Wed 3/03/21	100%
559	L4-Roof Blockwork - Infill Panels	4 d	Thu 4/03/21	Mon 8/03/21	100%
560	Subframes & Site Measure	3 d	Thu 25/03/21	Mon 29/03/21	100%
561	Install Windows	3 d	Tue 11/05/21	Thu 13/05/21	100%
562	**Render**	**55 d**	**Wed 3/03/21**	**Mon 24/05/21**	**100%**
563	L5-L2 Render External Walls - Western Elevation	25 d	Wed 3/03/21	Thu 8/04/21	100%
564	L5-L2 Render External Walls - Southern Elevation	25 d	Wed 3/03/21	Thu 8/04/21	100%
565	L5-L2 Render External Walls - Northern Elevation	25 d	Wed 3/03/21	Thu 8/04/21	100%
566	L5-L2 Render External Walls - Eastern Elevation	25 d	Wed 3/03/21	Thu 8/04/21	100%
567	L2-L1 Render External Walls - All Elevations	6 d	Mon 17/05/21	Mon 24/05/21	100%
568	**Painting**	**50 d**	**Fri 9/04/21**	**Wed 23/06/21**	**100%**
569	L5-L2 Paint External Walls - Western Elevation	5 d	Fri 9/04/21	Thu 15/04/21	100%
570	L5-L2 Paint External Walls - Southern Elevation	5 d	Fri 16/04/21	Thu 22/04/21	100%
571	L5-L2 Paint External Walls - Northern Elevation	8 d	Fri 23/04/21	Thu 6/05/21	100%
572	L5-L2 Paint External Walls - Eastern Elevation	5 d	Fri 7/05/21	Thu 13/05/21	100%
573	L2-L1 Paint External Walls - All Elevations	20 d	Tue 25/05/21	Wed 23/06/21	100%
574	**ACP Cassette Feature Band**	**12 d**	**Tue 4/05/21**	**Wed 19/05/21**	**100%**
575	Framing for ACP Cassette	6 d	Tue 4/05/21	Tue 11/05/21	100%
576	Alpolic Cladding of Feature Band	6 d	Wed 12/05/21	Wed 19/05/21	100%
577	**Aluminium Screens - Arcadia**	**25 d**	**Wed 23/06/21**	**Tue 27/07/21**	**50%**
578	Install Screening (From EWP's)	25 d	Wed 23/06/21	Tue 27/07/21	50%
579	**Builders Clean of Façade Elevations**	**2 d**	**Mon 9/08/21**	**Tue 10/08/21**	**0%**
580	Pressure Cleaning Façade Elevations	2 d	Mon 9/08/21	Tue 10/08/21	0%
581	**MISCELLANEOUS ROOFS**	**38 d**	**Wed 24/03/21**	**Fri 21/05/21**	**100%**
582	**L3 Lift \ Corridor Link**	**5 d**	**Wed 24/03/21**	**Tue 30/03/21**	**100%**
583	Structural Steel	2 d	Thu 25/03/21	Fri 26/03/21	100%
584	Roof Framing & Purlins	2 d	Mon 29/03/21	Tue 30/03/21	100%
585	Insulation & Sarking	2 d	Wed 24/03/21	Thu 25/03/21	100%
586	Roof Sheeting	1 d	Fri 26/03/21	Fri 26/03/21	100%
587	Trims & Flashings	2 d	Mon 29/03/21	Tue 30/03/21	100%
588	**L2 Advert Room**	**5 d**	**Mon 17/05/21**	**Fri 21/05/21**	**100%**
589	Roof Framing & Purlins	1 d	Mon 17/05/21	Mon 17/05/21	100%

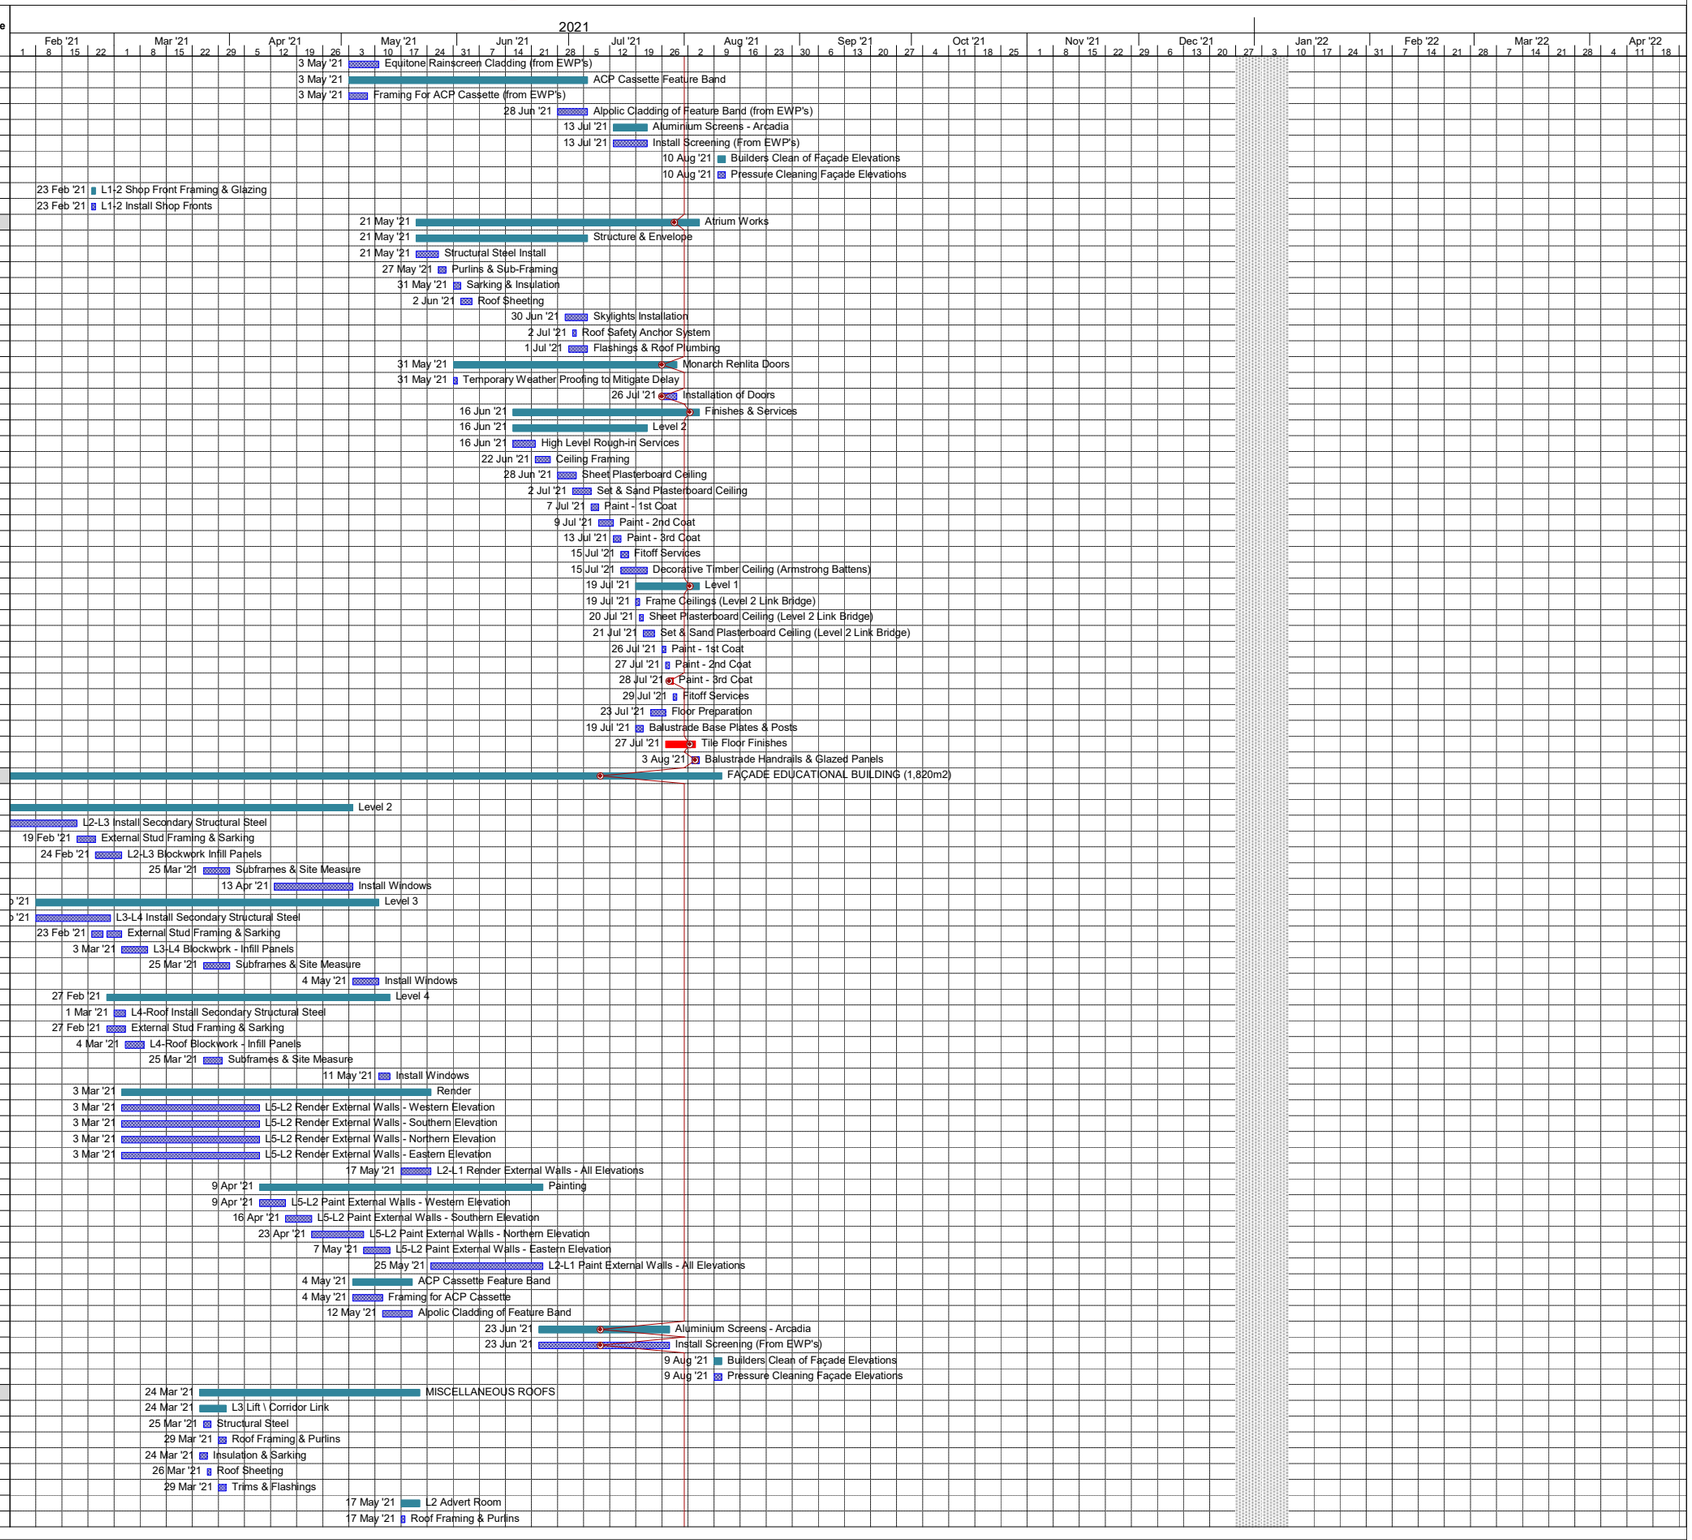


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
590	Insulation & Sarking	1 d	Tue 18/05/21	Tue 18/05/21	100%
591	Roof Sheeting	1 d	Wed 19/05/21	Wed 19/05/21	100%
592	Trims & Flashings	2 d	Thu 20/05/21	Fri 21/05/21	100%
593	**FAÇADE HERITAGE / PUBLIC BUILDING**	**115 d**	**Mon 18/01/21**	**Wed 30/06/21**	**100%**
594	Paint and Repairs - Level 4 Tower & Projections	20 d	Mon 18/01/21	Fri 12/02/21	100%
595	Paint and Repairs - Level 3 Façade	20 d	Tue 2/02/21	Wed 24/02/21	100%
596	Paint and Repairs - Level 2 Façade	20 d	Thu 25/02/21	Mon 22/03/21	100%
597	Paint and Repairs - Level 1 Façade	25 d	Tue 25/05/21	Wed 30/06/21	100%
598	**FINISHES & SERVICES**	**303 d**	**Fri 26/06/20**	**Mon 9/08/21**	**99%**
599	**BUILDING C - RESIDENTIAL BUILDING**	**219 d**	**Fri 2/10/20**	**Mon 9/08/21**	**99%**
600	**Level 1**	**207 d**	**Fri 2/10/20**	**Thu 22/07/21**	**99%**
601	**Residential Rooms_C.L1.19 to C.L1.34**	**190 d**	**Fri 2/10/20**	**Tue 29/06/21**	**100%**
602	Mark Up Slab	1 d	Fri 2/10/20	Fri 2/10/20	100%
603	Service Risers and Top Track	6 d	Wed 7/10/20	Tue 13/10/20	100%
604	Blockwork to Back of House Areas	20 d	Wed 7/10/20	Thu 29/10/20	100%
605	Run High Level Fire Sprinkler	20 d	Fri 9/10/20	Sat 31/10/20	100%
606	Run High Level Hydraulic Services	6 d	Fri 9/10/20	Thu 15/10/20	100%
607	Run High Level Mechanical Services	25 d	Fri 9/10/20	Fri 6/11/20	100%
608	Frame Internal Partitions (excl External Walls)	6 d	Wed 14/10/20	Tue 20/10/20	100%
609	Run High Level Electrical Services	6 d	Fri 16/10/20	Thu 22/10/20	100%
610	Sheet Partitions 1 Side	12 d	Wed 21/10/20	Tue 3/11/20	100%
611	Rough In Services & Insulation to Partition Walls	7 d	Sat 7/11/20	Sat 14/11/20	100%
612	Consultant Inspections Before Closing	1 d	Mon 16/11/20	Mon 16/11/20	100%
613	Sheet and Close 2nd Side Partitions	4 d	Tue 17/11/20	Fri 20/11/20	100%
614	Frame Ceilings	6 d	Sat 12/12/20	Fri 18/12/20	100%
615	Sheet Ceilings & Bulkheads	6 d	Thu 17/12/20	Mon 4/01/21	100%
616	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	6 d	Tue 22/12/20	Fri 8/01/21	100%
617	Paint - 1st Coat	6 d	Sat 30/01/21	Fri 5/02/21	100%
618	Defects Inspection & Patch Walls	1 d	Sat 6/02/21	Sat 6/02/21	100%
619	Repairs to Plasterboard	6 d	Wed 7/04/21	Wed 14/04/21	100%
620	Paint - 2nd Coat	3 d	Tue 13/04/21	Thu 15/04/21	100%
621	Joinery	3 d	Fri 16/04/21	Tue 20/04/21	100%
622	Floor Finishes - Vinyl	3 d	Mon 19/04/21	Wed 21/04/21	100%
623	Carpentry - Hang Doors & Fix Skirtings	3 d	Thu 22/04/21	Wed 28/04/21	100%
624	Paint - 3rd Coat	3 d	Mon 3/05/21	Wed 5/05/21	100%
625	Fitoff Services	3 d	Thu 6/05/21	Mon 10/05/21	100%
626	Door Hardware	5 d	Tue 4/05/21	Mon 10/05/21	100%
627	FFE	2 d	Mon 28/06/21	Tue 29/06/21	100%
628	**Wet Areas**	**134 d**	**Sat 19/12/20**	**Tue 6/07/21**	**100%**
629	Frame Ceilings	3 d	Sat 19/12/20	Tue 22/12/20	100%
630	Sheet Ceilings & Bulkheads	3 d	Mon 4/01/21	Wed 6/01/21	100%
631	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Thu 7/01/21	Sat 9/01/21	100%
632	Paint - 1st Coat	1 d	Mon 11/01/21	Mon 11/01/21	100%
633	Wall Tiling	6 d	Tue 12/01/21	Mon 18/01/21	100%
634	Set P50 Shadowline	2 d	Tue 19/01/21	Wed 20/01/21	100%
635	Membrane	2 d	Thu 21/01/21	Fri 22/01/21	100%
636	Flood Test	1 d	Wed 27/01/21	Wed 27/01/21	100%
637	Screed	2 d	Thu 28/01/21	Fri 29/01/21	100%
638	Demolish Defective Screeds	3 d	Sat 6/03/21	Tue 9/03/21	100%
639	Membrane	2 d	Wed 10/03/21	Thu 11/03/21	100%
640	Flood Test	1 d	Mon 15/03/21	Mon 15/03/21	100%
641	Re-Screed	2 d	Tue 16/03/21	Wed 17/03/21	100%
642	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
643	Vinyl Floor Finishes	3 d	Fri 26/03/21	Tue 30/03/21	100%
644	Joinery	2 d	Wed 31/03/21	Thu 1/04/21	100%
645	Toilet Partitions	5 d	Wed 7/04/21	Tue 13/04/21	100%
646	Carpentry - Hang Doors	2 d	Wed 14/04/21	Thu 15/04/21	100%
647	Door Hardware	1 d	Fri 16/04/21	Fri 16/04/21	100%
648	Paint - 3rd Coat	1 d	Mon 19/04/21	Mon 19/04/21	100%
649	Fit Off PC Items	12 d	Tue 20/04/21	Fri 7/05/21	100%
650	Fit Off Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
651	FFE	2 d	Mon 5/07/21	Tue 6/07/21	100%
652	**Kitchen - C.L1.07**	**125 d**	**Mon 11/01/21**	**Tue 6/07/21**	**100%**
653	Frame and Sheet Plasterboard Ceiling	6 d	Mon 11/01/21	Sat 16/01/21	100%
654	Set & Sand Plasterboard Ceiling	3 d	Mon 18/01/21	Wed 20/01/21	100%
655	Membrane	4 d	Mon 1/02/21	Thu 4/02/21	100%
656	Flood Test	1 d	Sat 6/02/21	Sat 6/02/21	100%
657	Screed	5 d	Tue 9/02/21	Sat 13/02/21	100%
658	Floor & Wall Tiling	15 d	Mon 15/02/21	Wed 3/03/21	100%
659	Paint - 2nd Coat	3 d	Thu 25/03/21	Mon 29/03/21	100%
660	Paint - 3rd Coat	3 d	Tue 30/03/21	Thu 1/04/21	100%
661	Kitchen Fitout (4 wk lead time from completion of tiling)	10 d	Mon 19/04/21	Tue 4/05/21	100%
662	Fitoff Services	2 d	Mon 3/05/21	Tue 4/05/21	100%
663	FFE	2 d	Mon 5/07/21	Tue 6/07/21	100%
664	**Cool Room - C.L1.09**	**98 d**	**Sat 13/02/21**	**Mon 5/07/21**	**100%**
665	Cool Room Panelling & Equipment	4 d	Sat 13/02/21	Wed 17/02/21	100%
666	Floor Topping	1 d	Tue 2/03/21	Tue 2/03/21	100%
667	Ceiling Framing	1 d	Wed 3/03/21	Wed 3/03/21	100%
668	Coolroom Soffit	1 d	Thu 4/03/21	Thu 4/03/21	100%
669	Epoxy Flooring	1 d	Fri 5/03/21	Fri 5/03/21	100%
670	Services Fit Off	2 d	Tue 9/03/21	Wed 10/03/21	100%
671	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
672	**Dry Goods Store - C.L1.04**	**66 d**	**Thu 25/03/21**	**Mon 5/07/21**	**100%**
673	Membrane	1 d	Thu 25/03/21	Thu 25/03/21	100%
674	Flood Test	1 d	Mon 29/03/21	Mon 29/03/21	100%
675	Screed	1 d	Tue 30/03/21	Tue 30/03/21	100%
676	Render	3 d	Wed 7/04/21	Fri 9/04/21	100%
677	Paint - 1st Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
678	Defects Inspection & Patch Walls	1 d	Tue 4/05/21	Tue 4/05/21	100%
679	Ceiling Framing	1 d	Mon 12/04/21	Mon 12/04/21	100%
680	Sheet Ceilings	1 d	Wed 14/04/21	Wed 14/04/21	100%
681	Set & Sand Plasterboard Ceilings	3 d	Mon 3/05/21	Wed 5/05/21	100%
682	Floor Tiling	1 d	Tue 20/04/21	Tue 20/04/21	100%

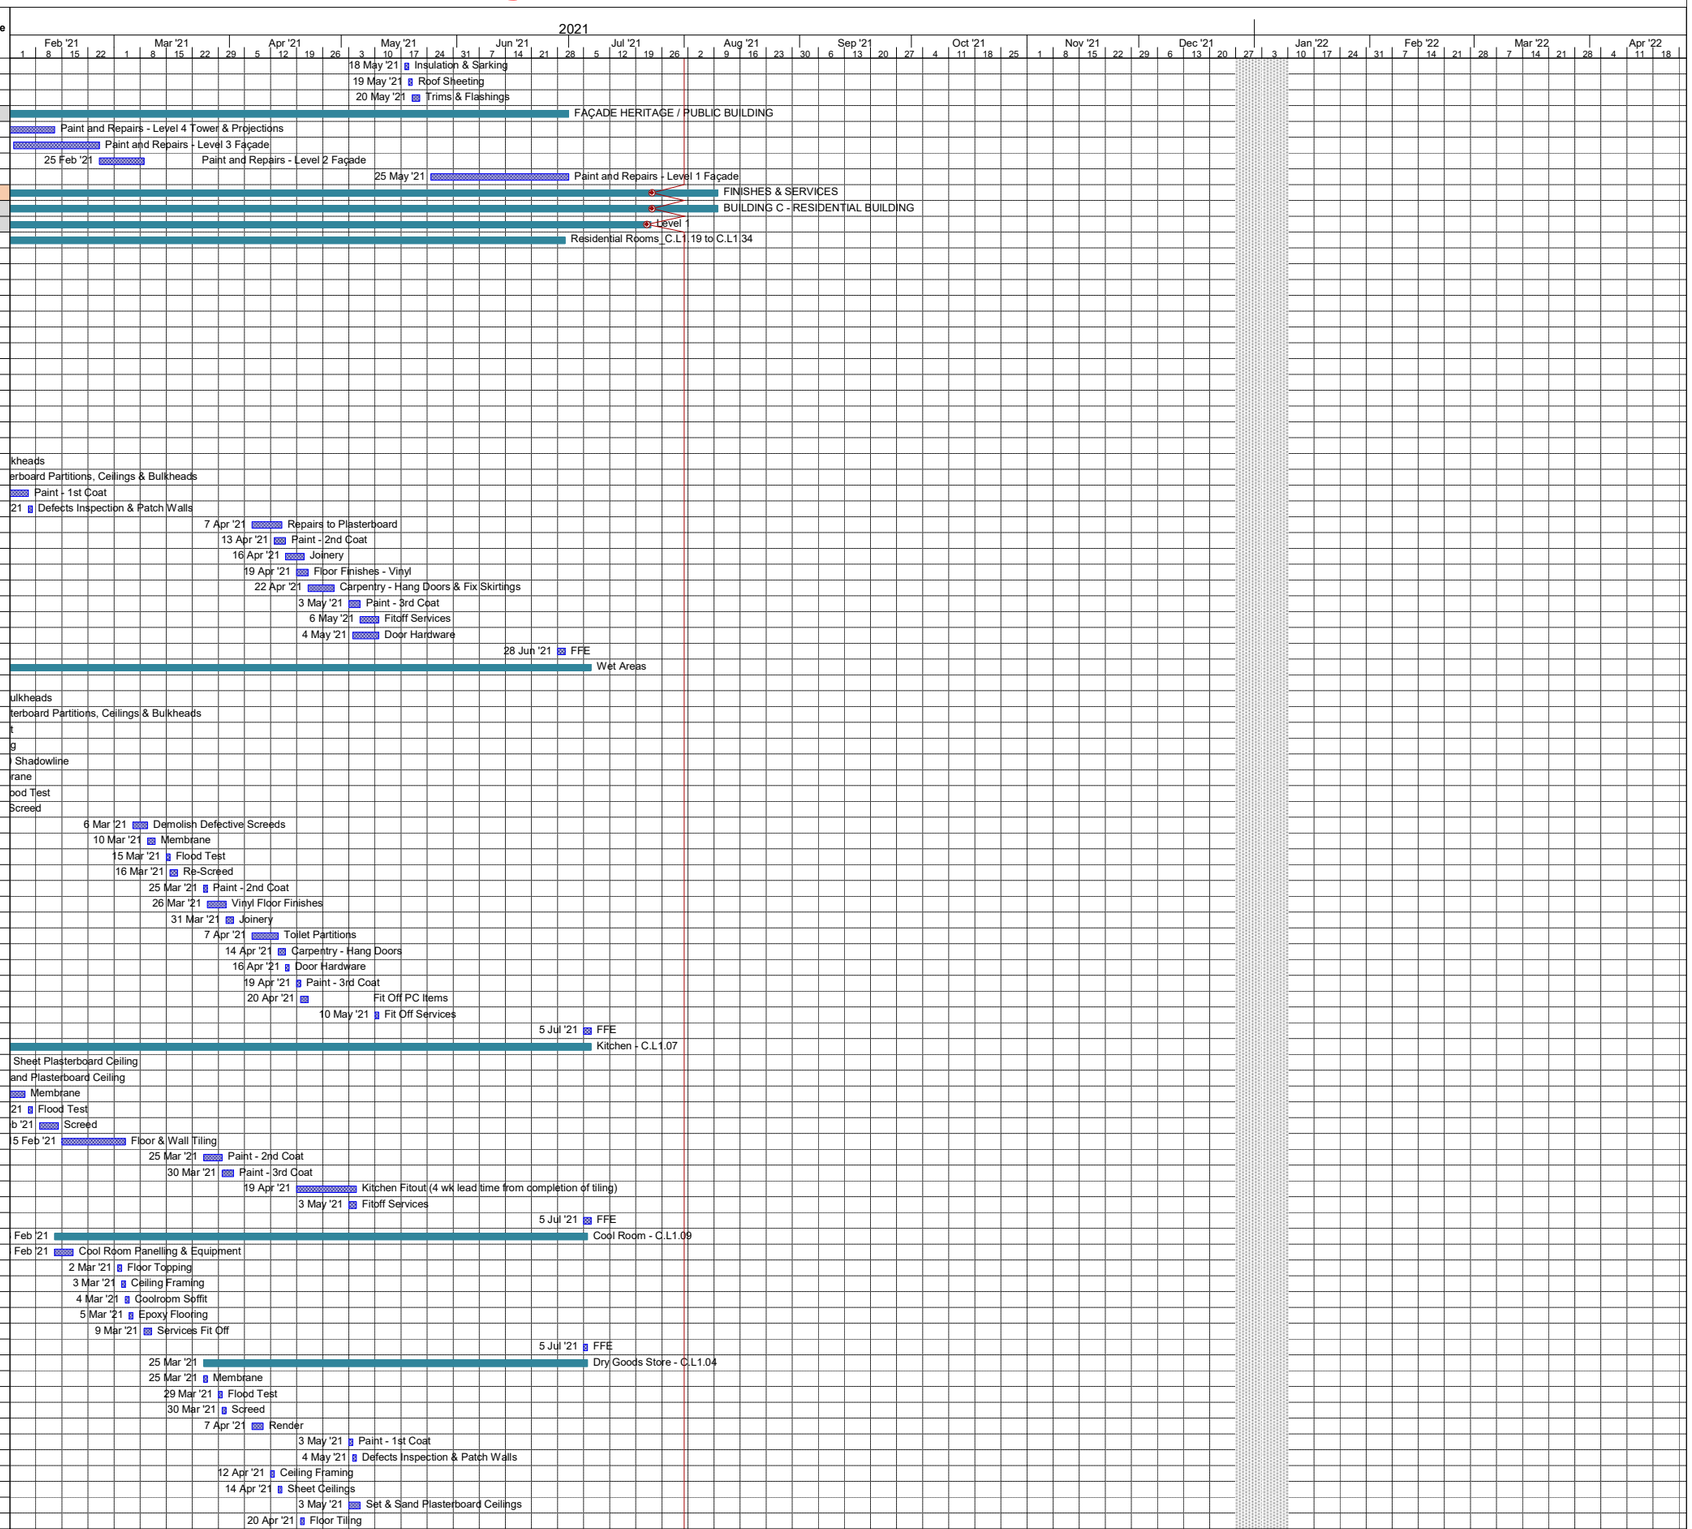


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
683	Paint - 2nd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
684	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
685	Services Fit Off	1 d	Mon 10/05/21	Mon 10/05/21	100%
686	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
687	**Access Corridor - C.L1.08**	**82 d**	**Thu 4/03/21**	**Mon 5/07/21**	**100%**
688	Wall Tiling	2 d	Thu 4/03/21	Fri 5/03/21	100%
689	Membrane	1 d	Fri 26/03/21	Fri 26/03/21	100%
690	Flood Test	1 d	Tue 30/03/21	Tue 30/03/21	100%
691	Screed	1 d	Wed 31/03/21	Wed 31/03/21	100%
692	Ceiling Framing	1 d	Thu 18/03/21	Thu 18/03/21	100%
693	Sheet Ceilings	1 d	Thu 1/04/21	Thu 1/04/21	100%
694	Paint - 1st Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
695	Defects Inspection & Patch Walls	1 d	Fri 7/05/21	Fri 7/05/21	100%
696	Set & Sand Plasterboard Ceilings	3 d	Mon 10/05/21	Wed 12/05/21	100%
697	Floor Tiling	1 d	Thu 29/04/21	Thu 29/04/21	100%
698	Paint - 2nd Coat	1 d	Thu 13/05/21	Thu 13/05/21	100%
699	Paint - 3rd Coat	1 d	Fri 14/05/21	Fri 14/05/21	100%
700	Services Fit Off	1 d	Mon 17/05/21	Mon 17/05/21	100%
701	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
702	**Kitchen Waste Room - C.L1.10**	**85 d**	**Mon 1/03/21**	**Mon 5/07/21**	**100%**
703	Epoxy Flooring	1 d	Mon 15/03/21	Mon 15/03/21	100%
704	Paint - 1st Coat	1 d	Mon 1/03/21	Mon 1/03/21	100%
705	Render	3 d	Wed 7/04/21	Fri 9/04/21	100%
706	Paint - 1st Coat	1 d	Mon 12/04/21	Mon 12/04/21	100%
707	Install Roller Door	2 d	Mon 3/05/21	Tue 4/05/21	100%
708	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
709	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
710	Install Bin Rails	1 d	Wed 5/05/21	Wed 5/05/21	100%
711	Services Fit Off	2 d	Wed 5/05/21	Thu 6/05/21	100%
712	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
713	**Res / Edu Waste Room - C.L1.12**	**73 d**	**Tue 16/03/21**	**Mon 5/07/21**	**100%**
714	Epoxy Flooring	1 d	Tue 16/03/21	Tue 16/03/21	100%
715	Render	3 d	Mon 12/04/21	Wed 14/04/21	100%
716	Paint - 1st Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
717	Paint - 2nd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
718	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
719	Install Bin Rails	1 d	Mon 10/05/21	Mon 10/05/21	100%
720	Services Fit Off	2 d	Tue 11/05/21	Wed 12/05/21	100%
721	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
722	**Hot Water Plant Room - C.L1.16**	**65 d**	**Wed 24/03/21**	**Thu 1/07/21**	**100%**
723	Install Roller Door	2 d	Wed 5/05/21	Thu 6/05/21	100%
724	Epoxy Flooring	1 d	Wed 24/03/21	Wed 24/03/21	100%
725	Paint - 1st Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
726	Paint - 2nd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
727	Paint - 3rd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
728	Install Hot Water Plant & Equipment	2 d	Tue 13/04/21	Wed 14/04/21	100%
729	Install Bin Rails	1 d	Thu 1/07/21	Thu 1/07/21	100%
730	Services Fit Off	2 d	Wed 12/05/21	Thu 13/05/21	100%
731	**Hydrant / Sprinkler Pump Room - C.L1.13**	**25 d**	**Thu 25/03/21**	**Wed 5/05/21**	**100%**
732	Epoxy Flooring	1 d	Thu 25/03/21	Thu 25/03/21	100%
733	Paint - 1st Coat	1 d	Mon 19/04/21	Mon 19/04/21	100%
734	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
735	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
736	Hydrant and Sprinkler Pumps Installation	1 d	Thu 22/04/21	Thu 22/04/21	100%
737	Services Fit Off	1 d	Wed 5/05/21	Wed 5/05/21	100%
738	**Service Corridor - C.L1.11**	**133 d**	**Sat 7/11/20**	**Mon 17/05/21**	**100%**
739	Run High Level Services	6 d	Sat 7/11/20	Fri 13/11/20	100%
740	Consultant Inspections Before Closing	1 d	Thu 11/02/21	Thu 11/02/21	100%
741	Sheet Partitions	2 d	Fri 12/02/21	Sat 13/02/21	100%
742	Frame Ceilings	2 d	Mon 15/02/21	Tue 16/02/21	100%
743	Sheet Ceilings & Bulkheads	2 d	Wed 17/02/21	Thu 18/02/21	100%
744	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Fri 19/02/21	Mon 22/02/21	100%
745	Paint - 1st Coat	1 d	Wed 17/03/21	Wed 17/03/21	100%
746	Defects Inspection & Patch Walls	2 d	Thu 18/03/21	Fri 19/03/21	100%
747	Screed	1 d	Thu 25/03/21	Thu 25/03/21	100%
748	Paint - 2nd Coat	2 d	Fri 26/03/21	Mon 29/03/21	100%
749	Carpentry - Hang Doors & Fix Skirtings	2 d	Tue 4/05/21	Wed 5/05/21	100%
750	Paint - 3rd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
751	Door Hardware	2 d	Thu 8/04/21	Fri 9/04/21	100%
752	Fitoff Services	3 d	Mon 10/05/21	Wed 12/05/21	100%
753	Floor Finishes - Tiling	3 d	Thu 13/05/21	Mon 17/05/21	100%
754	**Laundry / Linen - C.L1.15**	**160 d**	**Sat 14/11/20**	**Mon 5/07/21**	**100%**
755	Run High Level Services	6 d	Sat 14/11/20	Fri 20/11/20	100%
756	Screed	1 d	Sat 30/01/21	Sat 30/01/21	100%
757	Frame Internal Partitions (excl External Walls)	2 d	Thu 18/02/21	Fri 19/02/21	100%
758	Rough In Services & Insulation to Partition Walls	2 d	Sat 20/02/21	Mon 22/02/21	100%
759	Consultant Inspections Before Closing	1 d	Tue 23/02/21	Tue 23/02/21	100%
760	Sheet Partitions	2 d	Wed 24/02/21	Thu 25/02/21	100%
761	Frame Ceilings & Bulkheads	2 d	Wed 24/02/21	Thu 25/02/21	100%
762	Sheet Ceilings & Bulkheads	2 d	Fri 26/02/21	Sat 27/02/21	100%
763	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	1 d	Mon 1/03/21	Mon 1/03/21	100%
764	Paint - 1st Coat	1 d	Tue 2/03/21	Tue 2/03/21	100%
765	Defects Inspection & Patch Walls	1 d	Thu 25/03/21	Thu 25/03/21	100%
766	Paint - 2nd Coat	2 d	Fri 26/03/21	Mon 29/03/21	100%
767	Joinery	1 d	Tue 30/03/21	Tue 30/03/21	100%
768	Floor Finishes - Vinyl	1 d	Wed 31/03/21	Wed 31/03/21	100%
769	Carpentry - Hang Doors & Fix Skirtings	2 d	Mon 3/05/21	Tue 4/05/21	100%
770	Paint - 3rd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
771	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
772	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
773	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
774	**Comms Room - C.L1.18**	**124 d**	**Sat 21/11/20**	**Thu 20/05/21**	**100%**
775	Run High Level Services	2 d	Sat 21/11/20	Mon 23/11/20	100%

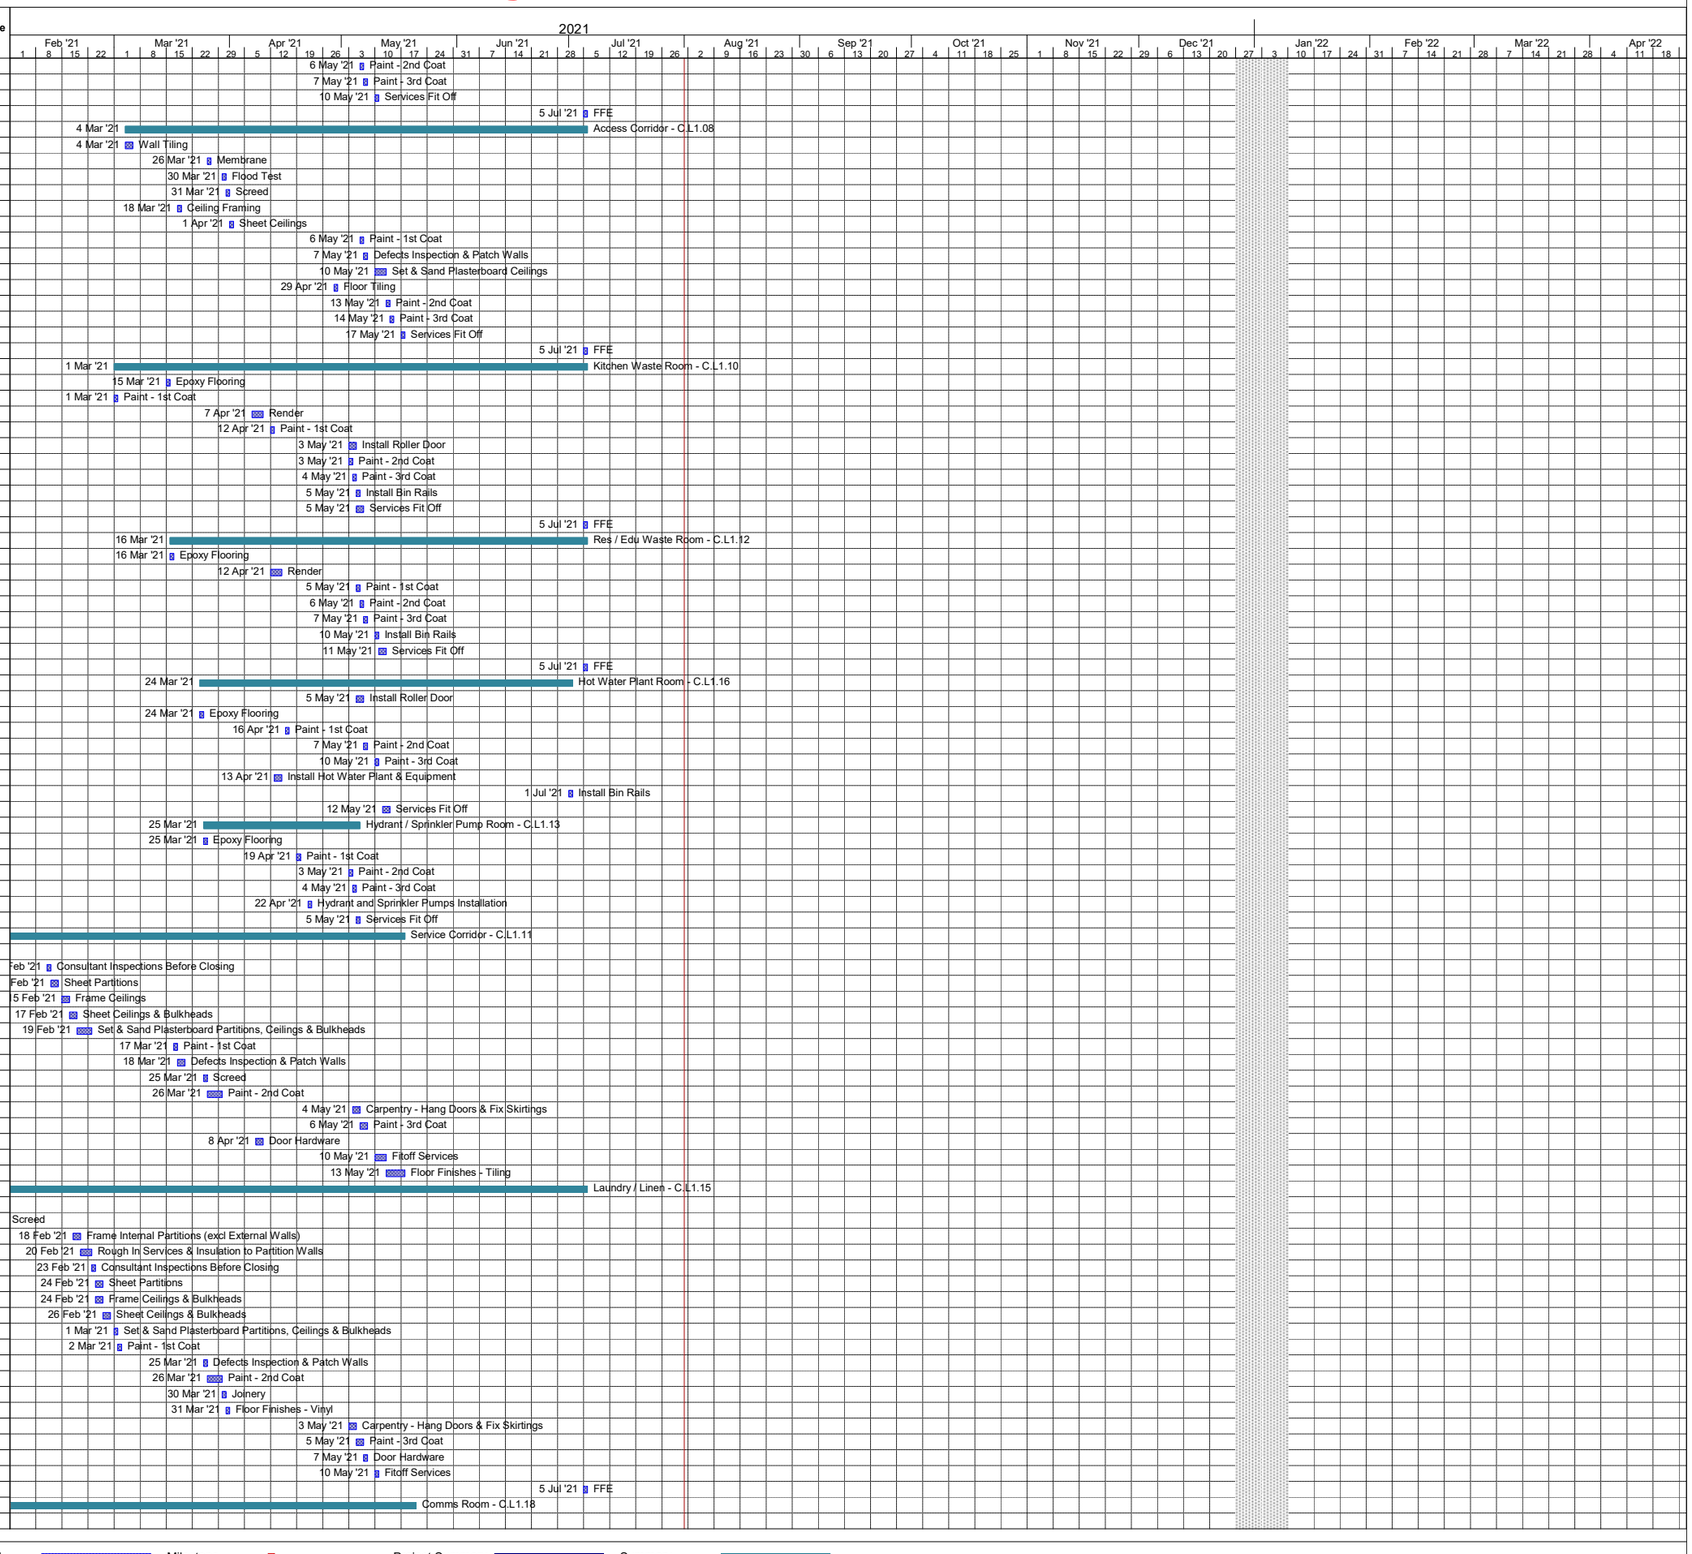

Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
776	Frame Internal Partitions (excl External Walls)	2 d	Tue 24/11/20	Wed 25/11/20	100%
777	Rough In Services & Insulation to Partition Walls	2 d	Tue 23/02/21	Wed 24/02/21	100%
778	Consultant Inspections Before Closing	1 d	Thu 25/02/21	Thu 25/02/21	100%
779	Sheet Partitions	1 d	Fri 26/02/21	Fri 26/02/21	100%
780	Frame Ceilings & Bulkheads	2 d	Sat 27/02/21	Mon 1/03/21	100%
781	Sheet Ceilings & Bulkheads	1 d	Tue 2/03/21	Tue 2/03/21	100%
782	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Wed 3/03/21	Fri 5/03/21	100%
783	Paint - 1st Coat	1 d	Mon 8/03/21	Mon 8/03/21	100%
784	Defects Inspection & Patch Walls	1 d	Thu 25/03/21	Thu 25/03/21	100%
785	Carpentry - Hang Doors & Fix Skirtings	1 d	Thu 25/03/21	Thu 25/03/21	100%
786	Paint - 2nd Coat	1 d	Fri 26/03/21	Fri 26/03/21	100%
787	Door Hardware	1 d	Mon 29/03/21	Mon 29/03/21	100%
788	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
789	Fitoff Services	1 d	Wed 31/03/21	Wed 31/03/21	100%
790	Floor Finishes	1 d	Thu 1/04/21	Thu 1/04/21	100%
791	Comms Racking Installation & Wiring	10 d	Fri 7/05/21	Thu 20/05/21	100%
792	**Kitchen / Staff Room - C.L1.36**	**160 d**	**Sat 14/11/20**	**Mon 5/07/21**	**100%**
793	Run High Level Services	6 d	Sat 14/11/20	Fri 20/11/20	100%
794	Frame Internal Partitions (excl External Walls)	2 d	Sat 21/11/20	Mon 23/11/20	100%
795	Rough In Services & Insulation to Partition Walls	2 d	Tue 24/11/20	Wed 25/11/20	100%
796	Consultant Inspections Before Closing	1 d	Thu 26/11/20	Thu 26/11/20	100%
797	Sheet Partitions	2 d	Fri 27/11/20	Sat 28/11/20	100%
798	Frame Ceilings & Bulkheads	2 d	Fri 26/02/21	Sat 27/02/21	100%
799	Sheet Ceilings & Bulkheads	2 d	Mon 1/03/21	Tue 2/03/21	100%
800	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	1 d	Wed 3/03/21	Wed 3/03/21	100%
801	Paint - 1st Coat	1 d	Fri 5/03/21	Fri 5/03/21	100%
802	Defects Inspection & Patch Walls	1 d	Thu 25/03/21	Thu 25/03/21	100%
803	Carpentry - Hang Doors & Fix Skirtings	2 d	Fri 26/03/21	Mon 29/03/21	100%
804	Paint - 2nd Coat	2 d	Tue 30/03/21	Wed 31/03/21	100%
805	Joinery	1 d	Thu 1/04/21	Thu 1/04/21	100%
806	Door Hardware	1 d	Wed 7/04/21	Wed 7/04/21	100%
807	Paint - 3rd Coat	2 d	Mon 3/05/21	Tue 4/05/21	100%
808	Fitoff Services	1 d	Wed 5/05/21	Wed 5/05/21	100%
809	Floor Finishes - Vinyl	3 d	Thu 6/05/21	Mon 10/05/21	100%
810	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
811	**House Keeping - C.L1.35**	**85 d**	**Mon 1/03/21**	**Mon 5/07/21**	**100%**
812	Frame Ceilings	1 d	Mon 1/03/21	Mon 1/03/21	100%
813	Sheet Ceilings	1 d	Tue 2/03/21	Tue 2/03/21	100%
814	Set & Sand Plasterboard Partitions & Ceilings	3 d	Thu 4/03/21	Sat 6/03/21	100%
815	Paint - 1st Coat	1 d	Tue 9/03/21	Tue 9/03/21	100%
816	Defects Inspection & Patch Walls	1 d	Mon 3/05/21	Mon 3/05/21	100%
817	Carpentry - Hang Doors & Fix Skirtings	1 d	Tue 4/05/21	Tue 4/05/21	100%
818	Paint - 2nd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
819	Joinery	1 d	Thu 6/05/21	Thu 6/05/21	100%
820	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
821	Paint - 3rd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
822	Fitoff Services	1 d	Tue 11/05/21	Tue 11/05/21	100%
823	Floor Finishes - Vinyl	1 d	Wed 12/05/21	Wed 12/05/21	100%
824	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
825	**Cafeteria - C.L1.06**	**119 d**	**Fri 22/01/21**	**Mon 12/07/21**	**100%**
826	High Level Services Rough In	8 d	Fri 22/01/21	Wed 3/02/21	100%
827	Consultant Inspections Before Closing	1 d	Sat 13/02/21	Sat 13/02/21	100%
828	Frame Ceilings	4 d	Mon 15/02/21	Thu 18/02/21	100%
829	Sheet Ceilings & Bulkheads	4 d	Fri 19/02/21	Tue 23/02/21	100%
830	Set & Sand Plasterboard Ceilings	4 d	Wed 24/02/21	Sat 27/02/21	100%
831	Paint - 1st Coat	2 d	Mon 1/03/21	Tue 2/03/21	100%
832	Defects Inspection & Patch Walls	1 d	Thu 25/03/21	Thu 25/03/21	100%
833	Paint - 2nd Coat	4 d	Fri 26/03/21	Wed 31/03/21	100%
834	Decorative Timber Ceiling (Armstrong Battens)	8 d	Thu 1/04/21	Thu 15/04/21	100%
835	Screed & Floor Prep	2 d	Fri 16/04/21	Mon 19/04/21	100%
836	Floor tiling	10 d	Mon 3/05/21	Fri 14/05/21	100%
837	Paint - 3rd Coat	4 d	Mon 17/05/21	Thu 20/05/21	100%
838	Joinery (reception desk)	1 d	Fri 21/05/21	Fri 21/05/21	100%
839	Fitoff Services	1 d	Mon 24/05/21	Mon 24/05/21	100%
840	Cafeteria FFE	5 d	Tue 6/07/21	Mon 12/07/21	100%
841	**Lounge & Resident Entrance C.L1.04 & C.L1.05**	**164 d**	**Sat 21/11/20**	**Mon 19/07/21**	**100%**
842	High Level Services Rough In	6 d	Sat 21/11/20	Fri 27/11/20	100%
843	Consultants Inspection Before Closing	1 d	Sat 28/11/20	Sat 28/11/20	100%
844	Frame Ceilings	4 d	Mon 15/02/21	Thu 18/02/21	100%
845	Sheet Ceilings	3 d	Fri 19/02/21	Mon 22/02/21	100%
846	Set & Sand Plasterboard Ceilings	4 d	Tue 23/02/21	Fri 26/02/21	100%
847	Paint - 1st Coat	2 d	Sat 20/02/21	Mon 22/02/21	100%
848	Defects Inspection & Patch Walls	1 d	Thu 25/03/21	Thu 25/03/21	100%
849	Paint - 2nd Coat	4 d	Fri 26/03/21	Wed 31/03/21	100%
850	Fitoff Services	2 d	Thu 6/05/21	Fri 7/05/21	100%
851	Hang Doors / Second Fix Carpentry	4 d	Mon 10/05/21	Thu 13/05/21	100%
852	Screed	2 d	Fri 14/05/21	Mon 17/05/21	100%
853	Vinyl Floor Finishes	2 d	Tue 18/05/21	Wed 19/05/21	100%
854	Tile Floor Finishes	4 d	Tue 18/05/21	Fri 21/05/21	100%
855	Paint - 3rd Coat	4 d	Mon 24/05/21	Thu 27/05/21	100%
856	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
857	**Service Corridor - C.L1.17**	**133 d**	**Sat 21/11/20**	**Wed 2/06/21**	**100%**
858	High Level Services Rough In	6 d	Sat 21/11/20	Fri 27/11/20	100%
859	Consultants Inspection Before Closing	1 d	Sat 28/11/20	Sat 28/11/20	100%
860	Frame Ceilings	4 d	Mon 1/03/21	Thu 4/03/21	100%
861	Sheet Ceilings	3 d	Fri 5/03/21	Mon 8/03/21	100%
862	Set & Sand Plasterboard Ceilings	4 d	Tue 9/03/21	Fri 12/03/21	100%
863	Paint - 1st Coat	1 d	Sat 13/03/21	Mon 15/03/21	100%
864	Defects Inspection & Patch Walls	1 d	Mon 10/05/21	Mon 10/05/21	100%
865	Paint - 2nd Coat	4 d	Tue 11/05/21	Fri 14/05/21	100%
866	Fitoff Services	2 d	Mon 17/05/21	Tue 18/05/21	100%
867	Hang Doors / Second Fix Carpentry	4 d	Wed 19/05/21	Mon 24/05/21	100%
868	Floor Finishes - Vinyl	3 d	Tue 25/05/21	Thu 27/05/21	100%




Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
869	Paint - 3rd Coat	4 d	Fri 28/05/21	Wed 2/06/21	100%
870	**Elevator Lounge / Lobby C.L1.02 \ C.L1.03**	**52 d**	**Thu 25/03/21**	**Fri 11/06/21**	**100%**
871	Frame Ceilings	2 d	Thu 25/03/21	Fri 26/03/21	100%
872	Sheet Plasterboard Ceiling	1 d	Thu 13/05/21	Thu 13/05/21	100%
873	Set & Sand Plasterboard Ceiling	4 d	Fri 14/05/21	Wed 19/05/21	100%
874	Hang Doors / Fix Skirtings	2 d	Thu 20/05/21	Fri 21/05/21	100%
875	Paint - 1st Coat	1 d	Mon 24/05/21	Mon 24/05/21	100%
876	Defects Inspection & Patch Walls	1 d	Tue 25/05/21	Tue 25/05/21	100%
877	Door Hardware	1 d	Wed 26/05/21	Wed 26/05/21	100%
878	Paint - 2nd Coat	2 d	Thu 27/05/21	Fri 28/05/21	100%
879	Fitoff Services	2 d	Mon 31/05/21	Tue 1/06/21	100%
880	Screed	2 d	Wed 2/06/21	Thu 3/06/21	100%
881	Tile Floor Finishes	4 d	Fri 4/06/21	Wed 9/06/21	100%
882	Paint - 3rd Coat	2 d	Thu 10/06/21	Fri 11/06/21	100%
883	**Floor Handover**	**27 d**	**Wed 16/06/21**	**Thu 22/07/21**	**89%**
884	Signage	4 d	Mon 19/07/21	Thu 22/07/21	75%
885	Initial Clean and Defects	5 d	Wed 16/06/21	Tue 22/06/21	100%
886	**Level 2**	**187 d**	**Fri 30/10/20**	**Fri 23/07/21**	**99%**
887	**Residential Rooms_Services, Walls & Ceilings**	**171 d**	**Fri 30/10/20**	**Thu 1/07/21**	**100%**
888	Mark Up Slab	1 d	Fri 30/10/20	Fri 30/10/20	100%
889	Service Risers and Top Track	6 d	Sat 31/10/20	Fri 6/11/20	100%
890	Run High Level Fire Sprinkler	4 d	Thu 5/11/20	Mon 9/11/20	100%
891	Run High Level Hydraulic Services	5 d	Sat 7/11/20	Thu 12/11/20	100%
892	Run High Level Mechanical Services	5 d	Sat 7/11/20	Thu 12/11/20	100%
893	Run High Level Electrical Services	5 d	Wed 11/11/20	Mon 16/11/20	100%
894	Frame Internal Partitions (excl External Walls)	6 d	Tue 17/11/20	Mon 23/11/20	100%
895	Sheet Partitions 1 Side	7.6 d	Tue 24/11/20	Wed 2/12/20	100%
896	Rough In Services & Insulation to Partition Walls	8 d	Thu 26/11/20	Fri 4/12/20	100%
897	Consultant Inspections Before Closing	1 d	Wed 9/12/20	Wed 9/12/20	100%
898	Sheet and Close 2nd Side Partitions	4 d	Thu 10/12/20	Mon 14/12/20	100%
899	Frame Ceilings	6 d	Sat 19/12/20	Wed 6/01/21	100%
900	Sheet Ceilings & Bulkheads	6 d	Fri 8/01/21	Thu 14/01/21	100%
901	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	6 d	Fri 15/01/21	Thu 21/01/21	100%
902	Paint - 1st Coat	6 d	Fri 22/01/21	Mon 1/02/21	100%
903	Defects Inspection & Patch Walls	1 d	Tue 2/02/21	Tue 2/02/21	100%
904	Paint - 2nd Coat	6 d	Wed 17/02/21	Tue 23/02/21	100%
905	Joinery	6 d	Thu 25/03/21	Thu 1/04/21	100%
906	Floor Finishes - Vinyl	6 d	Sat 13/03/21	Mon 22/03/21	100%
907	Carpentry - Hang Doors & Fix Skirtings	5 d	Wed 7/04/21	Tue 13/04/21	100%
908	Paint - 3rd Coat	4 d	Mon 3/05/21	Thu 6/05/21	100%
909	Door Hardware	6 d	Wed 14/04/21	Wed 21/04/21	100%
910	Fitoff Services	6 d	Fri 7/05/21	Fri 14/05/21	100%
911	FFE	4 d	Mon 28/06/21	Thu 1/07/21	100%
912	**Laundry**	**109 d**	**Fri 22/01/21**	**Mon 28/06/21**	**100%**
913	Frame Ceiling	2 d	Fri 22/01/21	Wed 27/01/21	100%
914	Sheet Plasterboard Ceiling	2 d	Thu 28/01/21	Fri 29/01/21	100%
915	Set Plasterboard Walls & Ceilings	3 d	Sat 30/01/21	Tue 2/02/21	100%
916	Membrane	1 d	Wed 3/02/21	Wed 3/02/21	100%
917	Flood Test	1 d	Thu 4/02/21	Thu 4/02/21	100%
918	Screed	1 d	Fri 5/02/21	Fri 5/02/21	100%
919	Paint - 1st Coat	1 d	Sat 6/02/21	Sat 6/02/21	100%
920	Defects Inspection & Patch Walls	1 d	Mon 8/02/21	Mon 8/02/21	100%
921	Paint - 2nd Coat	1 d	Mon 19/04/21	Mon 19/04/21	100%
922	Floor Finishes - Vinyl	2 d	Tue 20/04/21	Wed 21/04/21	100%
923	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
924	FFE	1 d	Mon 28/06/21	Mon 28/06/21	100%
925	**Kitchen**	**82 d**	**Fri 26/02/21**	**Mon 28/06/21**	**100%**
926	Frame Ceilings	2 d	Fri 26/02/21	Sat 27/02/21	100%
927	Sheet Ceilings & Bulkheads	2 d	Mon 1/03/21	Tue 2/03/21	100%
928	Set & Sand Plasterboard Ceilings & Bulkheads	3 d	Fri 5/03/21	Mon 8/03/21	100%
929	Paint - 1st Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
930	Wall Tiling	6 d	Mon 3/05/21	Mon 10/05/21	100%
931	Membrane	1 d	Thu 8/04/21	Thu 8/04/21	100%
932	Flood Test	1 d	Mon 12/04/21	Mon 12/04/21	100%
933	Screed	1 d	Tue 13/04/21	Tue 13/04/21	100%
934	Paint - 2nd Coat	1 d	Wed 14/04/21	Wed 14/04/21	100%
935	Floor Finishes - Vinyl	1 d	Mon 3/05/21	Mon 3/05/21	100%
936	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
937	Kitchen Fitout	10 d	Mon 19/04/21	Tue 4/05/21	100%
938	Fitoff Services	2 d	Tue 11/05/21	Wed 12/05/21	100%
939	FFE	1 d	Mon 28/06/21	Mon 28/06/21	100%
940	**Wet Areas**	**108 d**	**Wed 27/01/21**	**Mon 28/06/21**	**100%**
941	Membrane	2 d	Wed 27/01/21	Thu 28/01/21	100%
942	Flood Test	1 d	Sat 30/01/21	Sat 30/01/21	100%
943	Screed	2 d	Mon 1/02/21	Tue 2/02/21	100%
944	Wall Tiling	20 d	Wed 3/02/21	Thu 25/02/21	100%
945	Joinery	2 d	Thu 25/03/21	Fri 26/03/21	100%
946	Toilet Partitions	1 d	Mon 29/03/21	Mon 29/03/21	100%
947	Fit Off PC Items	2 d	Tue 30/03/21	Wed 31/03/21	100%
948	Floor Finishes - Vinyl	4 d	Thu 1/04/21	Fri 9/04/21	100%
949	FFE	1 d	Mon 28/06/21	Mon 28/06/21	100%
950	**External Terrace**	**50 d**	**Wed 3/02/21**	**Fri 9/04/21**	**100%**
951	Structural Steel	2 d	Wed 3/02/21	Thu 4/02/21	100%
952	Blockwork	5 d	Sat 20/02/21	Thu 25/02/21	100%
953	Render	3 d	Sat 27/02/21	Tue 2/03/21	100%
954	Glazing	2 d	Thu 25/03/21	Fri 26/03/21	100%
955	Waterproofing	3 d	Mon 29/03/21	Wed 31/03/21	100%
956	Watertest & Curing	2 d	Thu 1/04/21	Wed 7/04/21	100%
957	Internal Terrace Paving	2 d	Thu 8/04/21	Fri 9/04/21	100%
958	**Elevator Lobby - C.L2.50**	**103 d**	**Tue 2/02/21**	**Mon 28/06/21**	**100%**
959	High Level Services Rough In	8 d	Tue 2/02/21	Wed 10/02/21	100%
960	Sheet Wall Partitions	2 d	Tue 16/02/21	Wed 17/02/21	100%
961	Set & Sand Plasterboard Partitions	2 d	Thu 18/02/21	Fri 19/02/21	100%

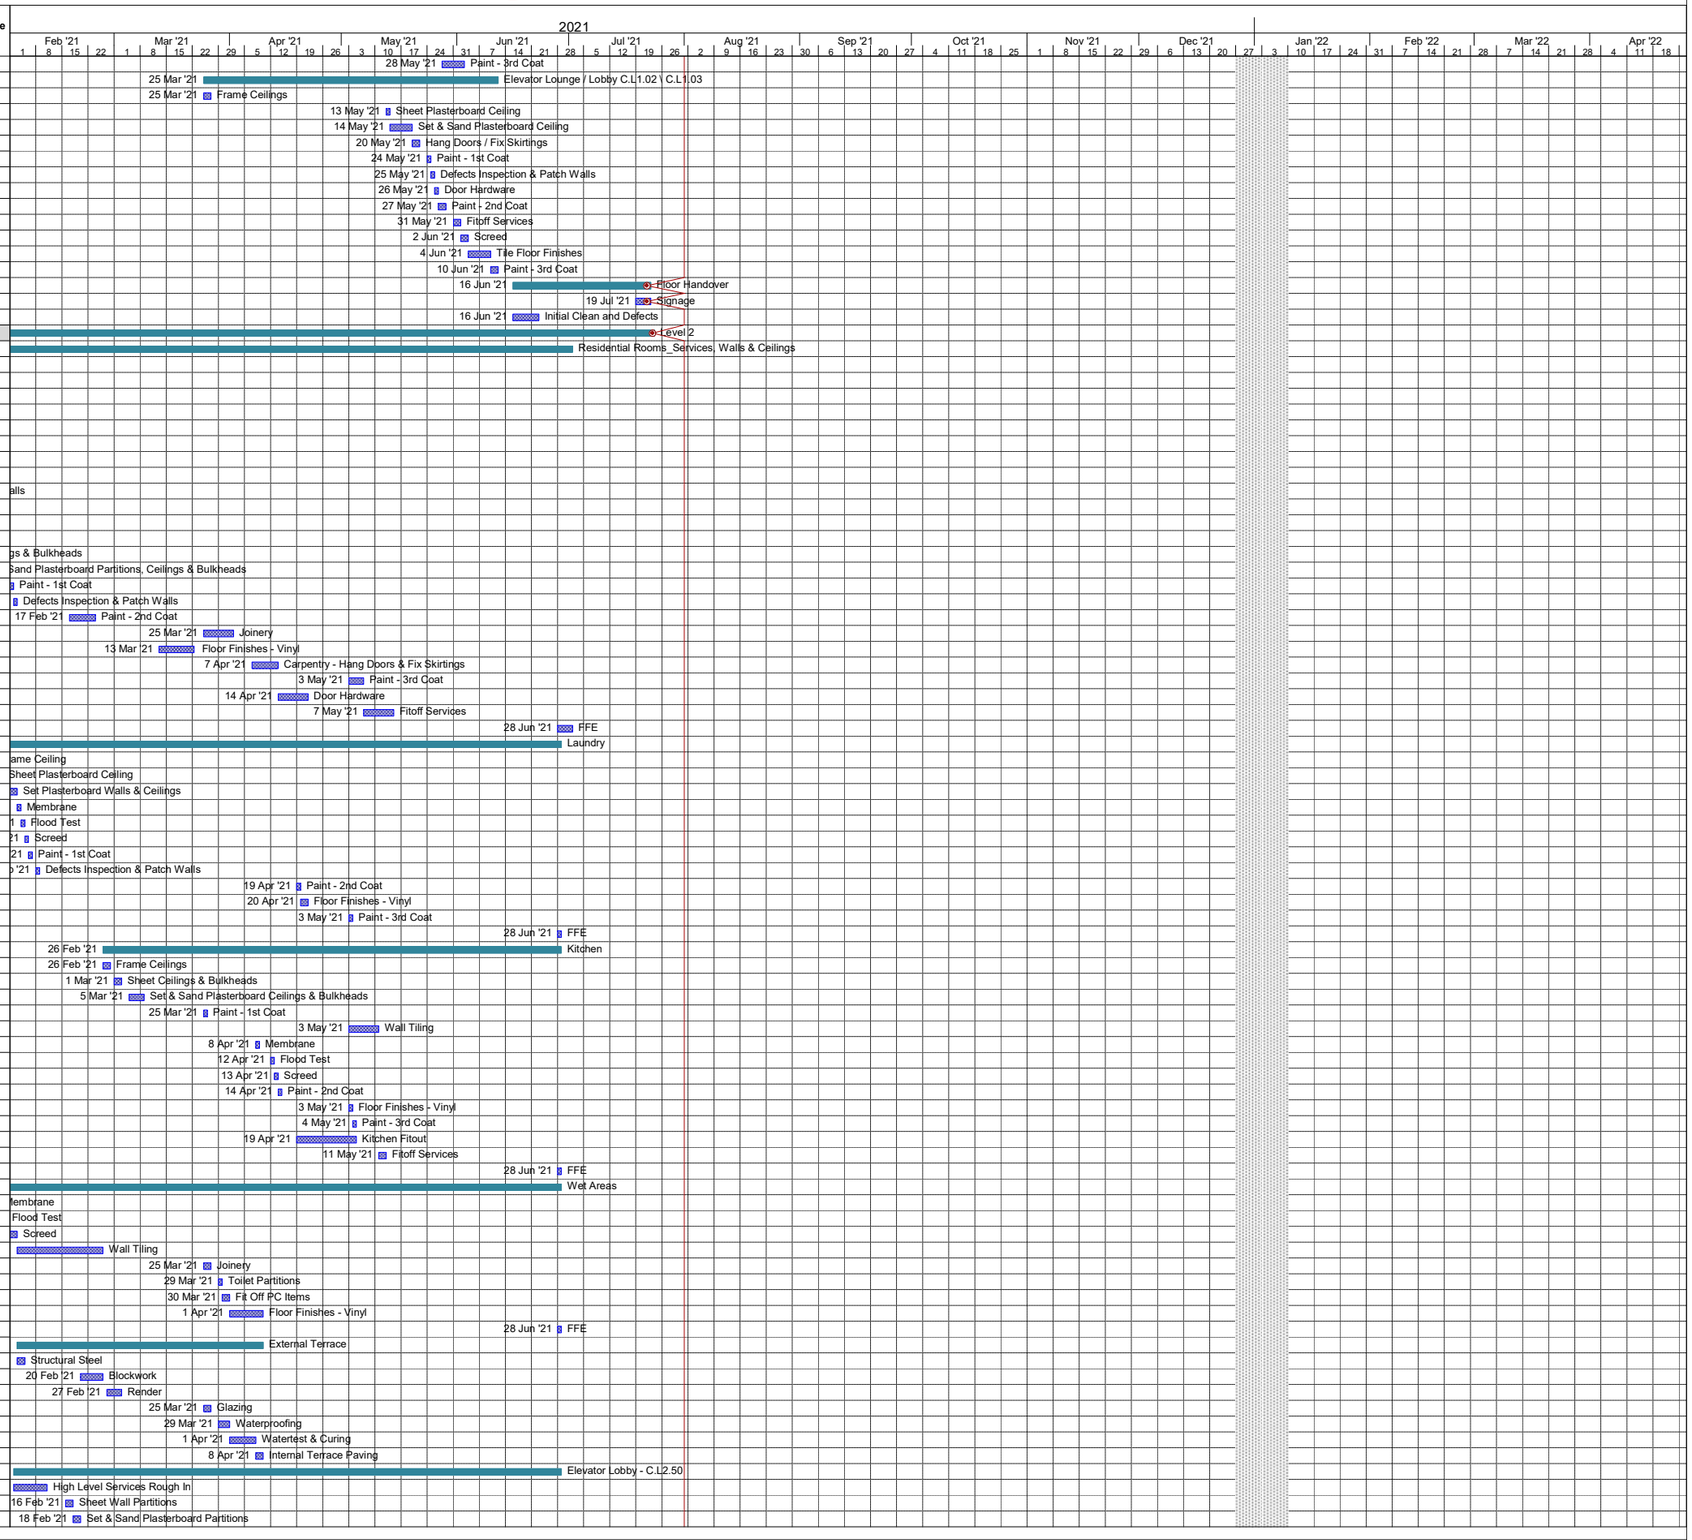


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
962	Render to Walls	3 d	Mon 1/03/21	Wed 3/03/21	100%
963	Frame Ceilings	1 d	Thu 1/04/21	Thu 1/04/21	100%
964	Sheet Ceilings	3 d	Fri 30/04/21	Tue 4/05/21	100%
965	Set & Sand Plasterboard Ceilings	3 d	Wed 5/05/21	Fri 7/05/21	100%
966	Paint - 1st Coat	1 d	Thu 11/03/21	Thu 11/03/21	100%
967	Defects Inspection & Patch Walls	1 d	Mon 3/05/21	Mon 3/05/21	100%
968	Screed	1 d	Tue 4/05/21	Tue 4/05/21	100%
969	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
970	Door Hardware	1 d	Thu 6/05/21	Thu 6/05/21	100%
971	Paint - 2nd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
972	Floor Finishes - Tiling	3 d	Mon 10/05/21	Wed 12/05/21	100%
973	Paint - 3rd Coat	1 d	Thu 13/05/21	Thu 13/05/21	100%
974	Fitoff Services	1 d	Mon 28/06/21	Mon 28/06/21	100%
975	**Common Area Corridors**	**41 d**	**Mon 22/03/21**	**Mon 24/05/21**	**100%**
976	Sheet Ceilings & Bulkheads	6 d	Mon 22/03/21	Mon 29/03/21	100%
977	Set & Sand Plasterboard, Ceilings & Bulkheads	5 d	Tue 30/03/21	Thu 8/04/21	100%
978	Paint - 1st Coat	2 d	Fri 9/04/21	Mon 12/04/21	100%
979	Defects Inspection & Patch Walls	1 d	Tue 13/04/21	Tue 13/04/21	100%
980	Paint - 2nd Coat	3 d	Wed 14/04/21	Fri 16/04/21	100%
981	Floor Finishes - Vinyl	3 d	Thu 13/05/21	Mon 17/05/21	100%
982	Paint - 3rd Coat	3 d	Tue 18/05/21	Thu 20/05/21	100%
983	Fitoff Services	2 d	Fri 21/05/21	Mon 24/05/21	100%
984	**Floor Handover**	**5 d**	**Mon 19/07/21**	**Fri 23/07/21**	**93%**
985	Initial Clean and Defects	5 d	Mon 19/07/21	Fri 23/07/21	100%
986	Signage	2 d	Mon 19/07/21	Tue 20/07/21	75%
987	**Level 3**	**185 d**	**Mon 2/11/20**	**Fri 23/07/21**	**99%**
988	**Residential Rooms_Services, Walls & Ceilings**	**170 d**	**Mon 2/11/20**	**Fri 2/07/21**	**100%**
989	Mark Up Slab	1 d	Mon 2/11/20	Mon 2/11/20	100%
990	Service Risers and Top Track	6 d	Sat 7/11/20	Fri 13/11/20	100%
991	Run High Level Fire Sprinkler	4 d	Sat 21/11/20	Wed 25/11/20	100%
992	Run High Level Hydraulic Services	10 d	Sat 14/11/20	Wed 25/11/20	100%
993	Run High Level Mechanical Services	5 d	Fri 4/12/20	Sat 12/12/20	100%
994	Run High Level Electrical Services	5 d	Fri 11/12/20	Wed 16/12/20	100%
995	Frame Internal Partitions (excl External Walls)	6 d	Thu 17/12/20	Mon 4/01/21	100%
996	Sheet Partitions 1 Side	6 d	Tue 5/01/21	Mon 11/01/21	100%
997	Rough In Services & Insulation to Partition Walls	8 d	Sat 9/01/21	Mon 18/01/21	100%
998	Consultant Inspections Before Closing	1 d	Tue 19/01/21	Tue 19/01/21	100%
999	Sheet and Close 2nd Side Partitions	4 d	Wed 20/01/21	Wed 27/01/21	100%
1000	Frame Ceilings	6 d	Thu 28/01/21	Wed 3/02/21	100%
1001	Sheet Ceilings & Bulkheads	6 d	Thu 4/02/21	Wed 10/02/21	100%
1002	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	6 d	Tue 9/02/21	Mon 15/02/21	100%
1003	Paint - 1st Coat	4 d	Tue 16/02/21	Fri 19/02/21	100%
1004	Defects Inspection & Patch Walls	4 d	Thu 25/03/21	Tue 30/03/21	100%
1005	Joinery	5 d	Wed 31/03/21	Fri 9/04/21	100%
1006	Paint - 2nd Coat	3 d	Thu 8/04/21	Mon 12/04/21	100%
1007	Floor Finishes - Vinyl	5 d	Mon 12/04/21	Fri 16/04/21	100%
1008	Carpentry - Hang Doors & Fix Skirtings	5 d	Mon 3/05/21	Fri 7/05/21	100%
1009	Paint - 3rd Coat	3 d	Mon 10/05/21	Wed 12/05/21	100%
1010	Door Hardware	5 d	Thu 13/05/21	Wed 19/05/21	100%
1011	Fitoff Services	5 d	Thu 13/05/21	Wed 19/05/21	100%
1012	FFE	4 d	Tue 29/06/21	Fri 2/07/21	100%
1013	**Laundry**	**111 d**	**Fri 29/01/21**	**Mon 5/07/21**	**100%**
1014	Membrane	1 d	Fri 29/01/21	Fri 29/01/21	100%
1015	Flood Test	1 d	Mon 1/02/21	Mon 1/02/21	100%
1016	Screed	1 d	Tue 2/02/21	Tue 2/02/21	100%
1017	Frame Ceiling	2 d	Tue 16/02/21	Wed 17/02/21	100%
1018	Sheet Plasterboard Ceiling	2 d	Thu 18/02/21	Fri 19/02/21	100%
1019	Set Plasterboard Walls & Ceilings	3 d	Sat 20/02/21	Tue 23/02/21	100%
1020	Paint - 1st Coat	1 d	Wed 24/02/21	Wed 24/02/21	100%
1021	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
1022	Floor Finishes - Vinyl	2 d	Mon 19/04/21	Tue 20/04/21	100%
1023	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1024	FFE	1 d	Mon 5/07/21	Mon 5/07/21	100%
1025	**Kitchen**	**81 d**	**Mon 1/03/21**	**Tue 29/06/21**	**100%**
1026	Frame Ceilings	2 d	Mon 1/03/21	Tue 2/03/21	100%
1027	Sheet Ceilings & Bulkheads	1 d	Thu 25/03/21	Thu 25/03/21	100%
1028	Set & Sand Plasterboard Ceilings & Bulkheads	3 d	Fri 26/03/21	Tue 30/03/21	100%
1029	Paint - 1st Coat	1 d	Wed 31/03/21	Wed 31/03/21	100%
1030	Wall Tiling	3 d	Mon 3/05/21	Wed 5/05/21	100%
1031	Membrane	1 d	Fri 9/04/21	Fri 9/04/21	100%
1032	Flood Test	1 d	Tue 13/04/21	Tue 13/04/21	100%
1033	Screed	1 d	Mon 3/05/21	Mon 3/05/21	100%
1034	Paint - 2nd Coat	1 d	Thu 15/04/21	Thu 15/04/21	100%
1035	Floor Finishes - Vinyl	2 d	Tue 4/05/21	Wed 5/05/21	100%
1036	Paint - 3rd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
1037	Kitchen Fitout	10 d	Mon 19/04/21	Tue 4/05/21	100%
1038	Fitoff Services	4 d	Wed 5/05/21	Mon 10/05/21	100%
1039	FFE	1 d	Tue 29/06/21	Tue 29/06/21	100%
1040	**Wet Areas**	**87 d**	**Sat 20/02/21**	**Mon 28/06/21**	**100%**
1041	Wall Tiling	6 d	Fri 26/02/21	Thu 4/03/21	100%
1042	Membrane	1 d	Sat 20/02/21	Sat 20/02/21	100%
1043	Flood Test	1 d	Tue 23/02/21	Tue 23/02/21	100%
1044	Screed	6 d	Fri 5/03/21	Thu 11/03/21	100%
1045	Joinery	2 d	Thu 25/03/21	Fri 26/03/21	100%
1046	Toilet Partitions	4 d	Mon 29/03/21	Thu 1/04/21	100%
1047	Fit Off PC Items	2 d	Wed 7/04/21	Thu 8/04/21	100%
1048	Floor Finishes - Vinyl	3 d	Fri 9/04/21	Tue 13/04/21	100%
1049	FFE	1 d	Mon 28/06/21	Mon 28/06/21	100%
1050	**External Terrace**	**73 d**	**Sat 30/01/21**	**Tue 11/05/21**	**100%**
1051	Structural Steel	1 d	Sat 30/01/21	Sat 30/01/21	100%
1052	Blockwork	5 d	Mon 22/02/21	Fri 26/02/21	100%
1053	Render	3 d	Sat 27/02/21	Tue 2/03/21	100%
1054	Glazing	1 d	Thu 25/03/21	Thu 25/03/21	100%

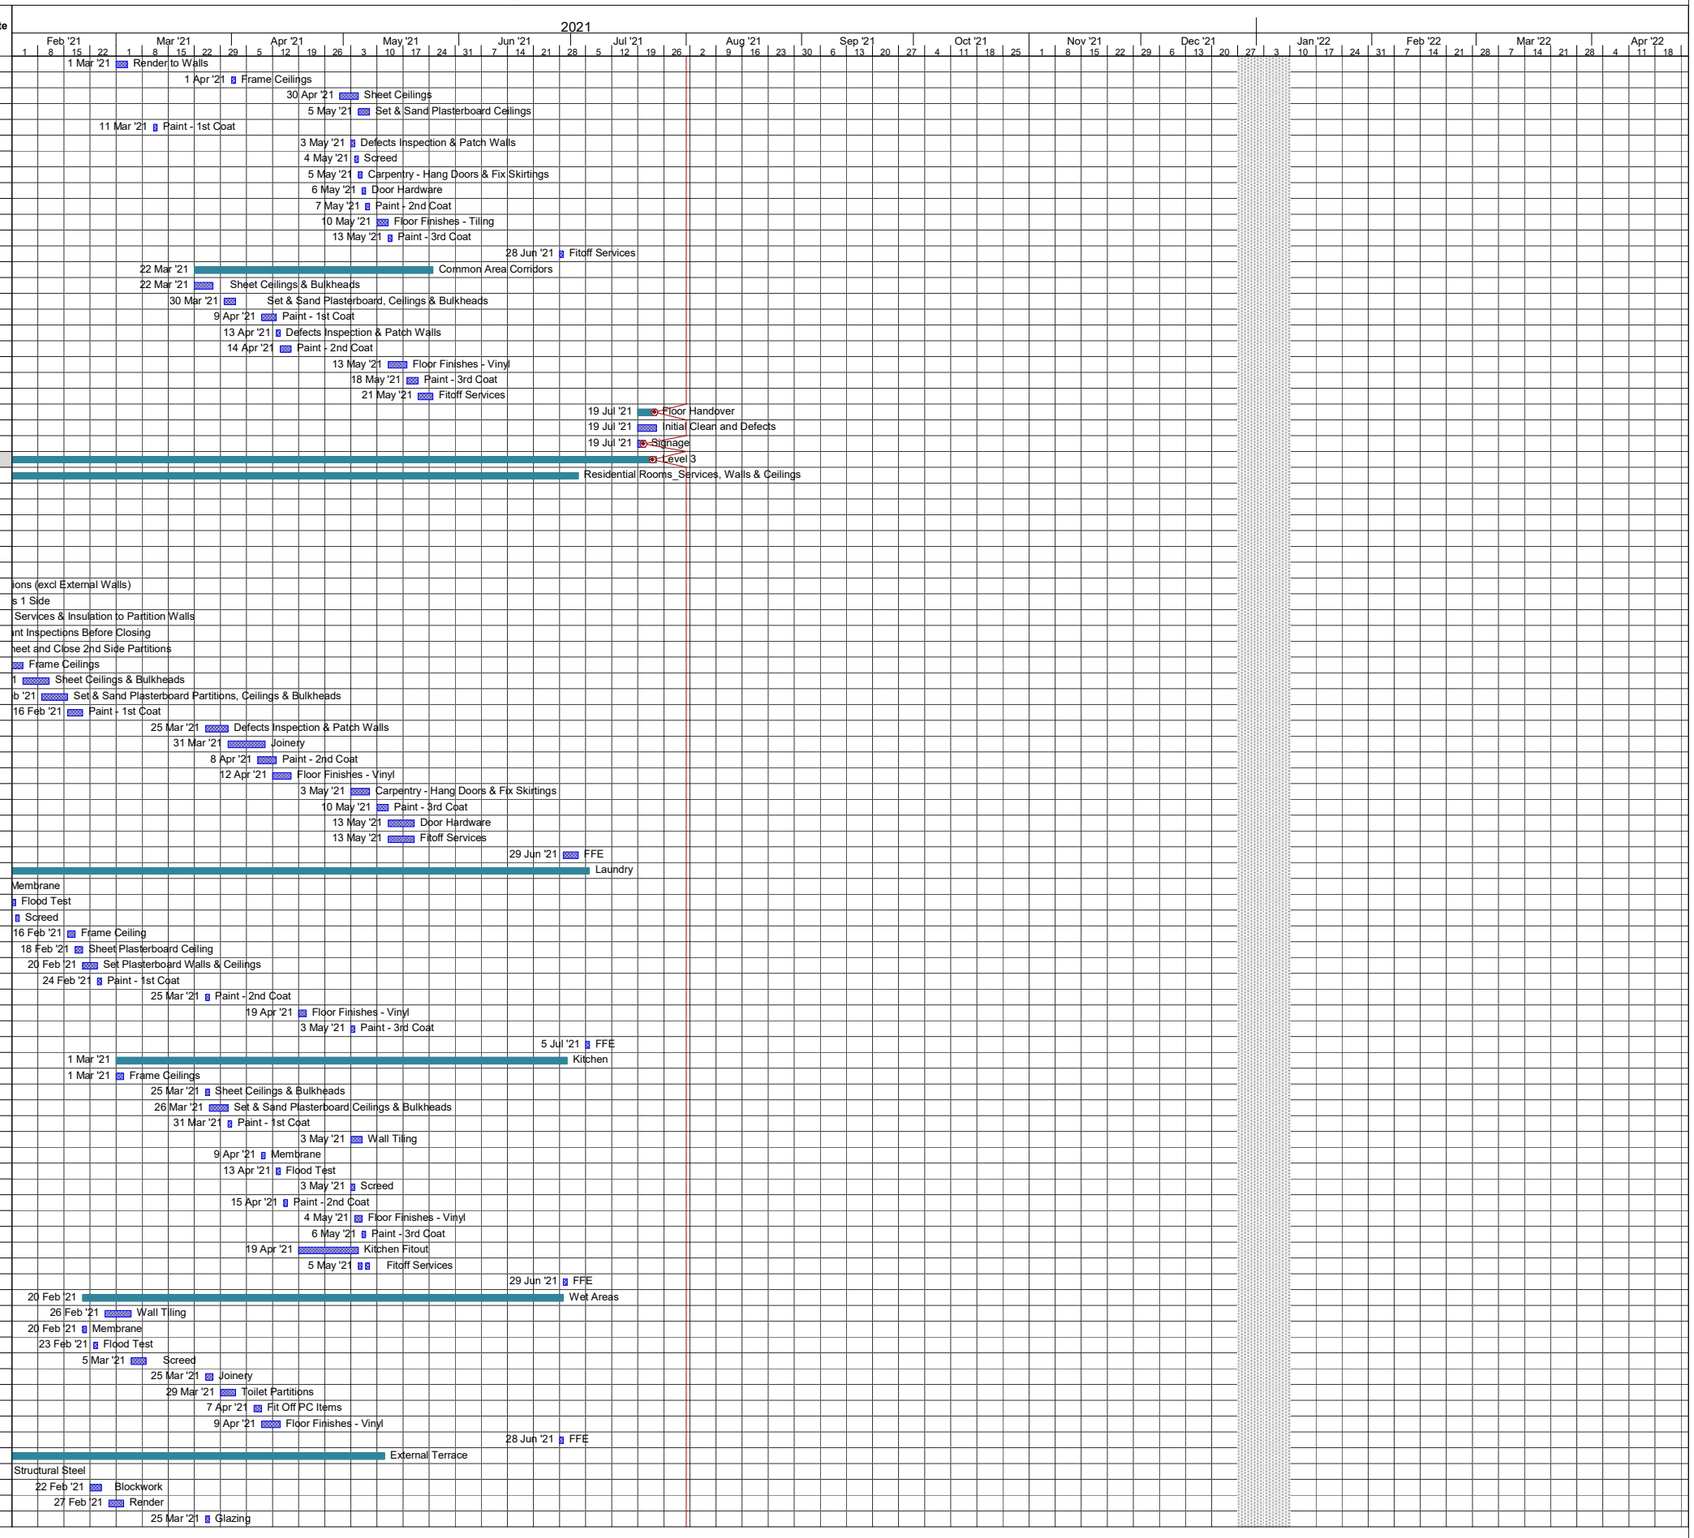


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1055	Waterproofing	3 d	Mon 3/05/21	Wed 5/05/21	100%
1056	Watertest & Curing	2 d	Thu 6/05/21	Fri 7/05/21	100%
1057	Internal Terrace Paving	2 d	Mon 10/05/21	Tue 11/05/21	100%
1058	**Elevator Lobby - C.L4.33**	**75 d**	**Wed 3/02/21**	**Tue 18/05/21**	**100%**
1059	Sheet Wall Partitions	1 d	Wed 3/02/21	Wed 3/02/21	100%
1060	Set & Sand Plasterboard Partitions	2 d	Thu 4/02/21	Fri 5/02/21	100%
1061	Render	3 d	Thu 25/03/21	Mon 29/03/21	100%
1062	Frame Ceilings	2 d	Tue 30/03/21	Wed 31/03/21	100%
1063	Sheet Ceilings	1 d	Thu 1/04/21	Thu 1/04/21	100%
1064	Set & Sand Plasterboard Ceilings	2 d	Wed 7/04/21	Thu 8/04/21	100%
1065	Paint - 1st Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1066	Defects Inspection & Patch Walls	1 d	Mon 12/04/21	Mon 12/04/21	100%
1067	Carpentry - Hang Doors & Fix Skirtings	2 d	Mon 3/05/21	Tue 4/05/21	100%
1068	Door Hardware	1 d	Wed 5/05/21	Wed 5/05/21	100%
1069	Paint - 2nd Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
1070	Floor Finishes - Vinyl	3 d	Wed 12/05/21	Fri 14/05/21	100%
1071	Paint - 3rd Coat	1 d	Mon 17/05/21	Mon 17/05/21	100%
1072	Fitoff Services	1 d	Tue 18/05/21	Tue 18/05/21	100%
1073	**Common Area Corridors**	**24 d**	**Thu 1/04/21**	**Tue 11/05/21**	**100%**
1074	Sheet Ceilings & Bulkheads	4 d	Thu 1/04/21	Fri 9/04/21	100%
1075	Set & Sand Plasterboard, Ceilings & Bulkheads	4 d	Mon 12/04/21	Thu 15/04/21	100%
1076	Paint - 1st Coat	2 d	Fri 16/04/21	Mon 19/04/21	100%
1077	Paint - 2nd Coat	2 d	Tue 20/04/21	Wed 21/04/21	100%
1078	Floor Finishes - Vinyl	3 d	Mon 3/05/21	Wed 5/05/21	100%
1079	Paint - 3rd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
1080	Fitoff Services	2 d	Mon 10/05/21	Tue 11/05/21	100%
1081	**Floor Handover**	**5 d**	**Mon 19/07/21**	**Fri 23/07/21**	**89%**
1082	Initial Clean and Defects	5 d	Mon 19/07/21	Fri 23/07/21	100%
1083	Signage	4 d	Mon 19/07/21	Thu 22/07/21	75%
1084	**Level 4**	**188 d**	**Mon 2/11/20**	**Wed 28/07/21**	**99%**
1085	**Services, Walls & Ceilings**	**170 d**	**Mon 2/11/20**	**Fri 2/07/21**	**100%**
1086	Mark Up Slab	1 d	Mon 2/11/20	Mon 2/11/20	100%
1087	Service Risers and Top Track	12 d	Sat 14/11/20	Fri 27/11/20	100%
1088	Run High Level Fire Sprinkler	2 d	Fri 4/12/20	Wed 9/12/20	100%
1089	Run High Level Hydraulic Services	6 d	Thu 10/12/20	Wed 16/12/20	100%
1090	Run High Level Mechanical Services	4 d	Thu 17/12/20	Mon 21/12/20	100%
1091	Run High Level Electrical Services	4 d	Sat 19/12/20	Mon 4/01/21	100%
1092	Frame Internal Partitions (excl External Walls)	4 d	Tue 5/01/21	Fri 8/01/21	100%
1093	Sheet Partitions 1 Side	4 d	Sat 9/01/21	Wed 13/01/21	100%
1094	Rough In Services & Insulation to Partition Walls	5 d	Tue 12/01/21	Sat 16/01/21	100%
1095	Consultant Inspections Before Closing	1 d	Mon 18/01/21	Mon 18/01/21	100%
1096	Sheet and Close 2nd Side Partitions	4 d	Tue 19/01/21	Fri 22/01/21	100%
1097	Frame Ceilings	20 d	Wed 27/01/21	Thu 18/02/21	100%
1098	Sheet Ceilings & Bulkheads	6 d	Fri 19/02/21	Thu 25/02/21	100%
1099	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Thu 25/03/21	Tue 30/03/21	100%
1100	Paint - 1st Coat	3 d	Wed 31/03/21	Wed 7/04/21	100%
1101	Defects Inspection & Patch Walls	1 d	Thu 8/04/21	Thu 8/04/21	100%
1102	Joinery	4 d	Fri 9/04/21	Wed 14/04/21	100%
1103	Floor Finishes - Vinyl	4 d	Mon 3/05/21	Thu 6/05/21	100%
1104	Paint - 2nd Coat	3 d	Fri 7/05/21	Tue 11/05/21	100%
1105	Carpentry - Hang Doors & Fix Skirtings	5 d	Wed 12/05/21	Tue 18/05/21	100%
1106	Paint - 3rd Coat	3 d	Wed 19/05/21	Fri 21/05/21	100%
1107	Door Hardware	4 d	Mon 24/05/21	Thu 27/05/21	100%
1108	Fitoff Services	6 d	Mon 24/05/21	Mon 31/05/21	100%
1109	FFE	4 d	Tue 29/06/21	Fri 2/07/21	100%
1110	**Wet Areas**	**83 d**	**Fri 26/02/21**	**Tue 29/06/21**	**100%**
1111	Wall Tiling	6 d	Thu 25/03/21	Thu 1/04/21	100%
1112	Membrane	1 d	Fri 26/02/21	Fri 26/02/21	100%
1113	Flood Test	1 d	Mon 1/03/21	Mon 1/03/21	100%
1114	Screed	2 d	Thu 25/03/21	Fri 26/03/21	100%
1115	Floor Finishes - Vinyl	3 d	Wed 7/04/21	Fri 9/04/21	100%
1116	Joinery	4 d	Thu 15/04/21	Tue 20/04/21	100%
1117	Toilet Partitions	4 d	Wed 21/04/21	Wed 28/04/21	100%
1118	Fit Off PC Items	4 d	Thu 29/04/21	Tue 4/05/21	100%
1119	FFE	1 d	Tue 29/06/21	Tue 29/06/21	100%
1120	**Laundry**	**82 d**	**Sat 27/02/21**	**Tue 29/06/21**	**100%**
1121	High Level Services Rough In	10 d	Sat 27/02/21	Wed 10/03/21	100%
1122	Consultant Inspections Before Closing	1 d	Thu 11/03/21	Thu 11/03/21	100%
1123	Frame Ceiling	2 d	Fri 12/03/21	Mon 15/03/21	100%
1124	Sheet Plasterboard Ceiling	2 d	Tue 16/03/21	Wed 17/03/21	100%
1125	Set Plasterboard Walls & Ceilings	3 d	Thu 18/03/21	Mon 22/03/21	100%
1126	Membrane	1 d	Tue 23/03/21	Tue 23/03/21	100%
1127	Flood Test	1 d	Thu 25/03/21	Thu 25/03/21	100%
1128	Screed	1 d	Fri 26/03/21	Fri 26/03/21	100%
1129	Paint - 1st Coat	1 d	Mon 29/03/21	Mon 29/03/21	100%
1130	Paint - 2nd Coat	1 d	Tue 30/03/21	Tue 30/03/21	100%
1131	Floor Finishes - Vinyl	1 d	Wed 31/03/21	Wed 31/03/21	100%
1132	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1133	FFE	1 d	Tue 29/06/21	Tue 29/06/21	100%
1134	**Comms Room - C.L4.34**	**63 d**	**Tue 9/03/21**	**Thu 10/06/21**	**100%**
1135	Sheet Partitions	1 d	Tue 9/03/21	Tue 9/03/21	100%
1136	Frame Ceilings & Bulkheads	2 d	Thu 25/03/21	Fri 26/03/21	100%
1137	Sheet Ceilings & Bulkheads	1 d	Mon 29/03/21	Mon 29/03/21	100%
1138	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Tue 30/03/21	Thu 1/04/21	100%
1139	Paint - 1st Coat	1 d	Wed 7/04/21	Wed 7/04/21	100%
1140	Defects Inspection & Patch Walls	1 d	Thu 8/04/21	Thu 8/04/21	100%
1141	Paint - 2nd Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1142	Floor Finishes - Vinyl	2 d	Mon 3/05/21	Tue 4/05/21	100%
1143	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1144	Paint - 3rd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
1145	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
1146	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
1147	Comms Racking Installation & Wiring	15 d	Fri 21/05/21	Thu 10/06/21	100%

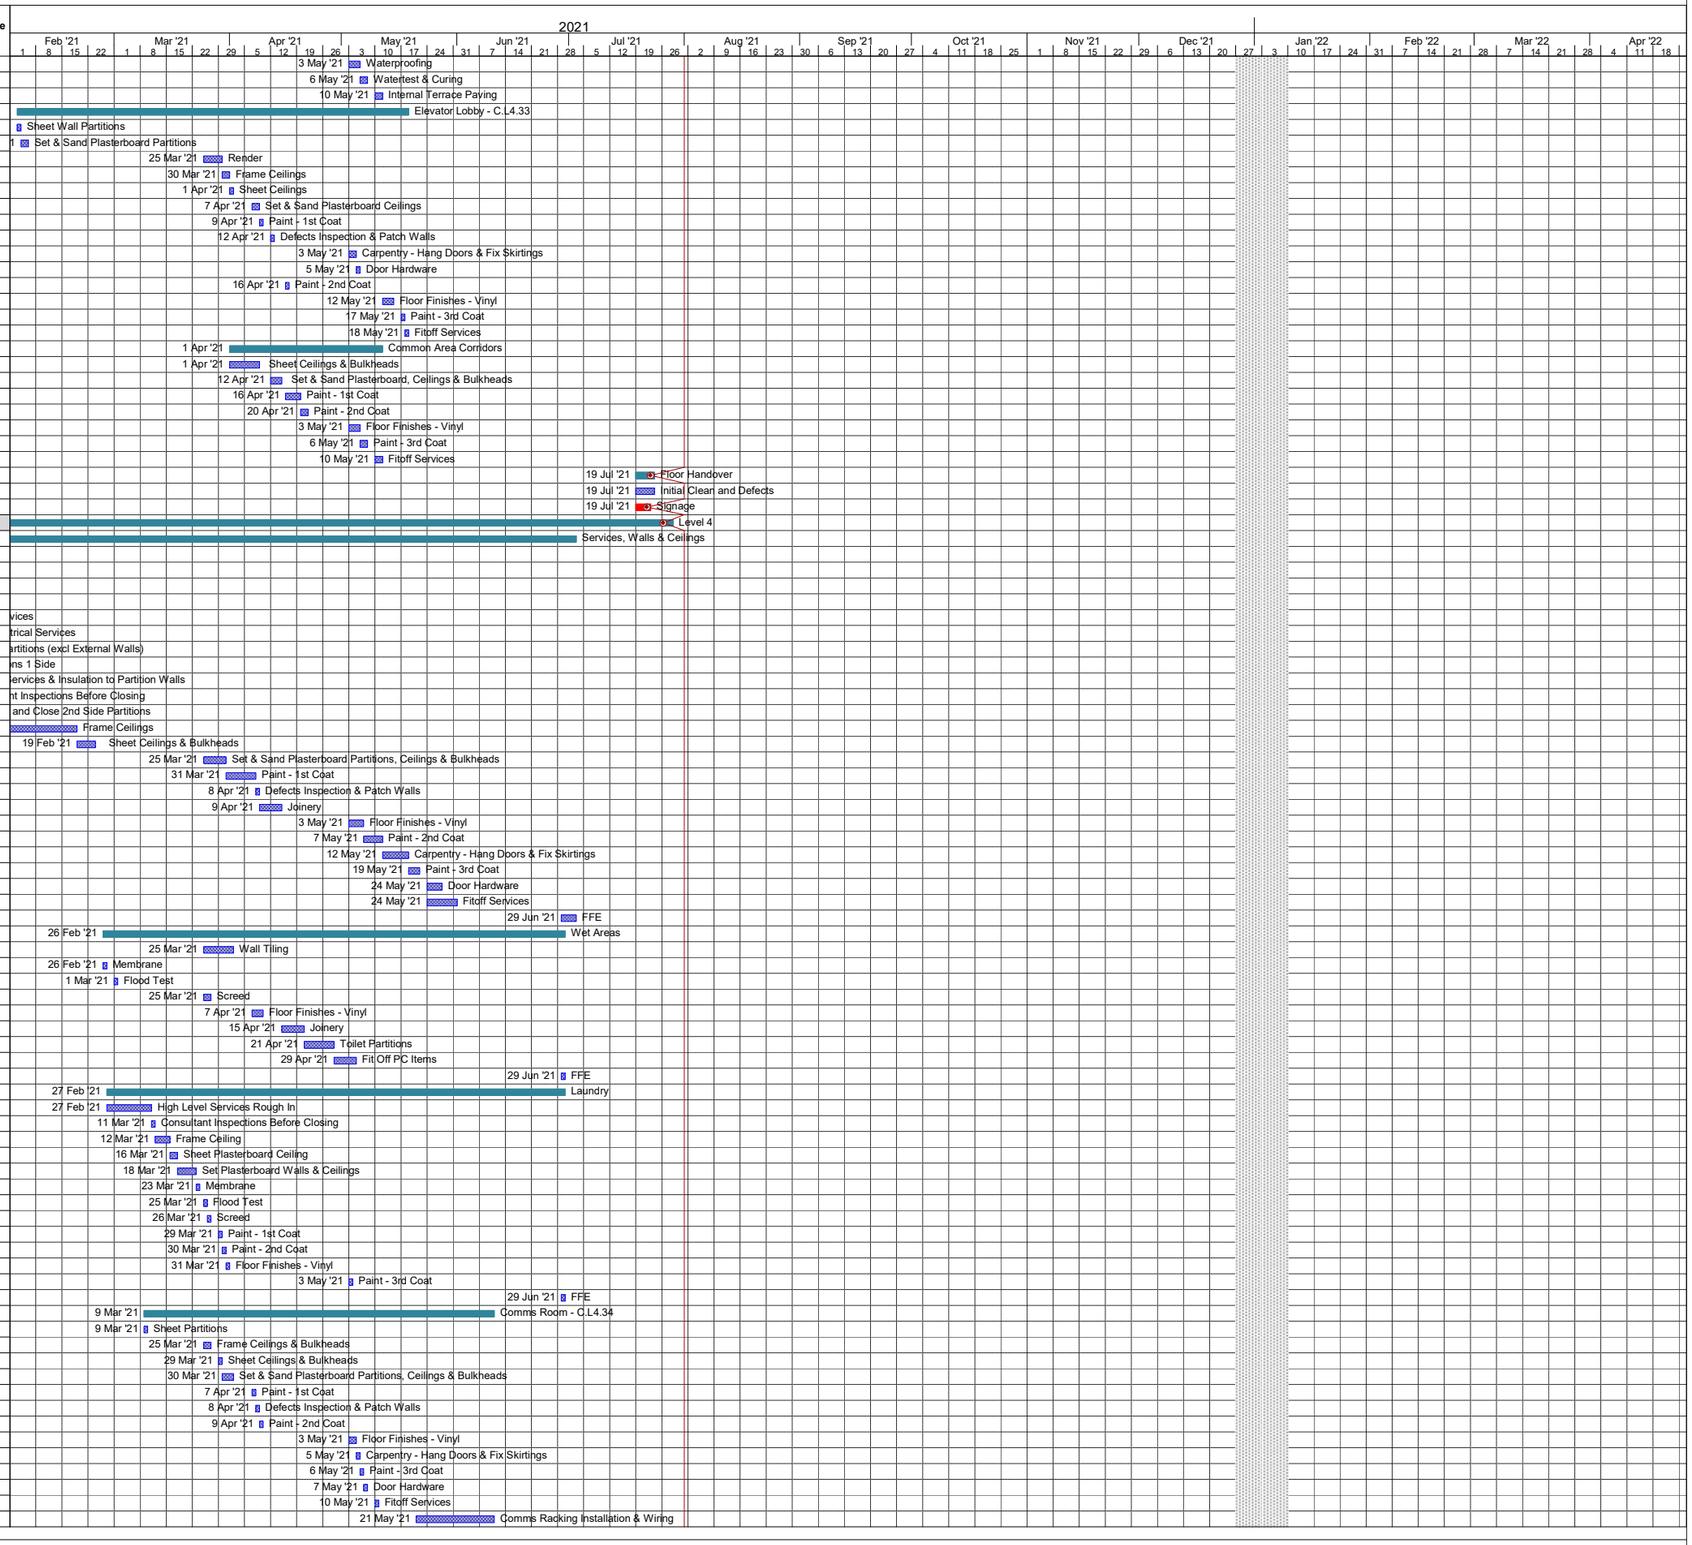


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
1148	**Level 4 Terrace**	**128 d**	**Wed 27/01/21**	**Mon 26/07/21**	**95%**
1149	Membrane	5 d	Wed 27/01/21	Mon 1/02/21	100%
1150	Stainless Steel Balustrading	6 d	Tue 2/02/21	Mon 8/02/21	100%
1151	Erect Columns and Roof Framing	5 d	Mon 1/03/21	Fri 5/03/21	100%
1152	Install Roof Pergola Elements	5 d	Fri 30/04/21	Thu 6/05/21	100%
1153	Mechanical Terrace Plant	5 d	Fri 7/05/21	Thu 13/05/21	100%
1154	Pedestal and Decking System	6 d	Mon 29/03/21	Thu 8/04/21	100%
1155	Glazing To Balustrade Installation	6 d	Fri 7/05/21	Fri 14/05/21	100%
1156	Plant Louvres & Screens	6 d	Tue 22/06/21	Tue 29/06/21	100%
1157	Zen Gardens Planting and Stone Work	6 d	Mon 19/07/21	Mon 26/07/21	75%
1158	FFE	1 d	Mon 19/07/21	Mon 19/07/21	0%
1159	**Elevator Lobby - C.L4.33**	**44 d**	**Thu 25/03/21**	**Tue 1/06/21**	**100%**
1160	Glazed Aluminium Installation	2 d	Thu 25/03/21	Fri 26/03/21	100%
1161	Sheet Wall Partitions	1 d	Mon 29/03/21	Mon 29/03/21	100%
1162	Set & Sand Plasterboard Partitions	1 d	Tue 30/03/21	Tue 30/03/21	100%
1163	Render	3 d	Tue 30/03/21	Thu 1/04/21	100%
1164	Screed	1 d	Wed 7/04/21	Wed 7/04/21	100%
1165	Frame Ceilings	1 d	Thu 8/04/21	Thu 8/04/21	100%
1166	Sheet Ceilings	3 d	Fri 9/04/21	Tue 13/04/21	100%
1167	Set & Sand Plasterboard Ceilings	1 d	Wed 14/04/21	Wed 14/04/21	100%
1168	Paint - 1st Coat	1 d	Thu 15/04/21	Thu 15/04/21	100%
1169	Defects Inspection & Patch Walls	1 d	Fri 16/04/21	Fri 16/04/21	100%
1170	Carpentry - Hang Doors & Fix Skirtings	1 d	Mon 3/05/21	Mon 3/05/21	100%
1171	Paint - 2nd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
1172	Door Hardware	1 d	Wed 5/05/21	Wed 5/05/21	100%
1173	Floor Finishes - Tiling	3 d	Thu 6/05/21	Mon 10/05/21	100%
1174	Paint - 3rd Coat	1 d	Mon 31/05/21	Mon 31/05/21	100%
1175	Fitoff Services	1 d	Tue 1/06/21	Tue 1/06/21	100%
1176	**Floor Handover**	**4 d**	**Fri 23/07/21**	**Wed 28/07/21**	**92%**
1177	Signage	1 d	Fri 23/07/21	Fri 23/07/21	75%
1178	Initial Clean and Defects	2 d	Tue 27/07/21	Wed 28/07/21	100%
1179	**Level 5 (Roof)**	**120 d**	**Sat 30/01/21**	**Mon 19/07/21**	**94%**
1180	Roof Access System	2 d	Sat 30/01/21	Mon 1/02/21	100%
1181	Membrane	2 d	Tue 2/02/21	Wed 3/02/21	100%
1182	Mechanical Roof Plant	5 d	Thu 8/04/21	Wed 14/04/21	100%
1183	Plant Louvres & Screens	6 d	Fri 7/05/21	Fri 14/05/21	100%
1184	Builders Clean	1 d	Mon 19/07/21	Mon 19/07/21	0%
1185	**Stair C1 - Fire Escape Stair (Lvls 1-4)**	**32 d**	**Wed 12/05/21**	**Mon 28/06/21**	**100%**
1186	Install Handrail Balustrading	8 d	Wed 12/05/21	Fri 21/05/21	100%
1187	Epoxy Flooring	4 d	Mon 24/05/21	Thu 27/05/21	100%
1188	Tactiles & Stair Nosings	1 d	Mon 28/06/21	Mon 28/06/21	100%
1189	Services Fit Off	1 d	Mon 31/05/21	Mon 31/05/21	100%
1190	**Stair C2 - Fire Escape Stair (Lvls 1-4)**	**24 d**	**Mon 24/05/21**	**Mon 28/06/21**	**100%**
1191	Install Handrail Balustrading	8 d	Mon 24/05/21	Wed 2/06/21	100%
1192	Epoxy Flooring	4 d	Thu 3/06/21	Tue 8/06/21	100%
1193	Tactiles & Stair Nosings	1 d	Mon 28/06/21	Mon 28/06/21	100%
1194	Services Fit Off	1 d	Thu 10/06/21	Thu 10/06/21	100%
1195	**Final Clean**	**6 d**	**Mon 2/08/21**	**Mon 9/08/21**	**0%**
1196	Final Detailed Clean	6 d	Mon 2/08/21	Mon 9/08/21	0%
1197	*Residential Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
1198	**BUILDING A EDUCATION BUILDING**	**168 d**	**Fri 4/12/20**	**Mon 9/08/21**	**98%**
1199	**Level 1 - Car Park**	**168 d**	**Fri 4/12/20**	**Mon 9/08/21**	**77%**
1200	L1 Mark Up Slab	1 d	Fri 4/12/20	Fri 4/12/20	100%
1201	L1 Run High Level Services - Pre Temp Accom	10 d	Wed 9/12/20	Sat 19/12/20	100%
1202	L1 Run High Level Services - Post Hoist Removal	5 d	Wed 12/05/21	Tue 18/05/21	100%
1203	*Permanent Power Available to Site*	*0 d*	*Mon 17/05/21*	*Mon 17/05/21*	*100%*
1204	**Main Switch Room**	**109 d**	**Tue 16/02/21**	**Thu 22/07/21**	**79%**
1205	MSB Installation	1 d	Tue 16/02/21	Tue 16/02/21	100%
1206	MSB Wiring	10 d	Thu 25/03/21	Mon 12/04/21	100%
1207	Paint - 1st Coat	1 d	Mon 19/07/21	Mon 19/07/21	0%
1208	Paint - 2nd Coat	1 d	Tue 20/07/21	Tue 20/07/21	0%
1209	Epoxy Flooring	2 d	Wed 5/05/21	Thu 6/05/21	100%
1210	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1211	Paint - 3rd Coat	1 d	Wed 21/07/21	Wed 21/07/21	0%
1212	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1213	Fitoff Services	1 d	Thu 22/07/21	Thu 22/07/21	0%
1214	**Car Park Finishes**	**12 d**	**Fri 23/07/21**	**Mon 9/08/21**	**53%**
1215	Clean Floor	2 d	Tue 27/07/21	Wed 28/07/21	100%
1216	Sealer	2 d	Thu 29/07/21	Fri 30/07/21	100%
1217	Roller Door Install	3 d	Fri 23/07/21	Tue 27/07/21	100%
1218	Line Marking	2 d	Mon 2/08/21	Tue 3/08/21	100%
1219	Misc Metalwork, Wheelstops, Bike Racks Etc	4 d	Mon 2/08/21	Thu 5/08/21	0%
1220	Signage	2 d	Wed 4/08/21	Thu 5/08/21	0%
1221	Initial Clean and Defects	2 d	Fri 6/08/21	Mon 9/08/21	0%
1222	**Level 2**	**125 d**	**Fri 22/01/21**	**Tue 20/07/21**	**100%**
1223	**Services & Finishes**	**17 d**	**Fri 22/01/21**	**Sat 13/02/21**	**100%**
1224	L2 Mark Up Slab	1 d	Fri 22/01/21	Fri 22/01/21	100%
1225	Service Risers and Top Track	4 d	Wed 27/01/21	Sat 30/01/21	100%
1226	Frame Internal Partitions (excl External Walls)	5 d	Fri 29/01/21	Wed 3/02/21	100%
1227	Run High Level Hydraulic Services	4 d	Thu 4/02/21	Mon 8/02/21	100%
1228	Run High Level Mechanical Services	5 d	Thu 4/02/21	Tue 9/02/21	100%
1229	Run High Level Electrical Services	5 d	Tue 9/02/21	Sat 13/02/21	100%
1230	**Small Classroom # 1 - A.L2.01**	**107 d**	**Mon 15/02/21**	**Mon 19/07/21**	**100%**
1231	Rough In Services & Insulation to Partition Walls	2 d	Mon 15/02/21	Tue 16/02/21	100%
1232	Consultant Inspections Before Closing	1 d	Mon 22/02/21	Mon 22/02/21	100%
1233	Sheet Plasterboard Partitions	2 d	Thu 25/03/21	Fri 26/03/21	100%
1234	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1235	Frame Ceilings	2 d	Wed 5/05/21	Thu 6/05/21	100%
1236	Sheet Perimeter Set Ceiling	3 d	Fri 7/05/21	Tue 11/05/21	100%
1237	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Wed 12/05/21	Thu 13/05/21	100%
1238	Paint - 1st Coat	1 d	Fri 14/05/21	Fri 14/05/21	100%
1239	Defects Inspection & Patch Walls	1 d	Mon 17/05/21	Mon 17/05/21	100%
1240	Paint - 2nd Coat	2 d	Tue 18/05/21	Wed 19/05/21	100%

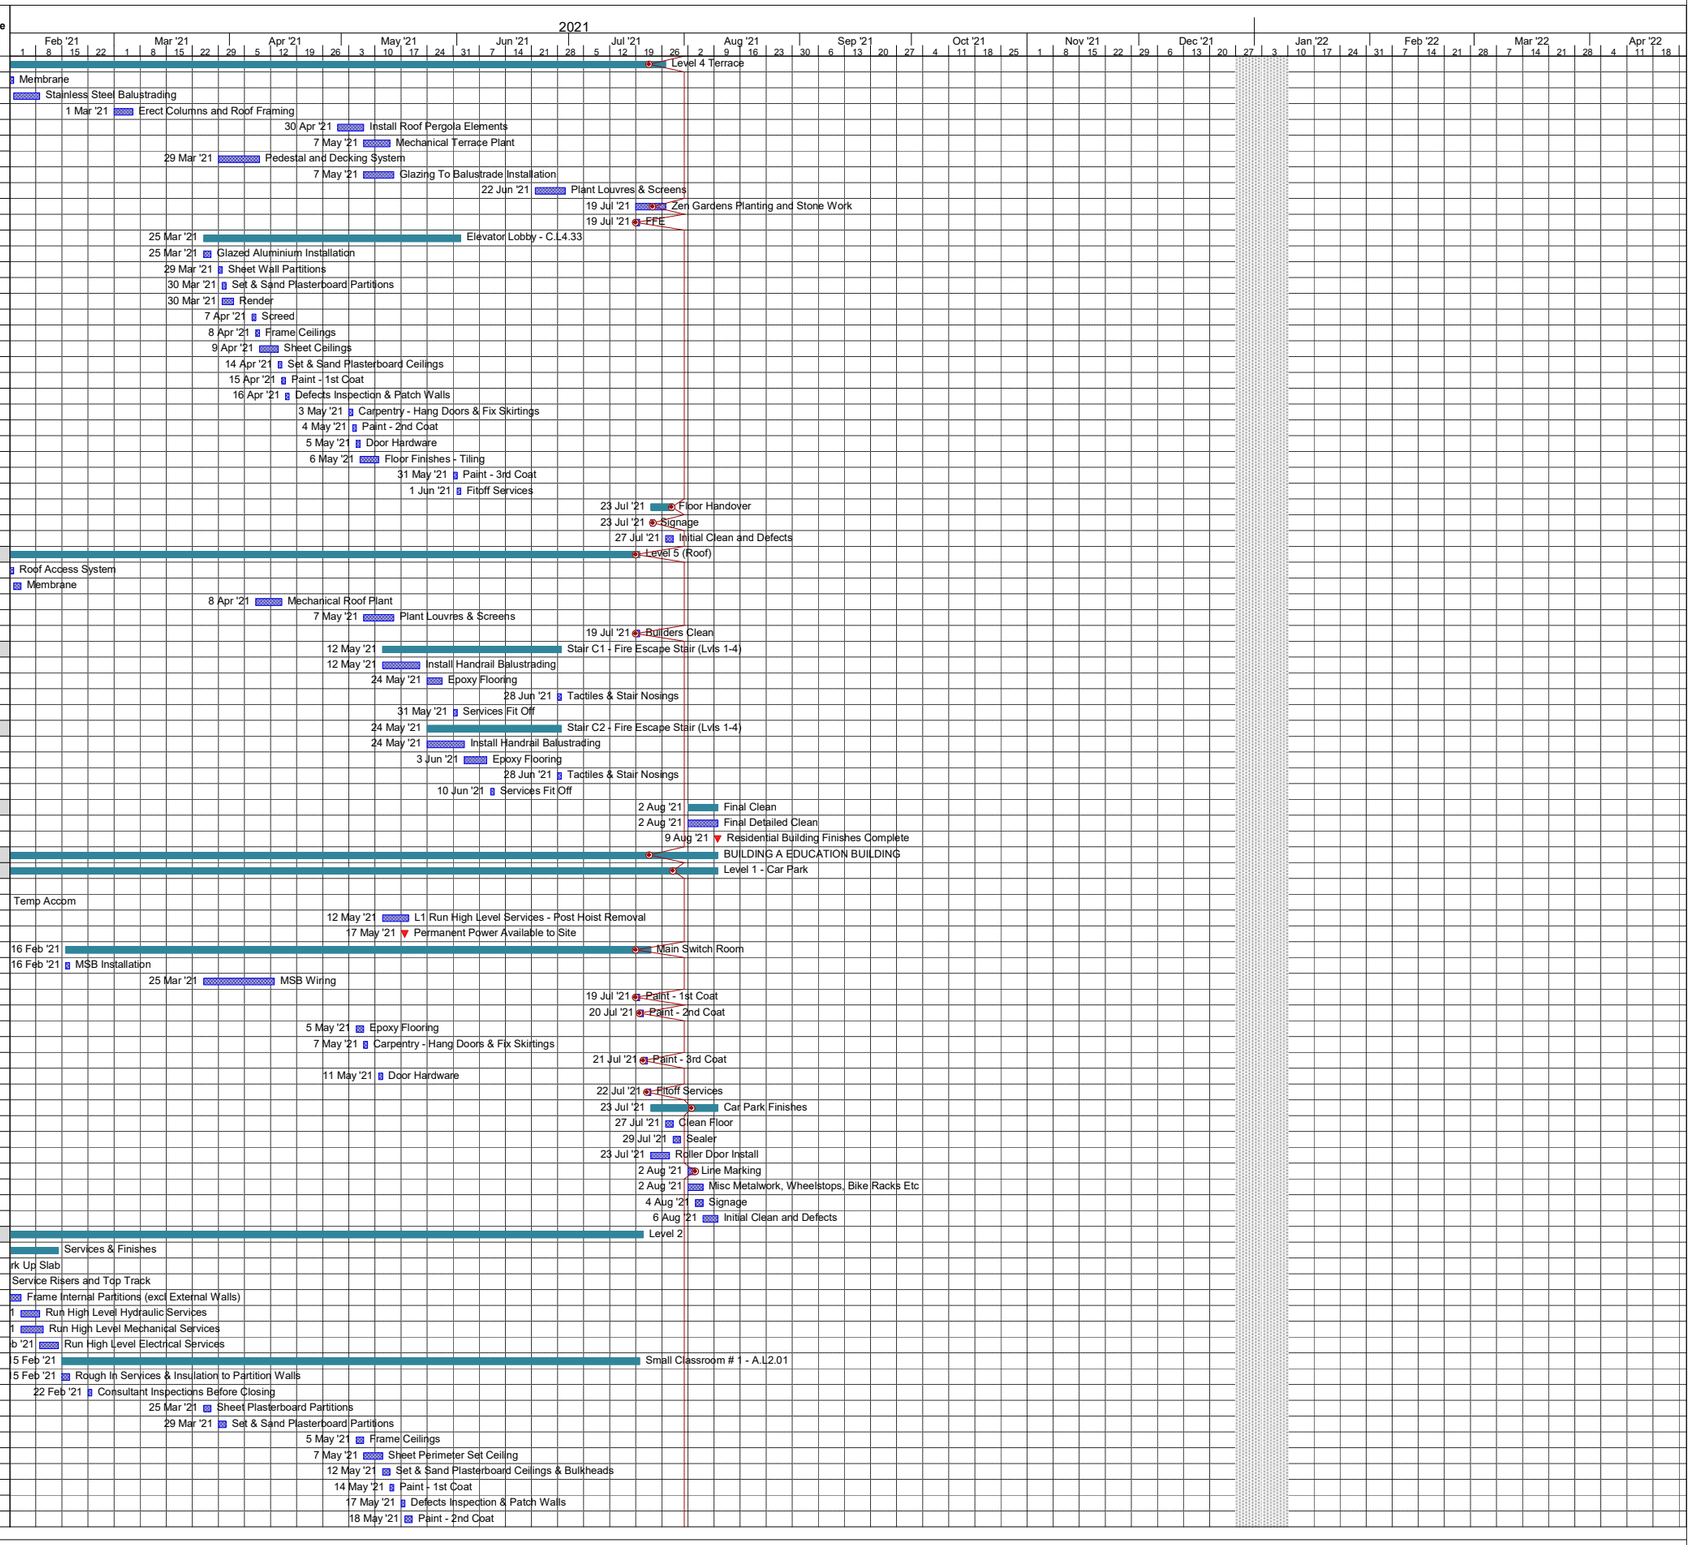


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1241	Raised Access Flooring	1 d	Tue 18/05/21	Tue 18/05/21	100%
1242	Joinery	1 d	Wed 19/05/21	Wed 19/05/21	100%
1243	Carpentry - Hang Doors & Fix Skirtings	1 d	Thu 20/05/21	Thu 20/05/21	100%
1244	Operable Wall Installation	1 d	Mon 12/07/21	Mon 12/07/21	100%
1245	Paint - 3rd Coat	2 d	Wed 26/05/21	Thu 27/05/21	100%
1246	Door Hardware	1 d	Fri 28/05/21	Fri 28/05/21	100%
1247	Floor Finishes - Carpet	2 d	Fri 28/05/21	Mon 31/05/21	100%
1248	Fitoff Services (inc. AV)	4 d	Tue 1/06/21	Fri 4/06/21	100%
1249	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1250	**Small Classroom # 2 - A.L2.02**	**105 d**	**Wed 17/02/21**	**Mon 19/07/21**	**100%**
1251	Rough In Services & Insulation to Partition Walls	2 d	Wed 17/02/21	Thu 18/02/21	100%
1252	Consultant Inspections Before Closing	1 d	Fri 19/02/21	Fri 19/02/21	100%
1253	Sheet Plasterboard Partitions	2 d	Thu 25/03/21	Fri 26/03/21	100%
1254	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1255	Frame Ceilings	2 d	Fri 7/05/21	Mon 10/05/21	100%
1256	Sheet Perimeter Set Ceiling	3 d	Tue 11/05/21	Thu 13/05/21	100%
1257	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Fri 14/05/21	Mon 17/05/21	100%
1258	Paint - 1st Coat	1 d	Tue 18/05/21	Tue 18/05/21	100%
1259	Defects Inspection & Patch Walls	1 d	Wed 19/05/21	Wed 19/05/21	100%
1260	Paint - 2nd Coat	1 d	Thu 20/05/21	Thu 20/05/21	100%
1261	Raised Access Flooring	1 d	Fri 21/05/21	Fri 21/05/21	100%
1262	Operable Wall Installation	1 d	Tue 13/07/21	Tue 13/07/21	100%
1263	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 26/05/21	Wed 26/05/21	100%
1264	Paint - 3rd Coat	1 d	Thu 27/05/21	Thu 27/05/21	100%
1265	Door Hardware	1 d	Fri 28/05/21	Fri 28/05/21	100%
1266	Floor Finishes - Carpet	2 d	Mon 31/05/21	Tue 1/06/21	100%
1267	Fitoff Services (inc. AV)	4 d	Fri 28/05/21	Wed 2/06/21	100%
1268	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1269	**Small Classroom # 3 - A.L2.03**	**103 d**	**Fri 19/02/21**	**Mon 19/07/21**	**100%**
1270	Rough In Services & Insulation to Partition Walls	2 d	Fri 19/02/21	Sat 20/02/21	100%
1271	Consultant Inspections Before Closing	1 d	Mon 22/02/21	Mon 22/02/21	100%
1272	Sheet Plasterboard Partitions	2 d	Thu 25/03/21	Fri 26/03/21	100%
1273	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1274	Frame Ceilings	2 d	Mon 3/05/21	Tue 4/05/21	100%
1275	Sheet Perimeter Set Ceiling	3 d	Wed 5/05/21	Fri 7/05/21	100%
1276	Set & Sand Plasterboard Ceilings & Bulkheads	4 d	Mon 10/05/21	Thu 13/05/21	100%
1277	Paint - 1st Coat	1 d	Fri 14/05/21	Fri 14/05/21	100%
1278	Defects Inspection & Patch Walls	1 d	Mon 17/05/21	Mon 17/05/21	100%
1279	Raised Access Flooring	1 d	Mon 24/05/21	Mon 24/05/21	100%
1280	Joinery	2 d	Tue 25/05/21	Wed 26/05/21	100%
1281	Carpentry - Hang Doors & Fix Skirtings	1 d	Thu 27/05/21	Thu 27/05/21	100%
1282	Paint - 2nd Coat	2 d	Fri 28/05/21	Mon 31/05/21	100%
1283	Door Hardware	1 d	Tue 1/06/21	Tue 1/06/21	100%
1284	Floor Finishes - Carpet	3 d	Wed 2/06/21	Fri 4/06/21	100%
1285	Paint - 3rd Coat	2 d	Mon 7/06/21	Tue 8/06/21	100%
1286	Fitoff Services (inc. AV)	3 d	Wed 9/06/21	Fri 11/06/21	100%
1287	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1288	**Small Classroom # 4 - A.L2.14**	**101 d**	**Mon 22/02/21**	**Mon 19/07/21**	**100%**
1289	Rough In Services & Insulation to Partition Walls	2 d	Mon 22/02/21	Tue 23/02/21	100%
1290	Consultant Inspections Before Closing	1 d	Wed 24/02/21	Wed 24/02/21	100%
1291	Sheet Partitions	4 d	Thu 25/02/21	Mon 1/03/21	100%
1292	Frame Ceilings	2 d	Thu 25/03/21	Fri 26/03/21	100%
1293	Sheet Perimeter Set Ceiling	3 d	Mon 29/03/21	Wed 31/03/21	100%
1294	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Thu 1/04/21	Fri 9/04/21	100%
1295	Paint - 1st Coat	1 d	Mon 12/04/21	Mon 12/04/21	100%
1296	Defects Inspection & Patch Walls	1 d	Tue 13/04/21	Tue 13/04/21	100%
1297	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1298	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1299	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1300	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1301	Floor Finishes - Carpet	3 d	Tue 11/05/21	Thu 13/05/21	100%
1302	Paint - 3rd Coat	3 d	Fri 14/05/21	Tue 18/05/21	100%
1303	Fitoff Services (inc. AV)	4 d	Wed 16/06/21	Mon 21/06/21	100%
1304	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1305	**Small Classroom # 5 - A.L2.13**	**99 d**	**Wed 24/02/21**	**Mon 19/07/21**	**100%**
1306	Rough In Services & Insulation to Partition Walls	2 d	Wed 24/02/21	Thu 25/02/21	100%
1307	Consultant Inspections Before Closing	1 d	Fri 26/02/21	Fri 26/02/21	100%
1308	Sheet Partitions	2 d	Thu 25/03/21	Fri 26/03/21	100%
1309	Frame Ceilings	2 d	Mon 29/03/21	Tue 30/03/21	100%
1310	Sheet Perimeter Set Ceiling	3 d	Wed 31/03/21	Wed 7/04/21	100%
1311	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Thu 8/04/21	Tue 13/04/21	100%
1312	Paint - 1st Coat	1 d	Wed 14/04/21	Wed 14/04/21	100%
1313	Defects Inspection & Patch Walls	1 d	Thu 15/04/21	Thu 15/04/21	100%
1314	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1315	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1316	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1317	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1318	Floor Finishes - Carpet	3 d	Tue 11/05/21	Thu 13/05/21	100%
1319	Paint - 3rd Coat	3 d	Fri 14/05/21	Tue 18/05/21	100%
1320	Fitoff Services (inc. AV)	4 d	Tue 22/06/21	Fri 25/06/21	100%
1321	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1322	**Small Classroom # 6 - A.L2.04**	**97 d**	**Fri 26/02/21**	**Mon 19/07/21**	**100%**
1323	Rough In Services & Insulation to Partition Walls	2 d	Fri 26/02/21	Sat 27/02/21	100%
1324	Consultant Inspections Before Closing	1 d	Mon 1/03/21	Mon 1/03/21	100%
1325	Sheet Partitions	4 d	Tue 2/03/21	Fri 5/03/21	100%
1326	Frame Ceilings	2 d	Thu 25/03/21	Fri 26/03/21	100%
1327	Sheet Perimeter Set Ceiling	3 d	Mon 29/03/21	Wed 31/03/21	100%
1328	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Thu 1/04/21	Fri 9/04/21	100%
1329	Paint - 1st Coat	1 d	Mon 12/04/21	Mon 12/04/21	100%
1330	Defects Inspection & Patch Walls	1 d	Tue 13/04/21	Tue 13/04/21	100%
1331	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1332	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1333	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%

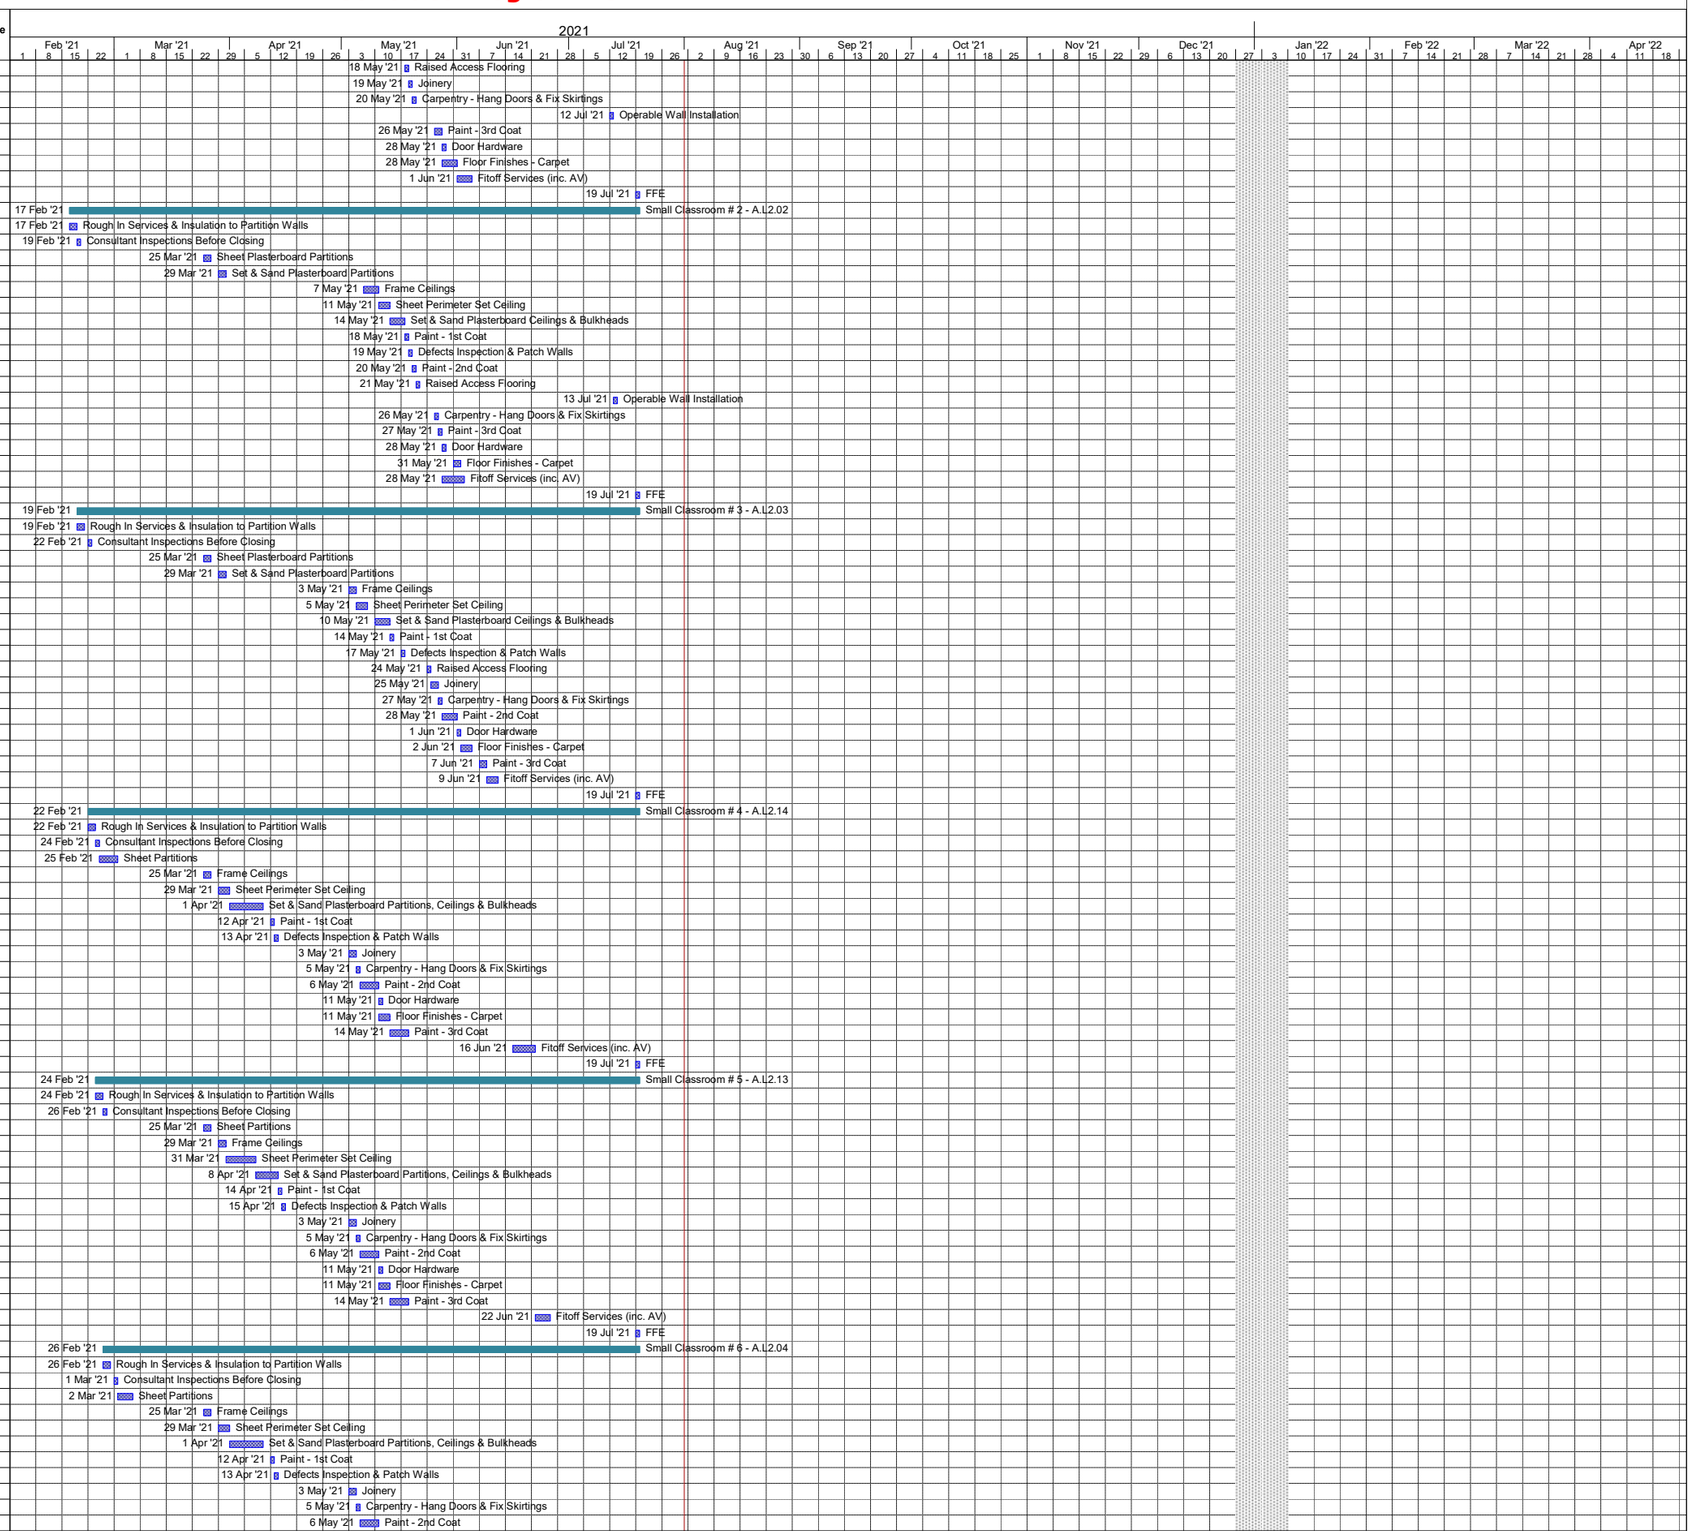

Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
1334	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1335	Floor Finishes - Carpet	3 d	Wed 12/05/21	Fri 14/05/21	100%
1336	Paint - 3rd Coat	3 d	Mon 17/05/21	Wed 19/05/21	100%
1337	Fitoff Services (inc. AV)	4 d	Mon 28/06/21	Thu 1/07/21	100%
1338	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1339	**Small Classroom # 7 - A.L2.05**	**95 d**	**Mon 1/03/21**	**Mon 19/07/21**	**100%**
1340	Rough In Services & Insulation to Partition Walls	2 d	Mon 1/03/21	Tue 2/03/21	100%
1341	Consultant Inspections Before Closing	1 d	Wed 3/03/21	Wed 3/03/21	100%
1342	Sheet Partitions	2 d	Thu 25/03/21	Fri 26/03/21	100%
1343	Frame Ceilings	2 d	Mon 29/03/21	Tue 30/03/21	100%
1344	Sheet Perimeter Set Ceiling	3 d	Wed 31/03/21	Wed 7/04/21	100%
1345	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Thu 8/04/21	Tue 13/04/21	100%
1346	Paint - 1st Coat	1 d	Wed 14/04/21	Wed 14/04/21	100%
1347	Defects Inspection & Patch Walls	1 d	Thu 15/04/21	Thu 15/04/21	100%
1348	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1349	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1350	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1351	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1352	Floor Finishes - Carpet	3 d	Wed 12/05/21	Fri 14/05/21	100%
1353	Paint - 3rd Coat	3 d	Mon 17/05/21	Wed 19/05/21	100%
1354	Fitoff Services (inc. AV)	4 d	Thu 20/05/21	Tue 25/05/21	100%
1355	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1356	**Language # 1 - A.L2.08**	**93 d**	**Wed 3/03/21**	**Mon 19/07/21**	**100%**
1357	Rough In Services & Insulation to Partition Walls	2 d	Wed 3/03/21	Thu 4/03/21	100%
1358	Consultant Inspections Before Closing	1 d	Fri 5/03/21	Fri 5/03/21	100%
1359	Sheet Partitions	4 d	Sat 6/03/21	Wed 10/03/21	100%
1360	Frame Ceilings	2 d	Thu 25/03/21	Fri 26/03/21	100%
1361	Sheet Ceilings & Bulkheads	3 d	Mon 29/03/21	Wed 31/03/21	100%
1362	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Thu 1/04/21	Thu 8/04/21	100%
1363	Paint - 1st Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1364	Defects Inspection & Patch Walls	1 d	Mon 12/04/21	Mon 12/04/21	100%
1365	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1366	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1367	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1368	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1369	Floor Finishes - Carpet	3 d	Tue 11/05/21	Thu 13/05/21	100%
1370	Paint - 3rd Coat	3 d	Fri 14/05/21	Tue 18/05/21	100%
1371	Fitoff Services (inc. AV)	4 d	Wed 19/05/21	Mon 24/05/21	100%
1372	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1373	**Language # 2 - A.L2.07**	**91 d**	**Fri 5/03/21**	**Mon 19/07/21**	**100%**
1374	Rough In Services & Insulation to Partition Walls	2 d	Fri 5/03/21	Sat 6/03/21	100%
1375	Consultant Inspections Before Closing	1 d	Mon 8/03/21	Mon 8/03/21	100%
1376	Sheet Partitions	4 d	Tue 9/03/21	Fri 12/03/21	100%
1377	Frame Ceilings	2 d	Thu 25/03/21	Fri 26/03/21	100%
1378	Sheet Ceilings & Bulkheads	3 d	Mon 29/03/21	Wed 31/03/21	100%
1379	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Thu 1/04/21	Thu 8/04/21	100%
1380	Paint - 1st Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1381	Defects Inspection & Patch Walls	1 d	Mon 12/04/21	Mon 12/04/21	100%
1382	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1383	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1384	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1385	Door Hardware	1 d	Thu 6/05/21	Thu 6/05/21	100%
1386	Floor Finishes - Carpet	3 d	Tue 11/05/21	Thu 13/05/21	100%
1387	Paint - 3rd Coat	3 d	Fri 14/05/21	Tue 18/05/21	100%
1388	Fitoff Services (inc. AV)	3 d	Wed 19/05/21	Fri 21/05/21	100%
1389	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1390	**Store - A.L2.06**	**47 d**	**Mon 8/03/21**	**Tue 18/05/21**	**100%**
1391	Rough In Services & Insulation to Partition Walls	2 d	Mon 8/03/21	Tue 9/03/21	100%
1392	Consultant Inspections Before Closing	1 d	Wed 10/03/21	Wed 10/03/21	100%
1393	Sheet Partitions	4 d	Thu 11/03/21	Tue 16/03/21	100%
1394	Frame Ceilings	1 d	Thu 25/03/21	Thu 25/03/21	100%
1395	Sheet Ceilings & Bulkheads	1 d	Fri 26/03/21	Fri 26/03/21	100%
1396	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	3 d	Mon 29/03/21	Wed 31/03/21	100%
1397	Paint - 1st Coat	1 d	Thu 1/04/21	Thu 1/04/21	100%
1398	Defects Inspection & Patch Walls	1 d	Wed 7/04/21	Wed 7/04/21	100%
1399	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1400	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1401	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1402	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
1403	Floor Finishes - Carpet	2 d	Mon 10/05/21	Tue 11/05/21	100%
1404	Paint - 3rd Coat	2 d	Wed 12/05/21	Thu 13/05/21	100%
1405	Fitoff Services	3 d	Fri 14/05/21	Tue 18/05/21	100%
1406	**Lounge - A.L2.18**	**49 d**	**Wed 10/03/21**	**Mon 24/05/21**	**100%**
1407	Rough In Services & Insulation to Partition Walls	2 d	Wed 10/03/21	Thu 11/03/21	100%
1408	Consultant Inspections Before Closing	1 d	Fri 12/03/21	Fri 12/03/21	100%
1409	Sheet Partitions	4 d	Thu 25/03/21	Tue 30/03/21	100%
1410	Frame Ceilings	2 d	Wed 31/03/21	Thu 1/04/21	100%
1411	Sheet Ceilings & Bulkheads	3 d	Wed 7/04/21	Fri 9/04/21	100%
1412	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Mon 12/04/21	Thu 15/04/21	100%
1413	Paint - 1st Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
1414	Defects Inspection & Patch Walls	1 d	Mon 19/04/21	Mon 19/04/21	100%
1415	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1416	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1417	Paint - 2nd Coat	3 d	Thu 6/05/21	Mon 10/05/21	100%
1418	Door Hardware	1 d	Thu 6/05/21	Thu 6/05/21	100%
1419	Floor Finishes - Carpet	3 d	Tue 11/05/21	Thu 13/05/21	100%
1420	Paint - 3rd Coat	3 d	Fri 14/05/21	Tue 18/05/21	100%
1421	Fitoff Services (inc. AV)	4 d	Wed 19/05/21	Mon 24/05/21	100%
1422	**Corridor A.L2.25**	**26 d**	**Wed 7/04/21**	**Fri 14/05/21**	**100%**
1423	Frame Ceilings	4 d	Wed 7/04/21	Mon 12/04/21	100%
1424	Sheet Ceilings & Bulkheads	4 d	Tue 13/04/21	Fri 16/04/21	100%
1425	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	4 d	Mon 19/04/21	Thu 22/04/21	100%
1426	Paint - 1st Coat	2 d	Fri 23/04/21	Wed 28/04/21	100%




Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
1427	Defects Inspection & Patch Walls	2 d	Thu 29/04/21	Fri 30/04/21	100%
1428	Paint - 2nd Coat	2 d	Mon 3/05/21	Tue 4/05/21	100%
1429	Floor Finishes - Vinyl	4 d	Wed 5/05/21	Mon 10/05/21	100%
1430	Paint - 3rd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
1431	Fitoff Services	2 d	Thu 13/05/21	Fri 14/05/21	100%
1432	**Wet Areas - A.L2.10, A.L2.11, A.L2.12**	**92 d**	**Thu 4/03/21**	**Mon 19/07/21**	**100%**
1433	Wall Tiling	6 d	Thu 25/03/21	Thu 1/04/21	100%
1434	Membrane	1 d	Thu 4/03/21	Thu 4/03/21	100%
1435	Flood Test	1 d	Sat 6/03/21	Sat 6/03/21	100%
1436	Screed	2 d	Thu 25/03/21	Fri 26/03/21	100%
1437	Joinery & Toilet Partitions	2 d	Thu 15/04/21	Fri 16/04/21	100%
1438	Fit Off PC Items	4 d	Mon 19/04/21	Thu 22/04/21	100%
1439	Floor Finishes - Vinyl	3 d	Fri 23/04/21	Thu 29/04/21	100%
1440	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
1441	**Terrace - A.L2.17**	**76 d**	**Wed 27/01/21**	**Tue 11/05/21**	**100%**
1442	Structural Steel	4 d	Wed 27/01/21	Sat 30/01/21	100%
1443	Blockwork	4 d	Sat 20/02/21	Wed 24/02/21	100%
1444	Render	4 d	Thu 25/03/21	Tue 30/03/21	100%
1445	Glazing	1 d	Wed 31/03/21	Wed 31/03/21	100%
1446	Waterproofing	3 d	Mon 3/05/21	Wed 5/05/21	100%
1447	Curing & Watertest	2 d	Thu 6/05/21	Fri 7/05/21	100%
1448	Internal Terrace Paving	2 d	Mon 10/05/21	Tue 11/05/21	100%
1449	**Advert Room - A.L2.24**	**17 d**	**Mon 28/06/21**	**Tue 20/07/21**	**100%**
1450	Glazing	1 d	Mon 28/06/21	Mon 28/06/21	100%
1451	Waterproofing	1 d	Tue 29/06/21	Tue 29/06/21	100%
1452	Screed	1 d	Thu 1/07/21	Thu 1/07/21	100%
1453	Paint - 1st Coat	1 d	Fri 2/07/21	Fri 2/07/21	100%
1454	Hang Door	1 d	Mon 5/07/21	Mon 5/07/21	100%
1455	Skirtings & Trims	1 d	Tue 6/07/21	Tue 6/07/21	100%
1456	Paint - 2nd Coat	1 d	Wed 7/07/21	Wed 7/07/21	100%
1457	Door Hardware	1 d	Thu 8/07/21	Thu 8/07/21	100%
1458	Floor Finishes - Vinyl	1 d	Mon 19/07/21	Mon 19/07/21	100%
1459	Paint - 3rd Coat	1 d	Tue 20/07/21	Tue 20/07/21	100%
1460	**Floor Handover**	**5 d**	**Tue 13/07/21**	**Mon 19/07/21**	**100%**
1461	Signage	4 d	Tue 13/07/21	Fri 16/07/21	100%
1462	Initial Clean and Defects	1 d	Mon 19/07/21	Mon 19/07/21	100%
1463	**Level 3**	**121 d**	**Sat 30/01/21**	**Tue 20/07/21**	**100%**
1464	**Services & Finishes**	**31 d**	**Sat 30/01/21**	**Sat 6/03/21**	**100%**
1465	L3 Mark Up Slab	1 d	Sat 30/01/21	Sat 30/01/21	100%
1466	Service Risers and Top Track	4 d	Mon 1/02/21	Thu 4/02/21	100%
1467	Frame Internal Partitions (excl External Walls)	6 d	Thu 4/02/21	Wed 10/02/21	100%
1468	Run High Level Hydraulic Services	5 d	Thu 11/02/21	Tue 16/02/21	100%
1469	Run High Level Mechanical Services	15 d	Thu 18/02/21	Sat 6/03/21	100%
1470	Run High Level Electrical Services	15 d	Thu 18/02/21	Sat 6/03/21	100%
1471	**Small Classroom # 1 - A.L3.01**	**77 d**	**Thu 25/03/21**	**Tue 20/07/21**	**100%**
1472	Rough In Services & Insulation to Partition Walls	3 d	Thu 25/03/21	Mon 29/03/21	100%
1473	Consultant Inspections Before Closing	1 d	Tue 30/03/21	Tue 30/03/21	100%
1474	Sheet Plasterboard Partitions	2 d	Wed 31/03/21	Thu 1/04/21	100%
1475	Set & Sand Plasterboard Partitions	2 d	Wed 7/04/21	Thu 8/04/21	100%
1476	Frame Ceilings	2 d	Fri 9/04/21	Mon 12/04/21	100%
1477	Sheet Perimeter Set Ceiling	2 d	Tue 13/04/21	Wed 14/04/21	100%
1478	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Mon 3/05/21	Tue 4/05/21	100%
1479	Paint - 1st Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
1480	Defects Inspection & Patch Walls	1 d	Thu 6/05/21	Thu 6/05/21	100%
1481	Paint - 2nd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
1482	Raised Access Flooring	1 d	Tue 11/05/21	Tue 11/05/21	100%
1483	Joinery	1 d	Wed 12/05/21	Wed 12/05/21	100%
1484	Carpentry - Hang Doors & Fix Skirtings	1 d	Thu 13/05/21	Thu 13/05/21	100%
1485	Paint - 3rd Coat	2 d	Fri 14/05/21	Mon 17/05/21	100%
1486	Door Hardware	1 d	Tue 18/05/21	Tue 18/05/21	100%
1487	Floor Finishes - Carpet	2 d	Tue 18/05/21	Wed 19/05/21	100%
1488	Operable Wall Installation	1 d	Wed 14/07/21	Wed 14/07/21	100%
1489	Fitoff Services (inc. AV)	2 d	Thu 20/05/21	Fri 21/05/21	100%
1490	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1491	**Small Classroom # 2 - A.L3.02**	**74 d**	**Tue 30/03/21**	**Tue 20/07/21**	**100%**
1492	Rough In Services & Insulation to Partition Walls	3 d	Tue 30/03/21	Thu 1/04/21	100%
1493	Consultant Inspections Before Closing	1 d	Wed 7/04/21	Wed 7/04/21	100%
1494	Sheet Plasterboard Partitions	2 d	Thu 8/04/21	Fri 9/04/21	100%
1495	Set & Sand Plasterboard Partitions	2 d	Mon 12/04/21	Tue 13/04/21	100%
1496	Frame Ceilings	2 d	Wed 14/04/21	Thu 15/04/21	100%
1497	Sheet Perimeter Set Ceiling	2 d	Fri 16/04/21	Mon 19/04/21	100%
1498	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Mon 3/05/21	Tue 4/05/21	100%
1499	Paint - 1st Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
1500	Defects Inspection & Patch Walls	1 d	Thu 6/05/21	Thu 6/05/21	100%
1501	Paint - 2nd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
1502	Raised Access Flooring	1 d	Tue 11/05/21	Tue 11/05/21	100%
1503	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 12/05/21	Wed 12/05/21	100%
1504	Paint - 3rd Coat	2 d	Thu 13/05/21	Fri 14/05/21	100%
1505	Door Hardware	1 d	Mon 17/05/21	Mon 17/05/21	100%
1506	Floor Finishes - Carpet	2 d	Mon 17/05/21	Tue 18/05/21	100%
1507	Operable Wall Installation	1 d	Thu 15/07/21	Thu 15/07/21	100%
1508	Fitoff Services (inc. AV)	2 d	Wed 19/05/21	Thu 20/05/21	100%
1509	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1510	**Small Classroom # 3 - A.L3.03**	**71 d**	**Wed 7/04/21**	**Tue 20/07/21**	**100%**
1511	Rough In Services & Insulation to Partition Walls	3 d	Wed 7/04/21	Fri 9/04/21	100%
1512	Consultant Inspections Before Closing	1 d	Mon 12/04/21	Mon 12/04/21	100%
1513	Sheet Plasterboard Partitions	2 d	Tue 13/04/21	Wed 14/04/21	100%
1514	Set & Sand Plasterboard Partitions	2 d	Thu 15/04/21	Fri 16/04/21	100%
1515	Frame Ceilings	2 d	Mon 19/04/21	Tue 20/04/21	100%
1516	Sheet Perimeter Set Ceiling	2 d	Wed 21/04/21	Thu 22/04/21	100%
1517	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Mon 3/05/21	Tue 4/05/21	100%
1518	Paint - 1st Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
1519	Defects Inspection & Patch Walls	1 d	Thu 6/05/21	Thu 6/05/21	100%

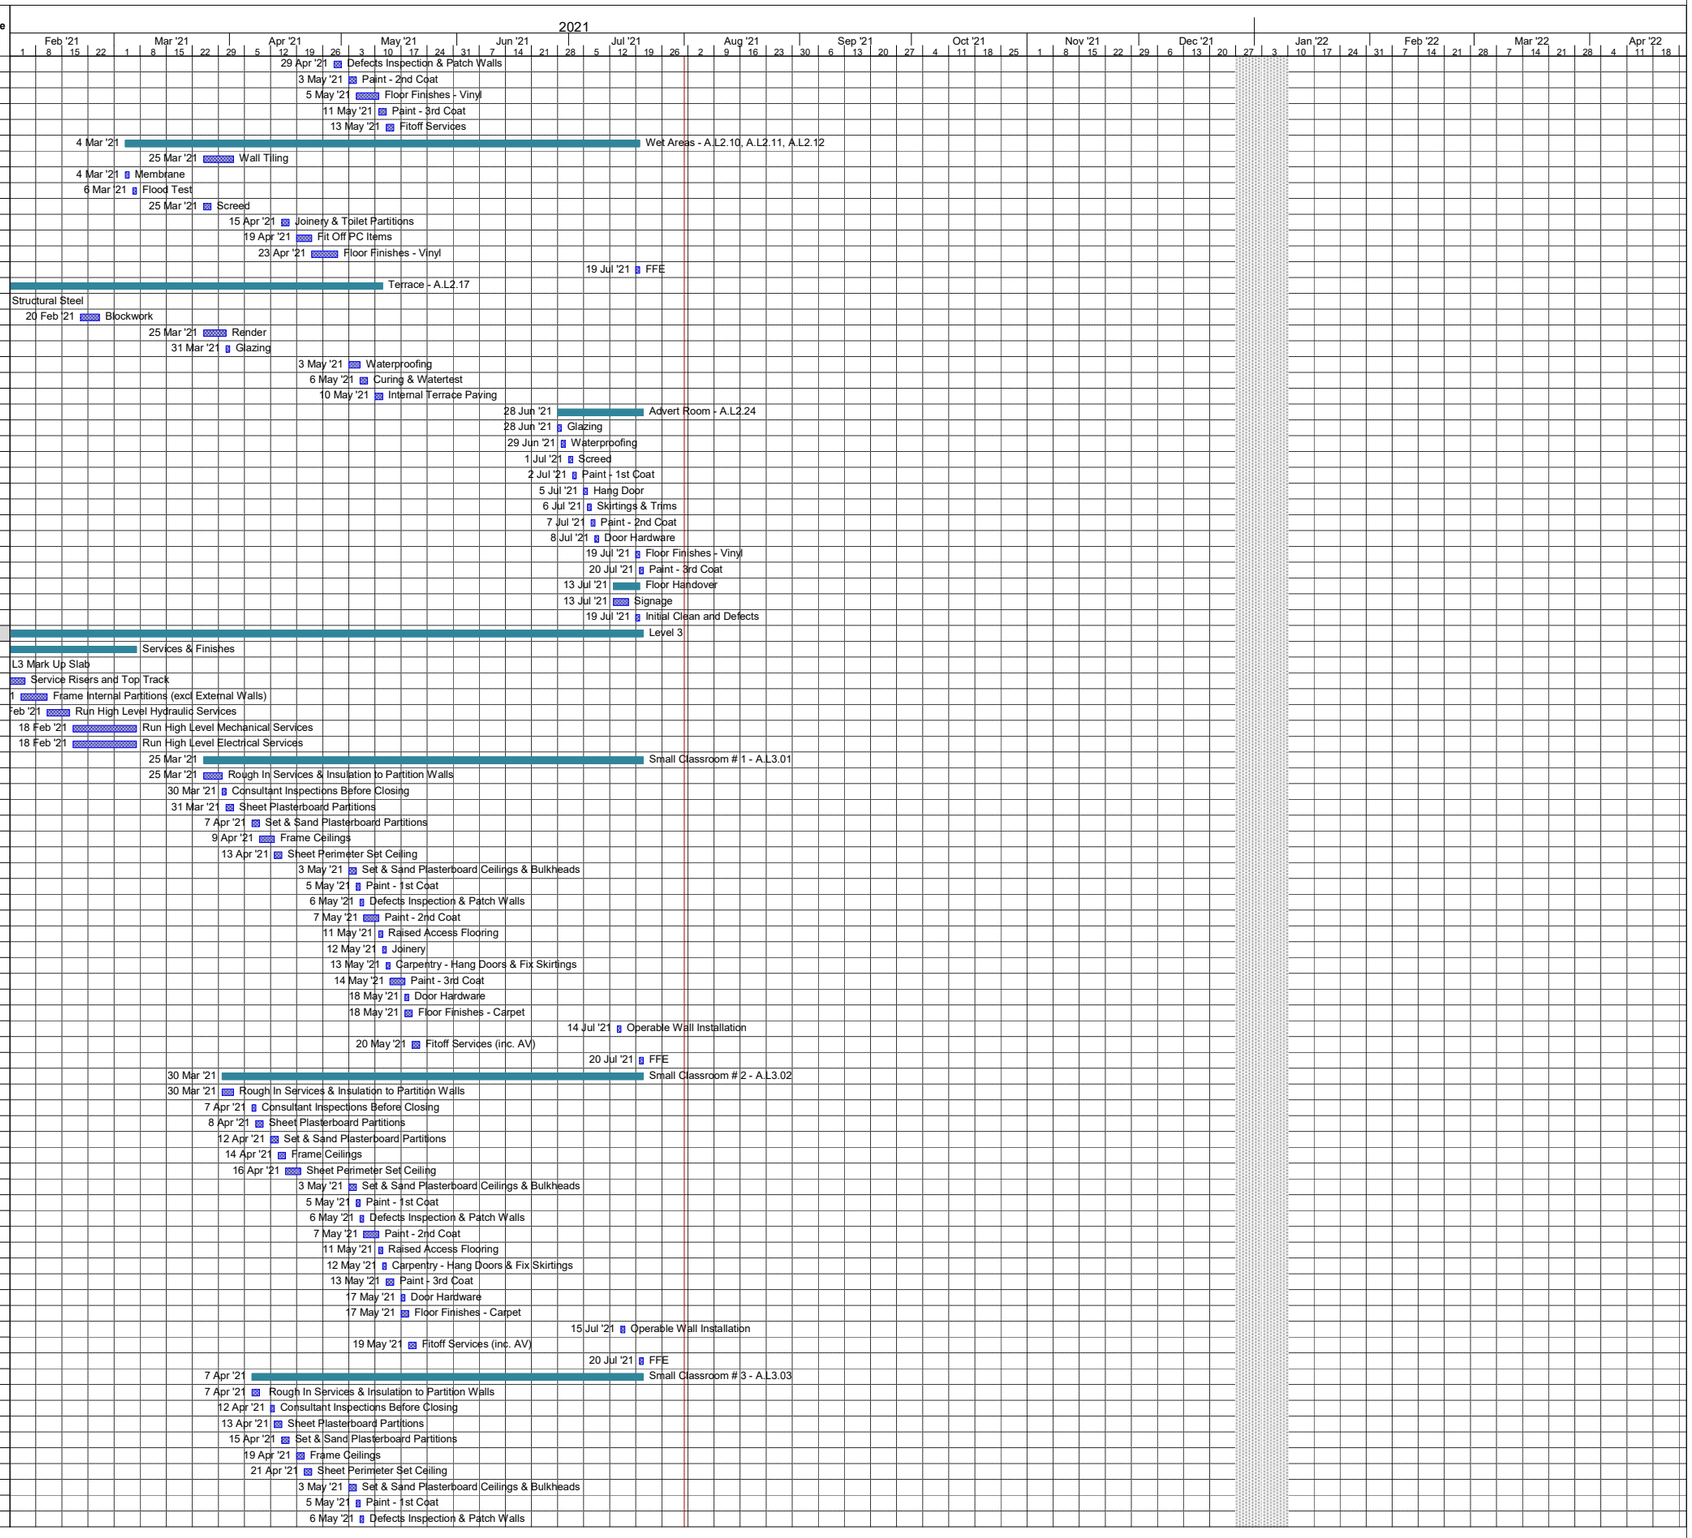


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
1520	Paint - 2nd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
1521	Raised Access Flooring	1 d	Wed 12/05/21	Wed 12/05/21	100%
1522	Joinery	2 d	Thu 13/05/21	Fri 14/05/21	100%
1523	Carpentry - Hang Doors & Fix Skirtings	1 d	Mon 17/05/21	Mon 17/05/21	100%
1524	Paint - 3rd Coat	2 d	Tue 18/05/21	Wed 19/05/21	100%
1525	Door Hardware	1 d	Thu 20/05/21	Thu 20/05/21	100%
1526	Floor Finishes - Carpet	2 d	Thu 20/05/21	Fri 21/05/21	100%
1527	Fitoff Services (inc. AV)	2 d	Mon 24/05/21	Tue 25/05/21	100%
1528	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1529	**Small Classroom # 4 - A.L3.13**	**84 d**	**Tue 16/03/21**	**Tue 20/07/21**	**100%**
1530	Rough In Services & Insulation to Partition Walls	2 d	Tue 16/03/21	Wed 17/03/21	100%
1531	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1532	Sheet Partitions	4 d	Fri 26/03/21	Wed 31/03/21	100%
1533	Frame Ceilings	2 d	Thu 1/04/21	Wed 7/04/21	100%
1534	Sheet Perimeter Set Ceiling	3 d	Thu 8/04/21	Mon 12/04/21	100%
1535	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Tue 13/04/21	Wed 14/04/21	100%
1536	Paint - 1st Coat	1 d	Thu 15/04/21	Thu 15/04/21	100%
1537	Defects Inspection & Patch Walls	1 d	Fri 16/04/21	Fri 16/04/21	100%
1538	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1539	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1540	Carpentry - Hang Doors & Fix Skirtings	1 d	Mon 3/05/21	Mon 3/05/21	100%
1541	Paint - 3rd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
1542	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
1543	Floor Finishes - Carpet	2 d	Fri 7/05/21	Mon 10/05/21	100%
1544	Fitoff Services (inc. AV)	2 d	Thu 13/05/21	Fri 14/05/21	100%
1545	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1546	**Small Classroom # 5 - A.L3.12**	**82 d**	**Thu 18/03/21**	**Tue 20/07/21**	**100%**
1547	Rough In Services & Insulation to Partition Walls	2 d	Thu 18/03/21	Fri 19/03/21	100%
1548	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1549	Sheet Partitions	4 d	Fri 26/03/21	Wed 31/03/21	100%
1550	Frame Ceilings	2 d	Thu 1/04/21	Wed 7/04/21	100%
1551	Sheet Perimeter Set Ceiling	3 d	Thu 8/04/21	Mon 12/04/21	100%
1552	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Tue 13/04/21	Wed 14/04/21	100%
1553	Paint - 1st Coat	1 d	Thu 15/04/21	Thu 15/04/21	100%
1554	Defects Inspection & Patch Walls	1 d	Fri 16/04/21	Fri 16/04/21	100%
1555	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1556	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1557	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1558	Paint - 3rd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
1559	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1560	Floor Finishes - Carpet	2 d	Wed 12/05/21	Thu 13/05/21	100%
1561	Fitoff Services (inc. AV)	2 d	Fri 14/05/21	Mon 17/05/21	100%
1562	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1563	**Small Classroom # 6 - A.L3.04**	**77 d**	**Thu 25/03/21**	**Tue 20/07/21**	**100%**
1564	Rough In Services & Insulation to Partition Walls	2 d	Thu 25/03/21	Fri 26/03/21	100%
1565	Consultant Inspections Before Closing	1 d	Mon 29/03/21	Mon 29/03/21	100%
1566	Sheet Partitions	4 d	Tue 30/03/21	Wed 7/04/21	100%
1567	Frame Ceilings	2 d	Thu 8/04/21	Fri 9/04/21	100%
1568	Sheet Perimeter Set Ceiling	3 d	Mon 12/04/21	Wed 14/04/21	100%
1569	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Thu 15/04/21	Fri 16/04/21	100%
1570	Paint - 1st Coat	1 d	Mon 19/04/21	Mon 19/04/21	100%
1571	Defects Inspection & Patch Walls	1 d	Mon 3/05/21	Mon 3/05/21	100%
1572	Joinery	2 d	Tue 4/05/21	Wed 5/05/21	100%
1573	Paint - 2nd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
1574	Carpentry - Hang Doors & Fix Skirtings	1 d	Thu 6/05/21	Thu 6/05/21	100%
1575	Paint - 3rd Coat	2 d	Mon 10/05/21	Tue 11/05/21	100%
1576	Door Hardware	1 d	Wed 12/05/21	Wed 12/05/21	100%
1577	Floor Finishes - Carpet	2 d	Wed 12/05/21	Thu 13/05/21	100%
1578	Fitoff Services (inc. AV)	2 d	Fri 14/05/21	Mon 17/05/21	100%
1579	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1580	**Small Classroom # 7 - A.L3.05**	**78 d**	**Wed 24/03/21**	**Tue 20/07/21**	**100%**
1581	Rough In Services & Insulation to Partition Walls	2 d	Wed 24/03/21	Thu 25/03/21	100%
1582	Consultant Inspections Before Closing	1 d	Fri 26/03/21	Fri 26/03/21	100%
1583	Sheet Partitions	4 d	Mon 29/03/21	Thu 1/04/21	100%
1584	Frame Ceilings	2 d	Wed 7/04/21	Thu 8/04/21	100%
1585	Sheet Perimeter Set Ceiling	3 d	Fri 9/04/21	Tue 13/04/21	100%
1586	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Wed 14/04/21	Thu 15/04/21	100%
1587	Paint - 1st Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
1588	Defects Inspection & Patch Walls	1 d	Mon 3/05/21	Mon 3/05/21	100%
1589	Joinery	2 d	Tue 4/05/21	Wed 5/05/21	100%
1590	Paint - 2nd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
1591	Carpentry - Hang Doors & Fix Skirtings	1 d	Mon 10/05/21	Mon 10/05/21	100%
1592	Paint - 3rd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
1593	Door Hardware	1 d	Thu 13/05/21	Thu 13/05/21	100%
1594	Floor Finishes - Carpet	2 d	Thu 13/05/21	Fri 14/05/21	100%
1595	Fitoff Services (inc. AV)	2 d	Mon 17/05/21	Tue 18/05/21	100%
1596	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1597	**Middle Classroom # 1 - A.L3.07**	**76 d**	**Fri 26/03/21**	**Tue 20/07/21**	**100%**
1598	Rough In Services & Insulation to Partition Walls	2 d	Fri 26/03/21	Mon 29/03/21	100%
1599	Consultant Inspections Before Closing	1 d	Tue 30/03/21	Tue 30/03/21	100%
1600	Sheet Partitions	2 d	Wed 31/03/21	Thu 1/04/21	100%
1601	Frame Ceilings	2 d	Wed 7/04/21	Thu 8/04/21	100%
1602	Sheet Ceilings & Bulkheads	3 d	Fri 9/04/21	Tue 13/04/21	100%
1603	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Wed 14/04/21	Thu 15/04/21	100%
1604	Paint - 1st Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
1605	Defects Inspection & Patch Walls	1 d	Mon 19/04/21	Mon 19/04/21	100%
1606	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1607	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1608	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1609	Paint - 3rd Coat	2 d	Mon 10/05/21	Tue 11/05/21	100%
1610	Door Hardware	1 d	Wed 12/05/21	Wed 12/05/21	100%
1611	Floor Finishes - Carpet	2 d	Wed 12/05/21	Thu 13/05/21	100%
1612	Fitoff Services (inc. AV)	2 d	Fri 14/05/21	Mon 17/05/21	100%

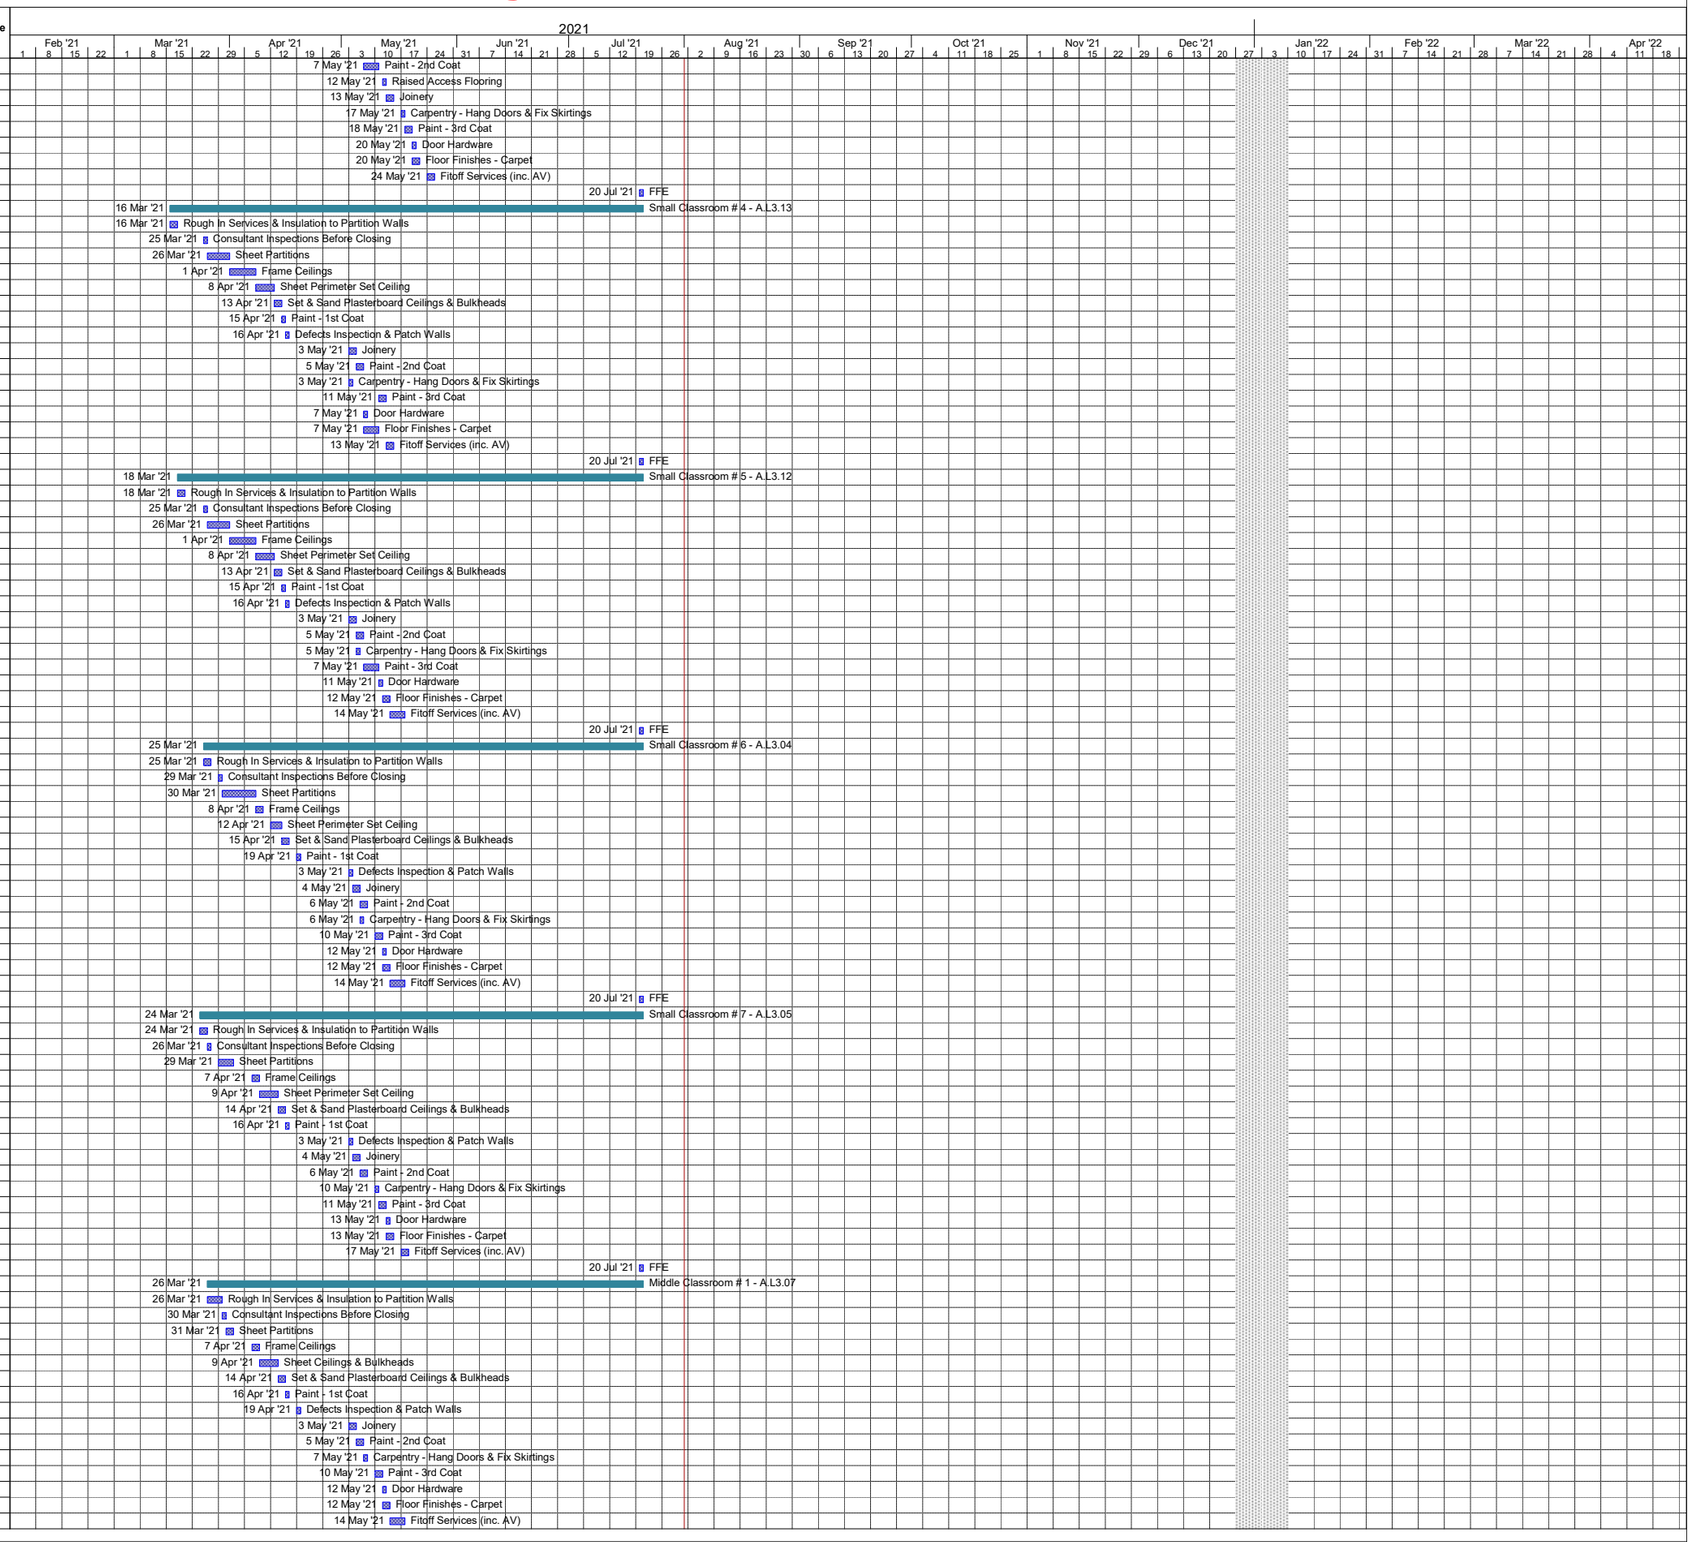


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1613	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1614	**Middle Classroom # 2 - A.L3.06**	**74 d**	**Tue 30/03/21**	**Tue 20/07/21**	**100%**
1615	Rough In Services & Insulation to Partition Walls	2 d	Tue 30/03/21	Wed 31/03/21	100%
1616	Consultant Inspections Before Closing	1 d	Thu 1/04/21	Thu 1/04/21	100%
1617	Sheet Partitions	4 d	Wed 7/04/21	Mon 12/04/21	100%
1618	Frame Ceilings	2 d	Tue 13/04/21	Wed 14/04/21	100%
1619	Sheet Ceilings & Bulkheads	3 d	Thu 15/04/21	Mon 19/04/21	100%
1620	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Tue 20/04/21	Wed 21/04/21	100%
1621	Paint - 1st Coat	1 d	Thu 22/04/21	Thu 22/04/21	100%
1622	Defects Inspection & Patch Walls	1 d	Fri 23/04/21	Fri 23/04/21	100%
1623	Joinery	2 d	Mon 3/05/21	Tue 4/05/21	100%
1624	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1625	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1626	Paint - 3rd Coat	2 d	Mon 10/05/21	Tue 11/05/21	100%
1627	Door Hardware	1 d	Wed 12/05/21	Wed 12/05/21	100%
1628	Floor Finishes - Carpet	2 d	Wed 12/05/21	Thu 13/05/21	100%
1629	Fitoff Services (inc. AV)	2 d	Fri 14/05/21	Mon 17/05/21	100%
1630	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1631	**Store - A.L3.08**	**22 d**	**Thu 1/04/21**	**Fri 7/05/21**	**100%**
1632	Rough In Services & Insulation to Partition Walls	2 d	Thu 1/04/21	Wed 7/04/21	100%
1633	Consultant Inspections Before Closing	1 d	Thu 8/04/21	Thu 8/04/21	100%
1634	Sheet Partitions	1 d	Fri 9/04/21	Fri 9/04/21	100%
1635	Frame Ceilings	1 d	Mon 12/04/21	Mon 12/04/21	100%
1636	Sheet Ceilings & Bulkheads	1 d	Tue 13/04/21	Tue 13/04/21	100%
1637	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Wed 14/04/21	Thu 15/04/21	100%
1638	Paint - 1st Coat	1 d	Fri 16/04/21	Fri 16/04/21	100%
1639	Defects Inspection & Patch Walls	1 d	Mon 19/04/21	Mon 19/04/21	100%
1640	Joinery	1 d	Mon 3/05/21	Mon 3/05/21	100%
1641	Paint - 2nd Coat	1 d	Wed 21/04/21	Wed 21/04/21	100%
1642	Carpentry - Hang Doors & Fix Skirtings	1 d	Tue 4/05/21	Tue 4/05/21	100%
1643	Paint - 3rd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
1644	Door Hardware	1 d	Thu 6/05/21	Thu 6/05/21	100%
1645	Floor Finishes - Vinyl	2 d	Fri 23/04/21	Wed 28/04/21	100%
1646	Fitoff Services	1 d	Fri 7/05/21	Fri 7/05/21	100%
1647	**Lounge - A.L3.17**	**28 d**	**Thu 8/04/21**	**Wed 19/05/21**	**100%**
1648	Rough In Services & Insulation to Partition Walls	2 d	Thu 8/04/21	Fri 9/04/21	100%
1649	Consultant Inspections Before Closing	1 d	Mon 12/04/21	Mon 12/04/21	100%
1650	Sheet Partitions	3 d	Tue 13/04/21	Thu 15/04/21	100%
1651	Set & Sand Plasterboard Partitions	2 d	Fri 16/04/21	Mon 19/04/21	100%
1652	Frame Ceilings	2 d	Fri 16/04/21	Mon 19/04/21	100%
1653	Sheet Ceilings & Bulkheads	3 d	Tue 20/04/21	Thu 22/04/21	100%
1654	Set & Sand Plasterboard Ceilings & Bulkheads	4 d	Fri 23/04/21	Fri 30/04/21	100%
1655	Paint - 1st Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1656	Defects Inspection & Patch Walls	1 d	Tue 4/05/21	Tue 4/05/21	100%
1657	Joinery	2 d	Wed 5/05/21	Thu 6/05/21	100%
1658	Paint - 2nd Coat	3 d	Fri 7/05/21	Tue 11/05/21	100%
1659	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1660	Paint - 3rd Coat	3 d	Wed 12/05/21	Fri 14/05/21	100%
1661	Door Hardware	1 d	Mon 17/05/21	Mon 17/05/21	100%
1662	Floor Finishes - Carpet	3 d	Wed 12/05/21	Fri 14/05/21	100%
1663	Fitoff Services (inc. AV)	2 d	Tue 18/05/21	Wed 19/05/21	100%
1664	**Corridor A.L3.23**	**23 d**	**Tue 20/04/21**	**Mon 24/05/21**	**100%**
1665	Frame Ceilings	3 d	Tue 20/04/21	Thu 22/04/21	100%
1666	Sheet Ceilings & Bulkheads	3 d	Fri 23/04/21	Thu 29/04/21	100%
1667	Set & Sand Plasterboard Ceilings & Bulkheads	3 d	Fri 30/04/21	Tue 4/05/21	100%
1668	Paint - 1st Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
1669	Defects Inspection & Patch Walls	2 d	Fri 7/05/21	Mon 10/05/21	100%
1670	Paint - 2nd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
1671	Floor Finishes - Vinyl	4 d	Thu 13/05/21	Tue 18/05/21	100%
1672	Paint - 3rd Coat	2 d	Wed 19/05/21	Thu 20/05/21	100%
1673	Fitoff Services	2 d	Fri 21/05/21	Mon 24/05/21	100%
1674	**Wet Areas**	**71 d**	**Wed 7/04/21**	**Tue 20/07/21**	**100%**
1675	Wall Tiling	6 d	Wed 7/04/21	Wed 14/04/21	100%
1676	Membrane	2 d	Thu 15/04/21	Fri 16/04/21	100%
1677	Flood Test	1 d	Tue 20/04/21	Tue 20/04/21	100%
1678	Screed	1 d	Wed 21/04/21	Wed 21/04/21	100%
1679	Floor Finishes - Vinyl	3 d	Wed 28/04/21	Fri 30/04/21	100%
1680	Joinery	4 d	Mon 3/05/21	Thu 6/05/21	100%
1681	Toilet Partitions	1 d	Fri 7/05/21	Fri 7/05/21	100%
1682	Fit Off PC Items	4 d	Mon 10/05/21	Thu 13/05/21	100%
1683	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
1684	**Terrace - A.L3.16**	**72 d**	**Mon 1/02/21**	**Tue 11/05/21**	**100%**
1685	Structural Steel	24 d	Mon 1/02/21	Sat 27/02/21	100%
1686	Blockwork	3 d	Thu 25/03/21	Mon 29/03/21	100%
1687	Render	1 d	Tue 30/03/21	Tue 30/03/21	100%
1688	Glazing	1 d	Wed 31/03/21	Wed 31/03/21	100%
1689	Waterproofing	3 d	Mon 3/05/21	Wed 5/05/21	100%
1690	Curing & Watertest	2 d	Thu 6/05/21	Fri 7/05/21	100%
1691	Internal Terrace Paving	2 d	Mon 10/05/21	Tue 11/05/21	100%
1692	**Floor Handover**	**5 d**	**Mon 28/06/21**	**Fri 2/07/21**	**100%**
1693	Signage	2 d	Mon 28/06/21	Tue 29/06/21	100%
1694	Initial Clean and Defects	3 d	Wed 30/06/21	Fri 2/07/21	100%
1695	**Level 4**	**119 d**	**Mon 8/02/21**	**Tue 27/07/21**	**99%**
1696	**Services & Finishes**	**43 d**	**Mon 8/02/21**	**Thu 1/04/21**	**100%**
1697	L4 Mark Up Slab	1 d	Mon 8/02/21	Mon 8/02/21	100%
1698	Service Risers and Top Track	2 d	Tue 9/02/21	Wed 10/02/21	100%
1699	Frame Internal Partitions (excl External Walls)	4 d	Thu 11/02/21	Mon 15/02/21	100%
1700	Run High Level Hydraulic Services	3 d	Wed 17/02/21	Fri 19/02/21	100%
1701	Run High Level Mechanical Services	6 d	Thu 25/03/21	Thu 1/04/21	100%
1702	Run High Level Electrical Services	5 d	Mon 8/03/21	Fri 12/03/21	100%
1703	**Lecture Room _A.L4.08**	**86 d**	**Sat 13/03/21**	**Wed 21/07/21**	**100%**
1704	Rough In Services & Insulation to Partition Walls	2 d	Sat 13/03/21	Tue 16/03/21	100%
1705	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%

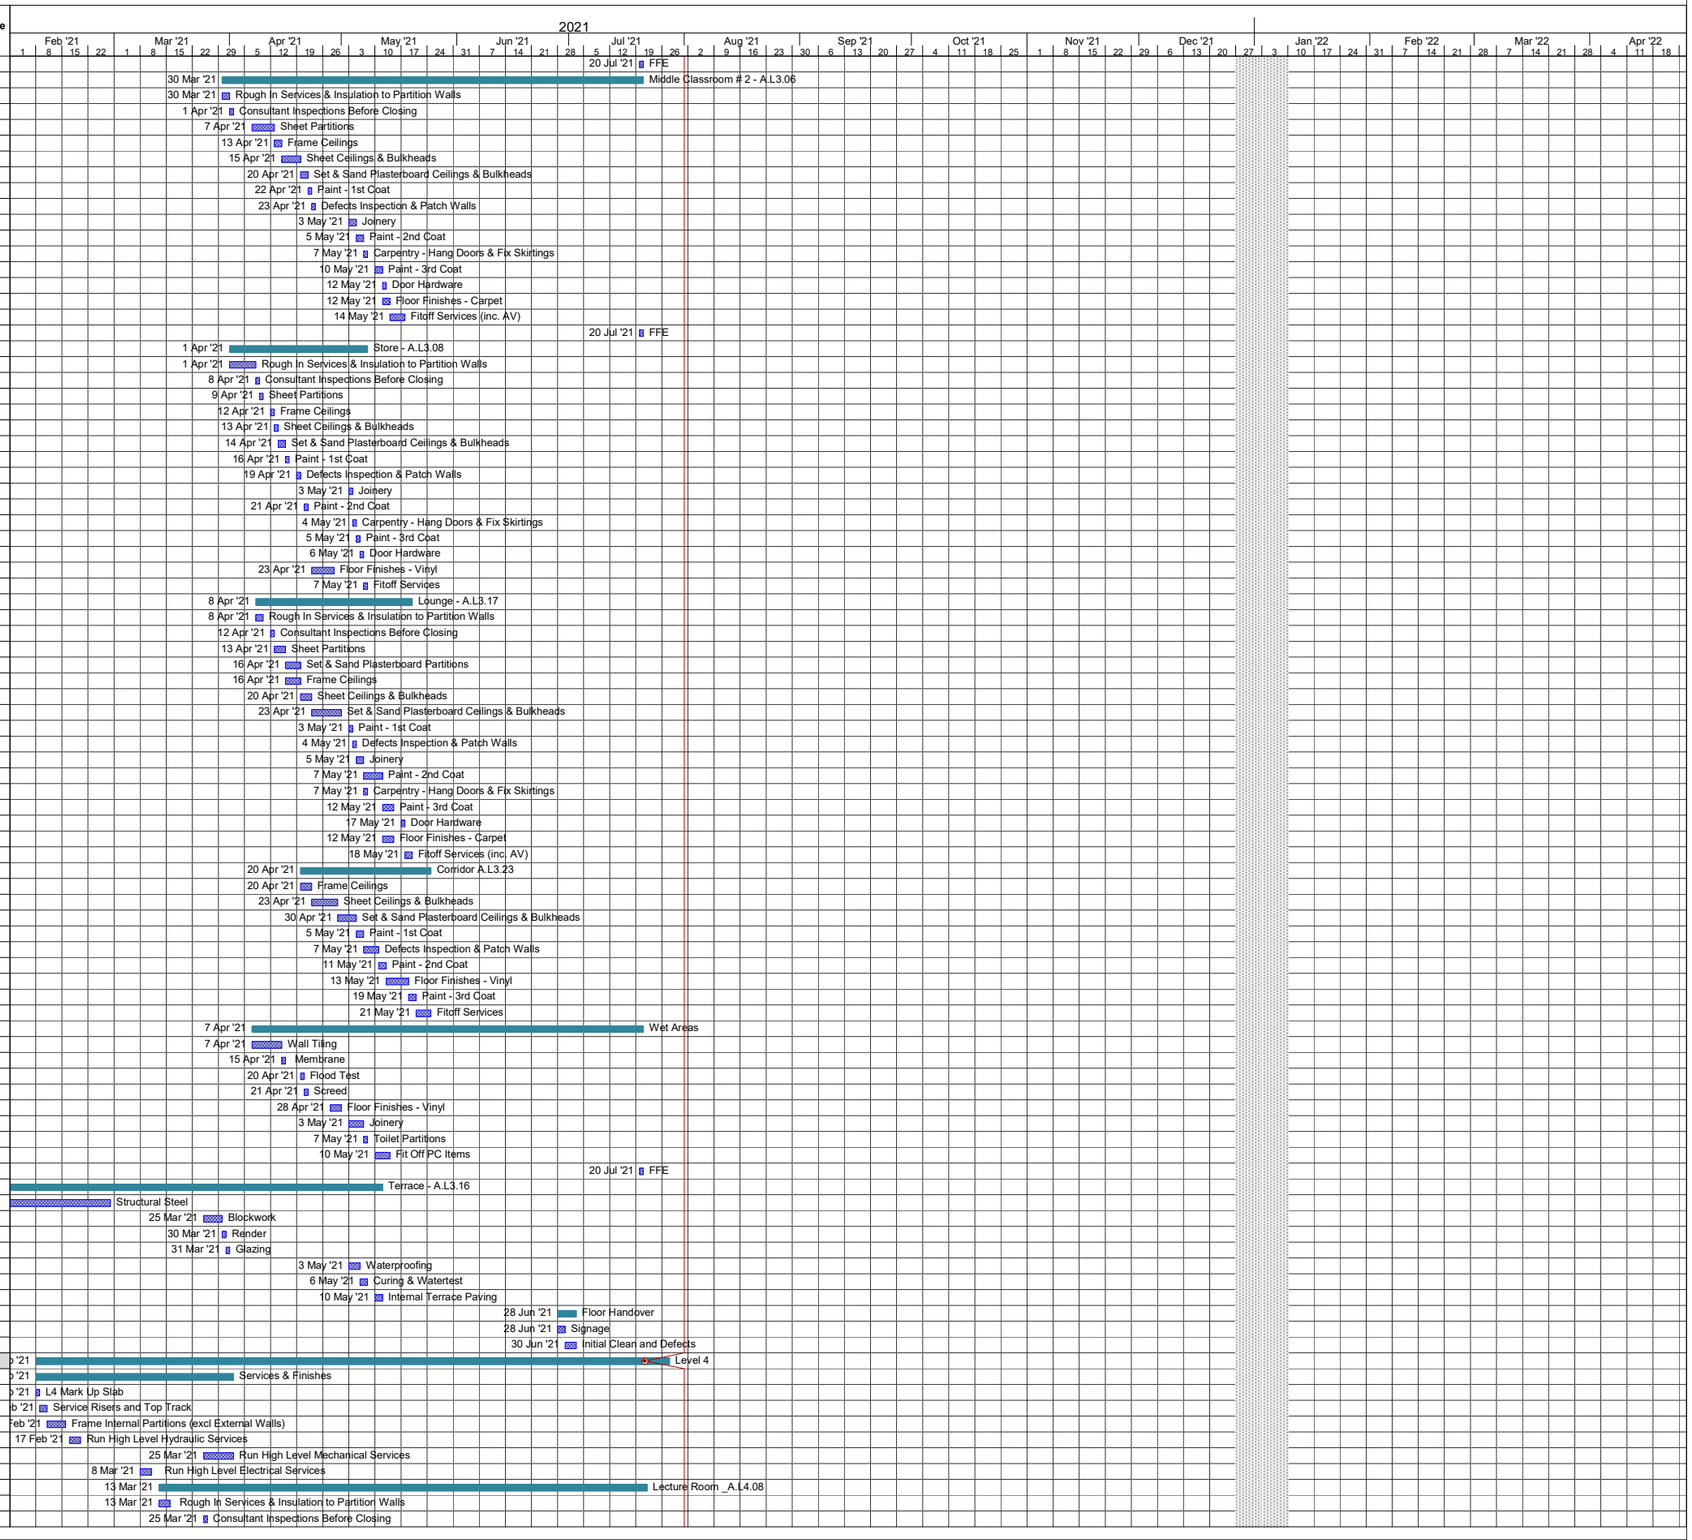


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1706	Sheet Plasterboard Partitions	2 d	Fri 26/03/21	Mon 29/03/21	100%
1707	Set & Sand Plasterboard Partitions	2 d	Tue 30/03/21	Wed 31/03/21	100%
1708	Frame Ceilings	3 d	Tue 30/03/21	Thu 1/04/21	100%
1709	Sheet Ceilings & Bulkheads	3 d	Wed 7/04/21	Fri 9/04/21	100%
1710	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Mon 12/04/21	Tue 13/04/21	100%
1711	Paint - 1st Coat	1 d	Fri 30/04/21	Fri 30/04/21	100%
1712	Defects Inspection & Patch Walls	1 d	Mon 3/05/21	Mon 3/05/21	100%
1713	Joinery	2 d	Tue 4/05/21	Wed 5/05/21	100%
1714	Paint - 2nd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
1715	Carpentry - Hang Doors & Fix Skirtings	1 d	Mon 10/05/21	Mon 10/05/21	100%
1716	Paint - 3rd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
1717	Door Hardware	1 d	Thu 13/05/21	Thu 13/05/21	100%
1718	Floor Finishes - Carpet	2 d	Thu 13/05/21	Fri 14/05/21	100%
1719	Operable Wall Installation	1 d	Fri 16/07/21	Fri 16/07/21	100%
1720	Fitoff Services (inc. AV)	2 d	Wed 19/05/21	Thu 20/05/21	100%
1721	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1722	**Store - A.L4.09**	**84 d**	**Wed 17/03/21**	**Wed 21/07/21**	**100%**
1723	Rough In Services & Insulation to Partition Walls	2 d	Wed 17/03/21	Thu 18/03/21	100%
1724	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1725	Sheet Plasterboard Partitions	1 d	Fri 26/03/21	Fri 26/03/21	100%
1726	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1727	Frame Ceilings	1 d	Mon 29/03/21	Mon 29/03/21	100%
1728	Sheet Ceilings & Bulkheads	1 d	Tue 30/03/21	Tue 30/03/21	100%
1729	Set & Sand Partitions, Ceilings & Bulkheads	2 d	Wed 31/03/21	Thu 1/04/21	100%
1730	Paint - 1st Coat	1 d	Wed 7/04/21	Wed 7/04/21	100%
1731	Defects Inspection & Patch Walls	1 d	Thu 8/04/21	Thu 8/04/21	100%
1732	Joinery	1 d	Mon 3/05/21	Mon 3/05/21	100%
1733	Paint - 2nd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
1734	Floor Finishes - Vinyl	2 d	Wed 5/05/21	Thu 6/05/21	100%
1735	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1736	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
1737	Door Hardware	1 d	Mon 10/05/21	Mon 10/05/21	100%
1738	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
1739	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1740	**Comms Room _A.L4.10**	**36 d**	**Fri 19/03/21**	**Fri 14/05/21**	**100%**
1741	Rough In Services & Insulation to Partition Walls	1 d	Fri 19/03/21	Fri 19/03/21	100%
1742	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1743	Sheet Plasterboard Partitions	1 d	Fri 26/03/21	Fri 26/03/21	100%
1744	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1745	Frame Ceilings	1 d	Wed 31/03/21	Wed 31/03/21	100%
1746	Sheet Ceilings & Bulkheads	1 d	Thu 1/04/21	Thu 1/04/21	100%
1747	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Wed 7/04/21	Thu 8/04/21	100%
1748	Paint - 1st Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1749	Defects Inspection & Patch Walls	1 d	Mon 12/04/21	Mon 12/04/21	100%
1750	Paint - 2nd Coat	1 d	Tue 13/04/21	Tue 13/04/21	100%
1751	Floor Finishes - Vinyl	2 d	Mon 3/05/21	Tue 4/05/21	100%
1752	Carpentry - Hang Doors & Fix Skirtings	1 d	Wed 5/05/21	Wed 5/05/21	100%
1753	Paint - 3rd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
1754	Door Hardware	1 d	Fri 7/05/21	Fri 7/05/21	100%
1755	Fitoff Services (inc. racks)	6 d	Fri 7/05/21	Fri 14/05/21	100%
1756	**HWU - A.L4.12**	**38 d**	**Mon 22/03/21**	**Wed 19/05/21**	**100%**
1757	Rough In Services & Insulation to Partition Walls	1 d	Mon 22/03/21	Mon 22/03/21	100%
1758	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1759	Sheet Plasterboard Partitions	1 d	Fri 26/03/21	Fri 26/03/21	100%
1760	Set & Sand Plasterboard Partitions	21 d	Mon 29/03/21	Mon 3/05/21	100%
1761	Frame Ceilings	1 d	Wed 31/03/21	Wed 31/03/21	100%
1762	Sheet Ceilings & Bulkheads	1 d	Mon 3/05/21	Mon 3/05/21	100%
1763	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Tue 4/05/21	Wed 5/05/21	100%
1764	Paint - 1st Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
1765	Defects Inspection & Patch Walls	1 d	Fri 7/05/21	Fri 7/05/21	100%
1766	Paint - 2nd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
1767	Floor Finishes - Epoxy	2 d	Wed 14/04/21	Thu 15/04/21	100%
1768	Carpentry - Hang Doors & Fix Skirtings	1 d	Tue 11/05/21	Tue 11/05/21	100%
1769	Paint - 3rd Coat	1 d	Wed 12/05/21	Wed 12/05/21	100%
1770	Door Hardware	1 d	Thu 13/05/21	Thu 13/05/21	100%
1771	Fitoff Services	4 d	Fri 14/05/21	Wed 19/05/21	100%
1772	**Small Classroom # 1 - A.L4.06**	**80 d**	**Tue 23/03/21**	**Wed 21/07/21**	**100%**
1773	Rough In Services & Insulation to Partition Walls	2 d	Tue 23/03/21	Wed 24/03/21	100%
1774	Consultant Inspections Before Closing	1 d	Thu 25/03/21	Thu 25/03/21	100%
1775	Sheet Plasterboard Partitions	1 d	Fri 26/03/21	Fri 26/03/21	100%
1776	Set & Sand Plasterboard Partitions	2 d	Mon 29/03/21	Tue 30/03/21	100%
1777	Frame Ceilings	1 d	Wed 31/03/21	Wed 31/03/21	100%
1778	Sheet Ceilings & Bulkheads	1 d	Thu 1/04/21	Thu 1/04/21	100%
1779	Set & Sand Plasterboard Partitions, Ceilings & Bulkheads	2 d	Wed 7/04/21	Thu 8/04/21	100%
1780	Paint - 1st Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
1781	Defects Inspection & Patch Walls	1 d	Mon 12/04/21	Mon 12/04/21	100%
1782	Joinery	1 d	Mon 3/05/21	Mon 3/05/21	100%
1783	Paint - 2nd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
1784	Floor Finishes - Vinyl	2 d	Wed 5/05/21	Thu 6/05/21	100%
1785	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1786	Paint - 3rd Coat	1 d	Tue 11/05/21	Tue 11/05/21	100%
1787	Door Hardware	1 d	Mon 10/05/21	Mon 10/05/21	100%
1788	Fitoff Services	1 d	Wed 12/05/21	Wed 12/05/21	100%
1789	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1790	**Small Classroom # 2 - A.L4.07**	**78 d**	**Thu 25/03/21**	**Wed 21/07/21**	**100%**
1791	Rough In Services & Insulation to Partition Walls	2 d	Thu 25/03/21	Fri 26/03/21	100%
1792	Consultant Inspections Before Closing	1 d	Mon 29/03/21	Mon 29/03/21	100%
1793	Sheet Plasterboard Partitions	1 d	Tue 30/03/21	Tue 30/03/21	100%
1794	Set & Sand Plasterboard Partitions	2 d	Wed 31/03/21	Thu 1/04/21	100%
1795	Frame Ceilings	1 d	Wed 7/04/21	Wed 7/04/21	100%
1796	Sheet Ceilings & Bulkheads	1 d	Thu 8/04/21	Thu 8/04/21	100%
1797	Set & Sand Plasterboard Ceilings & Bulkheads	2 d	Fri 9/04/21	Mon 12/04/21	100%
1798	Paint - 1st Coat	1 d	Tue 13/04/21	Tue 13/04/21	100%

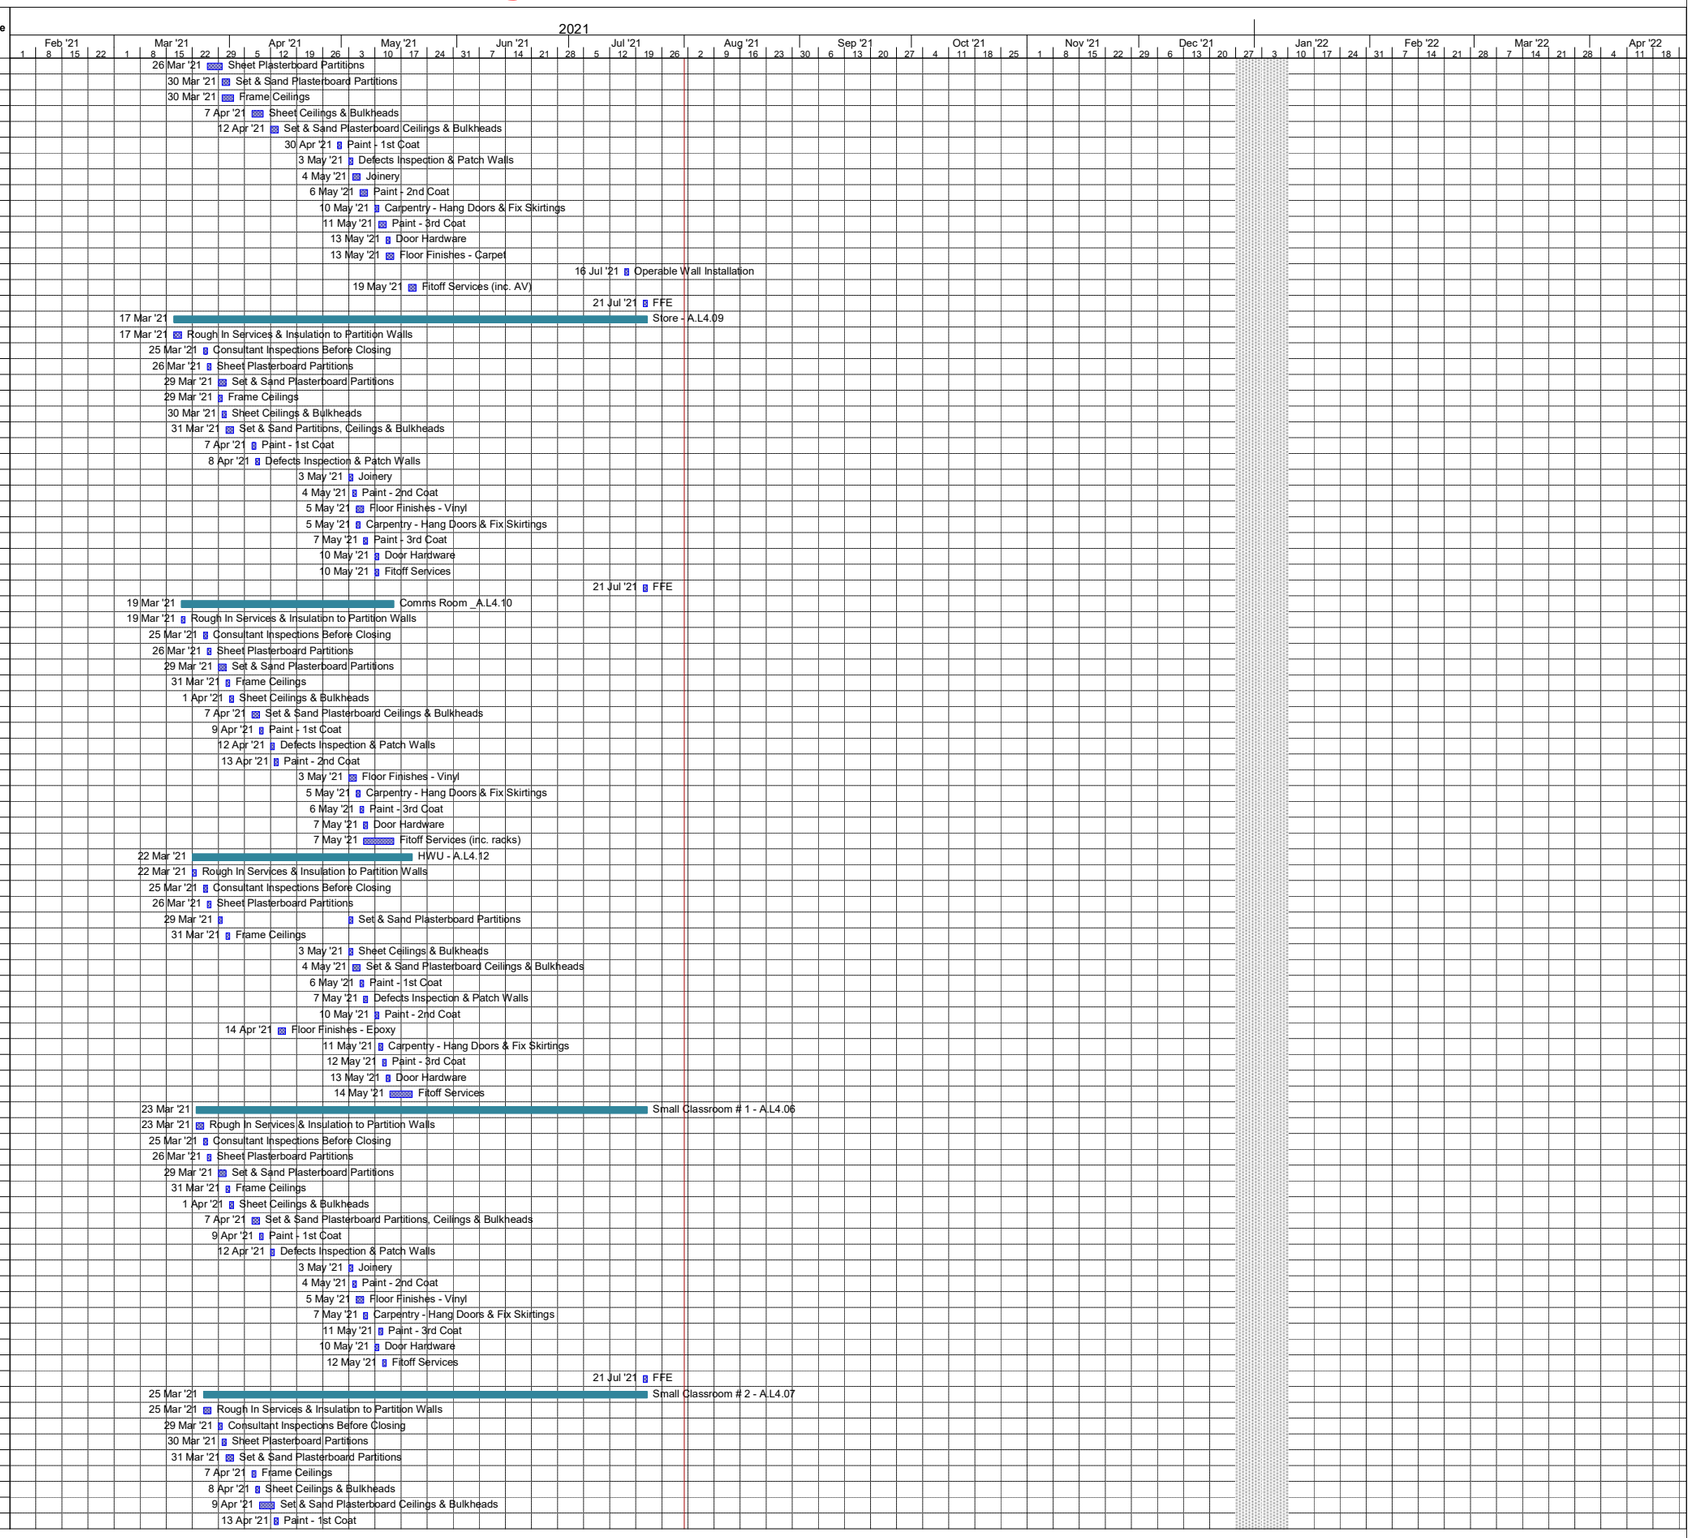


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1799	Defects Inspection & Patch Walls	1 d	Wed 14/04/21	Wed 14/04/21	100%
1800	Joinery	1 d	Mon 3/05/21	Mon 3/05/21	100%
1801	Paint - 2nd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
1802	Floor Finishes - Vinyl	2 d	Wed 5/05/21	Thu 6/05/21	100%
1803	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 7/05/21	Fri 7/05/21	100%
1804	Paint - 3rd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
1805	Door Hardware	1 d	Tue 11/05/21	Tue 11/05/21	100%
1806	Fitoff Services	1 d	Tue 11/05/21	Tue 11/05/21	100%
1807	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1808	**Corridor A.L4.13**	**54 d**	**Thu 8/04/21**	**Mon 28/06/21**	**100%**
1809	Sheet Plasterboard Partitions	3 d	Thu 8/04/21	Mon 12/04/21	100%
1810	Set & Sand Plasterboard Partitions	1 d	Tue 13/04/21	Tue 13/04/21	100%
1811	Sheet Ceilings & Bulkheads	2 d	Wed 14/04/21	Thu 15/04/21	100%
1812	Set & Sand Plasterboard Ceilings & Bulkheads	3 d	Fri 16/04/21	Tue 20/04/21	100%
1813	Paint - 1st Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1814	Defects Inspection & Patch Walls	1 d	Tue 4/05/21	Tue 4/05/21	100%
1815	Paint - 2nd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
1816	Floor Finishes - Vinyl	2 d	Thu 6/05/21	Fri 7/05/21	100%
1817	Paint - 3rd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
1818	Fitoff Services	1 d	Mon 28/06/21	Mon 28/06/21	100%
1819	**Wet Areas**	**86 d**	**Mon 15/03/21**	**Wed 21/07/21**	**100%**
1820	Sheet Wall Linings	1 d	Mon 15/03/21	Mon 15/03/21	100%
1821	Set & Sand Plasterboard Wall Linings	1 d	Tue 16/03/21	Tue 16/03/21	100%
1822	Wall Tiling	4 d	Thu 15/04/21	Tue 20/04/21	100%
1823	Frame Ceilings	1 d	Tue 23/03/21	Tue 23/03/21	100%
1824	Sheet Ceilings	1 d	Thu 25/03/21	Thu 25/03/21	100%
1825	Set & Sand Ceilings	1 d	Fri 26/03/21	Fri 26/03/21	100%
1826	Membrane	1 d	Wed 21/04/21	Wed 21/04/21	100%
1827	Flood Test	1 d	Fri 23/04/21	Fri 23/04/21	100%
1828	Screed	2 d	Wed 28/04/21	Thu 29/04/21	100%
1829	Paint - 1st Coat	1 d	Fri 30/04/21	Fri 30/04/21	100%
1830	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1831	Floor Finishes - Vinyl	3 d	Tue 4/05/21	Thu 6/05/21	100%
1832	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
1833	Joinery	2 d	Mon 10/05/21	Tue 11/05/21	100%
1834	Toilet Partitions	4 d	Wed 12/05/21	Mon 17/05/21	100%
1835	Fit Off PC Items	4 d	Tue 18/05/21	Fri 21/05/21	100%
1836	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1837	**Level 4 External Terrace**	**94 d**	**Tue 9/03/21**	**Tue 27/07/21**	**96%**
1838	Membrane	2 d	Tue 9/03/21	Wed 10/03/21	100%
1839	Stainless Steel Balustrading	5 d	Thu 25/03/21	Wed 31/03/21	100%
1840	Erect Columns and Roof Framing	5 d	Thu 25/03/21	Wed 31/03/21	100%
1841	Install Roof Pergola Elements	2 d	Mon 3/05/21	Tue 4/05/21	100%
1842	Pedestal and Decking System	15 d	Thu 8/04/21	Fri 30/04/21	100%
1843	Glazing To Stainless Steel Balustrading	4 d	Mon 3/05/21	Thu 6/05/21	100%
1844	Mechanical Terrace Plant	15 d	Mon 3/05/21	Fri 21/05/21	100%
1845	Plant Louvres & Screens	4 d	Mon 24/05/21	Thu 27/05/21	100%
1846	Zen Gardens Planting and Stone Work	6 d	Mon 19/07/21	Mon 26/07/21	75%
1847	FFE	1 d	Tue 27/07/21	Tue 27/07/21	0%
1848	**Floor Handover**	**8 d**	**Tue 29/06/21**	**Thu 8/07/21**	**100%**
1849	Signage	2 d	Tue 29/06/21	Wed 30/06/21	100%
1850	Initial Clean and Defects	3 d	Tue 6/07/21	Thu 8/07/21	100%
1851	**Level 5 (Roof)**	**68 d**	**Wed 17/02/21**	**Tue 25/05/21**	**100%**
1852	Roof Access System	2 d	Wed 17/02/21	Thu 18/02/21	100%
1853	Membrane	2 d	Fri 19/02/21	Sat 20/02/21	100%
1854	Mechanical Roof Plant	2 d	Mon 24/05/21	Tue 25/05/21	100%
1855	**Final Clean**	**6 d**	**Mon 2/08/21**	**Mon 9/08/21**	**0%**
1856	Final Detailed Clean	6 d	Mon 2/08/21	Mon 9/08/21	0%
1857	*Education Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	0%
1858	**BUILDING B - HERITAGE COURTHOUSE**	**296 d**	**Fri 26/06/20**	**Thu 29/07/21**	**99%**
1859	**LEVEL 1**	**290 d**	**Fri 26/06/20**	**Wed 21/07/21**	**100%**
1860	Hydraulic Services In Ground	10 d	Fri 26/06/20	Tue 7/07/20	100%
1861	FRP New Floors	10 d	Wed 8/07/20	Sat 18/07/20	100%
1862	Brickwork Alterations & Lintels	20 d	Mon 20/07/20	Tue 11/08/20	100%
1863	Structural Strengthening & Carpentry	20 d	Wed 12/08/20	Thu 3/09/20	100%
1864	Hydraulic Services Run High Level \ Chase Walls	20 d	Fri 31/07/20	Sat 22/08/20	100%
1865	Mechanical Services Run High Level	20 d	Mon 24/08/20	Tue 15/09/20	100%
1866	Electrical Services (Lights\power\fire\security\comms) Run High Leve	20 d	Sat 29/08/20	Mon 21/09/20	100%
1867	Wet Fire Run High Level	10 d	Thu 10/09/20	Mon 21/09/20	100%
1868	**Plant Room & SubFloor Spaces**	**20 d**	**Wed 16/09/20**	**Mon 12/10/20**	**100%**
1869	Mechanical Ductwork	20 d	Wed 16/09/20	Mon 12/10/20	100%
1870	**Cells 1, 2 & 3**	**33 d**	**Thu 11/03/21**	**Mon 3/05/21**	**100%**
1871	Minor Repairs to Walls	10 d	Thu 11/03/21	Wed 24/03/21	100%
1872	Clean & Apply Sealer to Walls	2 d	Thu 25/03/21	Fri 26/03/21	100%
1873	Cap \ Seal Existing Services	1 d	Thu 25/03/21	Thu 25/03/21	100%
1874	Fit Off Services	1 d	Mon 3/05/21	Mon 3/05/21	100%
1875	**Male WC**	**215 d**	**Tue 22/09/20**	**Wed 21/07/21**	**100%**
1876	Frame Walls & Ceilings	1 d	Tue 22/09/20	Tue 22/09/20	100%
1877	Rough In Services & Insulation to Partition Walls	2 d	Wed 23/09/20	Thu 24/09/20	100%
1878	Consultant Inspections Before Closing	1 d	Wed 30/09/20	Wed 30/09/20	100%
1879	Villaboard Linings	1 d	Wed 30/09/20	Wed 30/09/20	100%
1880	Sheet & Close Plasterboard Ceilings	1 d	Fri 30/10/20	Fri 30/10/20	100%
1881	Sheet and Close Plasterboard Ceilings\ Cornice	3 d	Sat 31/10/20	Tue 3/11/20	100%
1882	Paint - 1st Coat	1 d	Sat 30/01/21	Sat 30/01/21	100%
1883	Waterproofing	1 d	Thu 5/11/20	Thu 5/11/20	100%
1884	Screed	1 d	Sat 7/11/20	Sat 7/11/20	100%
1885	Wall Tiling	3 d	Fri 4/12/20	Thu 10/12/20	100%
1886	Paint - 2nd Coat	1 d	Sat 20/02/21	Sat 20/02/21	100%
1887	Lay Vinyl Flooring	2 d	Mon 22/02/21	Tue 23/02/21	100%
1888	Toilet Partitions	4 d	Thu 25/03/21	Tue 30/03/21	100%
1889	Joinery	4 d	Wed 24/02/21	Sat 27/02/21	100%
1890	Fit Off PC Items	1 d	Wed 31/03/21	Wed 31/03/21	100%
1891	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%

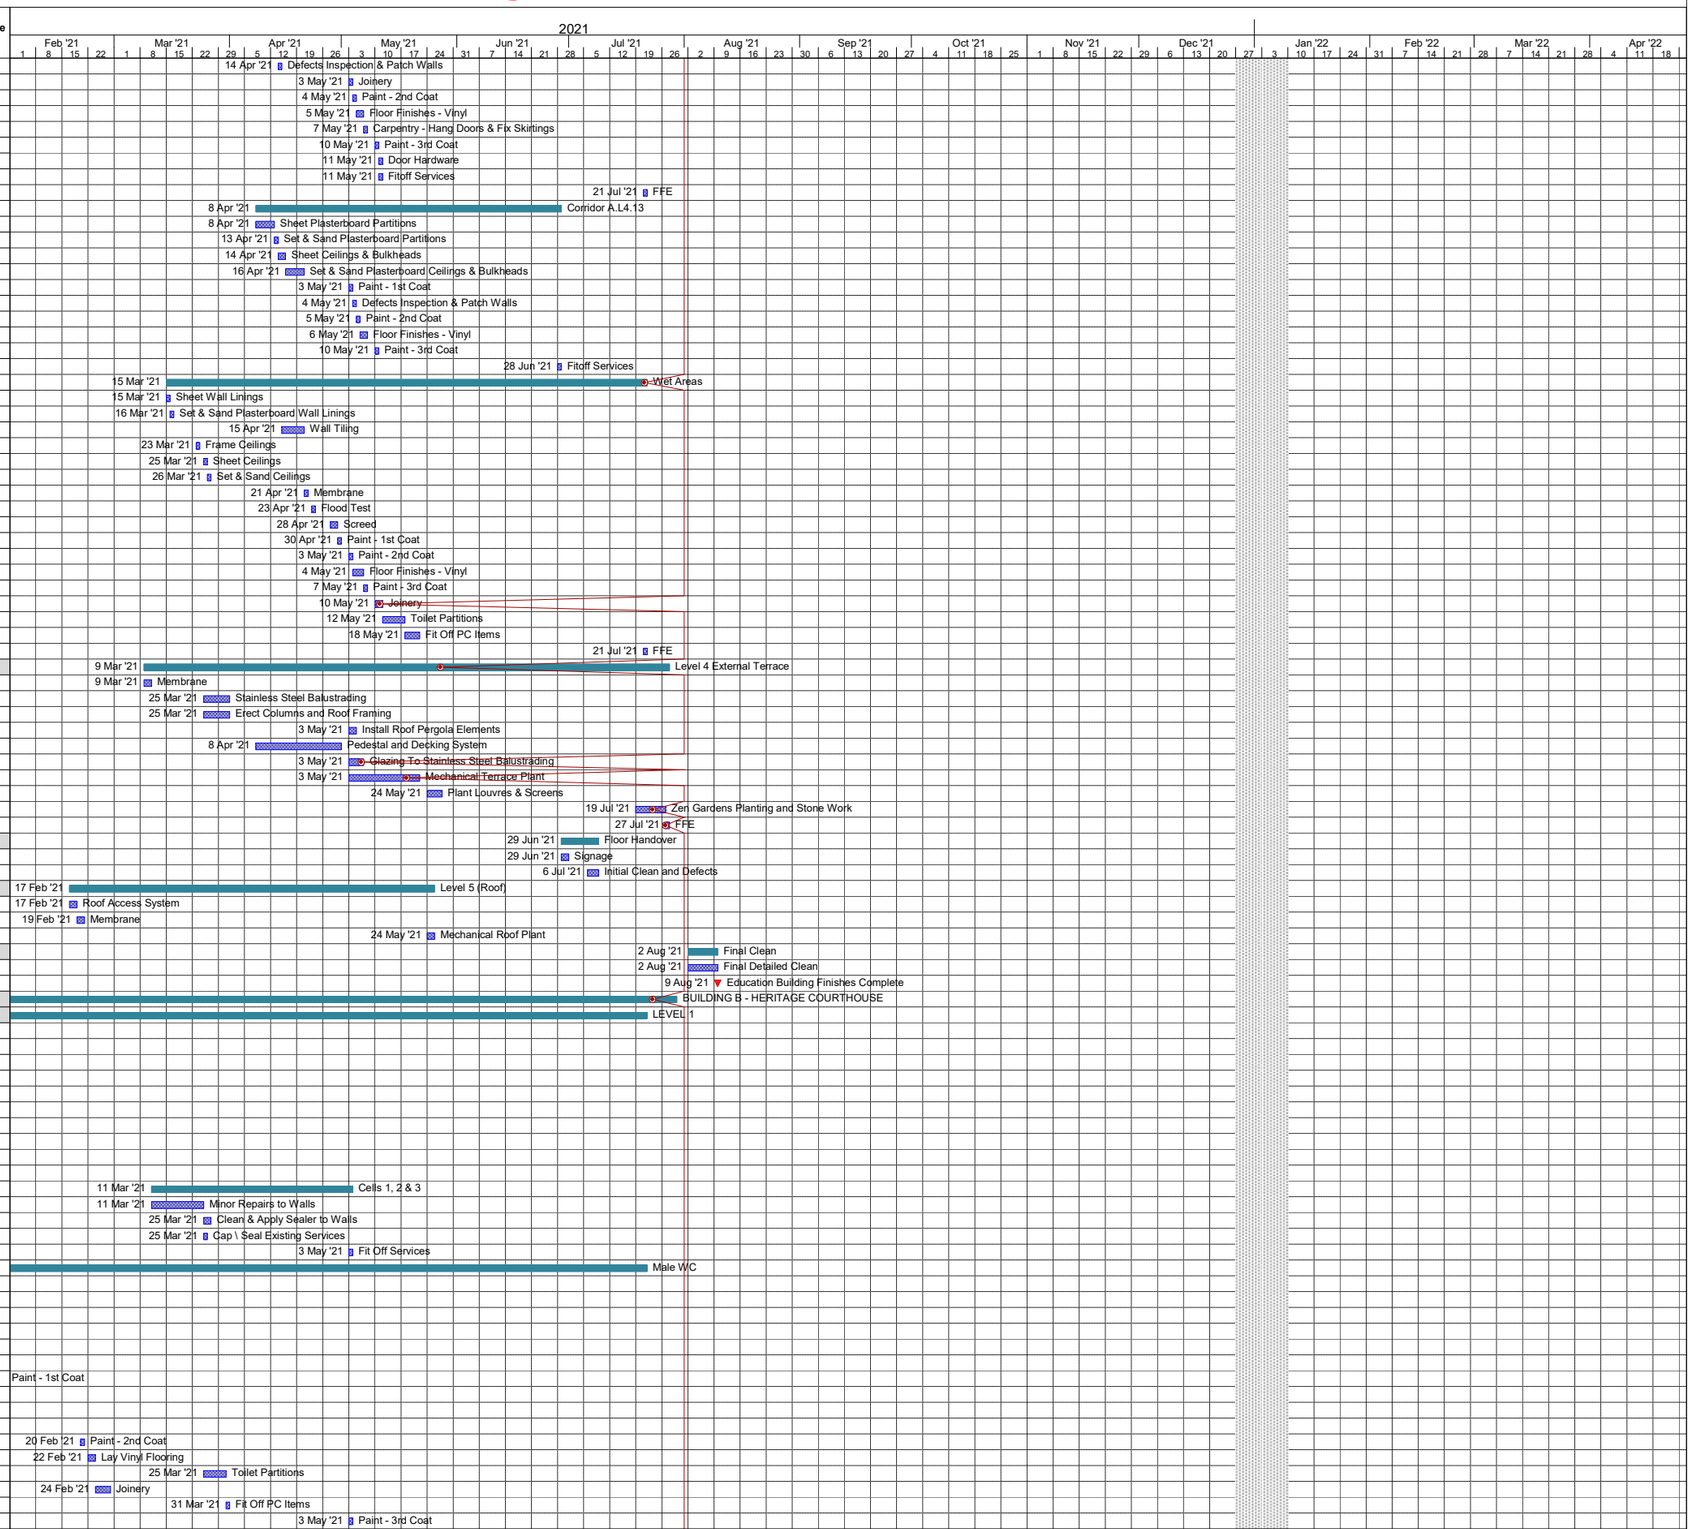


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
1892	Fit Off Services	1 d	Wed 7/04/21	Wed 7/04/21	100%
1893	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1894	**Female WC**	**214 d**	**Wed 23/09/20**	**Wed 21/07/21**	**100%**
1895	Frame Walls & Ceilings	1 d	Wed 23/09/20	Wed 23/09/20	100%
1896	Rough In Services & Insulation to Partition Walls	2 d	Thu 24/09/20	Fri 25/09/20	100%
1897	Consultant Inspections Before Closing	1 d	Wed 30/09/20	Wed 30/09/20	100%
1898	Villaboard Linings	1 d	Thu 1/10/20	Thu 1/10/20	100%
1899	Sheet & Close Plasterboard Ceilings	1 d	Sat 31/10/20	Sat 31/10/20	100%
1900	Set & Sand Ceilings & Bulkheads	4 d	Wed 4/11/20	Sat 7/11/20	100%
1901	Paint - 1st Coat	1 d	Mon 1/02/21	Mon 1/02/21	100%
1902	Waterproofing	1 d	Mon 9/11/20	Mon 9/11/20	100%
1903	Screed	1 d	Wed 11/11/20	Wed 11/11/20	100%
1904	Wall Tiling	3 d	Fri 4/12/20	Thu 10/12/20	100%
1905	Paint - 2nd Coat	1 d	Sat 20/02/21	Sat 20/02/21	100%
1906	Lay Vinyl Flooring	2 d	Mon 22/02/21	Tue 23/02/21	100%
1907	Toilet Partitions	6 d	Wed 24/02/21	Tue 2/03/21	100%
1908	Joinery	4 d	Wed 24/02/21	Sat 27/02/21	100%
1909	Fit Off PC Items	1 d	Thu 25/03/21	Thu 25/03/21	100%
1910	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1911	Fit Off Services	1 d	Mon 29/03/21	Mon 29/03/21	100%
1912	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1913	**Cleaners Store**	**213 d**	**Thu 24/09/20**	**Wed 21/07/21**	**100%**
1914	Frame Walls & Ceilings	1 d	Thu 24/09/20	Thu 24/09/20	100%
1915	Rough In Services & Insulation to Partition Walls	1 d	Fri 25/09/20	Fri 25/09/20	100%
1916	Consultant Inspections Before Closing	1 d	Wed 30/09/20	Wed 30/09/20	100%
1917	Villaboard Linings	1 d	Fri 2/10/20	Fri 2/10/20	100%
1918	Sheet & Close Plasterboard Ceilings	1 d	Mon 2/11/20	Mon 2/11/20	100%
1919	Set & Sand Ceilings & Bulkheads	4 d	Sat 7/11/20	Wed 11/11/20	100%
1920	Paint - 1st Coat	1 d	Tue 2/02/21	Tue 2/02/21	100%
1921	Waterproofing	1 d	Thu 12/11/20	Thu 12/11/20	100%
1922	Screed	1 d	Sat 14/11/20	Sat 14/11/20	100%
1923	Wall Tiling	3 d	Fri 4/12/20	Thu 10/12/20	100%
1924	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
1925	Lay Vinyl Flooring	2 d	Fri 12/03/21	Mon 15/03/21	100%
1926	Fit Off PC Items	2 d	Tue 16/03/21	Wed 17/03/21	100%
1927	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1928	Fit Off Services	1 d	Mon 29/03/21	Mon 29/03/21	100%
1929	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1930	**Access WC**	**212 d**	**Fri 25/09/20**	**Wed 21/07/21**	**100%**
1931	Frame Walls & Ceilings	1 d	Fri 25/09/20	Fri 25/09/20	100%
1932	Rough In Services & Insulation to Partition Walls	1 d	Sat 26/09/20	Sat 26/09/20	100%
1933	Consultant Inspections Before Closing	1 d	Wed 30/09/20	Wed 30/09/20	100%
1934	Villaboard Linings	1 d	Wed 7/10/20	Wed 7/10/20	100%
1935	Sheet & Close Plasterboard Ceilings	1 d	Tue 3/11/20	Tue 3/11/20	100%
1936	Set & Sand Ceilings & Bulkheads	5 d	Fri 8/01/21	Wed 13/01/21	100%
1937	Paint - 1st Coat	1 d	Wed 3/02/21	Wed 3/02/21	100%
1938	Waterproofing	1 d	Fri 13/11/20	Fri 13/11/20	100%
1939	Screed	1 d	Mon 16/11/20	Mon 16/11/20	100%
1940	Wall Tiling	3 d	Fri 4/12/20	Thu 10/12/20	100%
1941	Paint - 2nd Coat	1 d	Sat 20/02/21	Sat 20/02/21	100%
1942	Lay Vinyl Flooring	2 d	Mon 22/02/21	Tue 23/02/21	100%
1943	Joinery	1 d	Thu 25/03/21	Thu 25/03/21	100%
1944	Fit Off PC Items	1 d	Fri 26/03/21	Fri 26/03/21	100%
1945	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1946	Fit Off Services	1 d	Tue 30/03/21	Tue 30/03/21	100%
1947	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1948	**Book Storage**	**211 d**	**Sat 26/09/20**	**Wed 21/07/21**	**100%**
1949	Stud Framing\Furring Channels to Walls	2 d	Fri 30/10/20	Sat 31/10/20	100%
1950	Frame Ceilings	2 d	Sat 26/09/20	Mon 28/09/20	100%
1951	Consultant Inspections Before Closing	1 d	Sat 10/10/20	Sat 10/10/20	100%
1952	Sheet & Close Plasterboard Wall Linings	2 d	Mon 2/11/20	Tue 3/11/20	100%
1953	Sheet & Close Plasterboard Ceilings	1 d	Wed 4/11/20	Wed 4/11/20	100%
1954	Set & Sand Ceilings & Bulkheads	3 d	Thu 5/11/20	Sat 7/11/20	100%
1955	Paint - 1st Coat	1 d	Fri 15/01/21	Fri 15/01/21	100%
1956	Defects Inspection & Patch	1 d	Sat 16/01/21	Sat 16/01/21	100%
1957	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
1958	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1959	Lay Vinyl Flooring	2 d	Tue 2/02/21	Wed 3/02/21	100%
1960	Fitoff Services	1 d	Tue 4/05/21	Tue 4/05/21	100%
1961	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1962	**Interview Room**	**209 d**	**Tue 29/09/20**	**Wed 21/07/21**	**100%**
1963	Frame Ceilings	2 d	Tue 29/09/20	Wed 30/09/20	100%
1964	Patch \ Make Good Walls	2 d	Mon 2/11/20	Tue 3/11/20	100%
1965	Consultant Inspections Before Closing	1 d	Tue 13/10/20	Tue 13/10/20	100%
1966	Set & Sand Ceilings & Bulkheads	3 d	Thu 5/11/20	Sat 7/11/20	100%
1967	Set & Sand Ceilings & Bulkheads	3 d	Mon 9/11/20	Wed 11/11/20	100%
1968	Paint - 1st Coat	2 d	Sat 30/01/21	Mon 1/02/21	100%
1969	Defects Inspection & Patch	1 d	Sat 20/02/21	Sat 20/02/21	100%
1970	Paint - 2nd Coat	25.5 d	Mon 22/02/21	Thu 25/03/21	100%
1971	Paint - 3rd Coat	2 d	Mon 3/05/21	Tue 4/05/21	100%
1972	Lay Vinyl Flooring	2 d	Mon 29/03/21	Wed 31/03/21	100%
1973	Fitoff Services	1 d	Wed 31/03/21	Thu 1/04/21	100%
1974	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1975	**Monitor Room**	**207 d**	**Thu 1/10/20**	**Wed 21/07/21**	**100%**
1976	Frame Ceilings	1 d	Thu 1/10/20	Thu 1/10/20	100%
1977	Patch \ Make Good Walls	4 d	Wed 4/11/20	Sat 7/11/20	100%
1978	Consultant Inspections Before Closing	1 d	Wed 14/10/20	Wed 14/10/20	100%
1979	Sheet and Close Plasterboard Ceilings	1 d	Fri 6/11/20	Fri 6/11/20	100%
1980	Set & Sand Ceilings & Bulkheads	3 d	Thu 12/11/20	Sat 14/11/20	100%
1981	Paint - 1st Coat	2 d	Tue 19/01/21	Wed 20/01/21	100%
1982	Defects Inspection & Patch	1 d	Thu 21/01/21	Thu 21/01/21	100%
1983	Install Joinery	1 d	Mon 3/05/21	Mon 3/05/21	100%
1984	Paint - 2nd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%

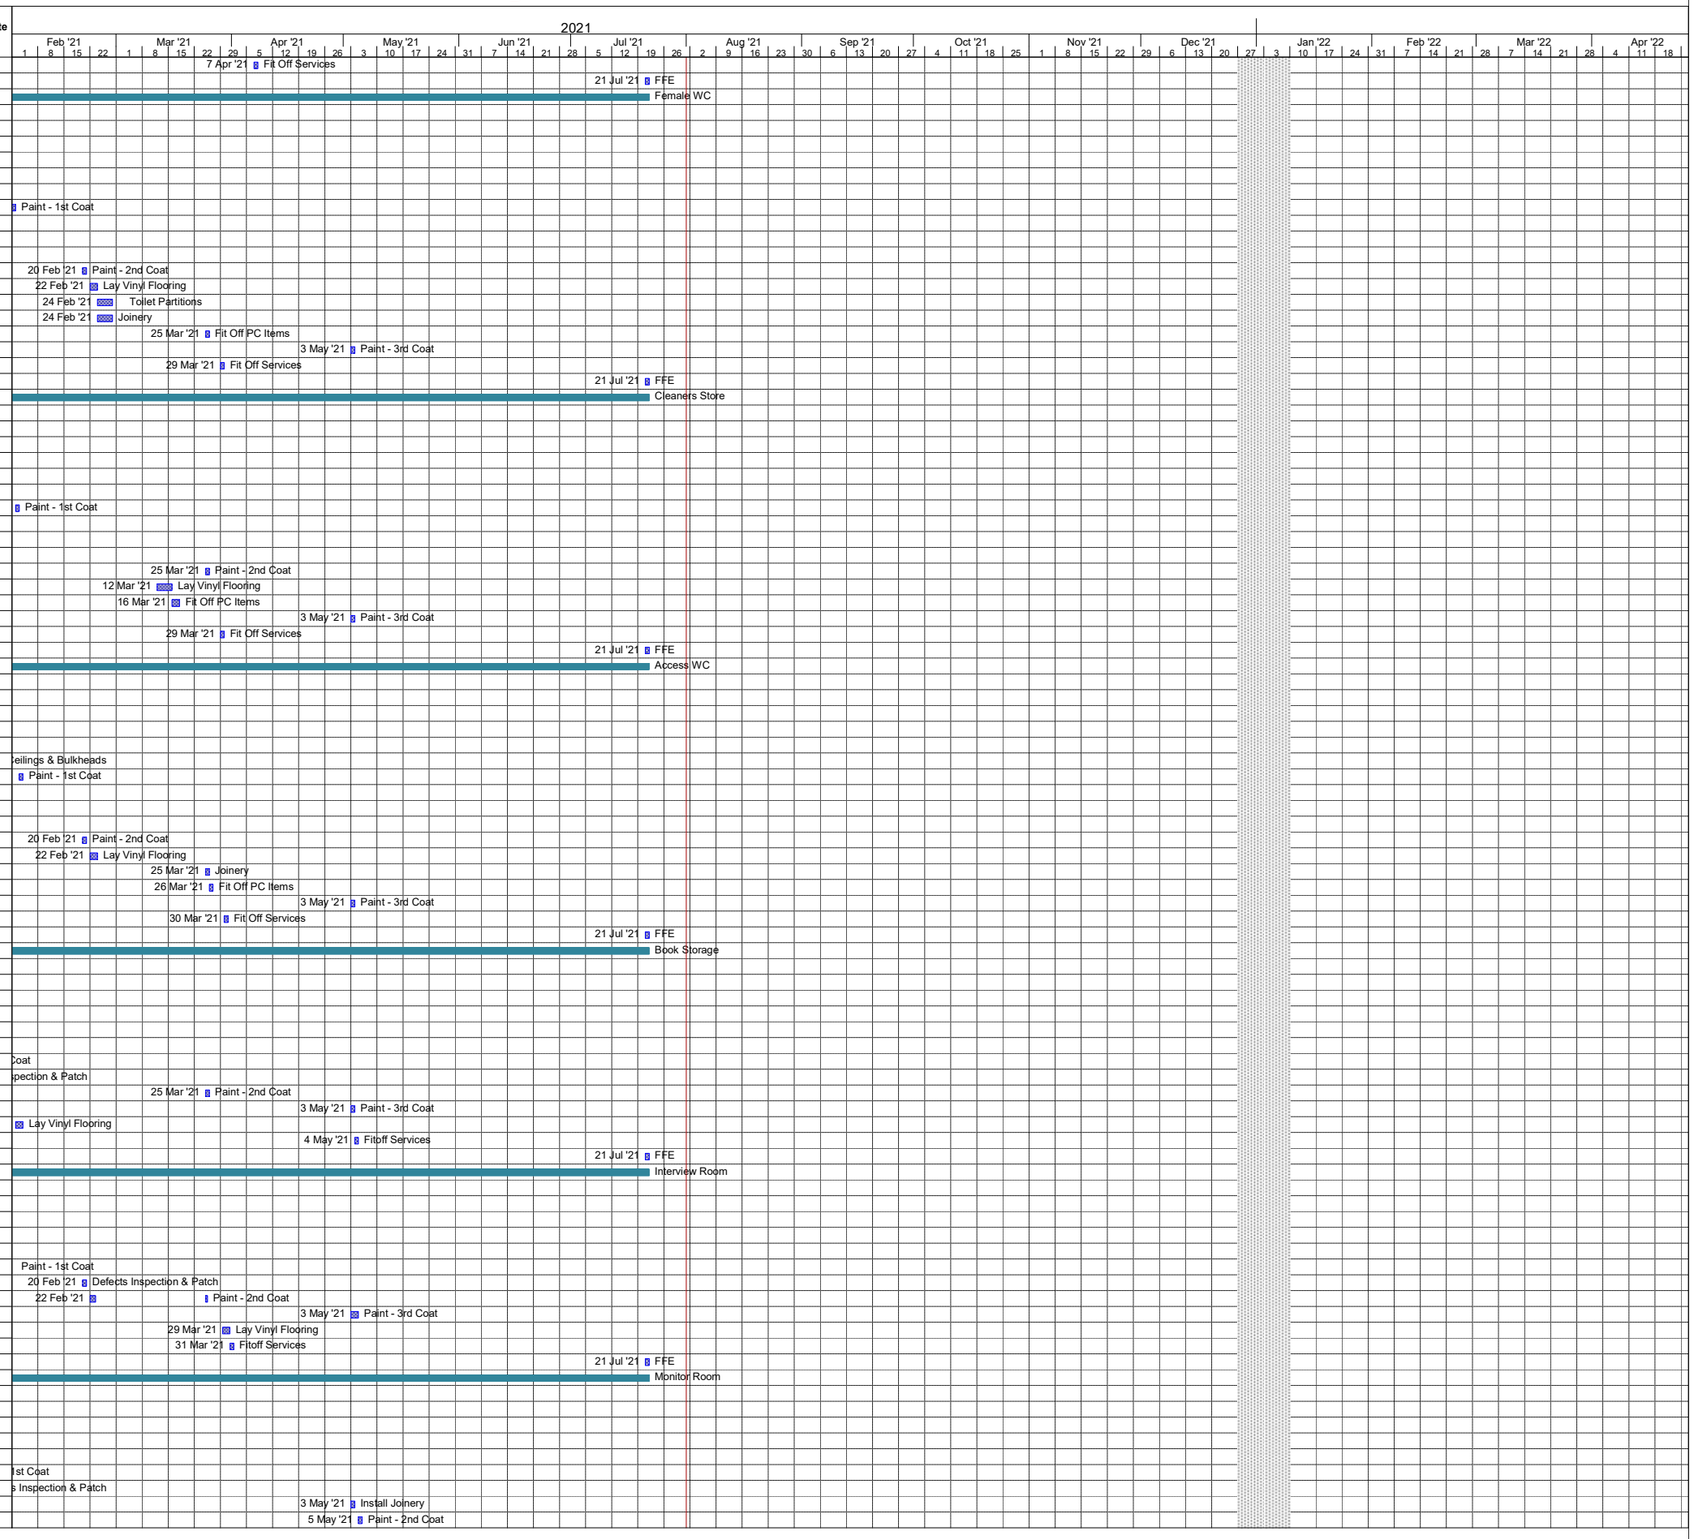


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
1985	Paint - 3rd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
1986	Lay Carpet Flooring	1 d	Fri 7/05/21	Fri 7/05/21	100%
1987	Fitoff Services	1 d	Fri 7/05/21	Fri 7/05/21	100%
1988	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1989	**Comms\Store Rooms**	**145 d**	**Thu 15/10/20**	**Wed 5/05/21**	**100%**
1990	Patch \ Make Good Walls	1 d	Thu 5/11/20	Thu 5/11/20	100%
1991	Consultant Inspections Before Closing	1 d	Thu 15/10/20	Thu 15/10/20	100%
1992	Frame Ceilings	1 d	Sat 27/02/21	Sat 27/02/21	100%
1993	Sheet and Close Plasterboard Ceilings	1 d	Thu 25/03/21	Thu 25/03/21	100%
1994	Set & Sand Ceilings & Bulkheads	3 d	Fri 26/03/21	Tue 30/03/21	100%
1995	Paint - 1st Coat	1 d	Wed 31/03/21	Wed 31/03/21	100%
1996	Defects Inspection & Patch	1 d	Thu 1/04/21	Thu 1/04/21	100%
1997	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
1998	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
1999	Lay Vinyl Flooring	1 d	Fri 9/04/21	Fri 9/04/21	100%
2000	Fitoff Services	1 d	Wed 5/05/21	Wed 5/05/21	100%
2001	**Administration Office**	**205 d**	**Wed 7/10/20**	**Wed 21/07/21**	**100%**
2002	Frame Ceilings	2 d	Wed 7/10/20	Thu 8/10/20	100%
2003	Patch \ Make Good Walls	26 d	Fri 6/11/20	Wed 9/12/20	100%
2004	Consultant Inspections Before Closing	1 d	Tue 20/10/20	Tue 20/10/20	100%
2005	Sheet and Close Plasterboard Ceilings\ Cornice	4 d	Fri 12/03/21	Wed 17/03/21	100%
2006	Set & Sand Ceilings & Bulkheads	3 d	Thu 18/03/21	Mon 22/03/21	100%
2007	Paint - 1st Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2008	Defects Inspection & Patch	1 d	Tue 4/05/21	Tue 4/05/21	100%
2009	Install Joinery	1 d	Wed 5/05/21	Wed 5/05/21	100%
2010	Paint - 2nd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
2011	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
2012	Lay Carpet Flooring	1 d	Mon 10/05/21	Mon 10/05/21	100%
2013	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
2014	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
2015	**Lounge (Old Teacher's Room)**	**203 d**	**Fri 9/10/20**	**Wed 21/07/21**	**100%**
2016	Frame Ceilings	4 d	Fri 9/10/20	Tue 13/10/20	100%
2017	Patch \ Make Good Walls	4 d	Thu 10/12/20	Mon 14/12/20	100%
2018	Consultant Inspections Before Closing	1 d	Sat 24/10/20	Sat 24/10/20	100%
2019	Sheet and Close Plasterboard Ceilings\ Cornice	2 d	Tue 10/11/20	Wed 11/11/20	100%
2020	Set & Sand Ceilings & Bulkheads	3 d	Mon 23/11/20	Wed 25/11/20	100%
2021	Paint - 1st Coat	1 d	Thu 28/01/21	Thu 28/01/21	100%
2022	Defects Inspection & Patch	1 d	Fri 29/01/21	Fri 29/01/21	100%
2023	Paint - 2nd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
2024	Paint - 3rd Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
2025	Lay Carpet Flooring	3 d	Tue 11/05/21	Thu 13/05/21	100%
2026	Fitoff Services	1 d	Fri 14/05/21	Fri 14/05/21	100%
2027	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
2028	**Lift Lobby**	**150 d**	**Wed 14/10/20**	**Tue 11/05/21**	**100%**
2029	Frame Ceilings	1 d	Wed 14/10/20	Wed 14/10/20	100%
2030	Consultant Inspections Before Closing	1 d	Tue 27/10/20	Tue 27/10/20	100%
2031	Patch \ Make Good Walls	2 d	Thu 25/03/21	Fri 26/03/21	100%
2032	Sheet & Close Plasterboard Ceilings	1 d	Mon 29/03/21	Mon 29/03/21	100%
2033	Set & Sand Ceilings & Bulkheads	3 d	Tue 30/03/21	Thu 1/04/21	100%
2034	Paint - 1st Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2035	Defects Inspection & Patch	1 d	Tue 4/05/21	Tue 4/05/21	100%
2036	Paint - 2nd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
2037	Paint - 3rd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
2038	Lay Carpet Flooring	2 d	Fri 7/05/21	Mon 10/05/21	100%
2039	Fitoff Services	1 d	Tue 11/05/21	Tue 11/05/21	100%
2040	**Corridor 1 & 2**	**151 d**	**Thu 15/10/20**	**Thu 13/05/21**	**100%**
2041	Frame Ceilings	2 d	Thu 15/10/20	Fri 16/10/20	100%
2042	Patch \ Make Good Walls	8 d	Mon 11/01/21	Tue 19/01/21	100%
2043	Consultant Inspections Before Closing	1 d	Sat 17/10/20	Sat 17/10/20	100%
2044	Sheet & Close Plasterboard Ceilings	2 d	Fri 13/11/20	Sat 14/11/20	100%
2045	Set & Sand Ceilings & Bulkheads	3 d	Mon 30/11/20	Wed 2/12/20	100%
2046	Paint - 1st Coat	3 d	Sat 30/01/21	Tue 2/02/21	100%
2047	Defects Inspection & Patch	2 d	Wed 3/02/21	Thu 4/02/21	100%
2048	Paint - 2nd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
2049	Paint - 3rd Coat	2 d	Mon 10/05/21	Tue 11/05/21	100%
2050	Lay Vinyl Flooring	2 d	Mon 15/02/21	Tue 16/02/21	100%
2051	Fitoff Services	2 d	Wed 12/05/21	Thu 13/05/21	100%
2052	**Corridor 3**	**148 d**	**Sat 17/10/20**	**Wed 12/05/21**	**100%**
2053	Frame Ceilings	2 d	Sat 17/10/20	Mon 19/10/20	100%
2054	Patch \ Make Good Walls	8 d	Wed 20/01/21	Mon 1/02/21	100%
2055	Consultant Inspections Before Closing	1 d	Tue 20/10/20	Tue 20/10/20	100%
2056	Sheet and Close Plasterboard Ceilings\ Cornice	3 d	Fri 8/01/21	Mon 11/01/21	100%
2057	Set & Sand Ceilings & Bulkheads	3 d	Tue 12/01/21	Thu 14/01/21	100%
2058	Paint - 1st Coat	3 d	Wed 3/02/21	Fri 5/02/21	100%
2059	Defects Inspection & Patch	2 d	Sat 6/02/21	Mon 8/02/21	100%
2060	Paint - 2nd Coat	2 d	Mon 3/05/21	Tue 4/05/21	100%
2061	Paint - 3rd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
2062	Lay Carpet Flooring	2 d	Fri 7/05/21	Mon 10/05/21	100%
2063	Fitoff Services	2 d	Tue 11/05/21	Wed 12/05/21	100%
2064	**Corridor 4**	**146 d**	**Tue 20/10/20**	**Wed 12/05/21**	**100%**
2065	Frame Ceilings	4 d	Tue 20/10/20	Fri 23/10/20	100%
2066	Patch \ Make Good Walls	4 d	Fri 27/11/20	Tue 1/12/20	100%
2067	Consultant Inspections Before Closing	1 d	Sat 24/10/20	Sat 24/10/20	100%
2068	Sheet and Close Plasterboard Ceilings\ Cornice	3 d	Wed 18/11/20	Fri 20/11/20	100%
2069	Set & Sand Ceilings & Bulkheads	3 d	Thu 10/12/20	Sat 12/12/20	100%
2070	Paint - 1st Coat	3 d	Sat 6/02/21	Tue 9/02/21	100%
2071	Defects Inspection & Patch	2 d	Wed 10/02/21	Thu 11/02/21	100%
2072	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
2073	Paint - 3rd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2074	Lay Vinyl Flooring	4 d	Fri 19/03/21	Wed 24/03/21	100%
2075	Fitoff Services	2 d	Tue 11/05/21	Wed 12/05/21	100%
2076	**Corridor 5**	**144 d**	**Sat 24/10/20**	**Fri 14/05/21**	**100%**
2077	Frame Ceilings	4 d	Sat 24/10/20	Wed 28/10/20	100%

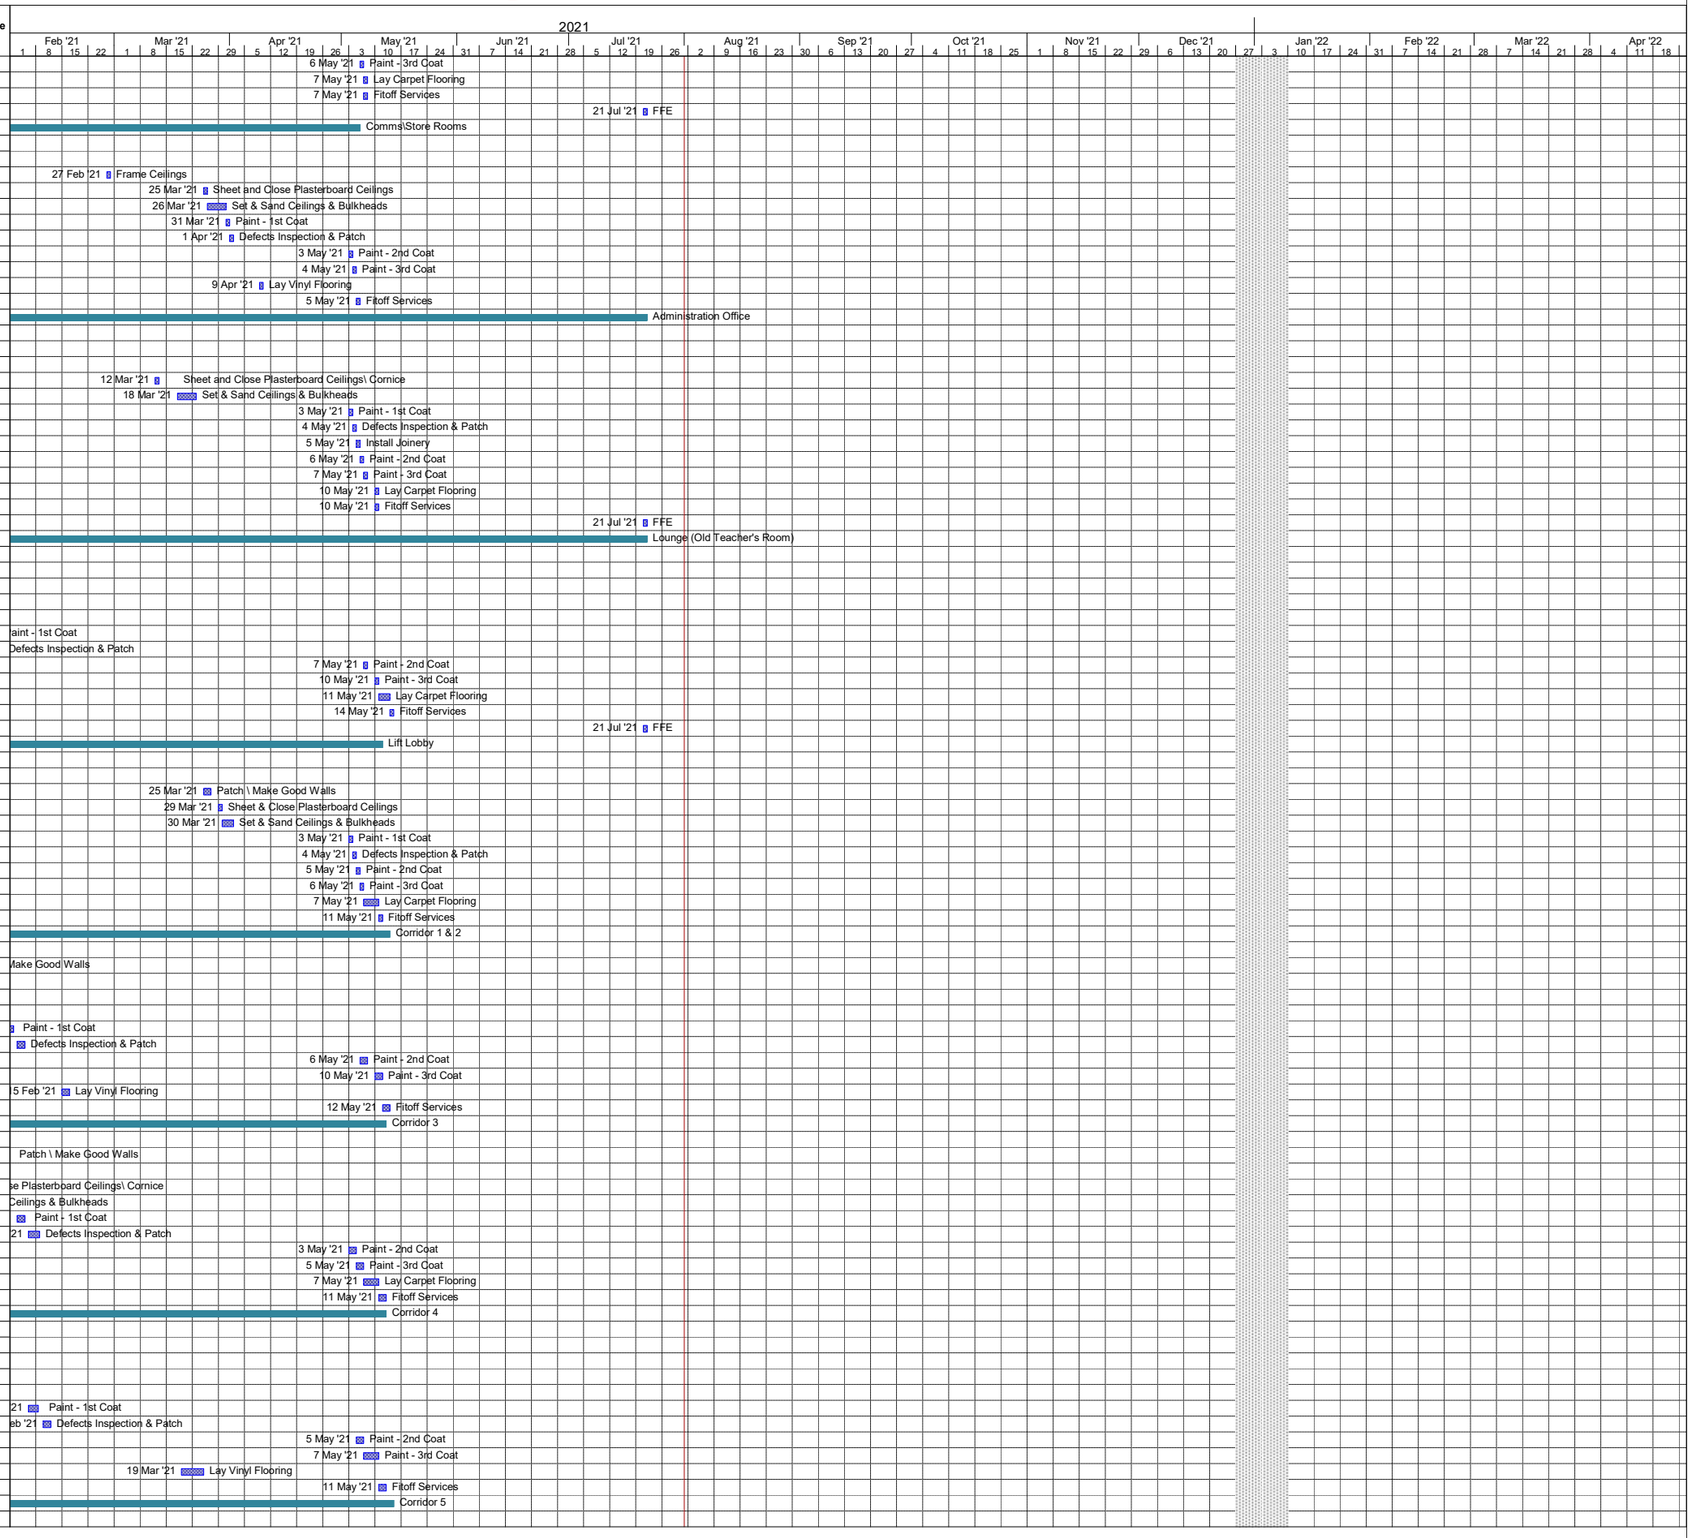


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
2078	Patch \ Make Good Walls	4 d	Wed 2/12/20	Wed 9/12/20	100%
2079	Consultant Inspections Before Closing	1 d	Thu 29/10/20	Thu 29/10/20	100%
2080	Sheet & Close Plasterboard Ceilings	3 d	Sat 21/11/20	Tue 24/11/20	100%
2081	Set & Sand Ceilings & Bulkheads	3 d	Mon 14/12/20	Wed 16/12/20	100%
2082	Paint - 1st Coat	6 d	Thu 17/12/20	Mon 4/01/21	100%
2083	Defects Inspection & Patch	2 d	Sat 30/01/21	Mon 1/02/21	100%
2084	Paint - 2nd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2085	Paint - 3rd Coat	2 d	Tue 11/05/21	Wed 12/05/21	100%
2086	Lay Vinyl Flooring	4 d	Fri 19/02/21	Tue 23/02/21	100%
2087	Fitoff Services	2 d	Thu 13/05/21	Fri 14/05/21	100%
2088	**Plant Room**	**61 d**	**Fri 12/02/21**	**Mon 10/05/21**	**100%**
2089	Run High Level Mechanical Services	24 d	Fri 12/02/21	Thu 11/03/21	100%
2090	Run High Level Electrical Services	2 d	Fri 12/03/21	Mon 15/03/21	100%
2091	Patch \ Make Good Walls	1 d	Tue 16/03/21	Tue 16/03/21	100%
2092	Paint - 1st Coat	1 d	Wed 17/03/21	Wed 17/03/21	100%
2093	Defects Inspection & Paint	1 d	Mon 3/05/21	Mon 3/05/21	100%
2094	Paint - 2nd Coat	2 d	Tue 4/05/21	Wed 5/05/21	100%
2095	Paint - 3rd Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
2096	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
2097	**LEVEL 2**	**256 d**	**Wed 12/08/20**	**Thu 29/07/21**	**99%**
2098	Brickwork Alterations & Lintels	20 d	Wed 12/08/20	Thu 3/09/20	100%
2099	Structural Strengthening & Carpentry	20 d	Wed 12/08/20	Thu 3/09/20	100%
2100	Hydraulic Services Run High Level \ Chase Walls	10 d	Tue 13/10/20	Fri 23/10/20	100%
2101	Mechanical Services Run High Level	10 d	Fri 8/01/21	Tue 19/01/21	100%
2102	Electrical Services (Lights\power\fire\security\comms) Run High Leve	10 d	Mon 28/09/20	Mon 12/10/20	100%
2103	**Amenities (Male\Female\Access WC's)**	**227 d**	**Thu 10/09/20**	**Fri 23/07/21**	**100%**
2104	Frame Walls & Ceilings	8 d	Thu 10/09/20	Fri 18/09/20	100%
2105	Rough In Services & Insulation to Partition Walls	6 d	Sat 19/09/20	Fri 25/09/20	100%
2106	Consultant Inspections Before Closing	1 d	Sat 26/09/20	Sat 26/09/20	100%
2107	Sheet & Close Plasterboard Walls	4 d	Fri 30/10/20	Tue 3/11/20	100%
2108	Sheet & Close Plasterboard Ceilings	4 d	Wed 4/11/20	Sat 7/11/20	100%
2109	Set & Sand Plasterboard Partitions & Ceilings	3 d	Mon 9/11/20	Wed 11/11/20	100%
2110	Paint - 1st Coat	2 d	Fri 26/02/21	Sat 27/02/21	100%
2111	Defects Inspection & Patch Walls	1 d	Mon 1/03/21	Mon 1/03/21	100%
2112	Waterproofing	1 d	Thu 19/11/20	Thu 19/11/20	100%
2113	Screed	1 d	Sat 21/11/20	Sat 21/11/20	100%
2114	Wall Tiling	4 d	Fri 4/12/20	Fri 11/12/20	100%
2115	Paint - 2nd Coat	2 d	Thu 25/03/21	Fri 26/03/21	100%
2116	Fit Off PC Items	4 d	Mon 3/05/21	Thu 6/05/21	100%
2117	Paint - 3rd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2118	Fitoff Services	18 d	Tue 11/05/21	Thu 3/06/21	100%
2119	FFE	2 d	Thu 22/07/21	Fri 23/07/21	100%
2120	**Magistrate \ Old Library \ Judges Room 4**	**201 d**	**Tue 13/10/20**	**Thu 22/07/21**	**100%**
2121	Chase Walls for Services	2 d	Tue 13/10/20	Wed 14/10/20	100%
2122	Frame Ceilings	4 d	Thu 5/11/20	Mon 9/11/20	100%
2123	Patch \ Make Good Walls	3 d	Fri 8/01/21	Mon 11/01/21	100%
2124	Consultant Inspections Before Closing	1 d	Tue 17/11/20	Tue 17/11/20	100%
2125	Sheet & Close Plasterboard Ceilings	2 d	Wed 18/11/20	Thu 19/11/20	100%
2126	Set & Sand Ceilings & Bulkheads	3 d	Fri 20/11/20	Mon 23/11/20	100%
2127	Paint - 1st Coat	2 d	Mon 28/06/21	Tue 29/06/21	100%
2128	Defects Inspection & Patch	1 d	Wed 30/06/21	Wed 30/06/21	100%
2129	Install Joinery	1 d	Thu 1/07/21	Thu 1/07/21	100%
2130	Paint - 2nd Coat	2 d	Fri 2/07/21	Mon 5/07/21	100%
2131	Paint - 3rd Coat	2 d	Tue 6/07/21	Wed 7/07/21	100%
2132	Lay Timber Flooring	4 d	Thu 8/07/21	Tue 13/07/21	100%
2133	Fitoff Services	1 d	Wed 14/07/21	Wed 14/07/21	100%
2134	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2135	**Magistrate Room**	**145 d**	**Thu 15/10/20**	**Wed 5/05/21**	**100%**
2136	Chase Walls for Services	1 d	Thu 15/10/20	Thu 15/10/20	100%
2137	Frame Ceilings	1 d	Tue 10/11/20	Tue 10/11/20	100%
2138	Patch \ Make Good Walls	2 d	Tue 12/01/21	Wed 13/01/21	100%
2139	Consultant Inspections Before Closing	1 d	Wed 11/11/20	Wed 11/11/20	100%
2140	Sheet & Close Plasterboard Ceilings	1 d	Thu 12/11/20	Thu 12/11/20	100%
2141	Set & Sand Ceilings & Bulkheads	3 d	Fri 13/11/20	Mon 16/11/20	100%
2142	Paint - 1st Coat	2 d	Tue 23/02/21	Wed 24/02/21	100%
2143	Defects Inspection & Patch	1 d	Thu 25/02/21	Thu 25/02/21	100%
2144	Paint - 2nd Coat	1 d	Fri 9/04/21	Fri 9/04/21	100%
2145	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2146	Lay Carpet Flooring	1 d	Tue 4/05/21	Tue 4/05/21	100%
2147	Fitoff Services	1 d	Wed 5/05/21	Wed 5/05/21	100%
2148	**Library**	**198 d**	**Fri 16/10/20**	**Thu 22/07/21**	**100%**
2149	Chase Walls for Services	1 d	Fri 16/10/20	Fri 16/10/20	100%
2150	Frame Ceilings	2 d	Fri 8/01/21	Sat 9/01/21	100%
2151	Patch \ Make Good Walls	4 d	Thu 14/01/21	Mon 18/01/21	100%
2152	Consultant Inspections Before Closing	1 d	Wed 20/01/21	Wed 20/01/21	100%
2153	Sheet and Close Plasterboard Ceilings\ Cornice	2 d	Thu 21/01/21	Fri 22/01/21	100%
2154	Set & Sand Ceilings & Bulkheads	3 d	Wed 27/01/21	Fri 29/01/21	100%
2155	Paint - 1st Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
2156	Defects Inspection & Patch	1 d	Mon 1/03/21	Mon 1/03/21	100%
2157	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2158	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
2159	Lay Carpet Flooring	2 d	Wed 5/05/21	Thu 6/05/21	100%
2160	Fitoff Services	1 d	Fri 7/05/21	Fri 7/05/21	100%
2161	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2162	**Lift Lobby**	**171 d**	**Fri 13/11/20**	**Mon 19/07/21**	**100%**
2163	Chase Walls for Services	1 d	Sat 30/01/21	Sat 30/01/21	100%
2164	Frame Ceilings	1 d	Fri 13/11/20	Fri 13/11/20	100%
2165	Patch \ Make Good Walls	2 d	Mon 1/02/21	Tue 2/02/21	100%
2166	Consultant Inspections Before Closing	1 d	Mon 3/05/21	Mon 3/05/21	100%
2167	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Tue 4/05/21	Tue 4/05/21	100%
2168	Set & Sand Ceilings & Bulkheads	3 d	Wed 5/05/21	Fri 7/05/21	100%
2169	Paint - 1st Coat	2 d	Mon 10/05/21	Tue 11/05/21	100%
2170	Defects Inspection & Patch	1 d	Wed 12/05/21	Wed 12/05/21	100%

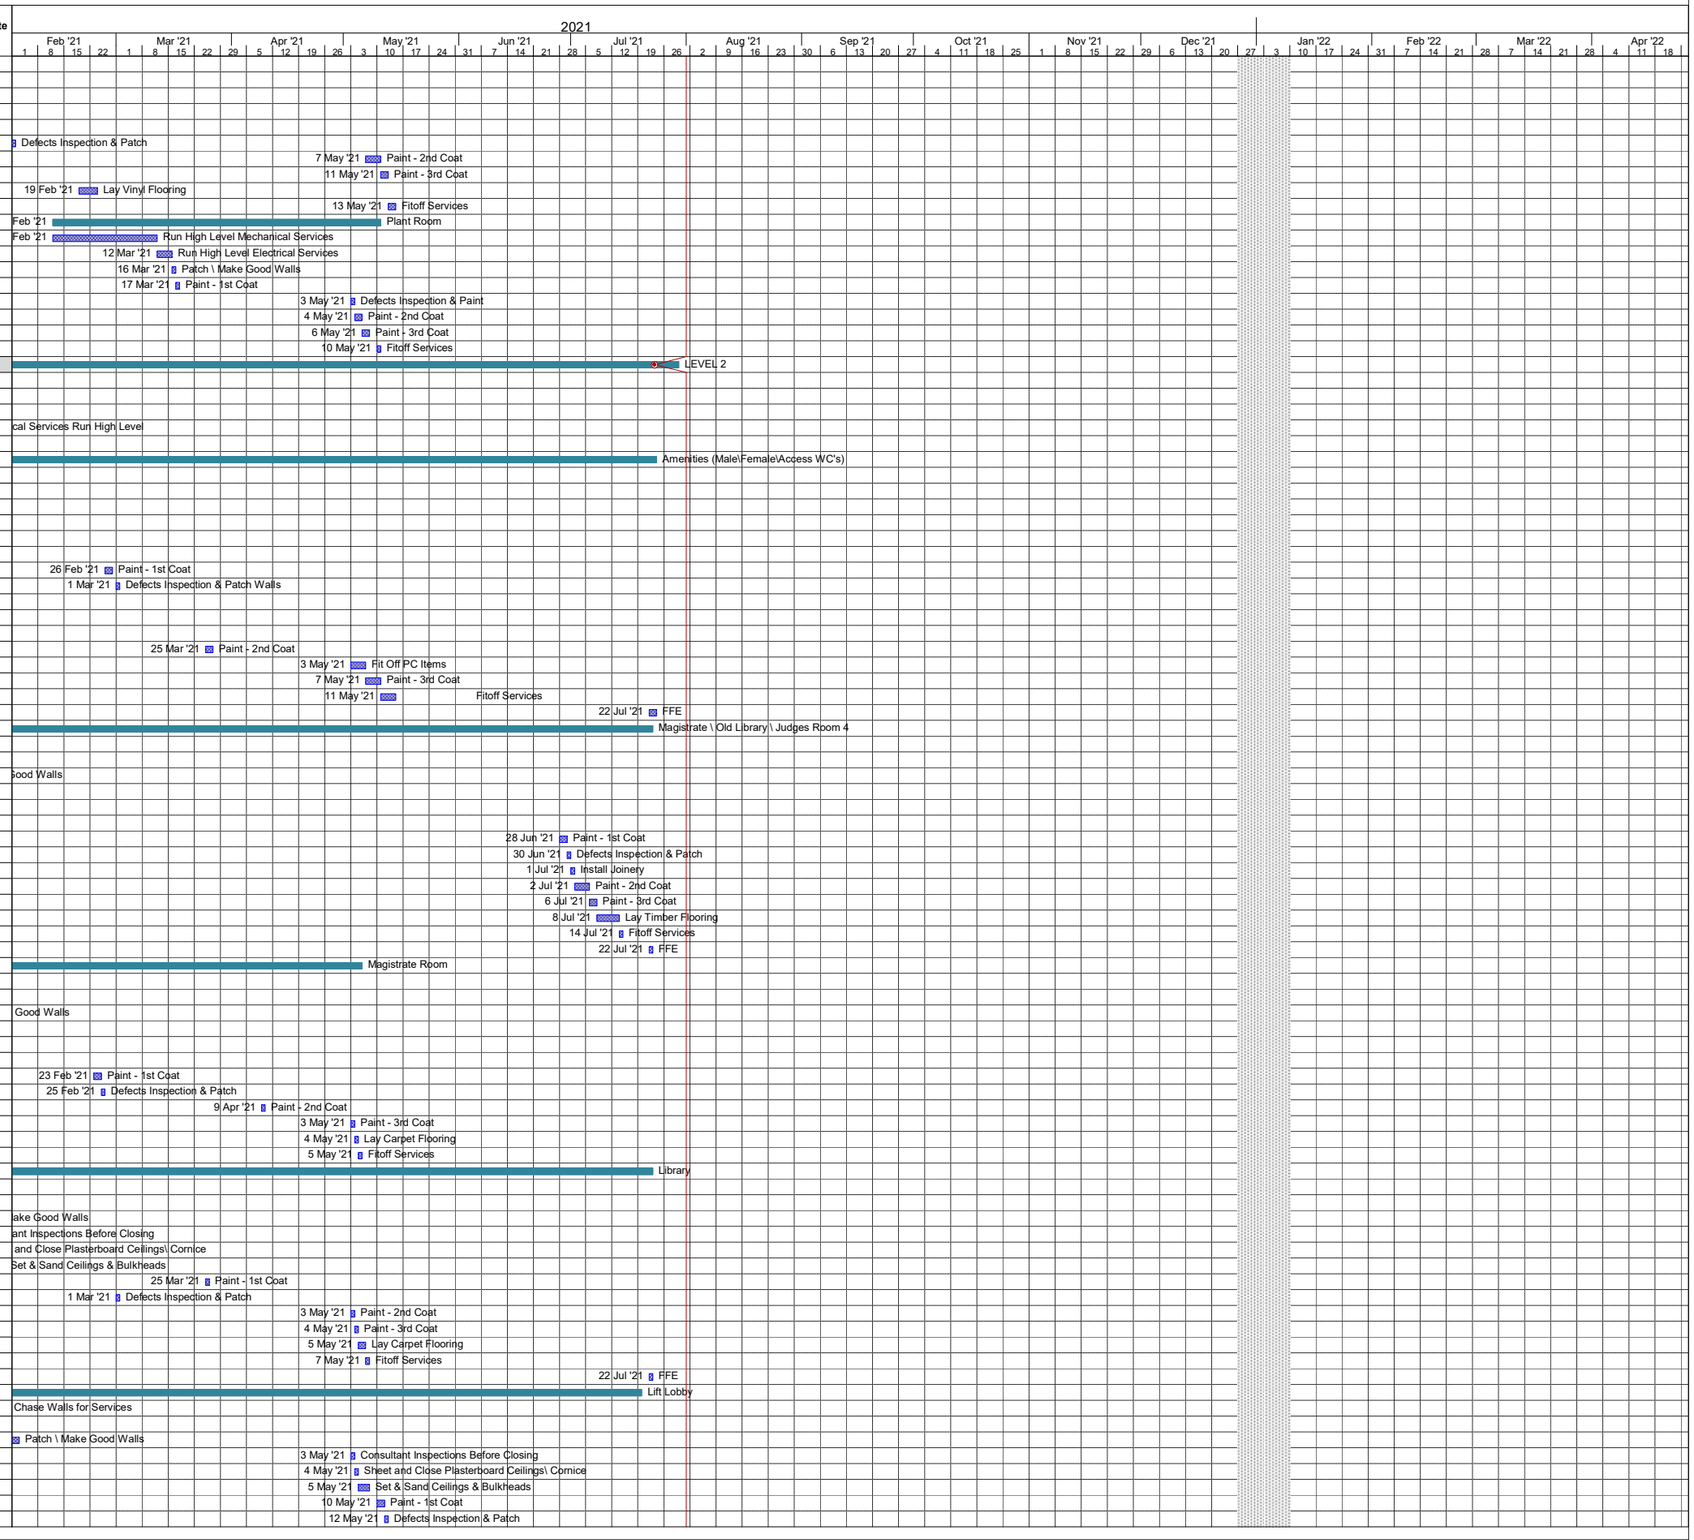


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
2171	Paint - 2nd Coat	1 d	Thu 13/05/21	Thu 13/05/21	100%
2172	Paint - 3rd Coat	1 d	Fri 14/05/21	Fri 14/05/21	100%
2173	Lay Carpet Flooring	1 d	Mon 19/07/21	Mon 19/07/21	100%
2174	Fitoff Services	1 d	Tue 29/06/21	Tue 29/06/21	100%
2175	**Corridor 7**	**179 d**	**Mon 19/10/20**	**Tue 29/06/21**	**100%**
2176	Chase Walls for Services	1 d	Mon 19/10/20	Mon 19/10/20	100%
2177	Patch \ Make Good Walls	6 d	Wed 3/02/21	Tue 9/02/21	100%
2178	Paint - 1st Coat	2 d	Thu 8/04/21	Fri 9/04/21	100%
2179	Defects Inspection & Patch	2 d	Mon 3/05/21	Tue 4/05/21	100%
2180	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
2181	Paint - 3rd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2182	Lay Carpet Flooring	3 d	Tue 18/05/21	Thu 20/05/21	100%
2183	Fitoff Services	2 d	Mon 28/06/21	Tue 29/06/21	100%
2184	**Office Room \ Remote Witness**	**155 d**	**Wed 9/12/20**	**Thu 22/07/21**	**100%**
2185	Chase Walls for Services	1 d	Wed 9/12/20	Wed 9/12/20	100%
2186	Frame Ceilings	1 d	Fri 8/01/21	Fri 8/01/21	100%
2187	Patch \ Make Good Walls	4 d	Thu 21/01/21	Thu 28/01/21	100%
2188	Consultant Inspections Before Closing	1 d	Wed 20/01/21	Wed 20/01/21	100%
2189	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Thu 28/01/21	Thu 28/01/21	100%
2190	Set & Sand Ceilings & Bulkheads	1 d	Fri 29/01/21	Fri 29/01/21	100%
2191	Paint - 1st Coat	1 d	Wed 3/03/21	Wed 3/03/21	100%
2192	Defects Inspection & Patch	1 d	Thu 11/03/21	Thu 11/03/21	100%
2193	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
2194	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2195	Lay Carpet Flooring	1 d	Tue 18/05/21	Tue 18/05/21	100%
2196	Fitoff Services	1 d	Wed 19/05/21	Wed 19/05/21	100%
2197	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2198	**Conserved Judge Room**	**139 d**	**Fri 8/01/21**	**Thu 22/07/21**	**100%**
2199	Chase Walls for Services	3 d	Fri 8/01/21	Mon 11/01/21	100%
2200	Frame Ceilings	1 d	Sat 9/01/21	Sat 9/01/21	100%
2201	Patch \ Make Good Walls	2 d	Fri 29/01/21	Sat 30/01/21	100%
2202	Consultant Inspections Before Closing	1 d	Wed 20/01/21	Wed 20/01/21	100%
2203	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Fri 29/01/21	Fri 29/01/21	100%
2204	Set & Sand Ceilings & Bulkheads	3 d	Sat 30/01/21	Tue 2/02/21	100%
2205	Paint - 1st Coat	2 d	Thu 11/03/21	Fri 12/03/21	100%
2206	Defects Inspection & Patch	1 d	Mon 15/03/21	Mon 15/03/21	100%
2207	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
2208	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2209	Lay Carpet Flooring	1 d	Wed 19/05/21	Wed 19/05/21	100%
2210	Fitoff Services	1 d	Thu 20/05/21	Thu 20/05/21	100%
2211	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2212	**Lecture Hall**	**124 d**	**Fri 8/01/21**	**Thu 1/07/21**	**100%**
2213	Erect Birdcage Scaffold	4 d	Fri 8/01/21	Tue 12/01/21	100%
2214	Substrate Repairs to Lantern and Ceiling	10 d	Sat 30/01/21	Wed 10/02/21	100%
2215	Paint - 1st Coat to Soffit	18 d	Sat 20/02/21	Fri 12/03/21	100%
2216	Defects Inspection & Patch	4 d	Mon 15/03/21	Thu 18/03/21	100%
2217	Paint - 2nd Coat to Soffit	4 d	Fri 19/03/21	Wed 24/03/21	100%
2218	Reinstall Globe Lighting Units	5 d	Mon 3/05/21	Fri 7/05/21	100%
2219	Paint - 3rd Coat to Soffit	4 d	Thu 1/04/21	Fri 9/04/21	100%
2220	Dismantle & Remove Birdcage Scaffold	2 d	Mon 3/05/21	Tue 4/05/21	100%
2221	Patch \ Make Good Walls	5 d	Wed 5/05/21	Tue 11/05/21	100%
2222	Paint - 1st Coat	5 d	Wed 12/05/21	Tue 18/05/21	100%
2223	Defects Inspection & Patch	4 d	Wed 19/05/21	Mon 24/05/21	100%
2224	Paint - 2nd Coat	4 d	Tue 25/05/21	Fri 28/05/21	100%
2225	Paint - 3rd Coat	4 d	Mon 31/05/21	Thu 3/06/21	100%
2226	Lay Carpet Flooring	4 d	Mon 28/06/21	Thu 1/07/21	100%
2227	**Multi Purpose Hall**	**166 d**	**Wed 4/11/20**	**Wed 30/06/21**	**100%**
2228	Erect Birdcage Scaffold	4 d	Wed 4/11/20	Sat 7/11/20	100%
2229	Substrate Repairs to Ceiling	25 d	Sat 9/01/21	Wed 10/02/21	100%
2230	Frame & Sheet New Ceiling	6 d	Fri 30/04/21	Fri 7/05/21	100%
2231	Paint - 1st Coat to Soffit	3 d	Mon 10/05/21	Wed 12/05/21	100%
2232	Defects Inspection & Patch	2 d	Thu 13/05/21	Fri 14/05/21	100%
2233	Paint - 2nd Coat to Soffit	2 d	Mon 17/05/21	Tue 18/05/21	100%
2234	Reinstall Globe Lighting Units	5 d	Wed 19/05/21	Tue 25/05/21	100%
2235	Paint - 3rd Coat to Soffit	2 d	Wed 26/05/21	Thu 27/05/21	100%
2236	Dismantle & Remove Birdcage Scaffold	2 d	Fri 28/05/21	Mon 31/05/21	100%
2237	Patch \ Make Good Walls	5 d	Tue 1/06/21	Mon 7/06/21	100%
2238	Paint - 1st Coat	3 d	Tue 8/06/21	Thu 10/06/21	100%
2239	Defects Inspection & Patch	2 d	Fri 11/06/21	Wed 16/06/21	100%
2240	Paint - 2nd Coat	3 d	Thu 17/06/21	Mon 21/06/21	100%
2241	Paint - 3rd Coat	3 d	Tue 22/06/21	Thu 24/06/21	100%
2242	Lay Carpet Flooring	3 d	Mon 28/06/21	Wed 30/06/21	100%
2243	**Corridor 8 \ Northern Corridor**	**136 d**	**Fri 11/12/20**	**Tue 29/06/21**	**100%**
2244	Chase Walls for Services	1 d	Fri 11/12/20	Fri 11/12/20	100%
2245	Patch \ Make Good Walls	14 d	Wed 24/02/21	Thu 11/03/21	100%
2246	Paint - 1st Coat	2 d	Thu 25/03/21	Fri 26/03/21	100%
2247	Defects Inspection & Patch	2 d	Mon 3/05/21	Tue 4/05/21	100%
2248	Paint - 2nd Coat	2 d	Wed 5/05/21	Thu 6/05/21	100%
2249	Paint - 3rd Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2250	Lay Carpet Flooring	3 d	Thu 20/05/21	Mon 24/05/21	100%
2251	Fitoff Services	2 d	Mon 28/06/21	Tue 29/06/21	100%
2252	**Gallery**	**117 d**	**Wed 13/01/21**	**Mon 28/06/21**	**100%**
2253	Chase Walls for Services	3 d	Wed 13/01/21	Fri 15/01/21	100%
2254	Frame Ceilings	1 d	Sat 30/01/21	Sat 30/01/21	100%
2255	Patch \ Make Good Walls	5 d	Mon 1/02/21	Fri 5/02/21	100%
2256	Consultant Inspections Before Closing	1 d	Thu 11/03/21	Thu 11/03/21	100%
2257	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Tue 2/02/21	Tue 2/02/21	100%
2258	Set & Sand Ceilings & Bulkheads	3 d	Thu 11/03/21	Mon 15/03/21	100%
2259	Paint - 1st Coat	2 d	Thu 25/03/21	Fri 26/03/21	100%
2260	Defects Inspection & Patch	1 d	Mon 3/05/21	Mon 3/05/21	100%
2261	Paint - 2nd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
2262	Paint - 3rd Coat	1 d	Wed 5/05/21	Wed 5/05/21	100%
2263	Lay Carpet Flooring	1 d	Thu 6/05/21	Thu 6/05/21	100%

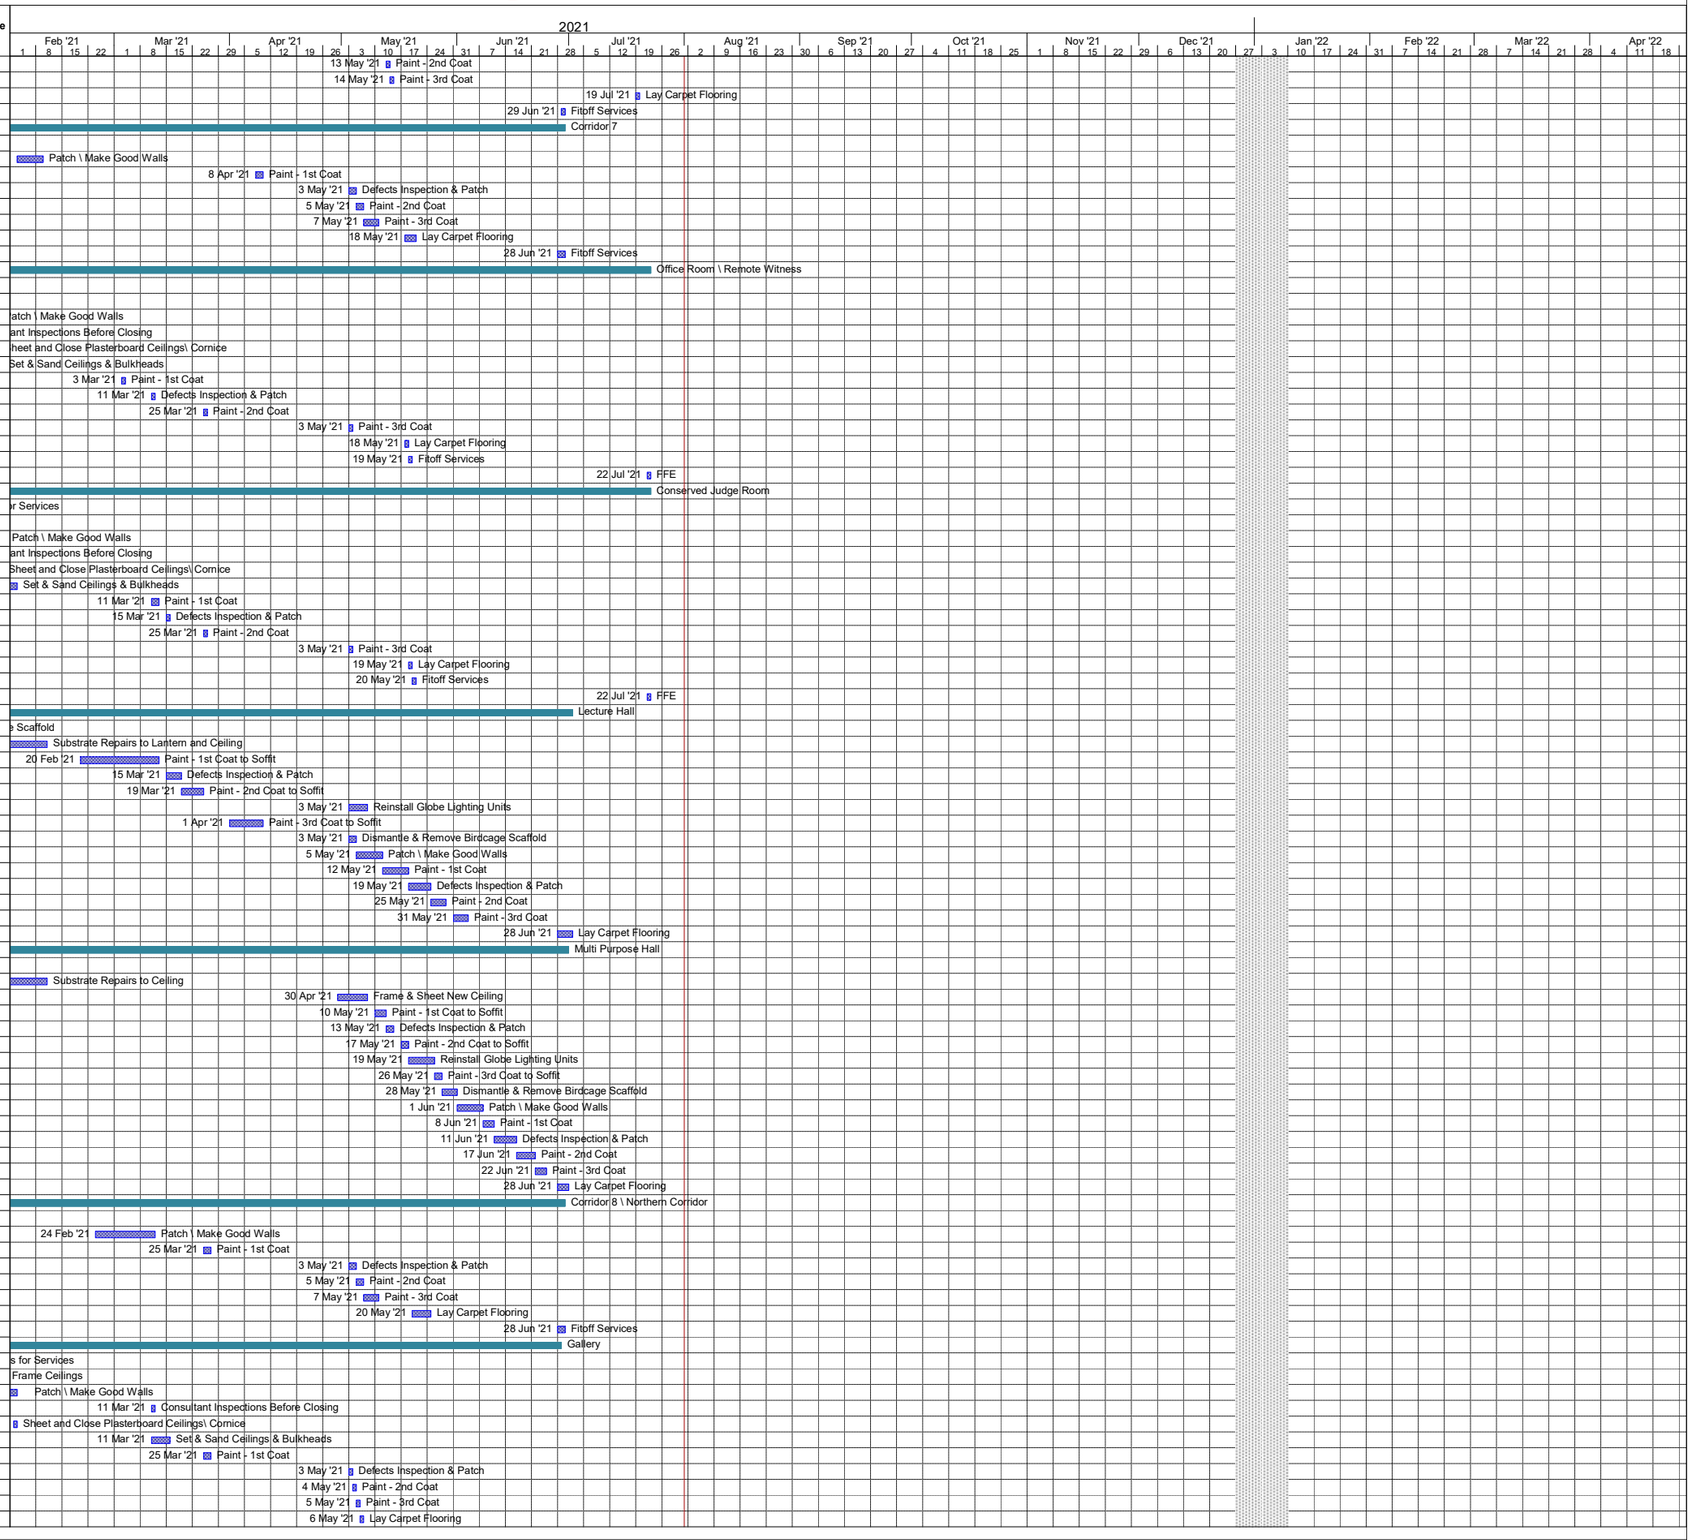


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.


ID	Task Name	Dur	Start	Finish	% Complete
2264	Fitoff Services	1 d	Mon 28/06/21	Mon 28/06/21	100%
2265	**Teacher's Room (Ex Lounge)**	**136 d**	**Tue 12/01/21**	**Thu 22/07/21**	**100%**
2266	Chase Walls for Services	2 d	Tue 12/01/21	Wed 13/01/21	100%
2267	Frame Ceilings	4 d	Mon 18/01/21	Thu 21/01/21	100%
2268	Patch \ Make Good Walls	4 d	Wed 20/01/21	Wed 27/01/21	100%
2269	Consultant Inspections Before Closing	1 d	Fri 22/01/21	Fri 22/01/21	100%
2270	Sheet and Close Plasterboard Ceilings\ Cornice	2 d	Wed 27/01/21	Thu 28/01/21	100%
2271	Set & Sand Ceilings & Bulkheads	4 d	Fri 29/01/21	Tue 2/02/21	100%
2272	Paint - 1st Coat	1 d	Sat 27/02/21	Sat 27/02/21	100%
2273	Defects Inspection & Patch	1 d	Thu 11/03/21	Thu 11/03/21	100%
2274	Paint - 2nd Coat	1 d	Thu 25/03/21	Thu 25/03/21	100%
2275	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2276	Lay Carpet Flooring	2 d	Tue 4/05/21	Wed 5/05/21	100%
2277	Fitoff Services	1 d	Tue 4/05/21	Tue 4/05/21	100%
2278	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2279	**Kitchenette**	**134 d**	**Thu 14/01/21**	**Thu 22/07/21**	**100%**
2280	Patch \ Make Good Walls	15 d	Tue 23/02/21	Thu 11/03/21	100%
2281	Chase Walls for Services	1 d	Thu 14/01/21	Thu 14/01/21	100%
2282	Frame Ceilings	1 d	Sat 30/01/21	Sat 30/01/21	100%
2283	Consultant Inspections Before Closing	1 d	Mon 1/02/21	Mon 1/02/21	100%
2284	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Tue 2/02/21	Tue 2/02/21	100%
2285	Set & Sand Ceilings & Bulkheads	3 d	Wed 3/02/21	Fri 5/02/21	100%
2286	Paint - 1st Coat	2 d	Thu 25/03/21	Fri 26/03/21	100%
2287	Defects Inspection & Patch	1 d	Mon 29/03/21	Mon 29/03/21	100%
2288	Paint - 2nd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2289	Paint - 3rd Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
2290	Lay Timber Flooring	1 d	Thu 6/05/21	Thu 6/05/21	100%
2291	Fitoff Services	1 d	Wed 5/05/21	Wed 5/05/21	100%
2292	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2293	**Corridor 6 & 9**	**120 d**	**Sat 30/01/21**	**Mon 19/07/21**	**100%**
2294	Chase Walls for Services	2 d	Sat 30/01/21	Mon 1/02/21	100%
2295	Patch \ Make Good Walls	6 d	Fri 12/03/21	Fri 19/03/21	100%
2296	Frame Ceilings	1 d	Thu 25/03/21	Thu 25/03/21	100%
2297	Consultant Inspections Before Closing	1 d	Fri 26/03/21	Fri 26/03/21	100%
2298	Sheet and Close Plasterboard Ceilings\ Cornice	1 d	Mon 29/03/21	Mon 29/03/21	100%
2299	Set & Sand Ceilings & Bulkheads	3 d	Mon 3/05/21	Wed 5/05/21	100%
2300	Paint - 1st Coat	2 d	Thu 6/05/21	Fri 7/05/21	100%
2301	Defects Inspection & Patch	1 d	Mon 10/05/21	Mon 10/05/21	100%
2302	Paint - 2nd Coat	1 d	Tue 11/05/21	Tue 11/05/21	100%
2303	Paint - 3rd Coat	1 d	Wed 12/05/21	Wed 12/05/21	100%
2304	Lay Carpet Flooring	1 d	Thu 13/05/21	Thu 13/05/21	100%
2305	Fitoff Services	1 d	Mon 19/07/21	Mon 19/07/21	100%
2306	**Lobby Lvl 1, 2 & 3**	**78 d**	**Fri 26/03/21**	**Thu 22/07/21**	**100%**
2307	Frame Ceilings	4 d	Fri 26/03/21	Wed 31/03/21	100%
2308	Patch \ Make Good Walls	5 d	Mon 3/05/21	Fri 7/05/21	100%
2309	Consultant Inspections Before Closing	1 d	Thu 1/04/21	Thu 1/04/21	100%
2310	Sheet and Close Plasterboard Ceilings\ Cornice	3 d	Wed 7/04/21	Fri 9/04/21	100%
2311	Set & Sand Ceilings & Bulkheads	3 d	Mon 12/04/21	Wed 14/04/21	100%
2312	Paint - 1st Coat	4 d	Mon 10/05/21	Thu 13/05/21	100%
2313	Defects Inspection & Patch	2 d	Fri 14/05/21	Mon 17/05/21	100%
2314	Paint - 2nd Coat	5 d	Tue 18/05/21	Mon 24/05/21	100%
2315	Paint - 3rd Coat	5 d	Tue 25/05/21	Mon 31/05/21	100%
2316	Lay Floor Finishes	4 d	Mon 19/07/21	Thu 22/07/21	100%
2317	Fitoff Services	4 d	Fri 2/07/21	Wed 7/07/21	100%
2318	**Entrance**	**74 d**	**Tue 13/04/21**	**Thu 29/07/21**	**86%**
2319	Patch \ Make Good Walls	5 d	Mon 10/05/21	Fri 14/05/21	100%
2320	Frame Ceilings	2 d	Tue 13/04/21	Wed 14/04/21	100%
2321	Consultant Inspections Before Closing	1 d	Thu 15/04/21	Thu 15/04/21	100%
2322	Sheet and Close Plasterboard Ceilings\ Cornice	2 d	Fri 16/04/21	Mon 19/04/21	100%
2323	Set & Sand Ceilings & Bulkheads	4 d	Tue 20/04/21	Fri 23/04/21	100%
2324	Paint - 1st Coat	5 d	Mon 17/05/21	Fri 21/05/21	100%
2325	Defects Inspection & Patch	2 d	Mon 24/05/21	Tue 25/05/21	100%
2326	Paint - 2nd Coat	4 d	Wed 26/05/21	Mon 31/05/21	100%
2327	Paint - 3rd Coat	4 d	Tue 1/06/21	Fri 4/06/21	100%
2328	Fitoff Services	1 d	Mon 19/07/21	Mon 19/07/21	100%
2329	Repair \ Deep Clean Existing Tiles	5 d	Fri 23/07/21	Thu 29/07/21	0%
2330	**LEVEL 3**	**106 d**	**Sat 30/01/21**	**Tue 29/06/21**	**100%**
2331	Hydraulic Services Run High Level \ Chase Walls	6 d	Sat 30/01/21	Fri 5/02/21	100%
2332	Mechanical Services Run High Level	6 d	Thu 4/02/21	Wed 10/02/21	100%
2333	Electrical Services (Lights\power\fire\security\comms) Run High Leve	10 d	Tue 9/02/21	Fri 19/02/21	100%
2334	**Stair B2**	**39 d**	**Mon 3/05/21**	**Mon 28/06/21**	**100%**
2335	Patch \ Make Good Walls	4 d	Mon 3/05/21	Thu 6/05/21	100%
2336	Paint - 1st Coat	2 d	Fri 7/05/21	Mon 10/05/21	100%
2337	Defects Inspection & Patch	1 d	Tue 11/05/21	Tue 11/05/21	100%
2338	Paint - 2nd Coat	1 d	Wed 12/05/21	Wed 12/05/21	100%
2339	Paint - 3rd Coat	1 d	Thu 13/05/21	Thu 13/05/21	100%
2340	Fitoff Services	1 d	Fri 14/05/21	Fri 14/05/21	100%
2341	Lay Carpet Flooring	1 d	Mon 28/06/21	Mon 28/06/21	100%
2342	**Staff Room / Guest Room**	**78 d**	**Wed 3/03/21**	**Mon 28/06/21**	**100%**
2343	Patch \ Make Good Walls	6 d	Wed 3/03/21	Tue 9/03/21	100%
2344	Repair Existing Windows\Architraves	2.5 d	Wed 10/03/21	Fri 12/03/21	100%
2345	Paint - 1st Coat	2 d	Mon 3/05/21	Tue 4/05/21	100%
2346	Defects Inspection & Patch	1 d	Wed 5/05/21	Wed 5/05/21	100%
2347	Paint - 2nd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%
2348	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
2349	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
2350	Lay Carpet Flooring	1 d	Mon 28/06/21	Mon 28/06/21	100%
2351	**Kitchen / Beverage Bay**	**61 d**	**Thu 25/03/21**	**Mon 28/06/21**	**100%**
2352	Patch \ Make Good Walls	2 d	Thu 25/03/21	Fri 26/03/21	100%
2353	Repair Existing Windows\Architraves	1 d	Mon 3/05/21	Mon 3/05/21	100%
2354	Paint - 1st Coat	1 d	Tue 4/05/21	Tue 4/05/21	100%
2355	Defects Inspection & Patch	1 d	Wed 5/05/21	Wed 5/05/21	100%
2356	Paint - 2nd Coat	1 d	Thu 6/05/21	Thu 6/05/21	100%

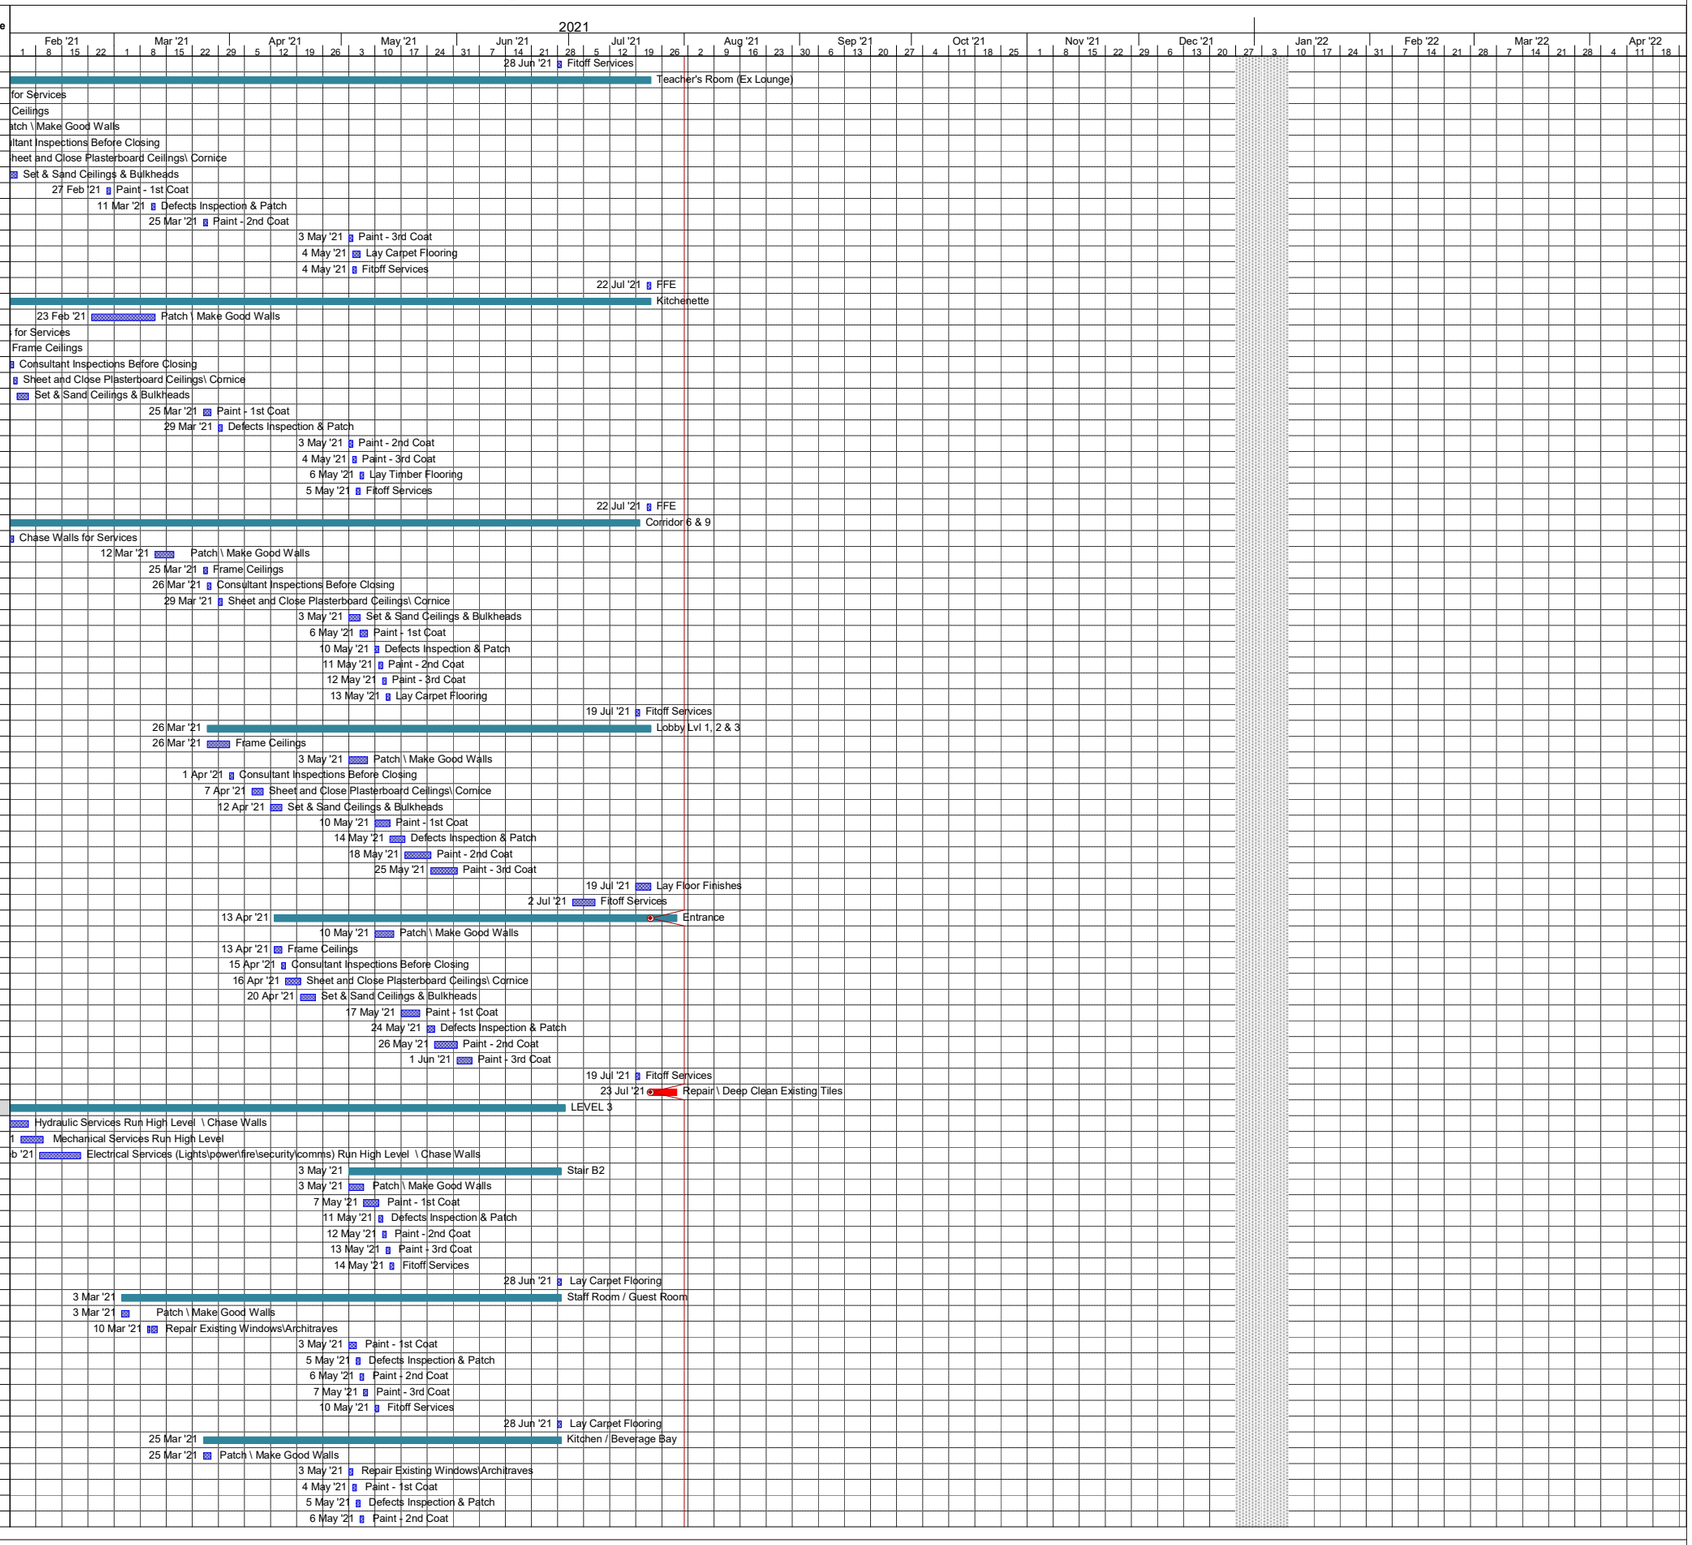

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
2357	Paint - 3rd Coat	1 d	Fri 7/05/21	Fri 7/05/21	100%
2358	Fitoff Services	1 d	Mon 10/05/21	Mon 10/05/21	100%
2359	Lay Timber Flooring	1 d	Mon 28/06/21	Mon 28/06/21	100%
2360	**Gallery**	**39 d**	**Mon 3/05/21**	**Mon 28/06/21**	**100%**
2361	Patch \ Make Good Walls	5 d	Mon 3/05/21	Fri 7/05/21	100%
2362	Paint - 1st Coat	1 d	Mon 10/05/21	Mon 10/05/21	100%
2363	Defects Inspection & Patch	1 d	Tue 11/05/21	Tue 11/05/21	100%
2364	Paint - 2nd Coat	1 d	Wed 12/05/21	Wed 12/05/21	100%
2365	Paint - 3rd Coat	1 d	Thu 13/05/21	Thu 13/05/21	100%
2366	Fitoff Services	1 d	Fri 14/05/21	Fri 14/05/21	100%
2367	Lay Carpet Flooring	1 d	Mon 28/06/21	Mon 28/06/21	100%
2368	**Store**	**34 d**	**Mon 10/05/21**	**Mon 28/06/21**	**100%**
2369	Patch \ Make Good Walls	2 d	Mon 10/05/21	Tue 11/05/21	100%
2370	Repair Existing Windows\Architraves	1 d	Wed 12/05/21	Wed 12/05/21	100%
2371	Paint - 1st Coat	2 d	Thu 13/05/21	Fri 14/05/21	100%
2372	Defects Inspection & Patch	1 d	Mon 17/05/21	Mon 17/05/21	100%
2373	Paint - 2nd Coat	1 d	Tue 18/05/21	Tue 18/05/21	100%
2374	Paint - 3rd Coat	1 d	Wed 19/05/21	Wed 19/05/21	100%
2375	Fitoff Services	1 d	Thu 20/05/21	Thu 20/05/21	100%
2376	Lay Carpet Flooring	1 d	Mon 28/06/21	Mon 28/06/21	100%
2377	**Lobby**	**33 d**	**Wed 12/05/21**	**Tue 29/06/21**	**100%**
2378	Patch \ Make Good Walls	5 d	Wed 12/05/21	Tue 18/05/21	100%
2379	Repair Existing Windows\Architraves	6 d	Wed 19/05/21	Wed 26/05/21	100%
2380	Paint - 1st Coat	6 d	Thu 27/05/21	Thu 3/06/21	100%
2381	Defects Inspection & Patch	2 d	Fri 4/06/21	Mon 7/06/21	100%
2382	Paint - 2nd Coat	2 d	Tue 8/06/21	Wed 9/06/21	100%
2383	Paint - 3rd Coat	2 d	Thu 10/06/21	Fri 11/06/21	100%
2384	Fitoff Services	2 d	Wed 16/06/21	Thu 17/06/21	100%
2385	Lay Carpet Flooring	2 d	Mon 28/06/21	Tue 29/06/21	100%
2386	**LEVEL 4**	**82 d**	**Sat 27/03/21**	**Thu 29/07/21**	**99%**
2387	**Maintenance Access Room**	**23 d**	**Sat 27/03/21**	**Wed 5/05/21**	**100%**
2388	Patch \ Make Good Walls	4 d	Sat 27/03/21	Thu 1/04/21	100%
2389	Repair Existing Windows\Architraves	4 d	Wed 7/04/21	Mon 12/04/21	100%
2390	Paint - 1st Coat	2 d	Tue 13/04/21	Wed 14/04/21	100%
2391	Defects Inspection & Patch	2 d	Thu 15/04/21	Fri 16/04/21	100%
2392	Paint - 2nd Coat	1 d	Thu 15/04/21	Thu 15/04/21	100%
2393	Paint - 3rd Coat	1 d	Mon 3/05/21	Mon 3/05/21	100%
2394	Fitoff Services	1 d	Tue 4/05/21	Tue 4/05/21	100%
2395	New Floor Finishes	1 d	Wed 5/05/21	Wed 5/05/21	100%
2396	*Heritage Building Finishes Complete*	*0 d*	*Thu 29/07/21*	*Thu 29/07/21*	*0%*
2397	**VERTICAL TRANSPORTATION**	**148 d**	**Mon 11/01/21**	**Fri 6/08/21**	**95%**
2398	**LIFTS 1&2 RESIDENTIAL MRLS (Serving L1 to L4)**	**53 d**	**Mon 11/01/21**	**Wed 17/03/21**	**100%**
2399	Lift Pit & Shaft works	6 wks	Mon 11/01/21	Wed 17/02/21	100%
2400	Commissioning \ Handover to Built	15 d	Sat 27/02/21	Wed 17/03/21	100%
2401	**LIFT 3 EDUCATIONAL MRLS (Serving L1 to L4)**	**75 d**	**Mon 8/02/21**	**Mon 24/05/21**	**100%**
2402	Lift Pit & Shaft works	8 wks	Mon 8/02/21	Mon 29/03/21	100%
2403	Commissioning \ Handover to Built	5 d	Tue 18/05/21	Mon 24/05/21	100%
2404	**ACCESS LIFT TO ATRIUM LEVEL**	**5 d**	**Mon 2/08/21**	**Fri 6/08/21**	**0%**
2405	Lift Installation	3 d	Mon 2/08/21	Wed 4/08/21	0%
2406	Commissioning \ Handover to Built	2 d	Thu 5/08/21	Fri 6/08/21	0%
2407	**SERVICES TESTING & COMMISSIONING**	**18 d**	**Thu 8/07/21**	**Mon 2/08/21**	**93%**
2408	Courthouse Building	17 d	Thu 8/07/21	Fri 30/07/21	95%
2409	Residential Building	16 d	Fri 9/07/21	Fri 30/07/21	95%
2410	Education Building	16 d	Fri 9/07/21	Fri 30/07/21	95%
2411	Integrated System Testing	1 d	Mon 2/08/21	Mon 2/08/21	0%
2412	**CHURCH STREET CIVIL WORKS**	**129 d**	**Tue 2/02/21**	**Wed 4/08/21**	**93%**
2413	**CHURCH STREET FOOTPATH & ENTRY WORKS**	**5 d**	**Tue 2/02/21**	**Mon 8/02/21**	**100%**
2414	*Close Church Street Footpath*	*0 d*	*Tue 2/02/21*	*Tue 2/02/21*	*100%*
2415	Install 'A' Class Hoarding	2 d	Wed 3/02/21	Thu 4/02/21	100%
2416	Remove 'B' Class Hoarding	3 d	Fri 5/02/21	Mon 8/02/21	100%
2417	**EXISTING SERVICES**	**60 d**	**Fri 19/02/21**	**Mon 17/05/21**	**100%**
2418	**AUSGRID \ GIANT**	**60 d**	**Fri 19/02/21**	**Mon 17/05/21**	**100%**
2419	Landing Kiosk Substation	1 d	Fri 19/02/21	Fri 19/02/21	100%
2420	Trench Excavation - Station 3 - 4 (Bldg C to B)	5 d	Sat 20/02/21	Thu 25/02/21	100%
2421	Trench Excavation - Station 4 - 2 (Bldg B to A)	5 d	Fri 26/02/21	Wed 3/03/21	100%
2422	Conduit & Cabling from Station 2 - 3	3 d	Thu 4/03/21	Sat 6/03/21	100%
2423	Cabling to Kiosk Substation	5 d	Mon 8/03/21	Fri 12/03/21	100%
2424	*Earthing to Kiosk Substation*	*0 d*	*Sat 13/03/21*	*Sat 13/03/21*	*100%*
2425	Ausgrid Outage Booking Period	11.6 wks	Mon 22/02/21	Mon 17/05/21	100%
2426	*Final Connections & Terminations*	*0 d*	*Mon 17/05/21*	*Mon 17/05/21*	*100%*
2427	*Energisation of Kiosk Substation*	*0 d*	*Mon 17/05/21*	*Mon 17/05/21*	*100%*
2428	*Permanent Power Available*	*0 d*	*Mon 17/05/21*	*Mon 17/05/21*	*100%*
2429	**TPG NBN**	**47 d**	**Fri 5/03/21**	**Fri 14/05/21**	**100%**
2430	Replace Damaged Fibre to Police Station	1 d	Fri 5/03/21	Fri 5/03/21	100%
2431	Re-route Xtg Conduits\Cables	2 d	Mon 10/05/21	Tue 11/05/21	100%
2432	Raise Xtg Pit	1 d	Wed 12/05/21	Wed 12/05/21	100%
2433	Testing & Commissioning	1 d	Thu 13/05/21	Thu 13/05/21	100%
2434	Backfill & Compact	1 d	Fri 14/05/21	Fri 14/05/21	100%
2435	**TELSTRA**	**10 d**	**Mon 29/03/21**	**Wed 14/04/21**	**100%**
2436	Trench Excavation \ Expose Existing Conduits	3 d	Mon 29/03/21	Wed 31/03/21	100%
2437	Demolish \ Remove Redundant Pits	1 d	Thu 1/04/21	Thu 1/04/21	100%
2438	Reconstruct Pits \ Lower Xtg Pits	3 d	Wed 7/04/21	Fri 9/04/21	100%
2439	Realign Xtg Conduits \ Cables	2 d	Mon 12/04/21	Tue 13/04/21	100%
2440	Backfill & Compact	1 d	Wed 14/04/21	Wed 14/04/21	100%
2441	**NBN Co.**	**7 d**	**Thu 25/03/21**	**Wed 7/04/21**	**100%**
2442	Modifying Node & Pillar Plinths	2 d	Thu 25/03/21	Fri 26/03/21	100%
2443	Adjusting\Jointing Affected Cables	3 d	Mon 29/03/21	Wed 31/03/21	100%
2444	Testing & Commissioning	1 d	Thu 1/04/21	Thu 1/04/21	100%
2445	Backfill & Compact	1 d	Wed 7/04/21	Wed 7/04/21	100%
2446	**VOCUS NBN**	**11 d**	**Mon 3/05/21**	**Mon 17/05/21**	**100%**
2447	Supply & Install New Pits	1 d	Mon 3/05/21	Mon 3/05/21	100%
2448	Re-route Xtg Conduits\Cables	1 d	Tue 4/05/21	Tue 4/05/21	100%
2449	Raise Xtg Pit	1 d	Wed 5/05/21	Wed 5/05/21	100%

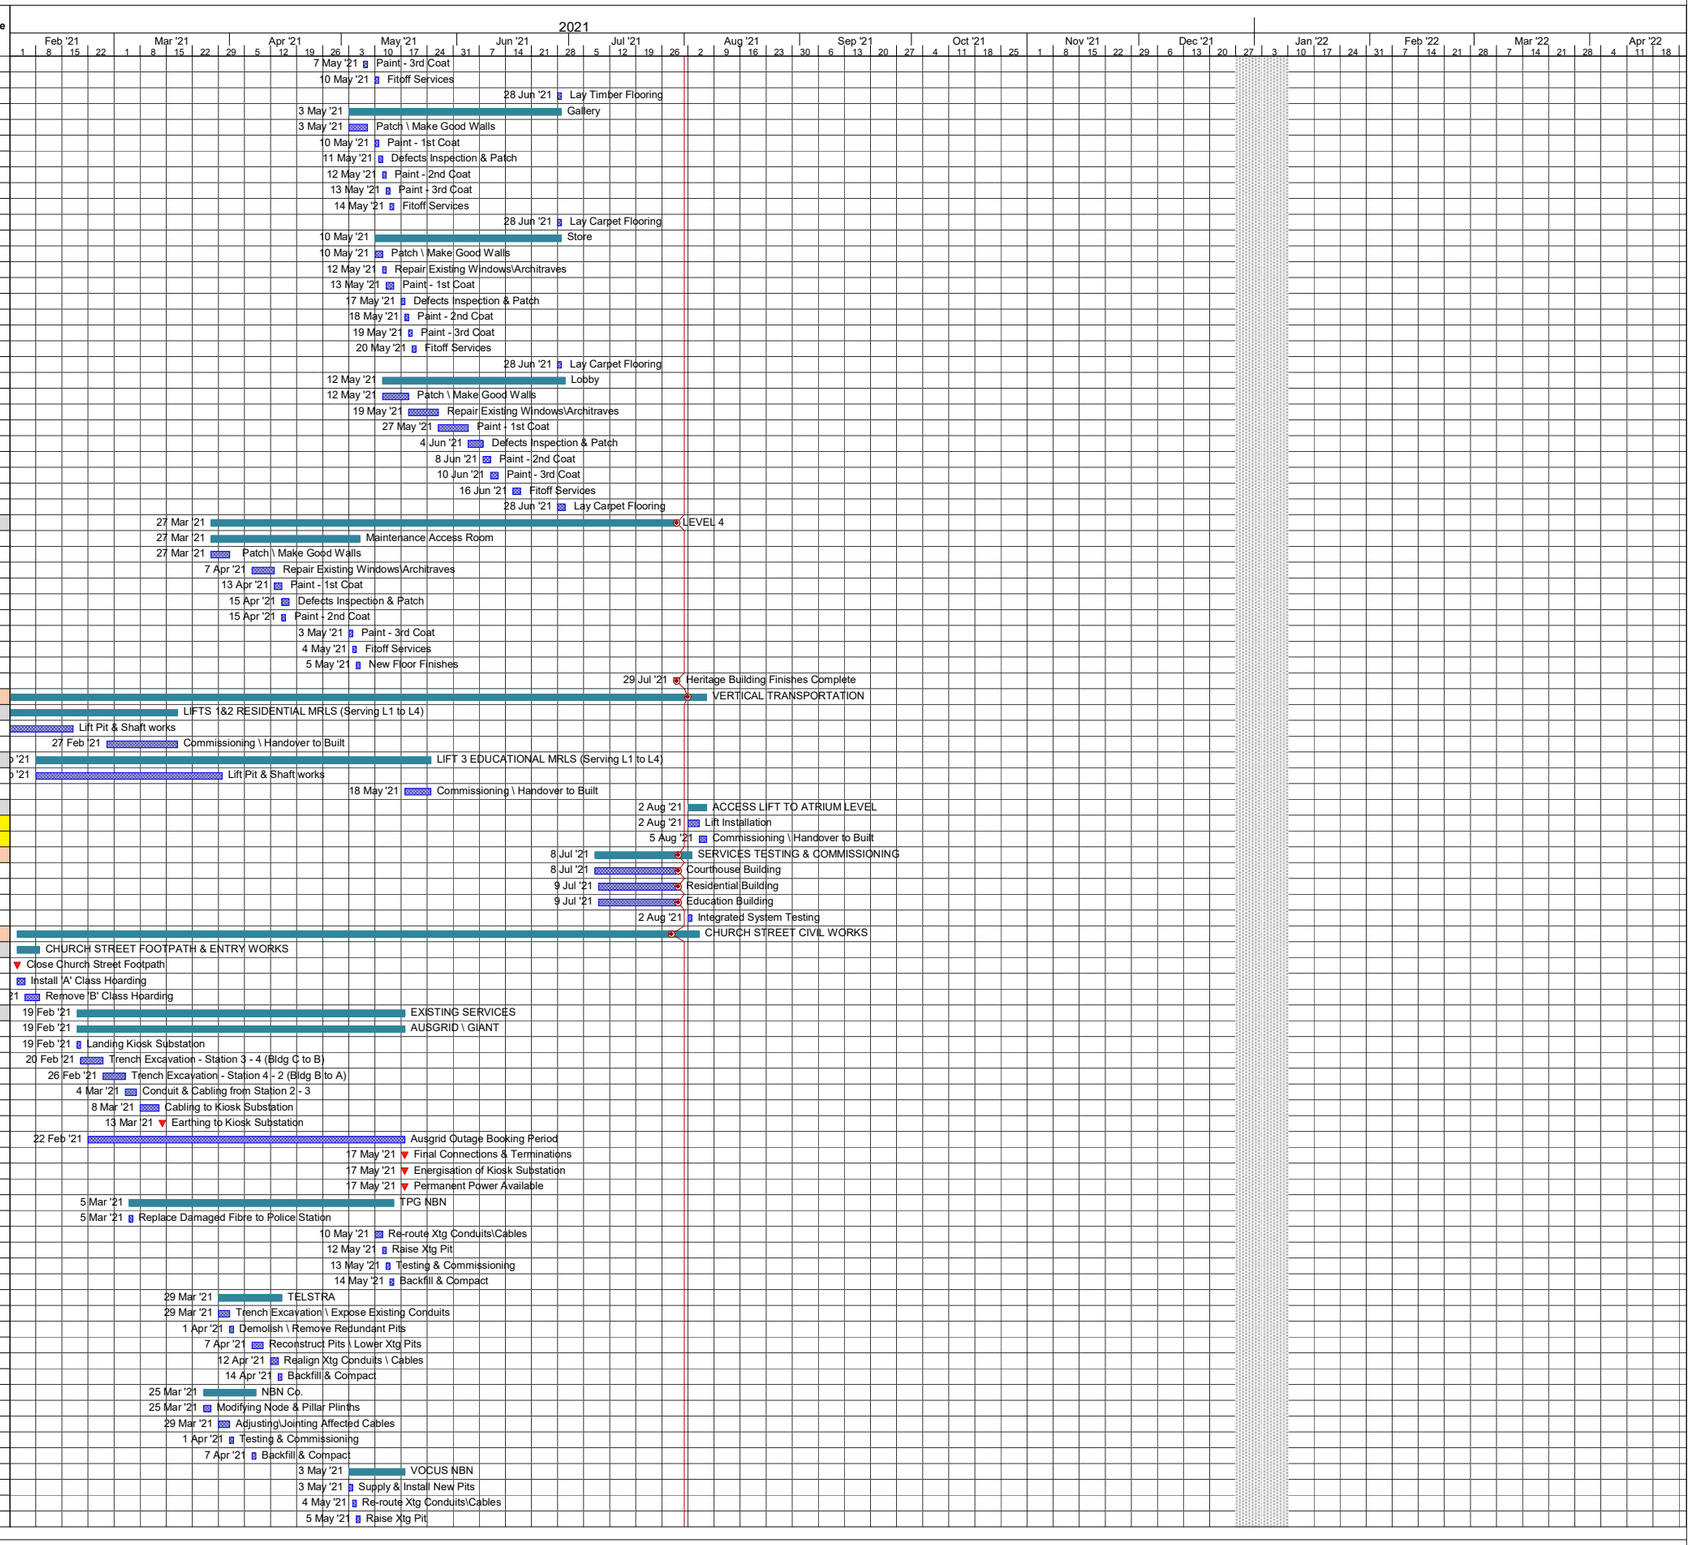


Critical Task — Non-critical — Milestone — Project Summary — Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
2450	New Fibre from Xtg to New Comms Room	5 d	Thu 6/05/21	Wed 12/05/21	100%
2451	Testing & Commissioning	1 d	Thu 13/05/21	Thu 13/05/21	100%
2452	Backfill & Compact	2 d	Fri 14/05/21	Mon 17/05/21	100%
2453	**S138 CIVIL WORKS**	**49 d**	**Thu 6/05/21**	**Thu 15/07/21**	**91%**
2454	**Church Street - South**	**62 d**	**Thu 6/05/21**	**Tue 3/08/21**	**89%**
2455	Demolish & Trim Existing Pavement & Kerb F1-D5	1 d	Thu 6/05/21	Thu 6/05/21	100%
2456	Excavate & Install Stormwater Pipe F1-D5	1 d	Fri 7/05/21	Fri 7/05/21	100%
2457	Construct New Pit D4	4 d	Mon 10/05/21	Thu 13/05/21	100%
2458	**Chainage 0 - 30**	**43 d**	**Wed 2/06/21**	**Tue 3/08/21**	**88%**
2459	Milling of Xtg Asphalt / Box Out to New Levels	1 d	Wed 2/06/21	Wed 2/06/21	100%
2460	Sub-Grade Preparation & Trim/Compact	1 d	Thu 3/06/21	Thu 3/06/21	100%
2461	Sub-Base & Trim/Compact	1 d	Fri 4/06/21	Fri 4/06/21	100%
2462	Sandstone Kerb Installation Inc Gutter / Laybacks	5 d	Mon 7/06/21	Fri 11/06/21	100%
2463	Box Out Footpath	3 d	Mon 28/06/21	Wed 30/06/21	100%
2464	Base Installation	2 d	Thu 1/07/21	Fri 2/07/21	100%
2465	Tree Pits Installation	1 d	Mon 5/07/21	Mon 5/07/21	100%
2466	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2467	**Chainage 30 - 60**	**31 d**	**Tue 22/06/21**	**Tue 3/08/21**	**87%**
2468	Milling of Xtg Asphalt / Box Out to New Levels	1 d	Tue 22/06/21	Tue 22/06/21	100%
2469	Sub-Grade Preparation & Trim/Compact	1 d	Wed 23/06/21	Wed 23/06/21	100%
2470	Sub-Base & Trim/Compact	1 d	Thu 24/06/21	Thu 24/06/21	100%
2471	Sandstone Kerb Installation Inc Gutter / Laybacks	4 d	Thu 24/06/21	Tue 29/06/21	100%
2472	Box Out Footpath	3 d	Thu 1/07/21	Mon 5/07/21	100%
2473	Base Installation	2 d	Tue 6/07/21	Wed 7/07/21	100%
2474	Relocate Sandstone Fountain	1 d	Thu 29/07/21	Thu 29/07/21	100%
2475	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2476	**Chainage 60 - 100**	**25 d**	**Wed 30/06/21**	**Tue 3/08/21**	**89%**
2477	Milling of Xtg Asphalt / Box Out to New Levels	2 d	Wed 30/06/21	Thu 1/07/21	100%
2478	Sub-Grade Preparation & Trim/Compact	2 d	Fri 2/07/21	Mon 5/07/21	100%
2479	Sub-Base & Trim/Compact	1 d	Tue 6/07/21	Tue 6/07/21	100%
2480	Sandstone Kerb Installation Inc Gutter / Laybacks	6 d	Wed 7/07/21	Wed 14/07/21	100%
2481	Box Out Footpath	2 d	Thu 15/07/21	Fri 16/07/21	100%
2482	Base Installation	3 d	Mon 19/07/21	Wed 21/07/21	100%
2483	Tree Pits Installation	1 d	Thu 22/07/21	Thu 22/07/21	100%
2484	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2485	**Church Street - North**	**8 d**	**Tue 20/07/21**	**Thu 29/07/21**	**100%**
2486	Demolish Existing Kerb E1-E2	1 d	Tue 20/07/21	Tue 20/07/21	100%
2487	Excavate & Install Stormwater Pipe to E2	1 d	Wed 21/07/21	Wed 21/07/21	100%
2488	Construct S/W Pits E1-E2	2 d	Thu 22/07/21	Fri 23/07/21	100%
2489	Sub-Grade Preparation E1-E2	1 d	Mon 26/07/21	Mon 26/07/21	100%
2490	Sub-Base E1-E2	1 d	Mon 26/07/21	Mon 26/07/21	100%
2491	Sandstone Kerb Installation Inc Gutter / Laybacks	2 d	Tue 27/07/21	Wed 28/07/21	100%
2492	Base Installation	1 d	Thu 29/07/21	Thu 29/07/21	100%
2493	**Church Street Asphalt**	**2 d**	**Mon 2/08/21**	**Tue 3/08/21**	**0%**
2494	Asphalt Pavement Works - Church Street	1 d	Mon 2/08/21	Mon 2/08/21	0%
2495	Pedestrian Xng/Island Concrete Works	1 d	Tue 3/08/21	Tue 3/08/21	0%
2496	**Heritage Works**	**16 d**	**Mon 12/07/21**	**Mon 2/08/21**	**81%**
2497	Heritage Palisade Fence_Concrete & Render Upstand - Bldg C Frontage	5 d	Mon 12/07/21	Fri 16/07/21	100%
2498	Heritage Palisade Fence_Sandstone Upstand - Bldg B Frontage	3 d	Thu 15/07/21	Mon 19/07/21	100%
2499	Heritage Palisade Fence_Sandstone Upstand - Bldg A Frontage	3 d	Thu 15/07/21	Mon 19/07/21	100%
2500	Heritage Palisade Fence_Palisade Fence - Bldg C Frontage	2 d	Fri 23/07/21	Mon 26/07/21	50%
2501	Heritage Palisade Fence_Palisade Fence - Bldg B Frontage	3 d	Tue 27/07/21	Thu 29/07/21	50%
2502	Heritage Palisade Fence_Palisade Fence - Bldg A Frontage	2 d	Fri 30/07/21	Mon 2/08/21	50%
2503	Heritage Brick Paving Pavement Reinstatement Ch0-30	3 d	Fri 16/07/21	Tue 20/07/21	100%
2504	Heritage Brick Paving Pavement Reinstatement Ch30-60	5 d	Mon 19/07/21	Fri 23/07/21	75%
2505	Heritage Brick Paving Pavement ReinstatementCh60-100	3 d	Wed 21/07/21	Fri 23/07/21	75%
2506	**Linemarking & Signage**	**2 d**	**Tue 3/08/21**	**Wed 4/08/21**	**0%**
2507	Linemarking & Signage	2 d	Tue 3/08/21	Wed 4/08/21	0%
2508	**EXTERNAL WORKS \ LANDSCAPING TO BUILDINGS A, B & C**	**27 d**	**Thu 27/05/21**	**Tue 6/07/21**	**68%**
2509	**Building A - Education Building**	**50 d**	**Thu 27/05/21**	**Fri 6/08/21**	**82%**
2510	**Courtyard - A.L1.04**	**37 d**	**Thu 27/05/21**	**Tue 20/07/21**	**100%**
2511	Initial Waterproofing	1 d	Thu 27/05/21	Thu 27/05/21	100%
2512	Blockwork - Planters	2 d	Fri 28/05/21	Mon 31/05/21	100%
2513	Waterproofing	1 d	Wed 30/06/21	Wed 30/06/21	100%
2514	Floor Finishes - Tiling	5 d	Tue 13/07/21	Mon 19/07/21	100%
2515	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
2516	**Courtyard - Lift Lobby \ Link Stairs**	**36 d**	**Tue 1/06/21**	**Thu 22/07/21**	**100%**
2517	Blockwork	2 d	Tue 1/06/21	Wed 2/06/21	100%
2518	Screed \ Floor Preparation	1 d	Mon 28/06/21	Mon 28/06/21	100%
2519	Glazed Aluminium Frame & Door Installation	2 d	Tue 29/06/21	Wed 30/06/21	100%
2520	Floor Finishes - Vinyl	1 d	Mon 19/07/21	Mon 19/07/21	100%
2521	Carpentry - Hang Doors & Fix Skirtings	1 d	Fri 2/07/21	Fri 2/07/21	100%
2522	Handrails and Tactiles	1 d	Thu 22/07/21	Thu 22/07/21	100%
2523	**Western_Lvl 2**	**47 d**	**Fri 28/05/21**	**Wed 4/08/21**	**67%**
2524	Initial Waterproofing	2 d	Fri 28/05/21	Mon 31/05/21	100%
2525	Blockwork - Planters	2 d	Tue 1/06/21	Wed 2/06/21	100%
2526	Waterproofing	1 d	Wed 30/06/21	Wed 30/06/21	100%
2527	Irrigation	1 d	Mon 19/07/21	Mon 19/07/21	100%
2528	Soil	1 d	Mon 2/08/21	Mon 2/08/21	0%
2529	Planting	2 d	Tue 3/08/21	Wed 4/08/21	0%
2530	**Southern_Lvl 2**	**47 d**	**Tue 1/06/21**	**Fri 6/08/21**	**64%**
2531	Initial Waterproofing	1 d	Tue 1/06/21	Tue 1/06/21	100%
2532	Blockwork - Planters	2 d	Wed 2/06/21	Thu 3/06/21	100%
2533	Waterproofing	2 d	Wed 30/06/21	Thu 1/07/21	100%
2534	Decomposed Granite	2 d	Mon 19/07/21	Tue 20/07/21	50%
2535	Irrigation	1 d	Wed 21/07/21	Wed 21/07/21	100%
2536	Soil	1 d	Tue 3/08/21	Tue 3/08/21	0%
2537	Planting	2 d	Thu 5/08/21	Fri 6/08/21	0%
2538	**Building B - Heritage Courthouse_South**	**28 d**	**Fri 2/07/21**	**Tue 10/08/21**	**55%**
2539	Waterproofing	2 d	Fri 2/07/21	Mon 5/07/21	100%
2540	Crushed Gravel	2 d	Wed 21/07/21	Thu 22/07/21	100%
2541	Decomposed Granite	2 d	Fri 23/07/21	Mon 26/07/21	50%
2542	Grates / Stepping Stones	1 d	Tue 27/07/21	Tue 27/07/21	0%

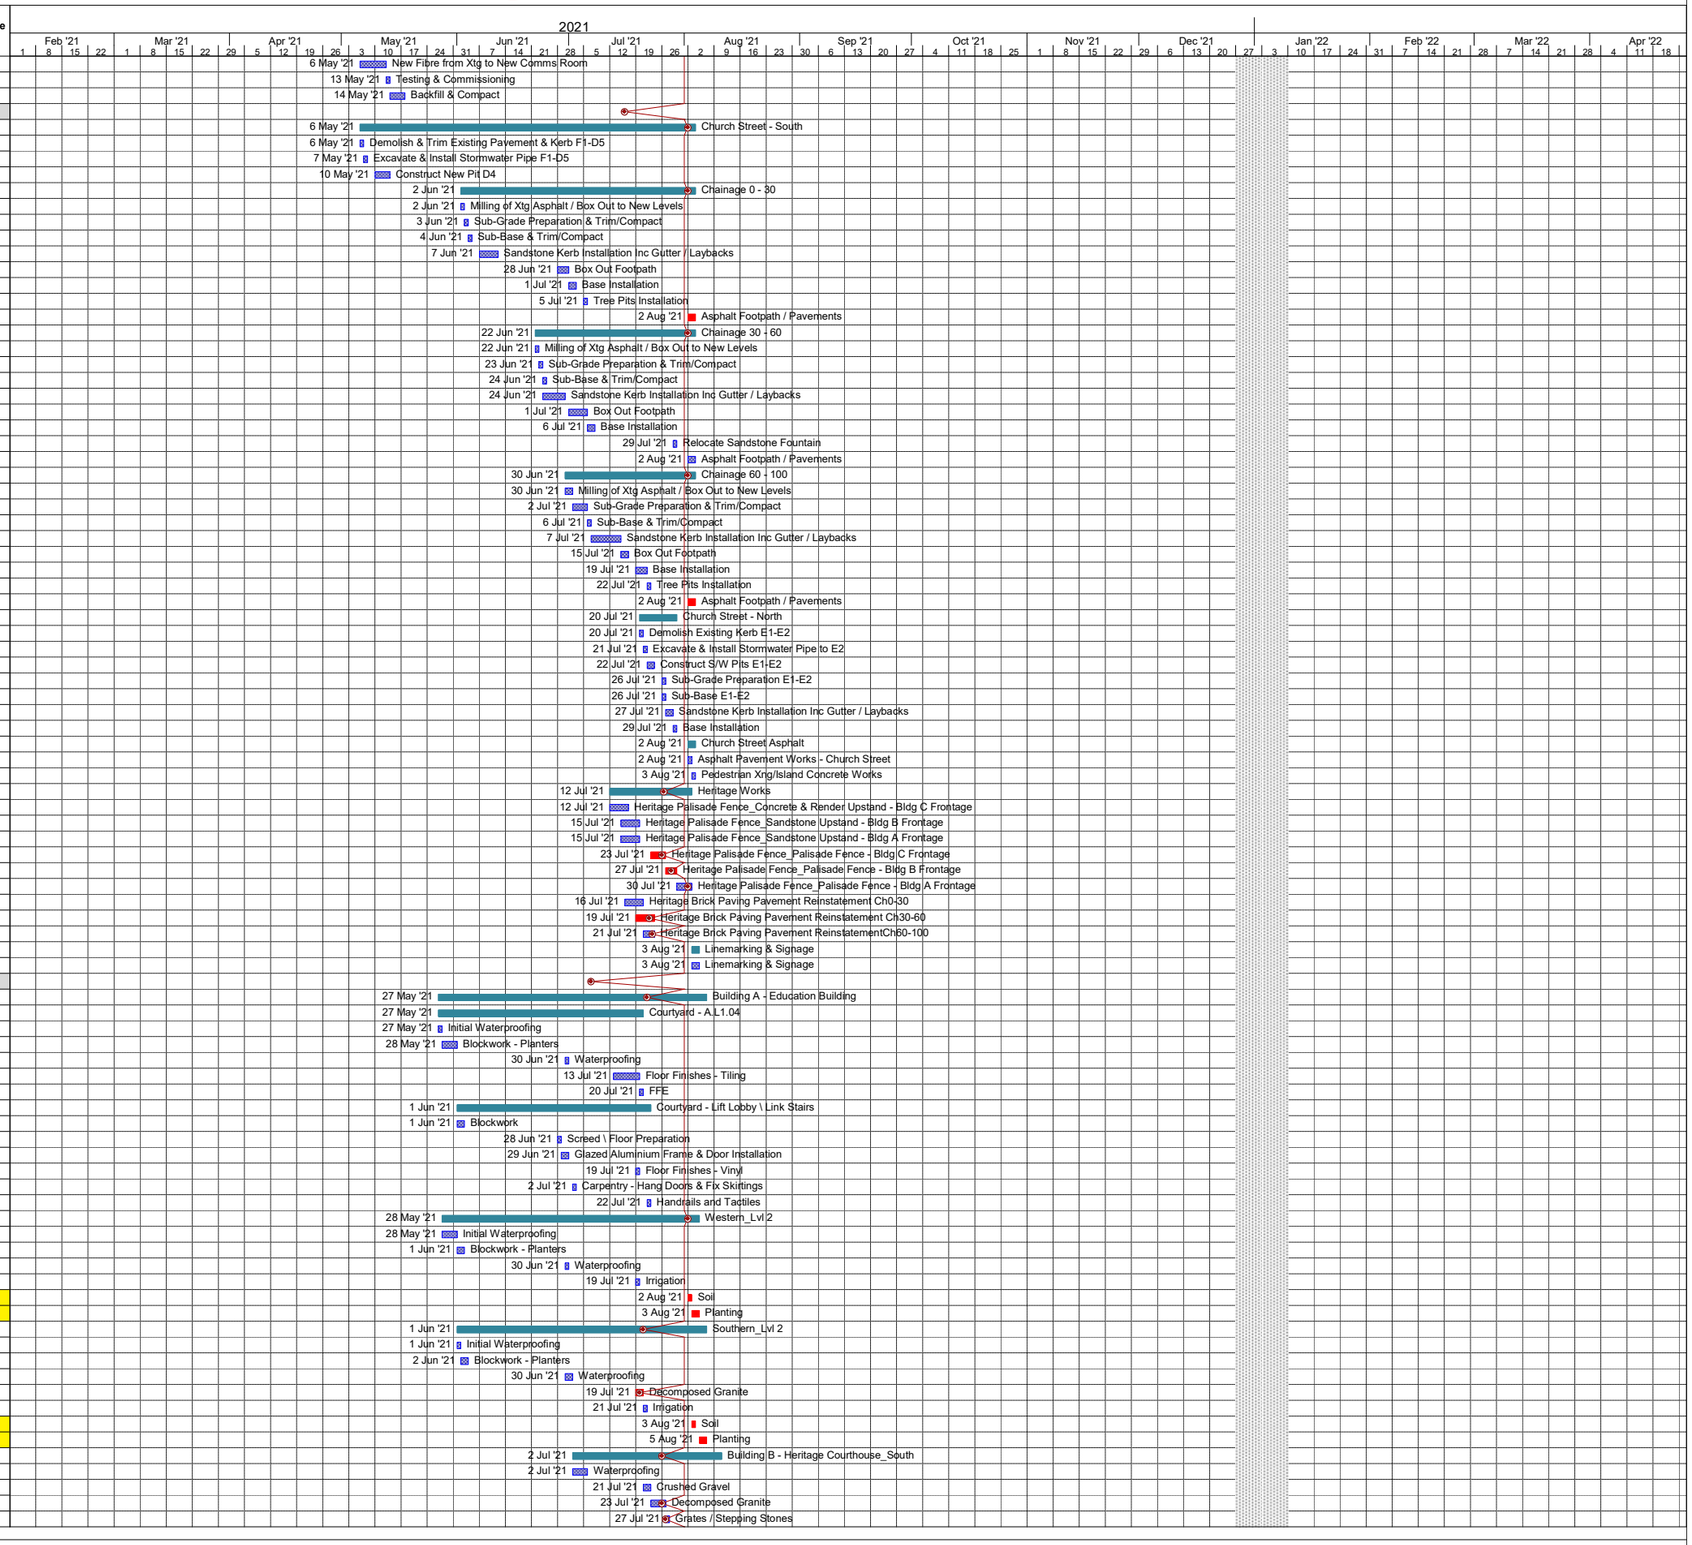


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
2543	Irrigation	1 d	Fri 23/07/21	Fri 23/07/21	100%
2544	Soil	1 d	Wed 4/08/21	Wed 4/08/21	0%
2545	Planting	2 d	Mon 9/08/21	Tue 10/08/21	0%
2546	**Building C - Residential Building_South**	**28 d**	**Tue 6/07/21**	**Thu 12/08/21**	**42%**
2547	Waterproofing	2 d	Tue 6/07/21	Wed 7/07/21	100%
2548	Crushed Gravel	2 d	Fri 23/07/21	Mon 26/07/21	100%
2549	Decomposed Granite	3 d	Tue 27/07/21	Thu 29/07/21	0%
2550	Grates / Stepping Stones	1 d	Fri 30/07/21	Fri 30/07/21	0%
2551	Irrigation	1 d	Mon 26/07/21	Mon 26/07/21	100%
2552	Soil	1 d	Thu 5/08/21	Thu 5/08/21	0%
2553	Planting	2 d	Wed 11/08/21	Thu 12/08/21	0%
2554	**Building C - Residential Building_East**	**28 d**	**Thu 8/07/21**	**Sat 14/08/21**	**57%**
2555	Waterproofing	2 d	Thu 8/07/21	Fri 9/07/21	100%
2556	Irrigation	2 d	Mon 19/07/21	Tue 20/07/21	100%
2557	Soil	1 d	Fri 6/08/21	Fri 6/08/21	0%
2558	Planting	2 d	Fri 13/08/21	Sat 14/08/21	0%
2559	**LANDSCAPING TO CHURCH STREET FRONTAGE**	**22 d**	**Mon 19/07/21**	**Mon 16/08/21**	**40%**
2560	**Residential Building C**	**18 d**	**Mon 19/07/21**	**Wed 11/08/21**	**25%**
2561	Irrigation	1 d	Mon 19/07/21	Mon 19/07/21	100%
2562	Topsoil	1 d	Mon 9/08/21	Mon 9/08/21	0%
2563	Planting	2 d	Tue 10/08/21	Wed 11/08/21	0%
2564	**Heritage Building B**	**20 d**	**Mon 19/07/21**	**Fri 13/08/21**	**50%**
2565	Waterproofing	2 d	Mon 19/07/21	Tue 20/07/21	100%
2566	Irrigation	1 d	Wed 21/07/21	Wed 21/07/21	100%
2567	Topsoil	1 d	Tue 10/08/21	Tue 10/08/21	0%
2568	Planting	2 d	Thu 12/08/21	Fri 13/08/21	0%
2569	**Education Building A**	**20 d**	**Wed 21/07/21**	**Mon 16/08/21**	**40%**
2570	Waterproofing	1 d	Wed 21/07/21	Wed 21/07/21	100%
2571	Irrigation	1 d	Thu 22/07/21	Thu 22/07/21	100%
2572	Topsoil	1 d	Wed 11/08/21	Wed 11/08/21	0%
2573	Planting	2 d	Sat 14/08/21	Mon 16/08/21	0%
2574	**QUALITY INSPECTIONS AND HANDOVER**	**21 d**	**Fri 23/07/21**	**Thu 19/08/21**	**8%**
2575	**ALL BUILDINGS**	**21 d**	**Fri 23/07/21**	**Thu 19/08/21**	**8%**
2576	Certifier \ Consultants Pre Inspect Buildings	2 d	Fri 23/07/21	Mon 26/07/21	50%
2577	Built Complete Final Defect List	1 d	Tue 27/07/21	Tue 27/07/21	0%
2578	Defects Actions	5 d	Wed 28/07/21	Tue 3/08/21	0%
2579	Fire Brigade Inspect & Life Safety Measures In Place	1 d	Wed 4/08/21	Wed 4/08/21	0%
2580	Certifier Final Inspection	1 d	Tue 17/08/21	Tue 17/08/21	0%
2581	Occupation Certificate Issued	1 d	Wed 18/08/21	Wed 18/08/21	0%
2582	DWP Issue Practical Completion	1 d	Thu 19/08/21	Thu 19/08/21	0%
2583	**DELAY ALLOWANCE**	**7 d**	**Fri 20/08/21**	**Fri 27/08/21**	**0%**
2584	**OVERALL DELAY ALLOWANCE**	**7 d**	**Fri 20/08/21**	**Fri 27/08/21**	**0%**
2585	Built Project Delay Allowance	7 d	Fri 20/08/21	Fri 27/08/21	0%
2586	*Built Project Complete*	*0 d*	*Fri 27/08/21*	*Fri 27/08/21*	0%

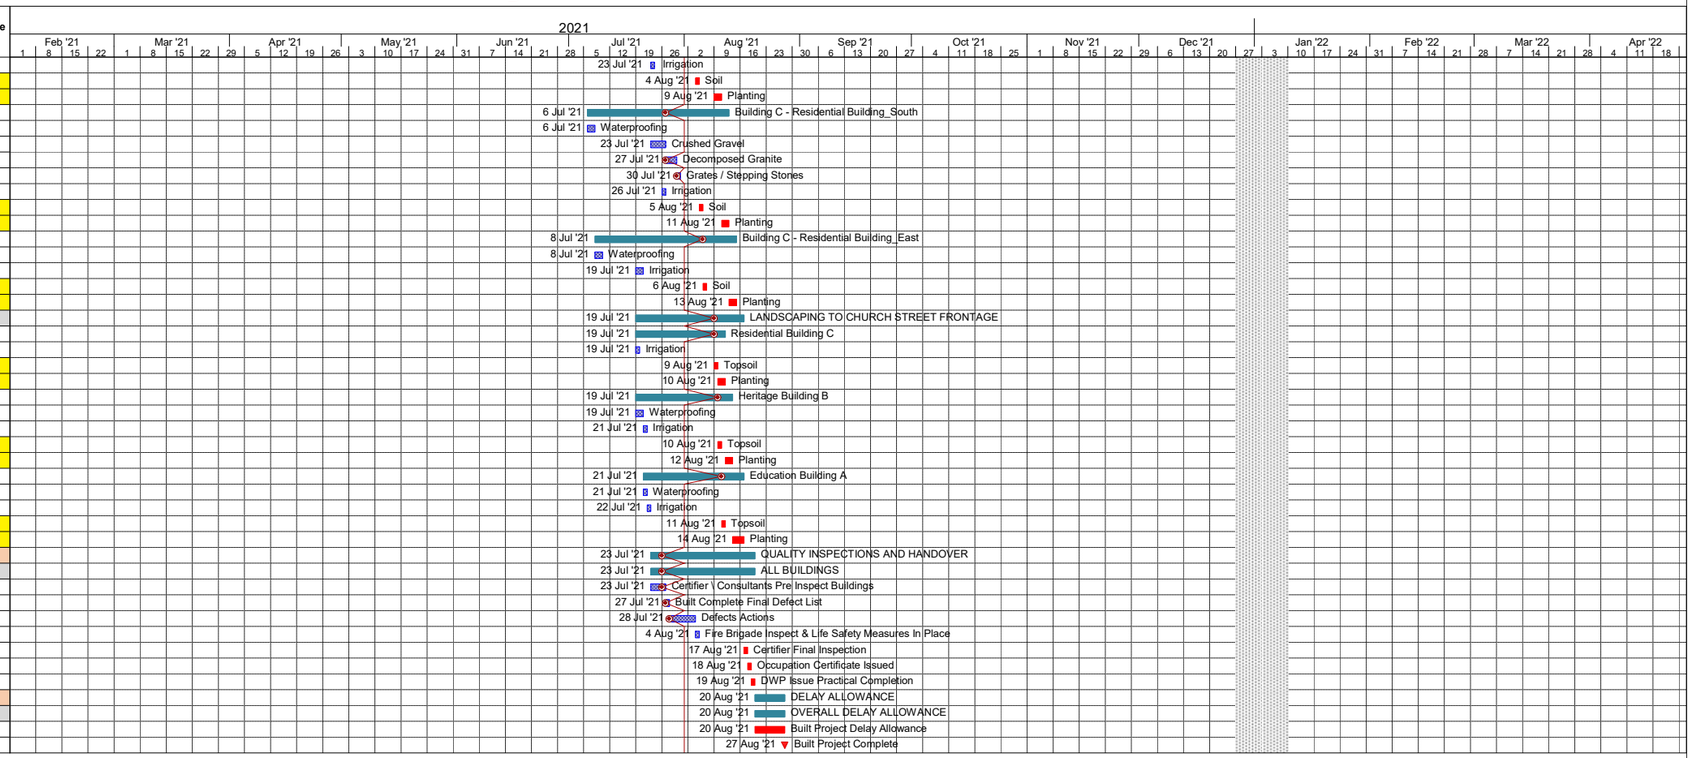

Critical Task | Non-critical | Milestone | Project Summary | Summary


Appendix E – Four Week Programme

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
0	**NIHON UNIVERSITY NEWCASTLE NSW AUSTRALIA**	**527 d**	**Wed 18/09/19**	**Fri 27/08/21**	**98%**
1	**KEY PROJECT MILESTONES**	**508 d**	**Mon 21/10/19**	**Fri 27/08/21**	**99%**
17	*Heritage Building Finishes Complete*	*0 d*	*Thu 29/07/21*	*Thu 29/07/21*	*0%*
18	*Residential Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
19	*Education Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
20	*Occupation Certificate Issued*	*0 d*	*Wed 18/08/21*	*Wed 18/08/21*	*0%*
21	*DWP Issue Practical Completion*	*0 d*	*Wed 18/08/21*	*Wed 18/08/21*	*0%*
22	*Built Project Complete*	*0 d*	*Fri 27/08/21*	*Fri 27/08/21*	*0%*
222	**CONSTRUCTION WORKS**	**456 d**	**Tue 17/12/19**	**Fri 27/08/21**	**98%**
461	**FAÇADE**	**253 d**	**Wed 26/08/20**	**Wed 11/08/21**	**97%**
462	**FAÇADE RESIDENTIAL BUILDING (1,820m2)**	**220 d**	**Wed 7/10/20**	**Wed 11/08/21**	**99%**
501	**Aluminium Screens - Arcadia**	**7 d**	**Tue 13/07/21**	**Wed 21/07/21**	**100%**
502	Install Screening (From EWP's)	7 d	Tue 13/07/21	Wed 21/07/21	100%
503	**Builders Clean of Façade Elevations**	**2 d**	**Tue 10/08/21**	**Wed 11/08/21**	**0%**
504	Pressure Cleaning Façade Elevations	2 d	Tue 10/08/21	Wed 11/08/21	0%
507	**Atrium Works**	**52 d**	**Fri 21/05/21**	**Wed 4/08/21**	**90%**
516	**Monarch Renlita Doors**	**42 d**	**Mon 31/05/21**	**Thu 29/07/21**	**20%**
518	Installation of Doors	4 d	Mon 26/07/21	Thu 29/07/21	0%
519	**Finishes & Services**	**36 d**	**Wed 16/06/21**	**Wed 4/08/21**	**93%**
530	**Level 1**	**13 d**	**Mon 19/07/21**	**Wed 4/08/21**	**83%**
536	Paint - 3rd Coat	1 d	Wed 28/07/21	Wed 28/07/21	0%
540	Tile Floor Finishes	6 d	Tue 27/07/21	Tue 3/08/21	75%
541	Balustrade Handrails & Glazed Panels	2 d	Tue 3/08/21	Wed 4/08/21	50%
542	**FAÇADE EDUCATIONAL BUILDING (1,820m2)**	**252 d**	**Wed 26/08/20**	**Tue 10/08/21**	**96%**
577	**Aluminium Screens - Arcadia**	**25 d**	**Wed 23/06/21**	**Tue 27/07/21**	**50%**
578	Install Screening (From EWP's)	25 d	Wed 23/06/21	Tue 27/07/21	50%
579	**Builders Clean of Façade Elevations**	**2 d**	**Mon 9/08/21**	**Tue 10/08/21**	**0%**
580	Pressure Cleaning Façade Elevations	2 d	Mon 9/08/21	Tue 10/08/21	0%
598	**FINISHES & SERVICES**	**303 d**	**Fri 26/06/20**	**Mon 9/08/21**	**99%**
599	**BUILDING C - RESIDENTIAL BUILDING**	**219 d**	**Fri 2/10/20**	**Mon 9/08/21**	**99%**
600	**Level 1**	**207 d**	**Fri 2/10/20**	**Thu 22/07/21**	**99%**
841	**Lounge & Resident Entrance C.L1.04 & C.L1.05**	**164 d**	**Sat 21/11/20**	**Mon 19/07/21**	**100%**
856	FFE	1 d	Mon 19/07/21	Mon 19/07/21	100%
883	**Floor Handover**	**27 d**	**Wed 16/06/21**	**Thu 22/07/21**	**89%**
884	Signage	4 d	Mon 19/07/21	Thu 22/07/21	75%
886	**Level 2**	**187 d**	**Fri 30/10/20**	**Fri 23/07/21**	**99%**
984	**Floor Handover**	**5 d**	**Mon 19/07/21**	**Fri 23/07/21**	**93%**
986	Signage	2 d	Mon 19/07/21	Tue 20/07/21	75%
987	**Level 3**	**185 d**	**Mon 2/11/20**	**Fri 23/07/21**	**99%**
1081	**Floor Handover**	**5 d**	**Mon 19/07/21**	**Fri 23/07/21**	**89%**
1083	Signage	4 d	Mon 19/07/21	Thu 22/07/21	75%
1084	**Level 4**	**188 d**	**Mon 2/11/20**	**Wed 28/07/21**	**99%**
1148	**Level 4 Terrace**	**128 d**	**Wed 27/01/21**	**Mon 26/07/21**	**95%**
1157	Zen Gardens Planting and Stone Work	6 d	Mon 19/07/21	Mon 26/07/21	75%
1158	FFE	1 d	Mon 19/07/21	Mon 19/07/21	0%
1176	**Floor Handover**	**4 d**	**Fri 23/07/21**	**Wed 28/07/21**	**92%**
1177	Signage	1 d	Fri 23/07/21	Fri 23/07/21	75%
1179	**Level 5 (Roof)**	**120 d**	**Sat 30/01/21**	**Mon 19/07/21**	**94%**
1184	Builders Clean	1 d	Mon 19/07/21	Mon 19/07/21	0%
1195	**Final Clean**	**6 d**	**Mon 2/08/21**	**Mon 9/08/21**	**0%**
1196	Final Detailed Clean	6 d	Mon 2/08/21	Mon 9/08/21	0%
1197	*Residential Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
1198	**BUILDING A EDUCATION BUILDING**	**168 d**	**Fri 4/12/20**	**Mon 9/08/21**	**98%**
1199	**Level 1 - Car Park**	**168 d**	**Fri 4/12/20**	**Mon 9/08/21**	**77%**
1204	**Main Switch Room**	**109 d**	**Tue 16/02/21**	**Thu 22/07/21**	**79%**
1207	Paint - 1st Coat	1 d	Mon 19/07/21	Mon 19/07/21	0%
1208	Paint - 2nd Coat	1 d	Tue 20/07/21	Tue 20/07/21	0%
1211	Paint - 3rd Coat	1 d	Wed 21/07/21	Wed 21/07/21	0%
1213	Fitoff Services	1 d	Thu 22/07/21	Thu 22/07/21	0%
1214	**Car Park Finishes**	**12 d**	**Fri 23/07/21**	**Mon 9/08/21**	**53%**
1215	Clean Floor	2 d	Tue 27/07/21	Wed 28/07/21	100%
1216	Sealer	2 d	Thu 29/07/21	Fri 30/07/21	100%
1218	Line Marking	2 d	Mon 2/08/21	Tue 3/08/21	100%
1219	Misc Metalwork, Wheelstops, Bike Racks Etc	4 d	Mon 2/08/21	Thu 5/08/21	0%
1220	Signage	2 d	Wed 4/08/21	Thu 5/08/21	0%
1221	Initial Clean and Defects	2 d	Fri 6/08/21	Mon 9/08/21	0%
1222	**Level 2**	**125 d**	**Fri 22/01/21**	**Tue 20/07/21**	**100%**
1449	**Advert Room - A.L2.24**	**17 d**	**Mon 28/06/21**	**Tue 20/07/21**	**100%**
1458	Floor Finishes - Vinyl	1 d	Mon 19/07/21	Mon 19/07/21	100%
1695	**Level 4**	**119 d**	**Mon 8/02/21**	**Tue 27/07/21**	**99%**
1837	**Level 4 External Terrace**	**94 d**	**Tue 9/03/21**	**Tue 27/07/21**	**96%**
1846	Zen Gardens Planting and Stone Work	6 d	Mon 19/07/21	Mon 26/07/21	75%
1847	FFE	1 d	Tue 27/07/21	Tue 27/07/21	0%
1855	**Final Clean**	**6 d**	**Mon 2/08/21**	**Mon 9/08/21**	**0%**
1856	Final Detailed Clean	6 d	Mon 2/08/21	Mon 9/08/21	0%
1857	*Education Building Finishes Complete*	*0 d*	*Mon 9/08/21*	*Mon 9/08/21*	*0%*
1858	**BUILDING B - HERITAGE COURTHOUSE**	**296 d**	**Fri 26/06/20**	**Thu 29/07/21**	**99%**
1859	**LEVEL 1**	**290 d**	**Fri 26/06/20**	**Wed 21/07/21**	**100%**
1875	**Male WC**	**215 d**	**Tue 22/09/20**	**Wed 21/07/21**	**100%**
1893	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1894	**Female WC**	**214 d**	**Wed 23/09/20**	**Wed 21/07/21**	**100%**
1912	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1913	**Cleaners Store**	**213 d**	**Thu 24/09/20**	**Wed 21/07/21**	**100%**
1929	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1930	**Access WC**	**212 d**	**Fri 25/09/20**	**Wed 21/07/21**	**100%**
1947	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1948	**Book Storage**	**211 d**	**Sat 26/09/20**	**Wed 21/07/21**	**100%**
1961	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1962	**Interview Room**	**209 d**	**Tue 29/09/20**	**Wed 21/07/21**	**100%**
1974	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
1975	**Monitor Room**	**207 d**	**Thu 1/10/20**	**Wed 21/07/21**	**100%**
1988	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
2001	**Administration Office**	**205 d**	**Wed 7/10/20**	**Wed 21/07/21**	**100%**

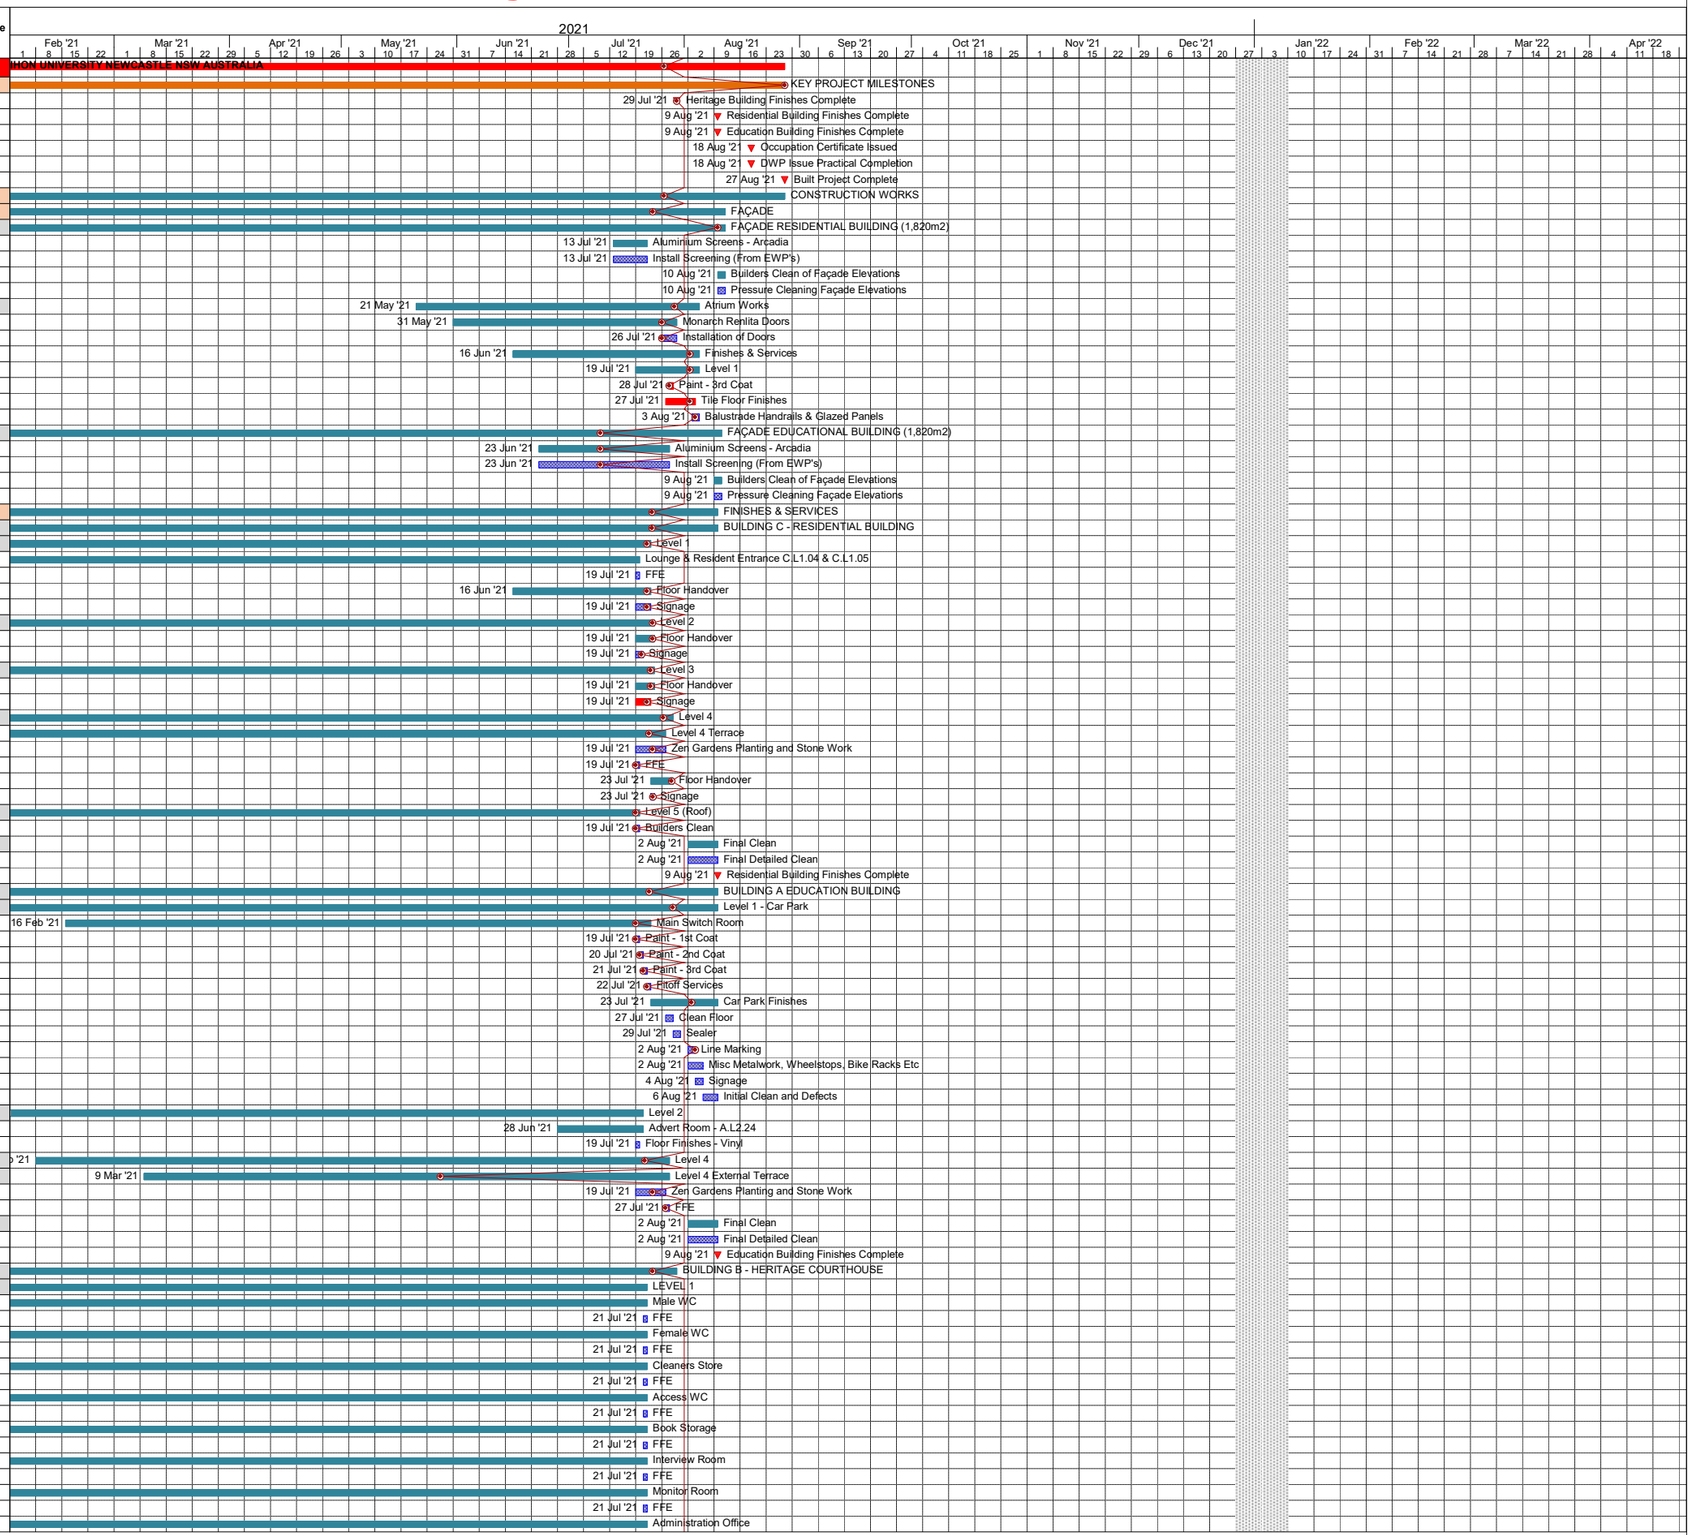


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

Built.

ID	Task Name	Dur	Start	Finish	% Complete
2014	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
2015	**Lounge (Old Teacher's Room)**	**203 d**	**Fri 9/10/20**	**Wed 21/07/21**	**100%**
2027	FFE	1 d	Wed 21/07/21	Wed 21/07/21	100%
2097	**LEVEL 2**	**256 d**	**Wed 12/08/20**	**Thu 29/07/21**	**99%**
2103	**Amenities (Male\Female\Access WC's)**	**227 d**	**Thu 10/09/20**	**Fri 23/07/21**	**100%**
2119	FFE	2 d	Thu 22/07/21	Fri 23/07/21	100%
2120	**Magistrate \ Old Library \ Judges Room 4**	**201 d**	**Tue 13/10/20**	**Thu 22/07/21**	**100%**
2134	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2148	**Library**	**198 d**	**Fri 16/10/20**	**Thu 22/07/21**	**100%**
2161	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2184	**Office Room \ Remote Witness**	**155 d**	**Wed 9/12/20**	**Thu 22/07/21**	**100%**
2197	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2198	**Conserved Judge Room**	**139 d**	**Fri 8/01/21**	**Thu 22/07/21**	**100%**
2211	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2265	**Teacher's Room (Ex Lounge)**	**136 d**	**Tue 12/01/21**	**Thu 22/07/21**	**100%**
2278	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2279	**Kitchenette**	**134 d**	**Thu 14/01/21**	**Thu 22/07/21**	**100%**
2292	FFE	1 d	Thu 22/07/21	Thu 22/07/21	100%
2318	**Entrance**	**74 d**	**Tue 13/04/21**	**Thu 29/07/21**	**86%**
2329	Repair \ Deep Clean Existing Tiles	5 d	Fri 23/07/21	Thu 29/07/21	0%
2386	**LEVEL 4**	**82 d**	**Sat 27/03/21**	**Thu 29/07/21**	**99%**
2396	*Heritage Building Finishes Complete*	*0 d*	*Thu 29/07/21*	*Thu 29/07/21*	*0%*
2397	**VERTICAL TRANSPORTATION**	**148 d**	**Mon 11/01/21**	**Fri 6/08/21**	**95%**
2404	**ACCESS LIFT TO ATRIUM LEVEL**	**5 d**	**Mon 2/08/21**	**Fri 6/08/21**	**0%**
2405	Lift Installation	3 d	Mon 2/08/21	Wed 4/08/21	0%
2406	Commissioning \ Handover to Built	2 d	Thu 5/08/21	Fri 6/08/21	0%
2407	**SERVICES TESTING & COMMISSIONING**	**18 d**	**Thu 8/07/21**	**Mon 2/08/21**	**93%**
2408	Courthouse Building	17 d	Thu 8/07/21	Fri 30/07/21	95%
2409	Residential Building	16 d	Fri 9/07/21	Fri 30/07/21	95%
2410	Education Building	16 d	Fri 9/07/21	Fri 30/07/21	95%
2411	Integrated System Testing	1 d	Mon 2/08/21	Mon 2/08/21	0%
2412	**CHURCH STREET CIVIL WORKS**	**129 d**	**Tue 2/02/21**	**Wed 4/08/21**	**93%**
2453	**S138 CIVIL WORKS**	**49 d**	**Thu 6/05/21**	**Thu 15/07/21**	**91%**
2454	**Church Street - South**	**62 d**	**Thu 6/05/21**	**Tue 3/08/21**	**89%**
2458	**Chainage 0 - 30**	**43 d**	**Wed 2/06/21**	**Tue 3/08/21**	**88%**
2466	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2467	**Chainage 30 - 60**	**31 d**	**Tue 22/06/21**	**Tue 3/08/21**	**87%**
2474	Relocate Sandstone Fountain	1 d	Thu 29/07/21	Thu 29/07/21	100%
2475	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2476	**Chainage 60 - 100**	**25 d**	**Wed 30/06/21**	**Tue 3/08/21**	**89%**
2484	Asphalt Footpath / Pavements	2 d	Mon 2/08/21	Tue 3/08/21	0%
2485	**Church Street - North**	**8 d**	**Tue 20/07/21**	**Thu 29/07/21**	**100%**
2487	Excavate & Install Stormwater Pipe to E2	1 d	Wed 21/07/21	Wed 21/07/21	100%
2488	Construct S/W Pits E1-E2	2 d	Thu 22/07/21	Fri 23/07/21	100%
2489	Sub-Grade Preparation E1-E2	1 d	Mon 26/07/21	Mon 26/07/21	100%
2490	Sub-Base E1-E2	1 d	Mon 26/07/21	Mon 26/07/21	100%
2491	Sandstone Kerb Installation Inc Gutter / Laybacks	2 d	Tue 27/07/21	Wed 28/07/21	100%
2492	Base Installation	1 d	Thu 29/07/21	Thu 29/07/21	100%
2493	**Church Street Asphalt**	**2 d**	**Mon 2/08/21**	**Tue 3/08/21**	**0%**
2494	Asphalt Pavement Works - Church Street	1 d	Mon 2/08/21	Mon 2/08/21	0%
2495	Pedestrian Xng/Island Concrete Works	1 d	Tue 3/08/21	Tue 3/08/21	0%
2496	**Heritage Works**	**16 d**	**Mon 12/07/21**	**Mon 2/08/21**	**81%**
2500	Heritage Palisade Fence_Palisade Fence - Bldg C Frontage	2 d	Fri 23/07/21	Mon 26/07/21	50%
2501	Heritage Palisade Fence_Palisade Fence - Bldg B Frontage	3 d	Tue 27/07/21	Thu 29/07/21	50%
2502	Heritage Palisade Fence_Palisade Fence - Bldg A Frontage	2 d	Fri 30/07/21	Mon 2/08/21	50%
2504	Heritage Brick Paving Pavement Reinstatement Ch30-60	5 d	Mon 19/07/21	Fri 23/07/21	75%
2505	Heritage Brick Paving Pavement ReinstatementCh60-100	3 d	Wed 21/07/21	Fri 23/07/21	75%
2506	**Linemarking & Signage**	**2 d**	**Tue 3/08/21**	**Wed 4/08/21**	**0%**
2507	Linemarking & Signage	2 d	Tue 3/08/21	Wed 4/08/21	0%
2508	**EXTERNAL WORKS \ LANDSCAPING TO BUILDINGS A, B & C**	**27 d**	**Thu 27/05/21**	**Tue 6/07/21**	**68%**
2509	**Building A - Education Building**	**50 d**	**Thu 27/05/21**	**Fri 6/08/21**	**82%**
2510	**Courtyard - A.L1.04**	**37 d**	**Thu 27/05/21**	**Tue 20/07/21**	**100%**
2515	FFE	1 d	Tue 20/07/21	Tue 20/07/21	100%
2516	**Courtyard - Lift Lobby \ Link Stairs**	**36 d**	**Tue 1/06/21**	**Thu 22/07/21**	**100%**
2522	Handrails and Tactiles	1 d	Thu 22/07/21	Thu 22/07/21	100%
2523	**Western_Lvl 2**	**47 d**	**Fri 28/05/21**	**Wed 4/08/21**	**67%**
2528	Soil	1 d	Mon 2/08/21	Mon 2/08/21	0%
2529	Planting	2 d	Tue 3/08/21	Wed 4/08/21	0%
2530	**Southern_Lvl 2**	**47 d**	**Tue 1/06/21**	**Fri 6/08/21**	**64%**
2534	Decomposed Granite	2 d	Mon 19/07/21	Tue 20/07/21	50%
2536	Soil	1 d	Tue 3/08/21	Tue 3/08/21	0%
2537	Planting	2 d	Thu 5/08/21	Fri 6/08/21	0%
2538	**Building B - Heritage Courthouse_South**	**28 d**	**Fri 2/07/21**	**Tue 10/08/21**	**55%**
2540	Crushed Gravel	2 d	Wed 21/07/21	Thu 22/07/21	100%
2541	Decomposed Granite	2 d	Fri 23/07/21	Mon 26/07/21	50%
2542	Grates / Stepping Stones	1 d	Tue 27/07/21	Tue 27/07/21	0%
2544	Soil	1 d	Wed 4/08/21	Wed 4/08/21	0%
2545	Planting	2 d	Mon 9/08/21	Tue 10/08/21	0%
2546	**Building C - Residential Building_South**	**28 d**	**Tue 6/07/21**	**Thu 12/08/21**	**42%**
2548	Crushed Gravel	2 d	Fri 23/07/21	Mon 26/07/21	100%
2549	Decomposed Granite	3 d	Tue 27/07/21	Thu 29/07/21	0%
2550	Grates / Stepping Stones	1 d	Fri 30/07/21	Fri 30/07/21	0%
2552	Soil	1 d	Thu 5/08/21	Thu 5/08/21	0%
2553	Planting	2 d	Wed 11/08/21	Thu 12/08/21	0%
2554	**Building C - Residential Building_East**	**28 d**	**Thu 8/07/21**	**Sat 14/08/21**	**57%**
2557	Soil	1 d	Fri 6/08/21	Fri 6/08/21	0%
2558	Planting	2 d	Fri 13/08/21	Sat 14/08/21	0%
2559	**LANDSCAPING TO CHURCH STREET FRONTAGE**	**22 d**	**Mon 19/07/21**	**Mon 16/08/21**	**40%**
2560	**Residential Building C**	**18 d**	**Mon 19/07/21**	**Wed 11/08/21**	**25%**
2562	Topsoil	1 d	Mon 9/08/21	Mon 9/08/21	0%
2563	Planting	2 d	Tue 10/08/21	Wed 11/08/21	0%
2564	**Heritage Building B**	**20 d**	**Mon 19/07/21**	**Fri 13/08/21**	**50%**
2567	Topsoil	1 d	Tue 10/08/21	Tue 10/08/21	0%

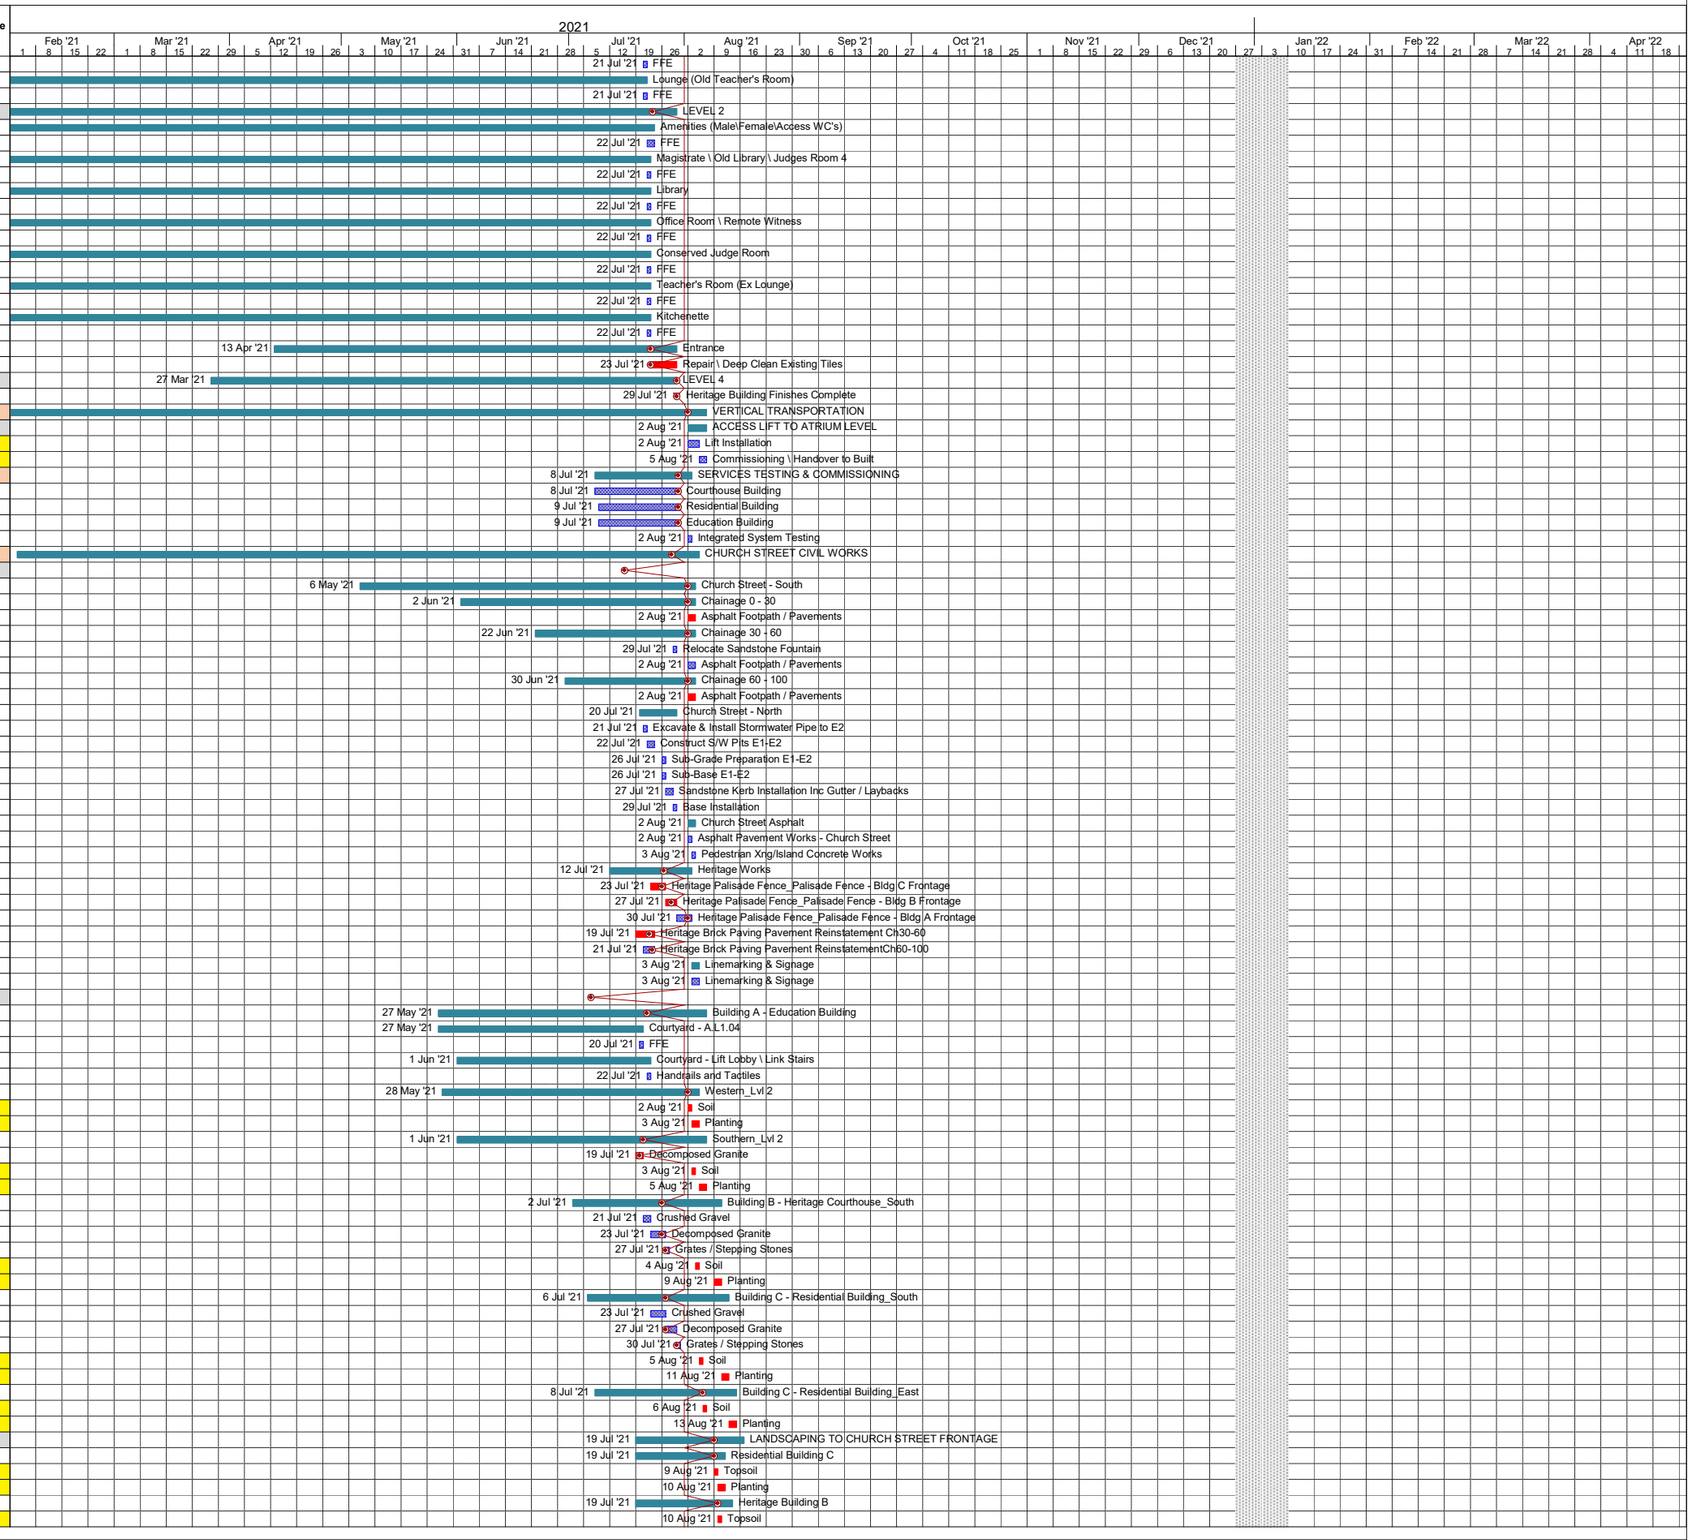


Critical Task | Non-critical | Milestone | Project Summary | Summary

Prepared By: RMc
Checked:
Revision : Rev 20 Contract

Built NIHON UNIVERSITY
9 CHURCH STREET NEWCASTLE 2300
Contract Programme

ID	Task Name	Dur	Start	Finish	% Complete
2568	Planting	2 d	Thu 12/08/21	Fri 13/08/21	0%
2569	**Education Building A**	**20 d**	**Wed 21/07/21**	**Mon 16/08/21**	**40%**
2572	Topsoil	1 d	Wed 11/08/21	Wed 11/08/21	0%
2573	Planting	2 d	Sat 14/08/21	Mon 16/08/21	0%
2574	**QUALITY INSPECTIONS AND HANDOVER**	**21 d**	**Fri 23/07/21**	**Thu 19/08/21**	**8%**
2575	**ALL BUILDINGS**	**21 d**	**Fri 23/07/21**	**Thu 19/08/21**	**8%**
2576	Certifier \ Consultants Pre Inspect Buildings	2 d	Fri 23/07/21	Mon 26/07/21	50%
2577	Built Complete Final Defect List	1 d	Tue 27/07/21	Tue 27/07/21	0%
2578	Defects Actions	5 d	Wed 28/07/21	Tue 3/08/21	0%
2579	Fire Brigade Inspect & Life Safety Measures In Place	1 d	Wed 4/08/21	Wed 4/08/21	0%
2580	Certifier Final Inspection	1 d	Tue 17/08/21	Tue 17/08/21	0%
2581	Occupation Certificate Issued	1 d	Wed 18/08/21	Wed 18/08/21	0%
2582	DWP Issue Practical Completion	1 d	Thu 19/08/21	Thu 19/08/21	0%
2583	**DELAY ALLOWANCE**	**7 d**	**Fri 20/08/21**	**Fri 27/08/21**	**0%**
2584	**OVERALL DELAY ALLOWANCE**	**7 d**	**Fri 20/08/21**	**Fri 27/08/21**	**0%**
2585	Built Project Delay Allowance	7 d	Fri 20/08/21	Fri 27/08/21	0%
2586	*Built Project Complete*	*0 d*	*Fri 27/08/21*	*Fri 27/08/21*	*0%*

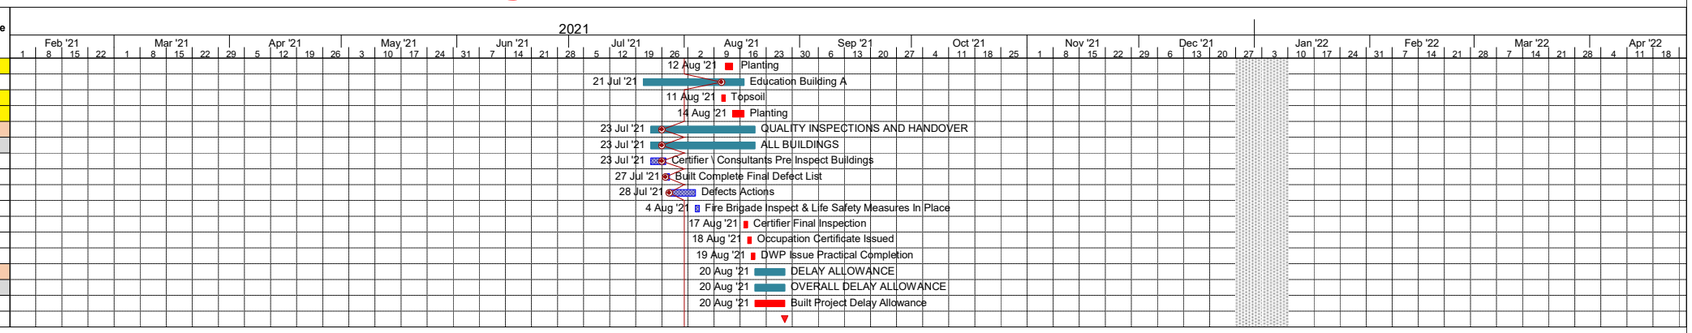

Critical Task | Non-critical | Milestone | Project Summary | Summary

Appendix F – Monthly Progress Photos

Building A – Education

Level 1

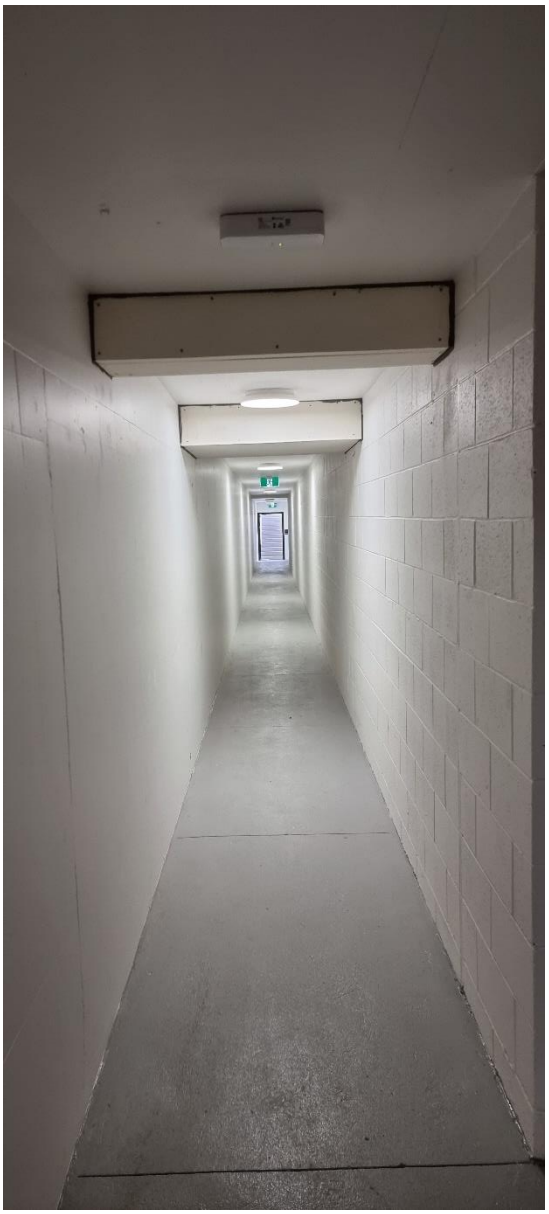


Photo 01

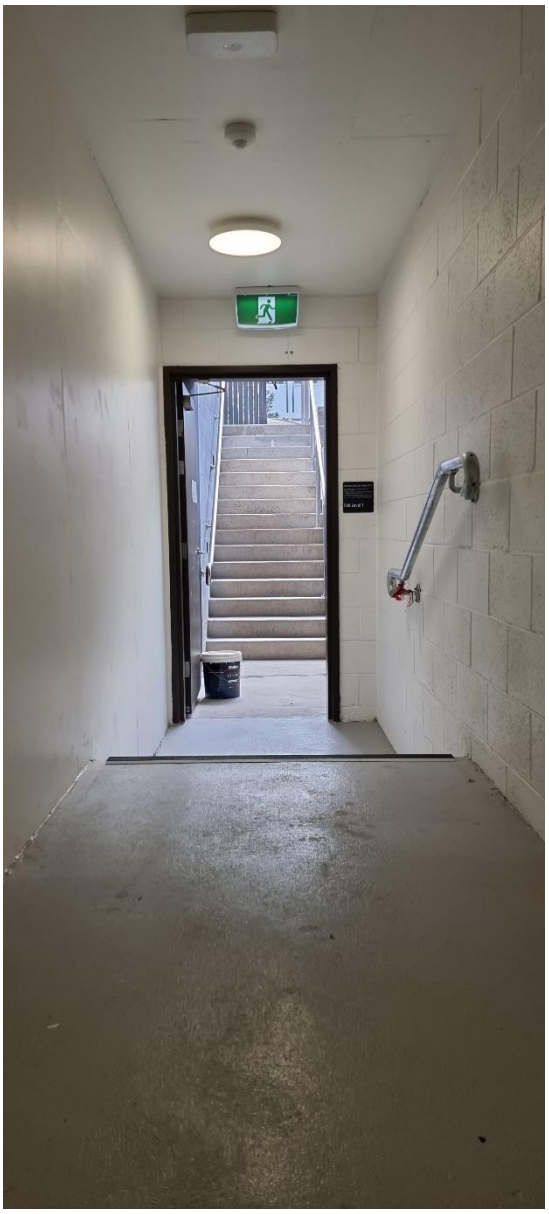


Photo 02

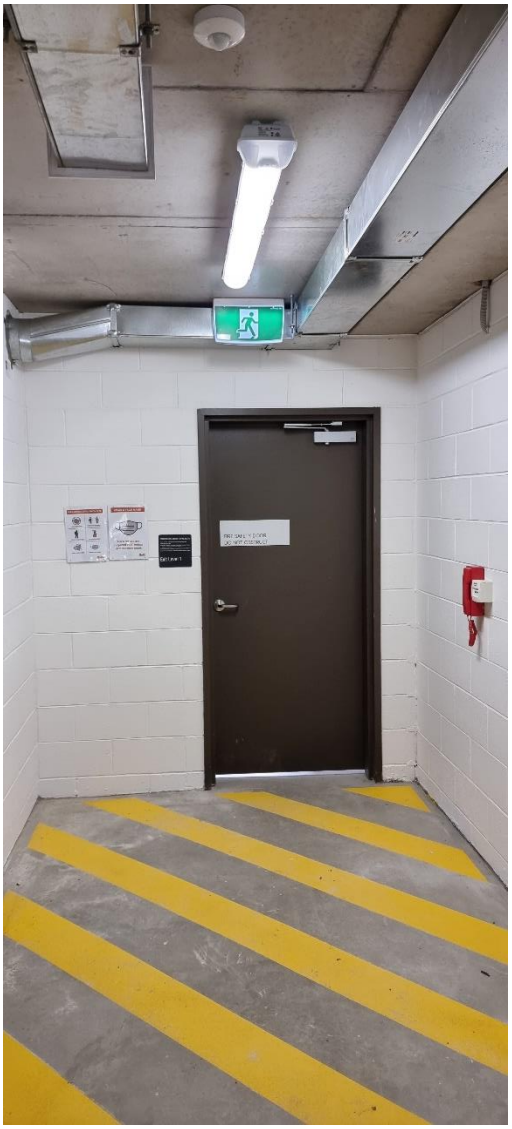


Photo 03

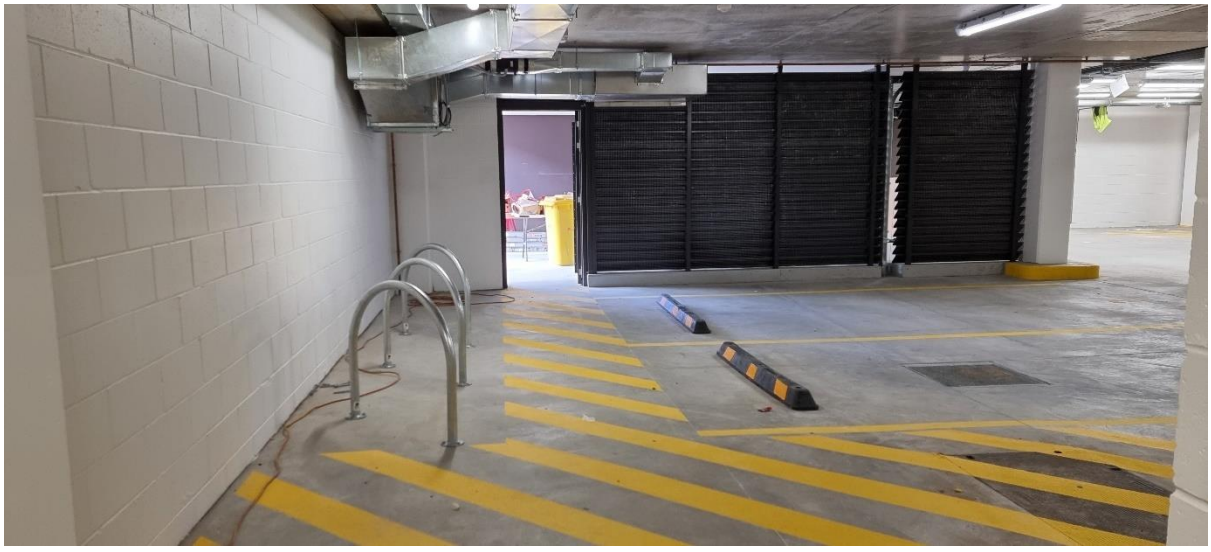


Photo 04

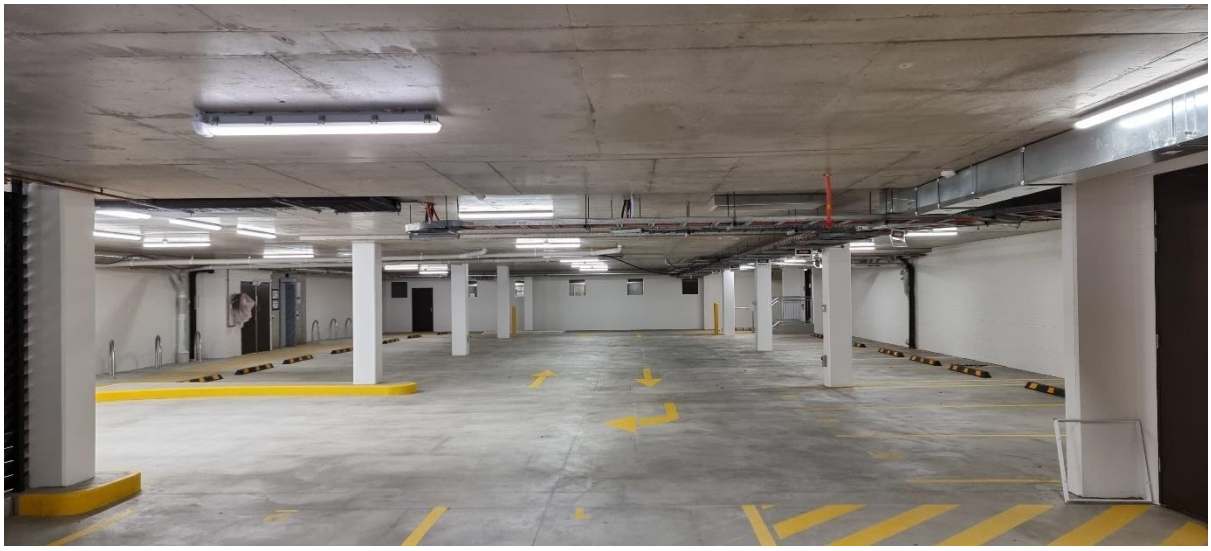


Photo 05

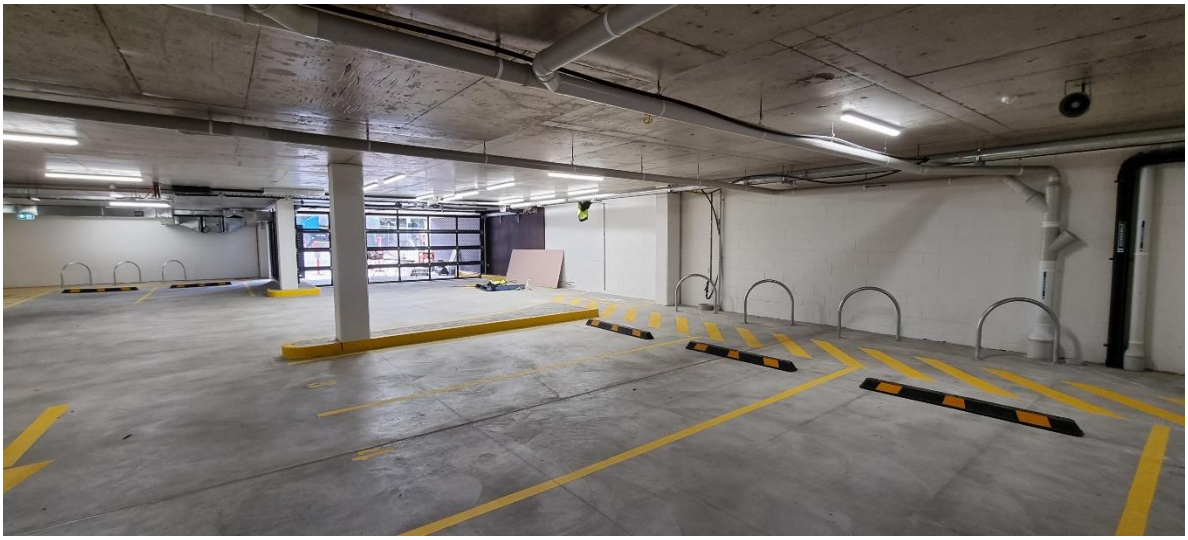


Photo 06

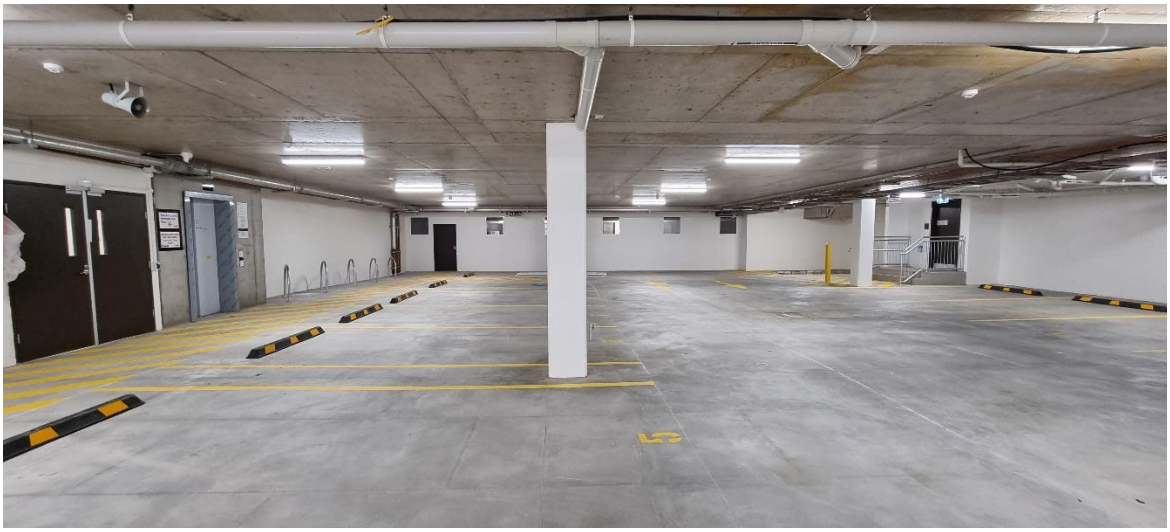


Photo 07

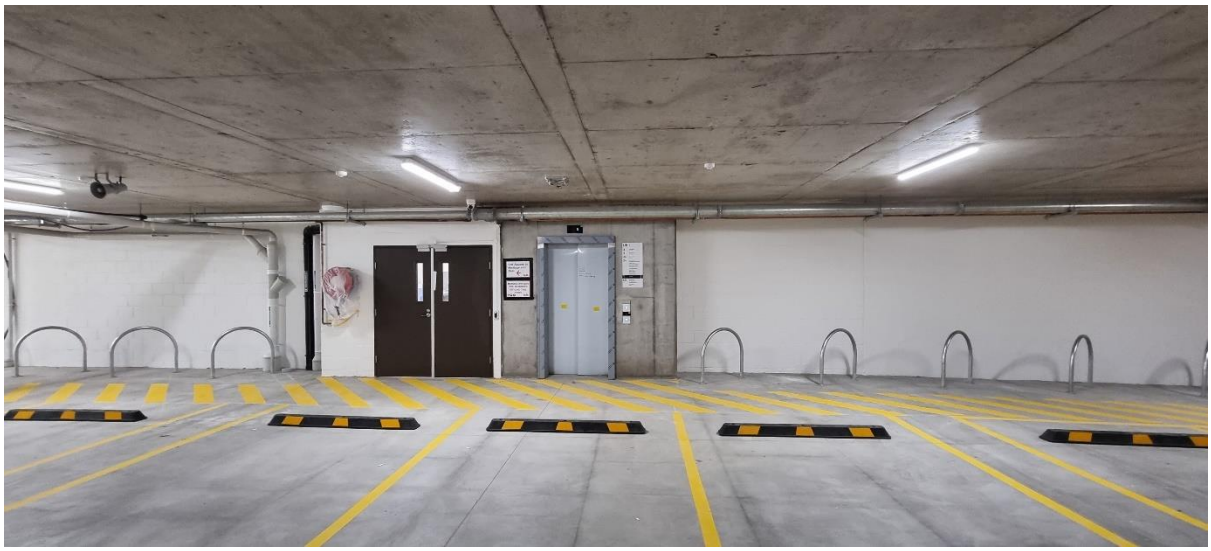


Photo 08

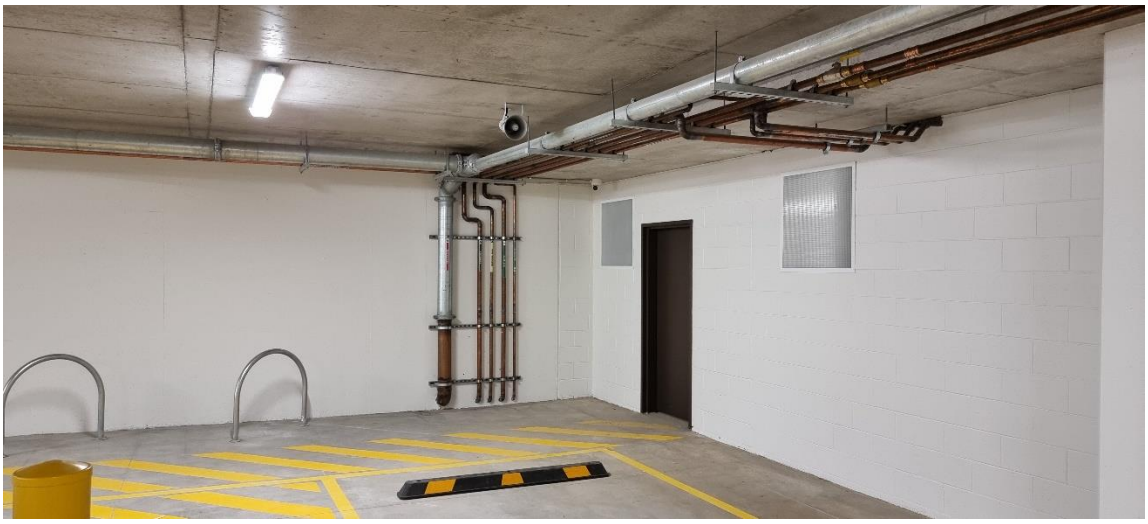


Photo 09

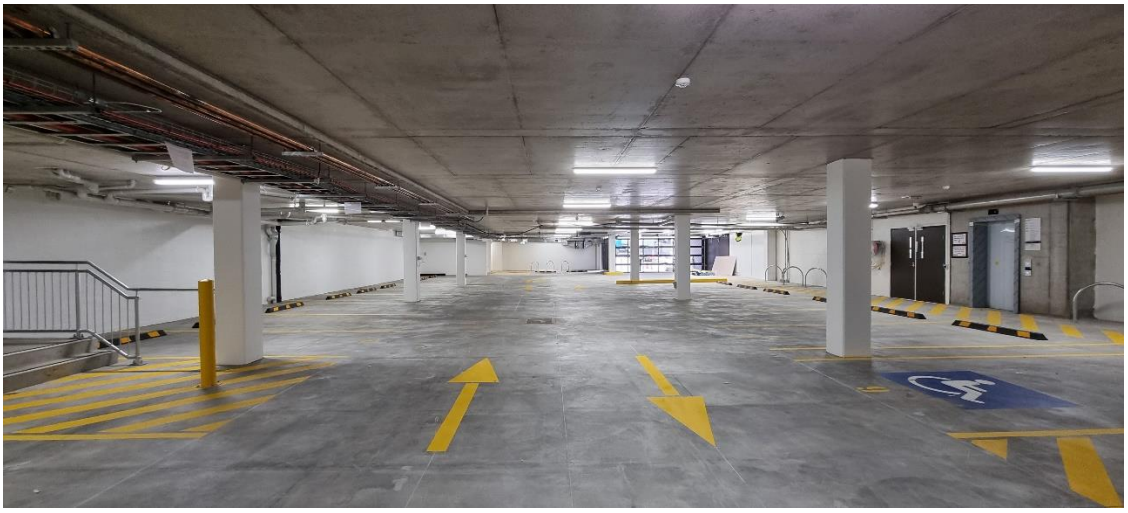


Photo 10

Level 2

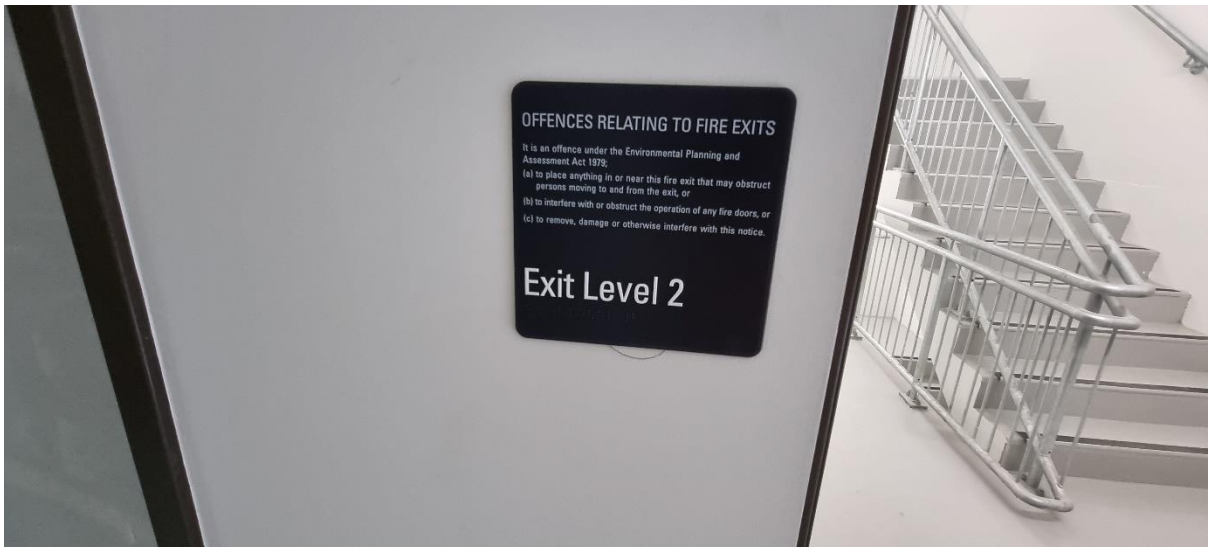


Photo 11



Photo 12



Photo 13



Photo 14



Photo 15



Photo 16



Photo 17



Photo 18


Do not use Toilets in this room
Built.
Female Toilet & Ambulant Toilet

Photo 19



Photo 20

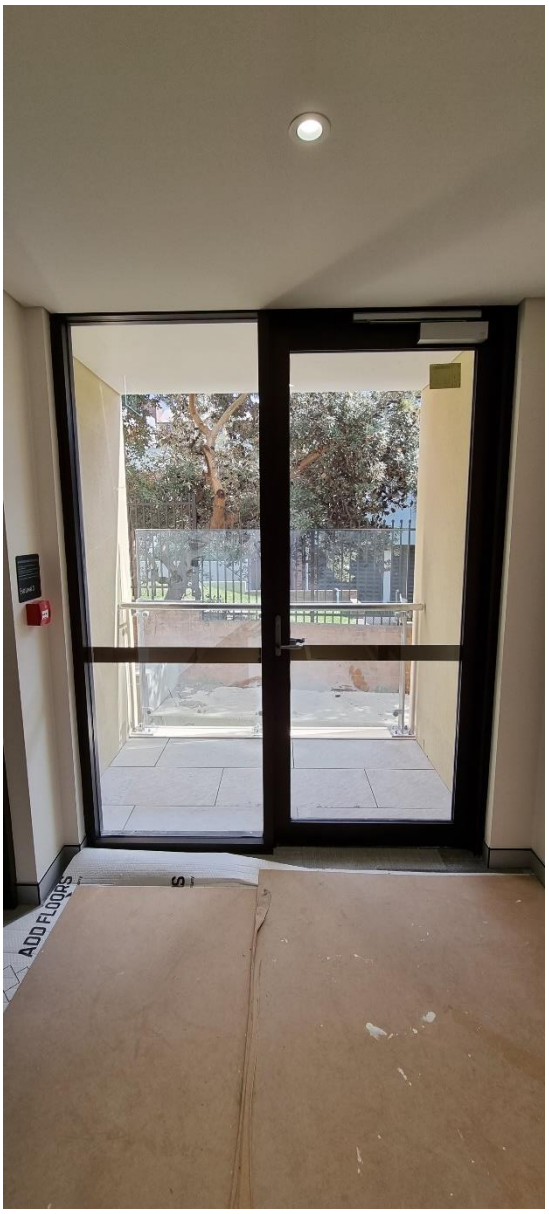


Photo 21

Level 3



Photo 22



Photo 23



Photo 24



Photo 25



Photo 26



Photo 27



Photo 28



Photo 29



Photo 30



Photo 31



Photo 32



Photo 33



Photo 34



Photo 35

Level 4



Photo 35



Photo 36



Photo 37



Photo 38



Photo 39



Photo 40



Photo 41



Photo 42



Photo 43



Photo 44



Photo 45



Photo 46

Building B – Heritage Courthouse

Level 1



Photo 47



Photo 48



Photo 49

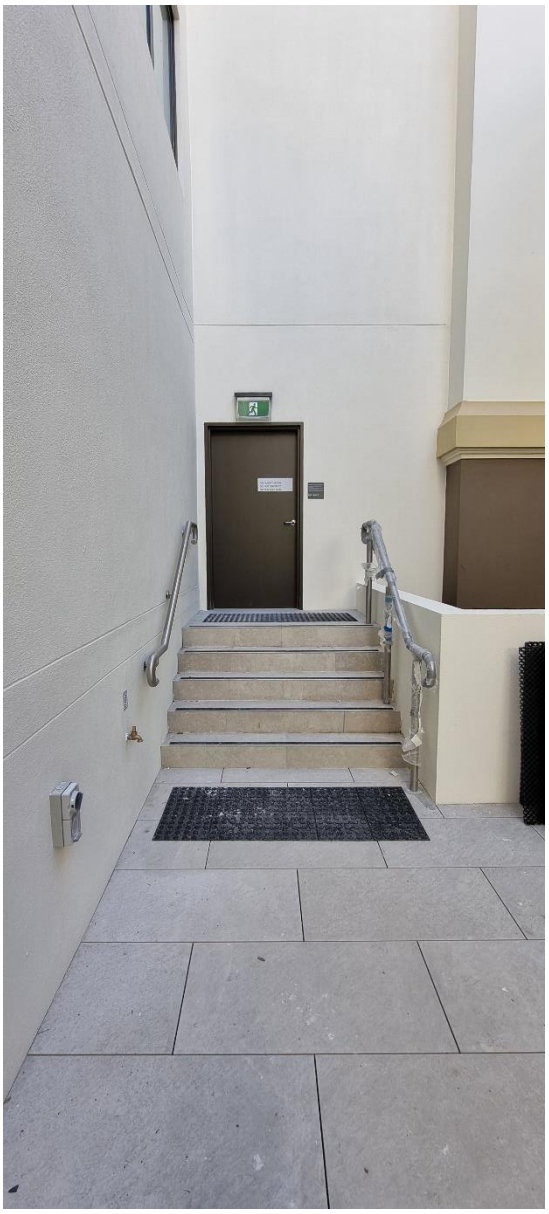


Photo 50

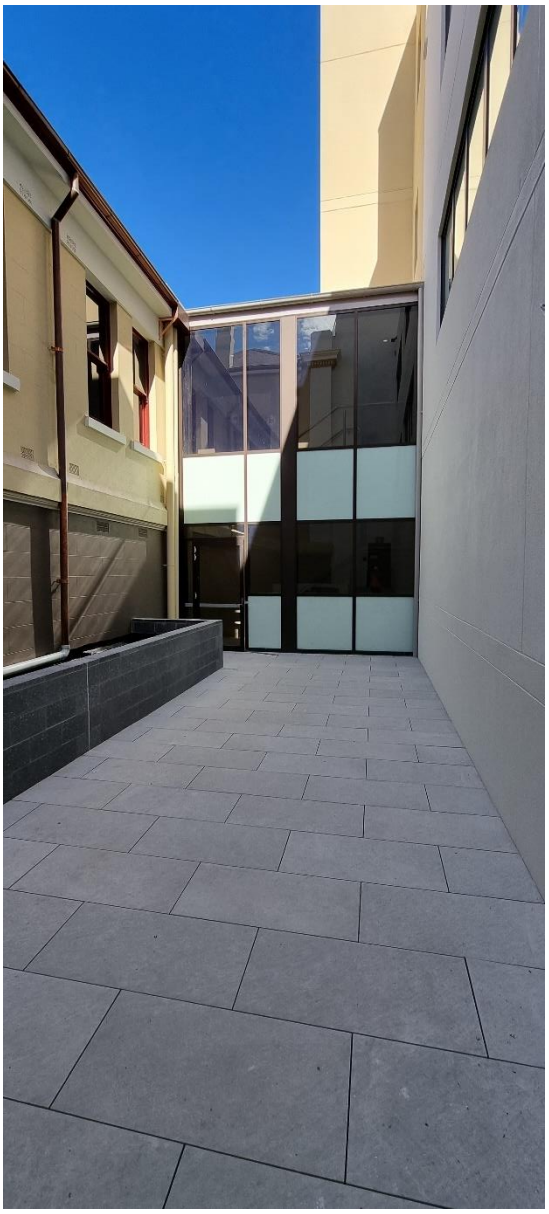


Photo 51

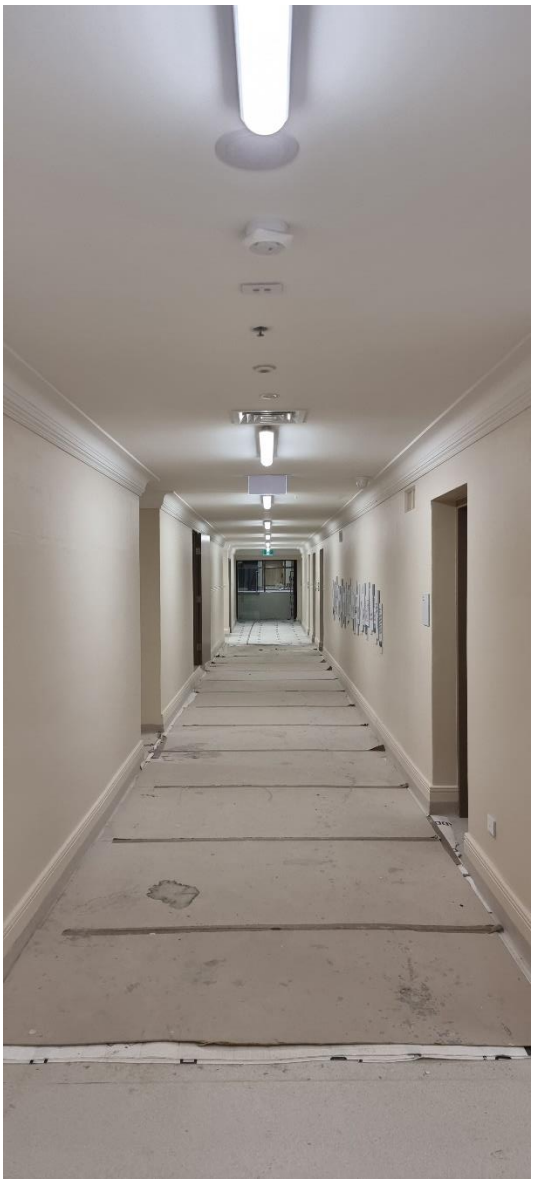


Photo 52

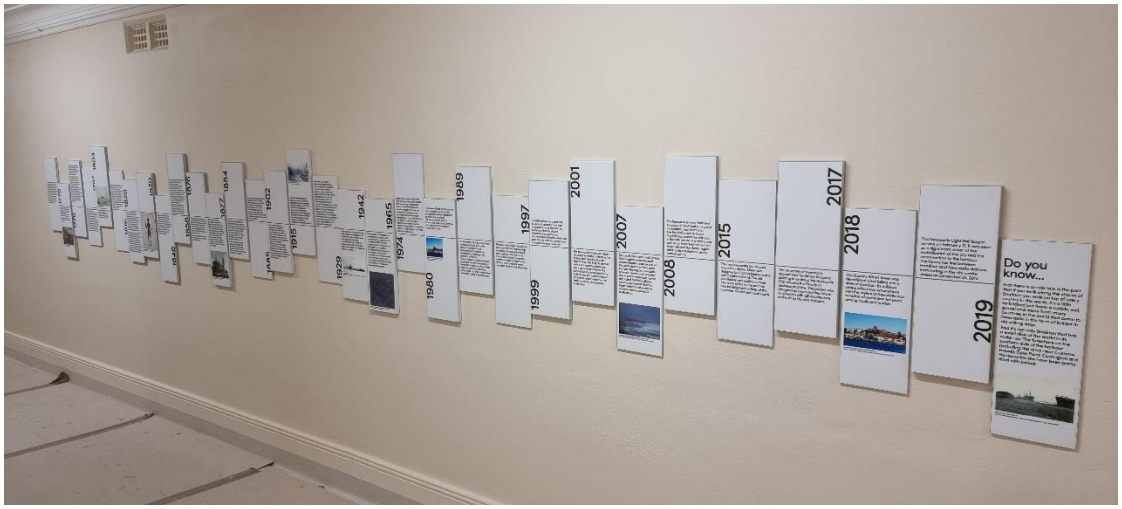


Photo 53



Photo 54



Photo 55



Photo 56



Photo 57



Photo 58



Photo 59



Photo 60



Photo 61

Level 2



Photo 62



Photo 63


C202
Yamada Room
Yamada Akiyoshi was a Japanese Statesman and one of the early leaders of the Meiji Restoration. In 1879 Yamada, also a Military Officer of high regard was appointed the position of a sangi (councillor), serving as Minister of Industry (1879–1880), Home Minister (1881–1883) and Minister of Justice (1885–1891). He is also acknowledged as having worked hard in helping develop the modern Japanese legal code as Minister of Justice. In this position Yamada also established Nihon University as 'Nihon Law School' in 1889 with other advocates.
The Yamada Room formerly held 'Court Room 3' of the Newcastle Courthouse, which was part of the original 1892 construction.
Yamada Room

Photo 64

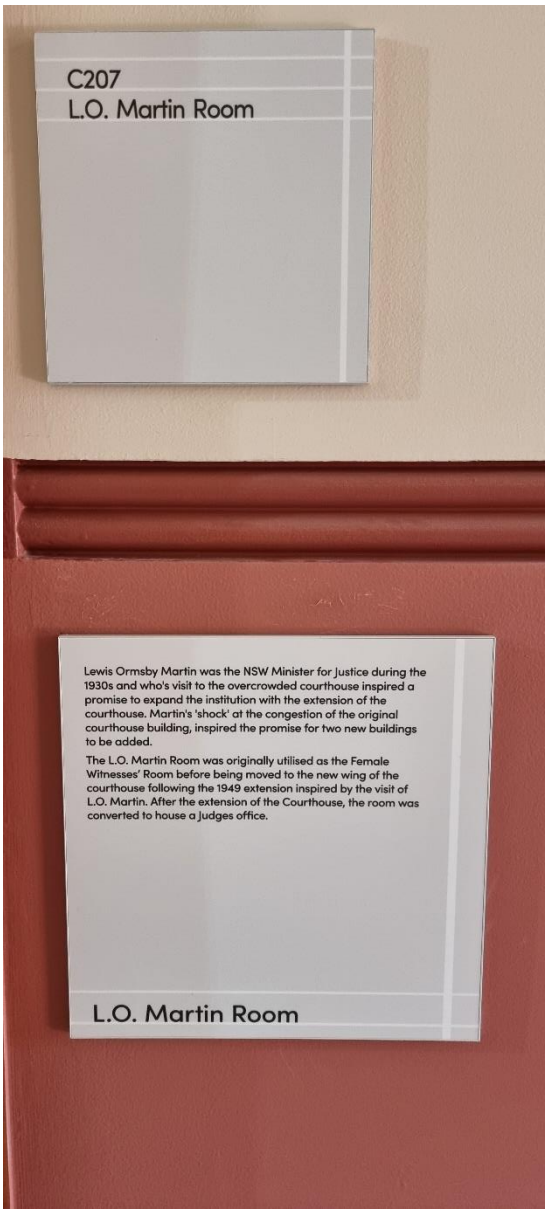

C207
L.O. Martin Room
Lewis Ormsby Martin was the NSW Minister for Justice during the 1930s and who's visit to the overcrowded courthouse inspired a promise to expand the institution with the extension of the courthouse. Martin's 'shock' at the congestion of the original courthouse building, inspired the promise for two new buildings to be added.
The L.O. Martin Room was originally utilised as the Female Witnesses' Room before being moved to the new wing of the courthouse following the 1949 extension inspired by the visit of L.O. Martin. After the extension of the Courthouse, the room was converted to house a Judges office.
L.O. Martin Room

Photo 65

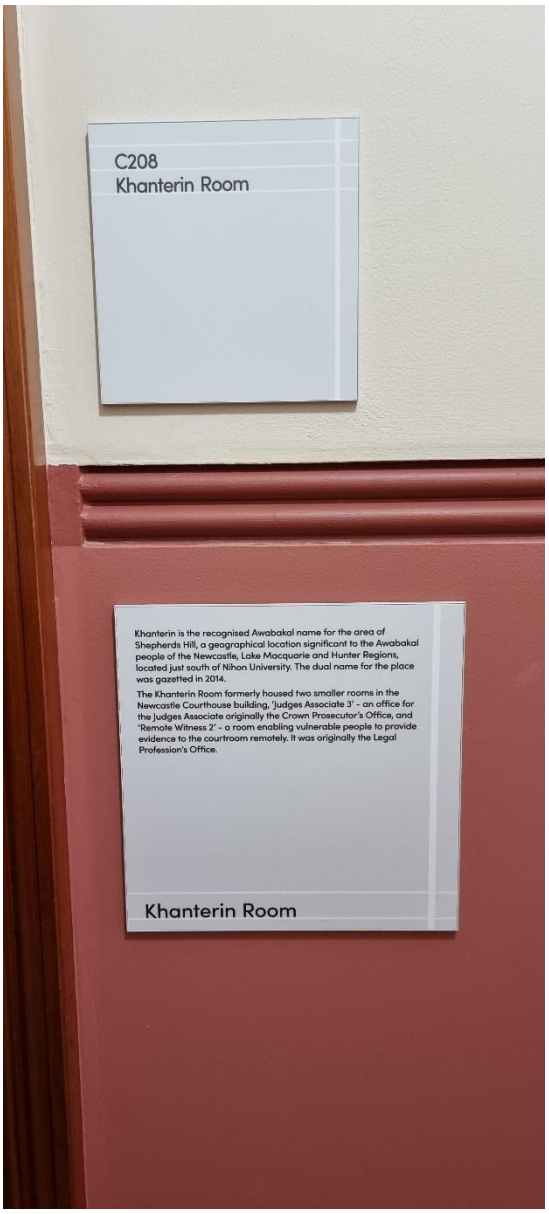


Photo 66



Photo 67



Photo 68

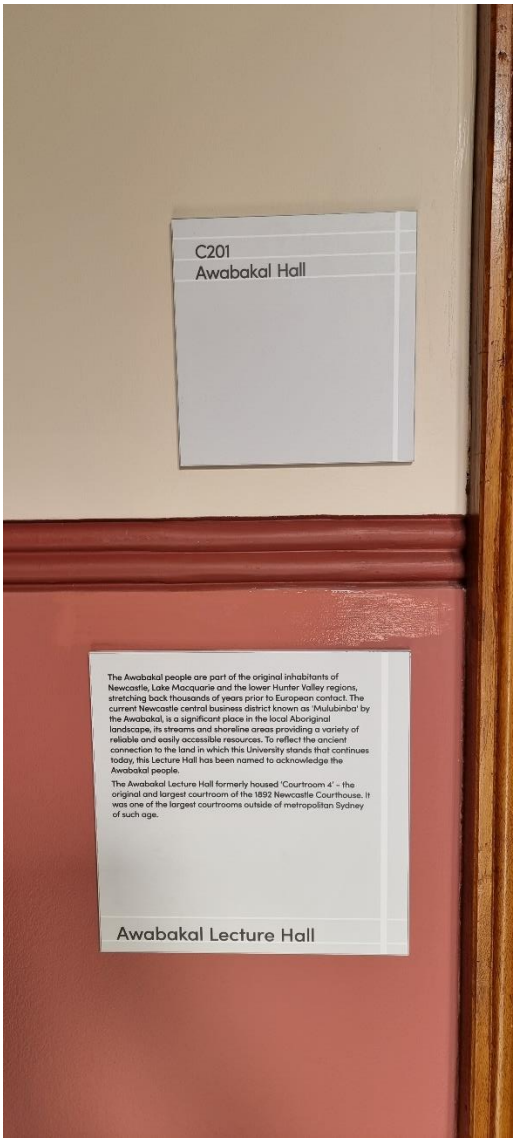


Photo 69

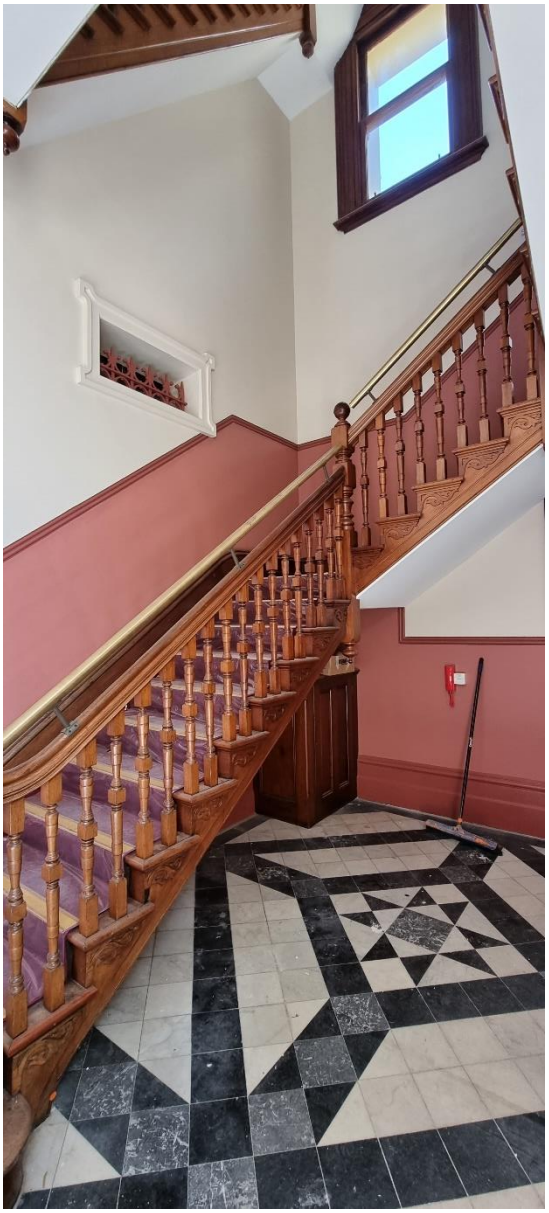


Photo 70



Photo 71



Photo 72



Photo 73



Photo 74

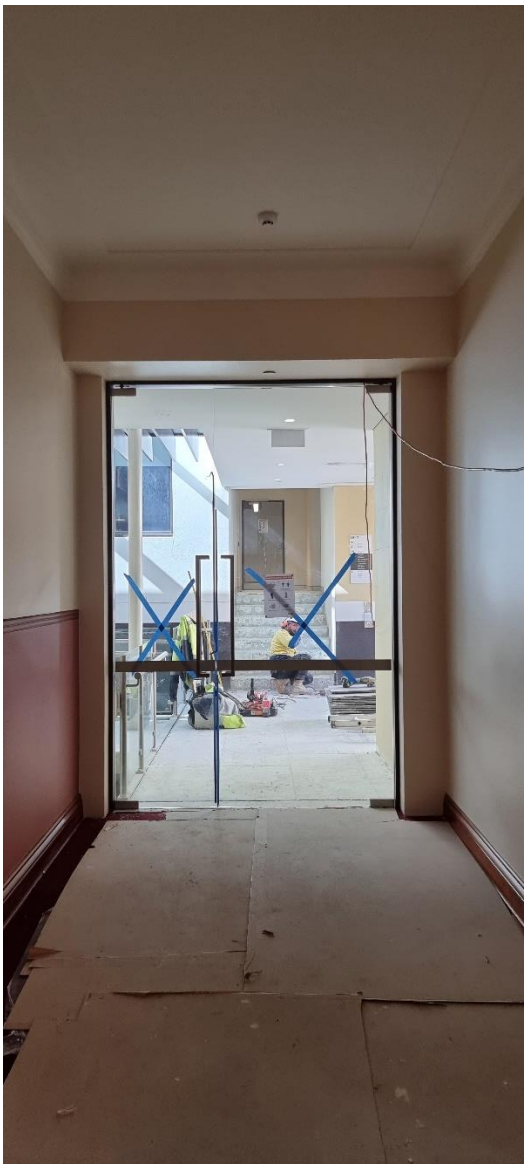


Photo 75



Photo 76



Photo 77



Photo 78



Photo 79



Photo 80



Photo 81


C203
Nihon Room
Nihon from 日本大学 (Nihon Daigaku) reflects the new owners of the Newcastle Courthouse building in Nihon University. Originally Nihon Law School, Nihon University (1903) was founded by Japanese Statesman Yamada Akiyoshi in 1889. Yamada strongly believed that the modernisation of Japan required education and research of legal principle on the basis of Japanese history, culture and traditions. In celebration of the strong link between the founding principles of Nihon University and the history of the Newcastle Courthouse, this room takes its name in honour of its new owners.
The Nihon Room formerly housed the legal aid room of the Newcastle Courthouse. It was the original 1892 Police Magistrate's Room. During times of heavy congestion in the courthouse particularly in the 1920s/30s, the Magistrate's Room held impromptu court sessions to ease the flow of cases.
Nihon Room

Photo 82

Level 3



Photo 83



Photo 84

Building C – Residential

Level 1

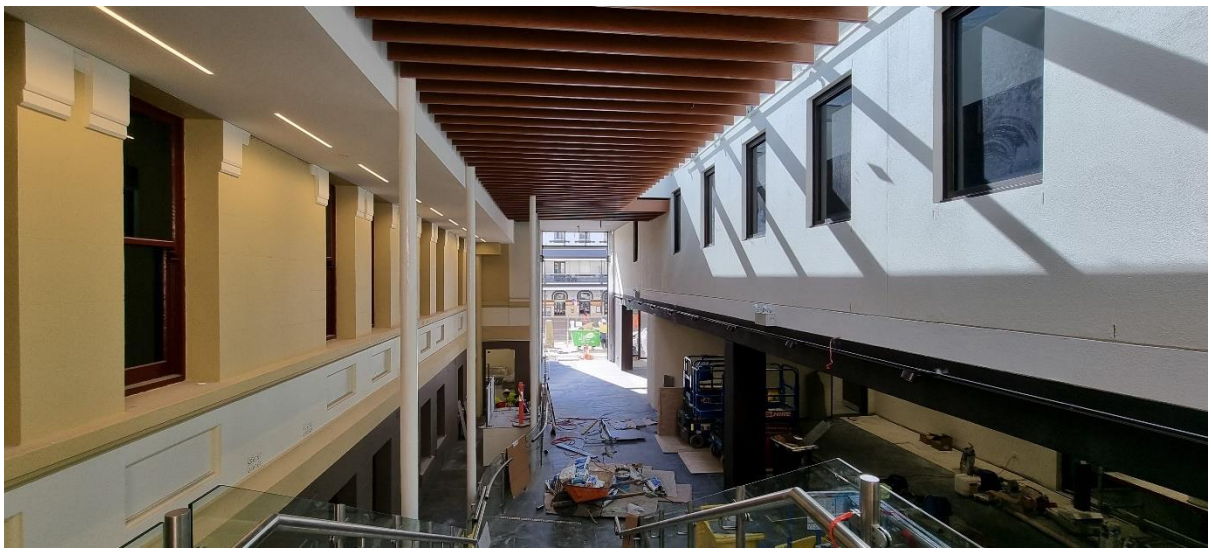


Photo 85



Photo 86



Photo 87



Photo 88

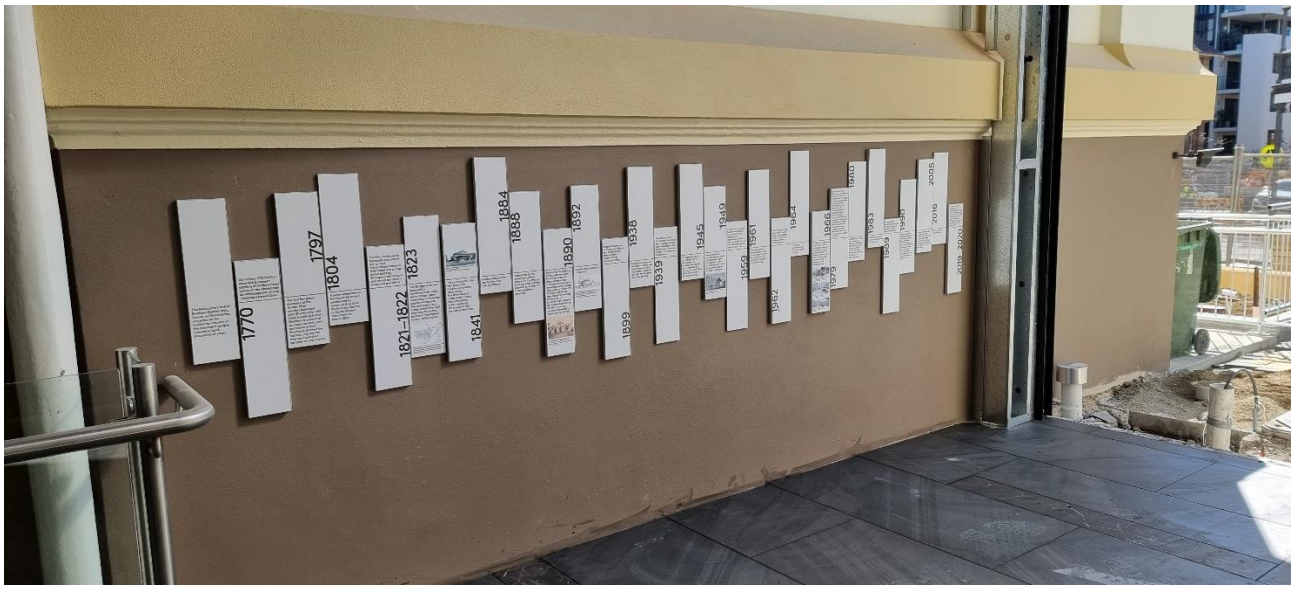


Photo 89

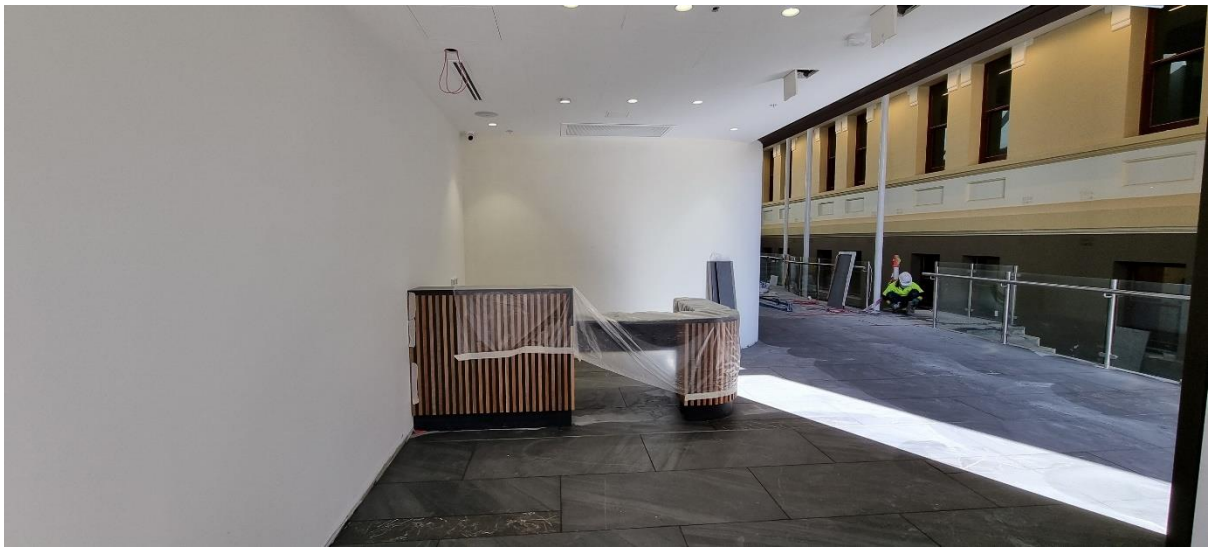


Photo 90



Photo 91



Photo 92



Photo 93



Photo 94



Photo 95



Photo 96



Photo 97



Photo 98



Photo 99

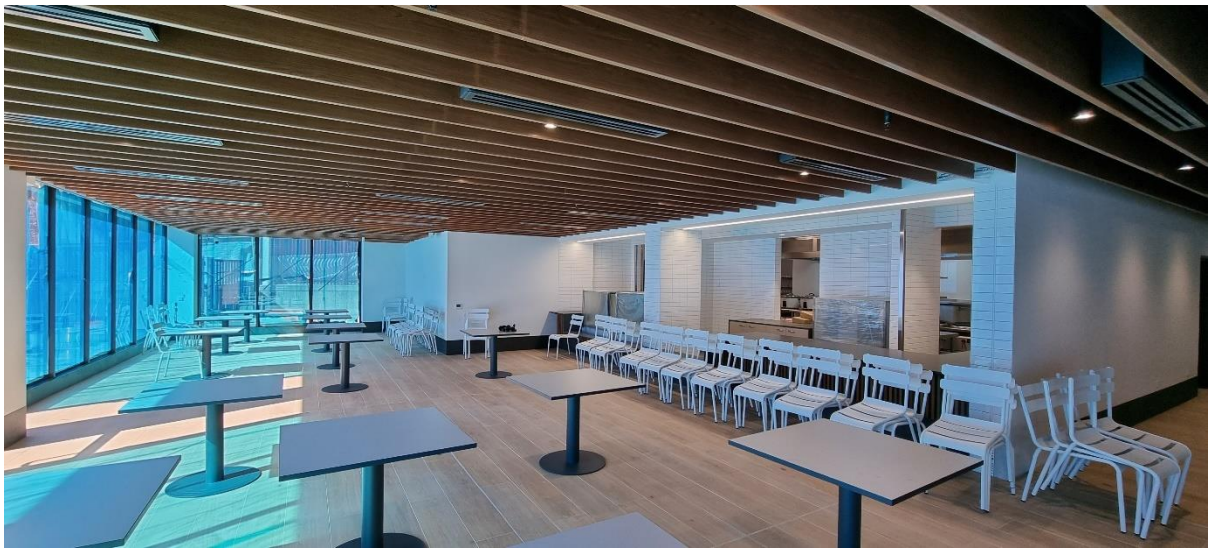


Photo 100



Photo 101



Photo 102



Photo 103



Photo 104



Photo 105



Photo 106



Photo 107



Photo 108

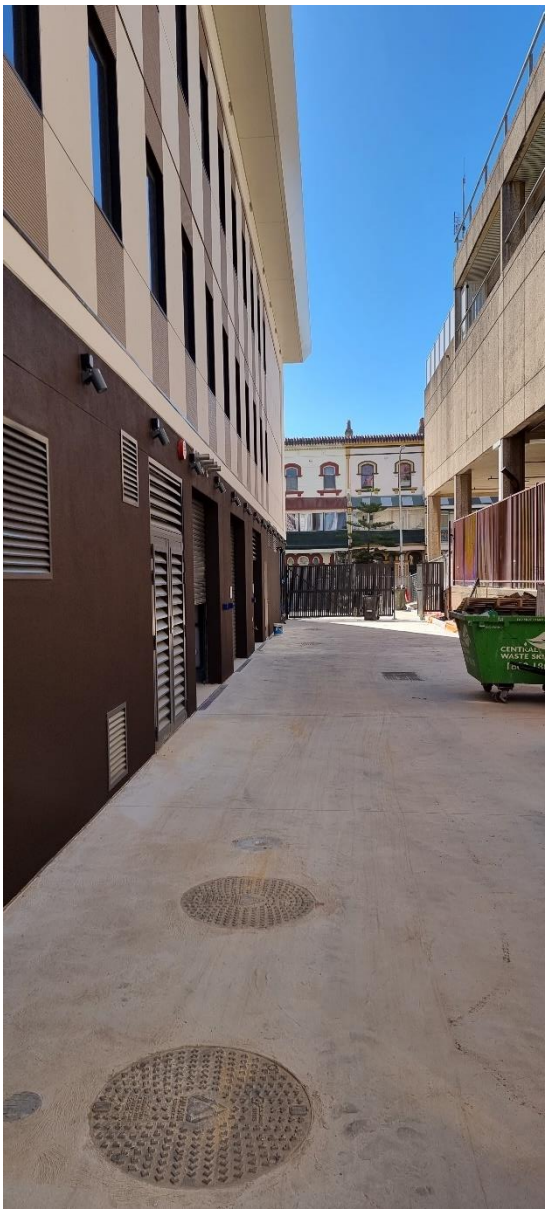


Photo 109

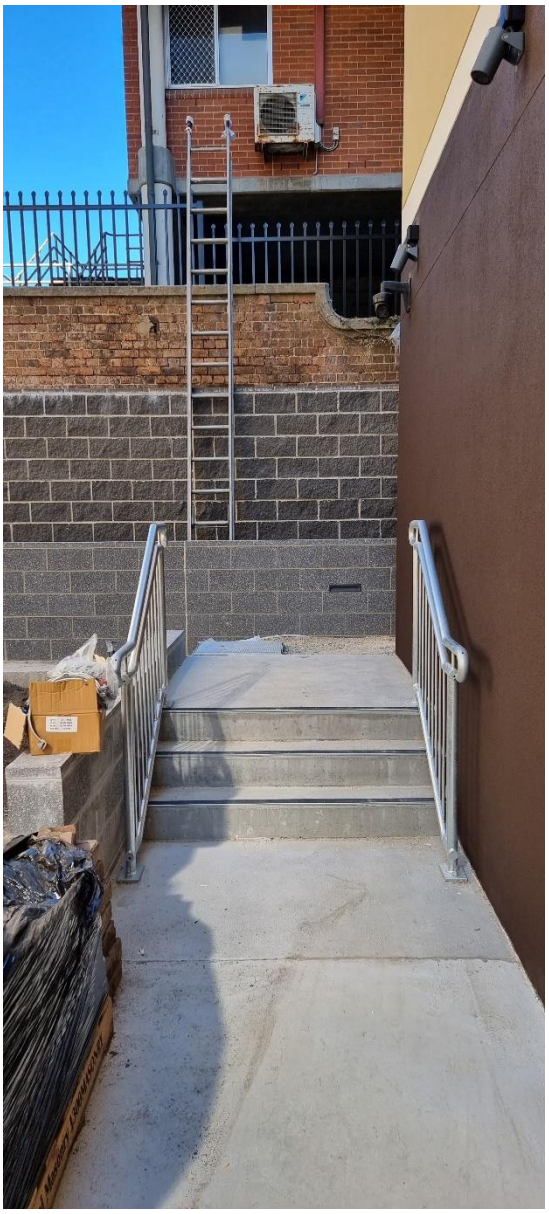


Photo 110

Level 2



Photo 111



Photo 112



Photo 113



Photo 114



Photo 115



Photo 116



Photo 117



Photo 118

Level 3



Photo 119



Photo 120



Photo 121



Photo 122



Photo 123



Photo 124

Level 4

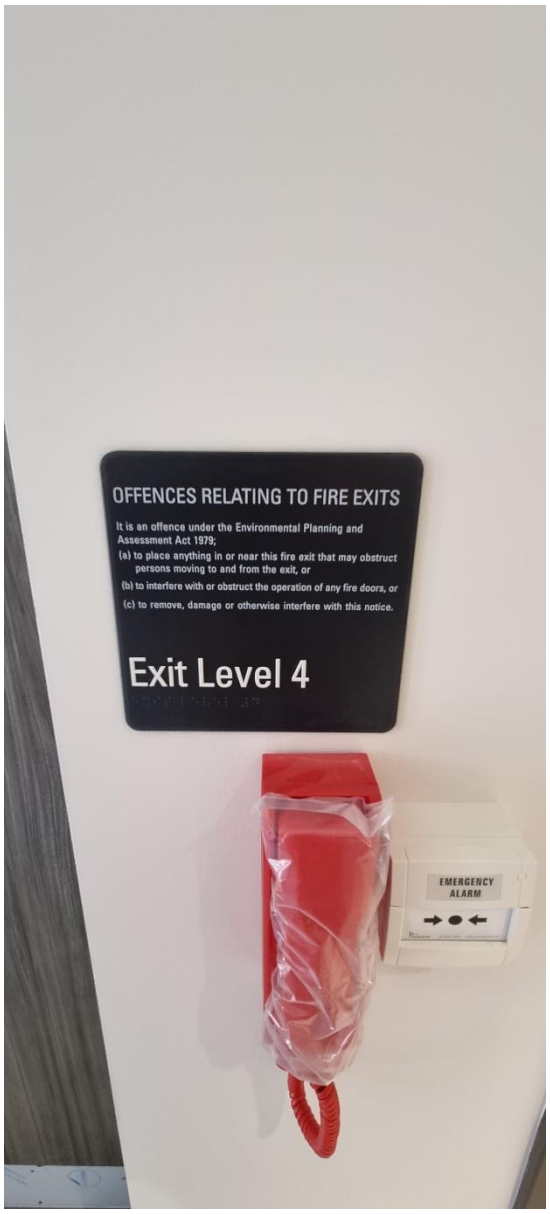


Photo 125



Photo 126



Photo 127

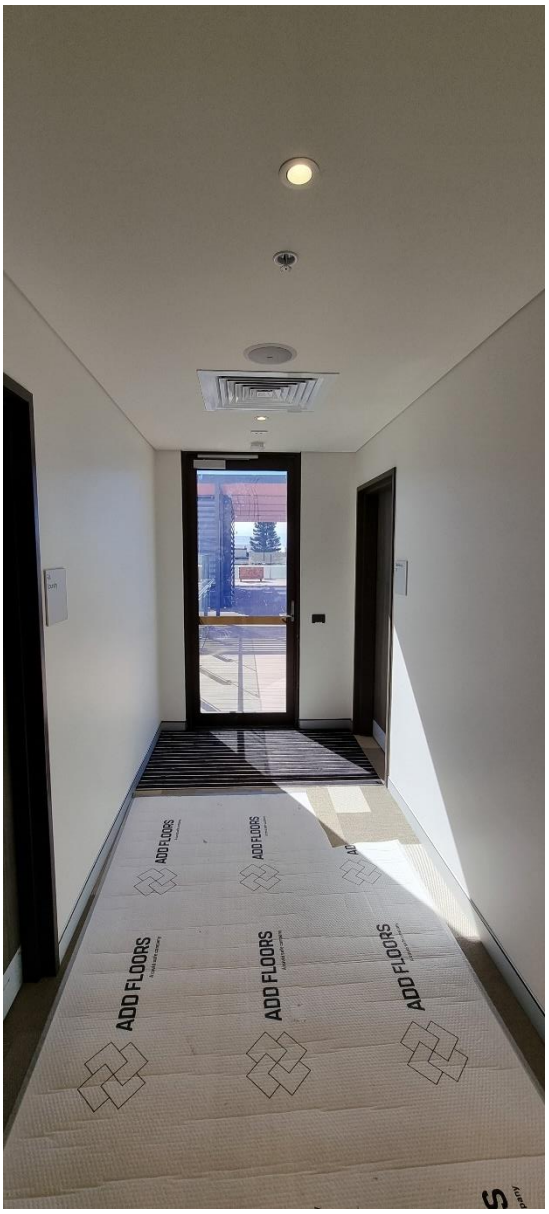


Photo 128



Photo 129



Photo 130



Photo 131



Photo 132



Photo 133



Photo 134



Photo 135



Photo 136



Photo 137

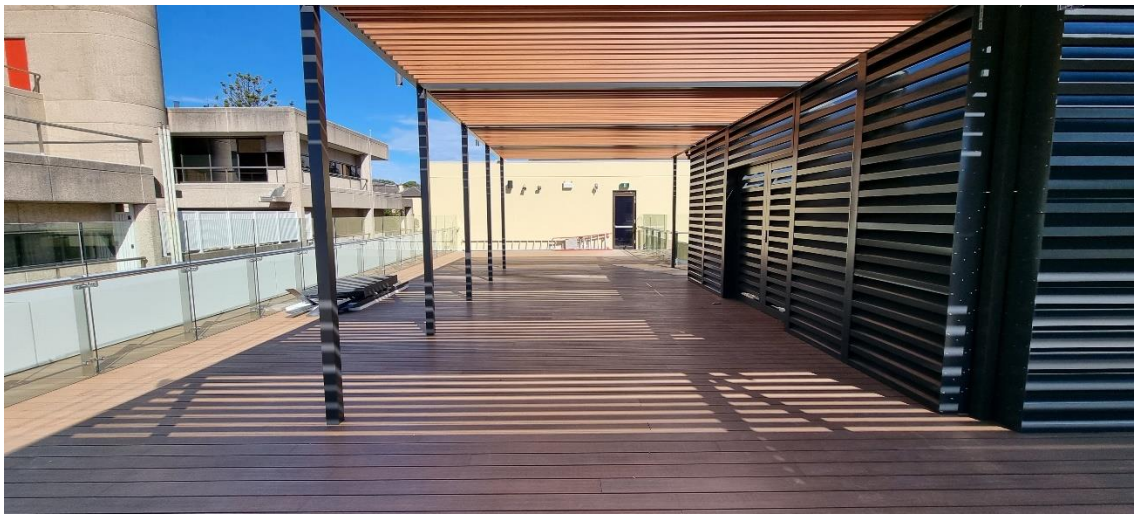


Photo 138

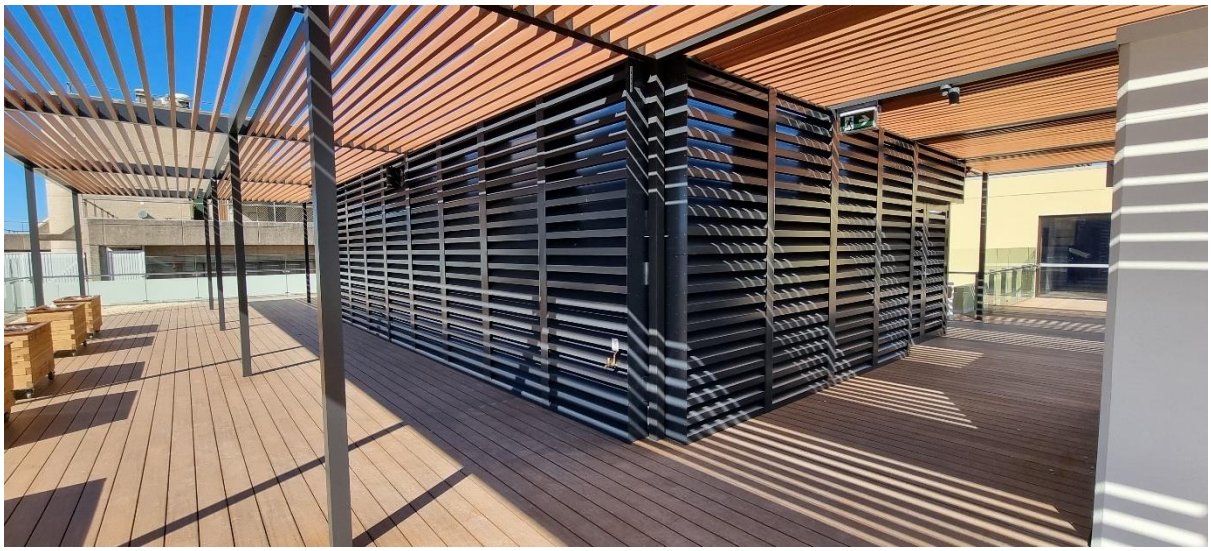


Photo 139

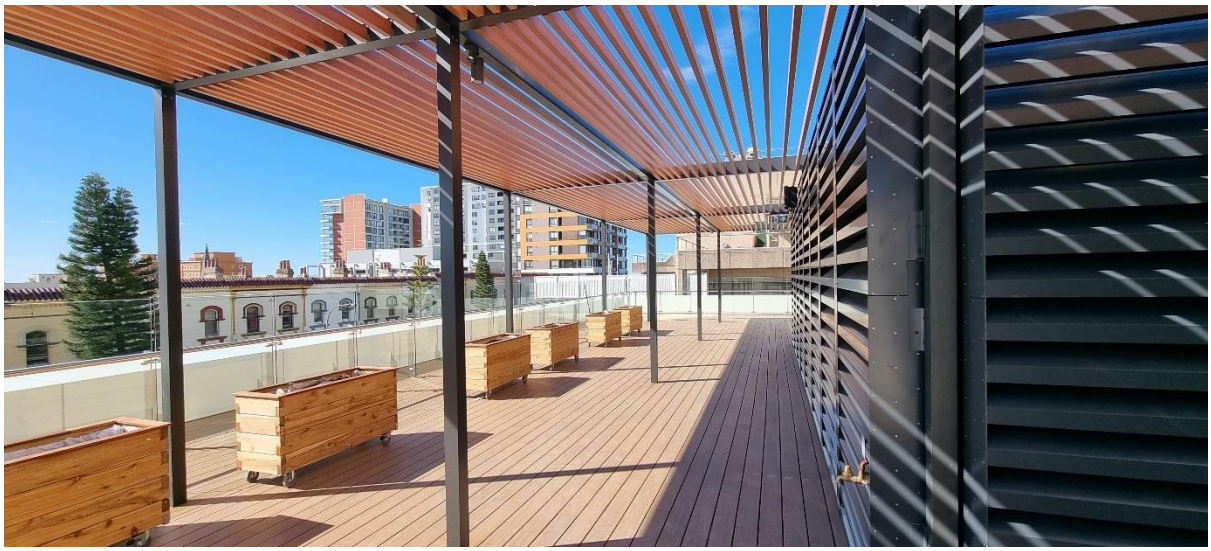


Photo 140

External



Photo 141



Photo 142



Photo 143



Photo 144



Photo 145

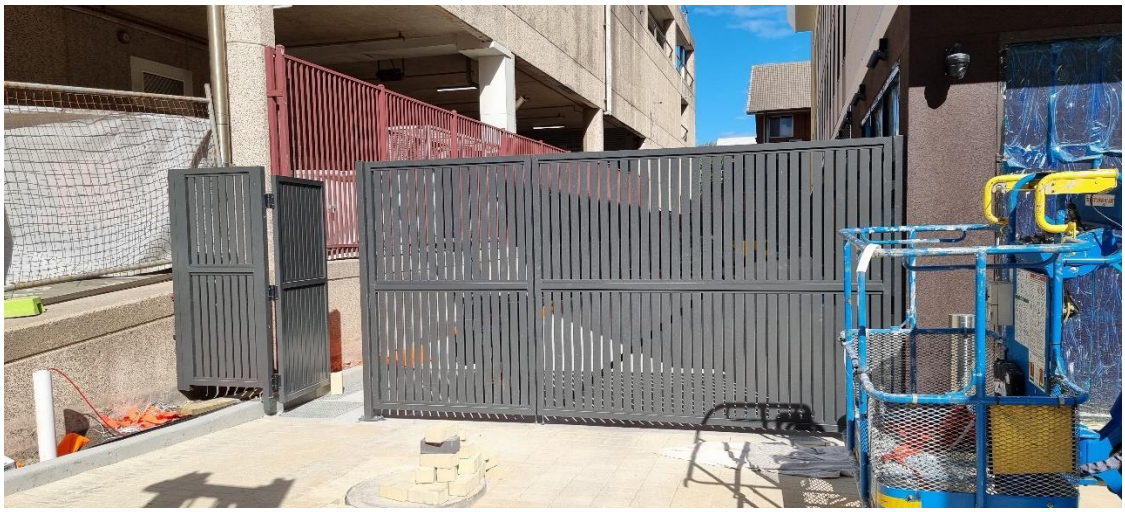


Photo 146



Photo 147



Photo 148



Photo 149



Photo 150



Photo 151



Photo 152



Photo 153



Photo 154



Photo 155



Photo 156



Photo 157



Photo 158



Photo 159



Photo 160



Photo 161

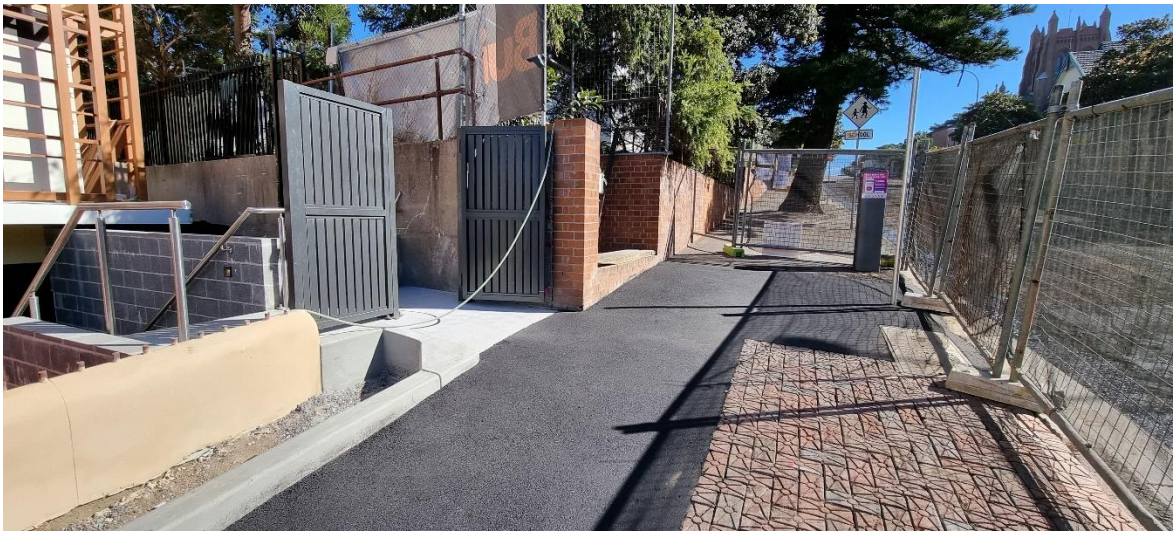


Photo 162



Photo 163



Photo 164



Photo 165

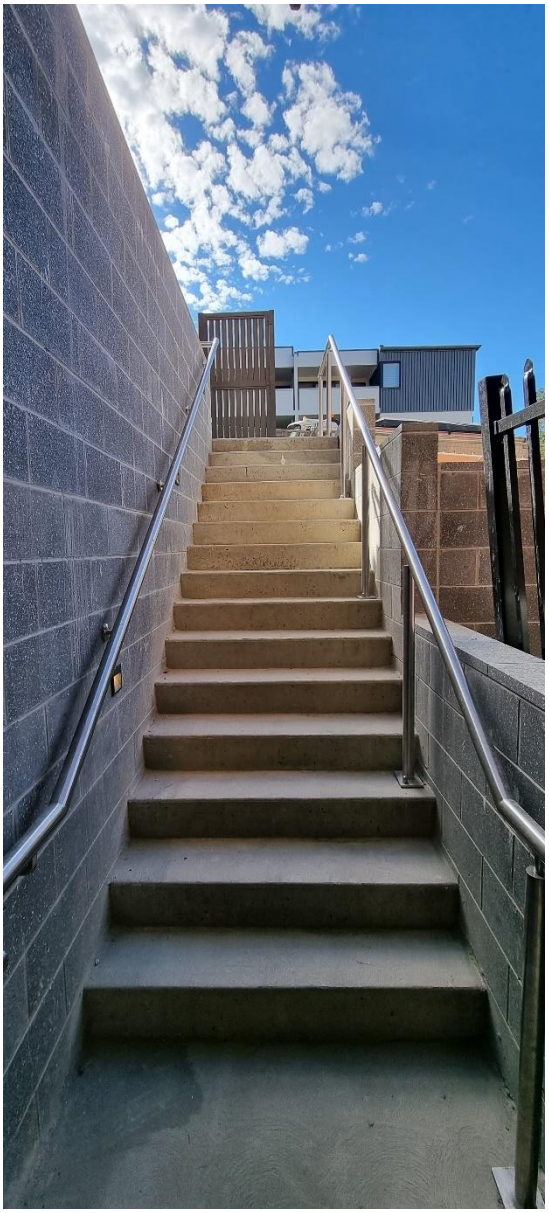


Photo 166



Photo 167



Photo 168



Photo 169



Photo 170



Photo 171



Photo 172



Photo 173

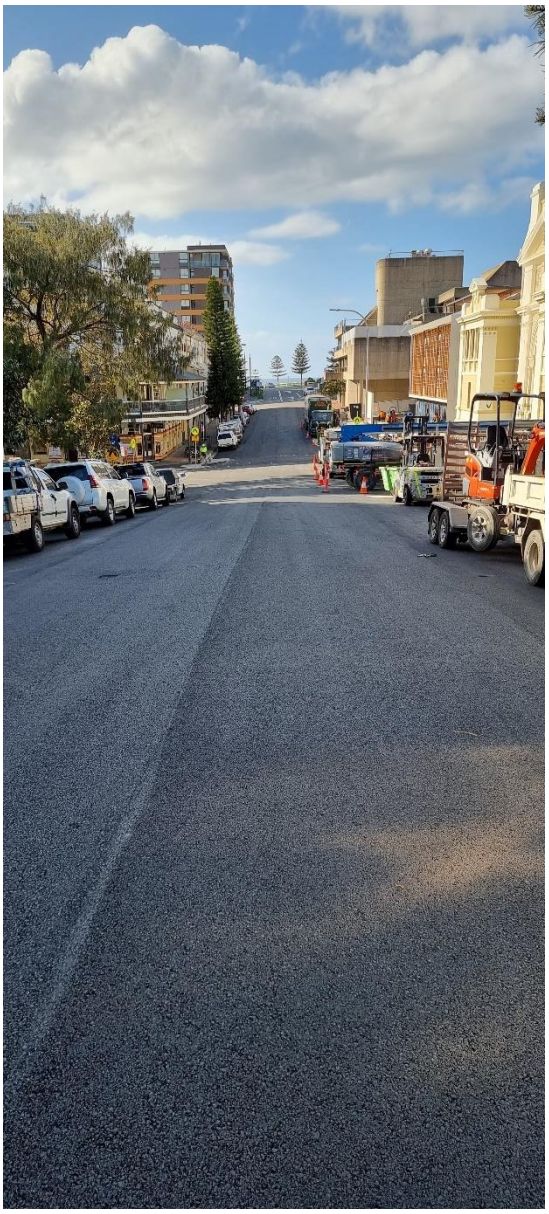


Photo 174

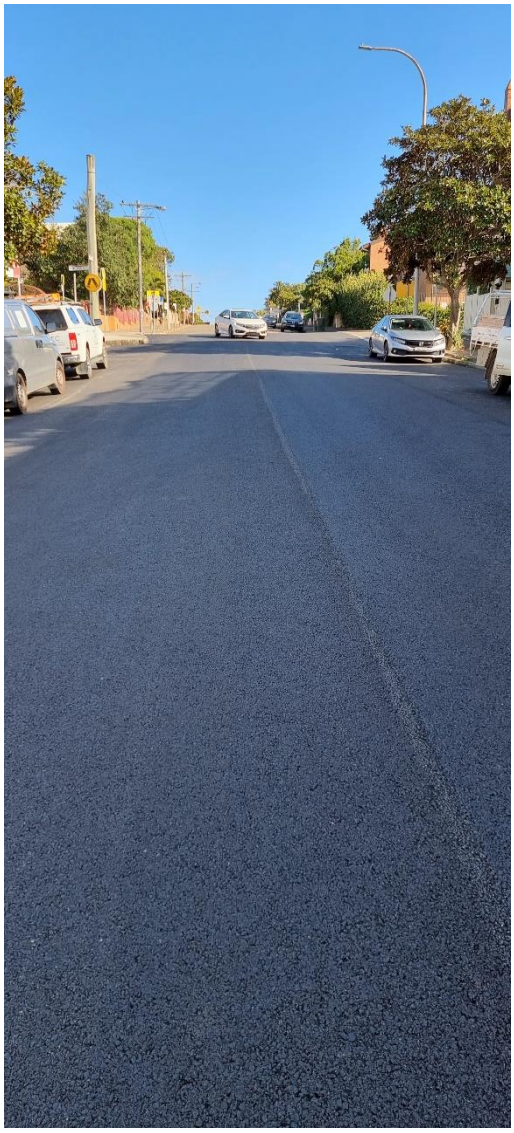


Photo 175



Photo 176



Photo 177



Photo 178



Photo 179



Photo 180



Photo 181



Photo 182



Photo 183



Photo 184



Photo 185

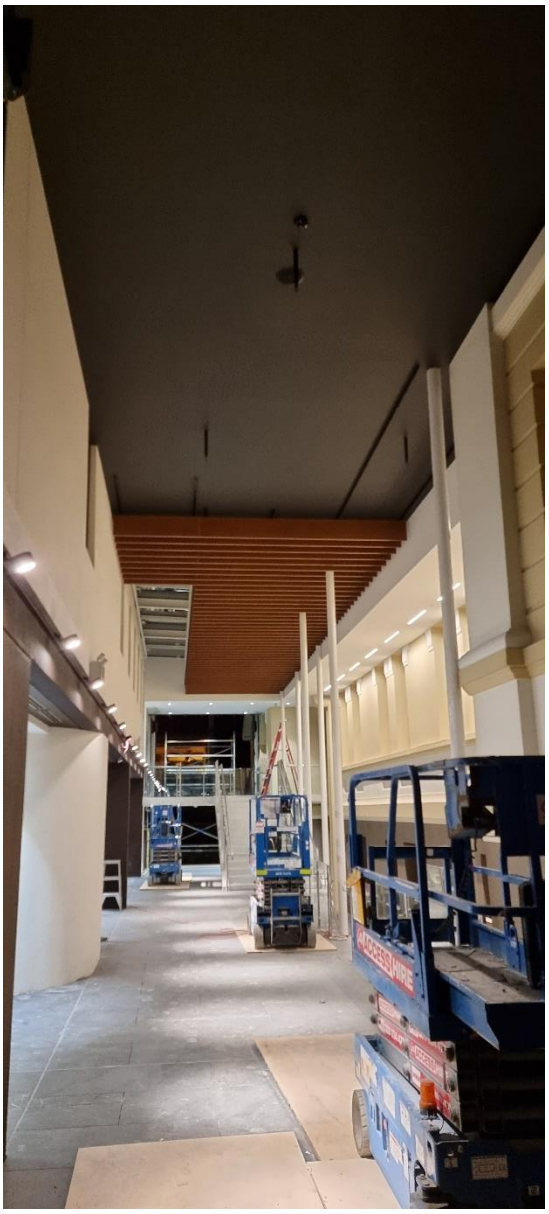


Photo 186



Photo 187



Photo 188



Photo 189

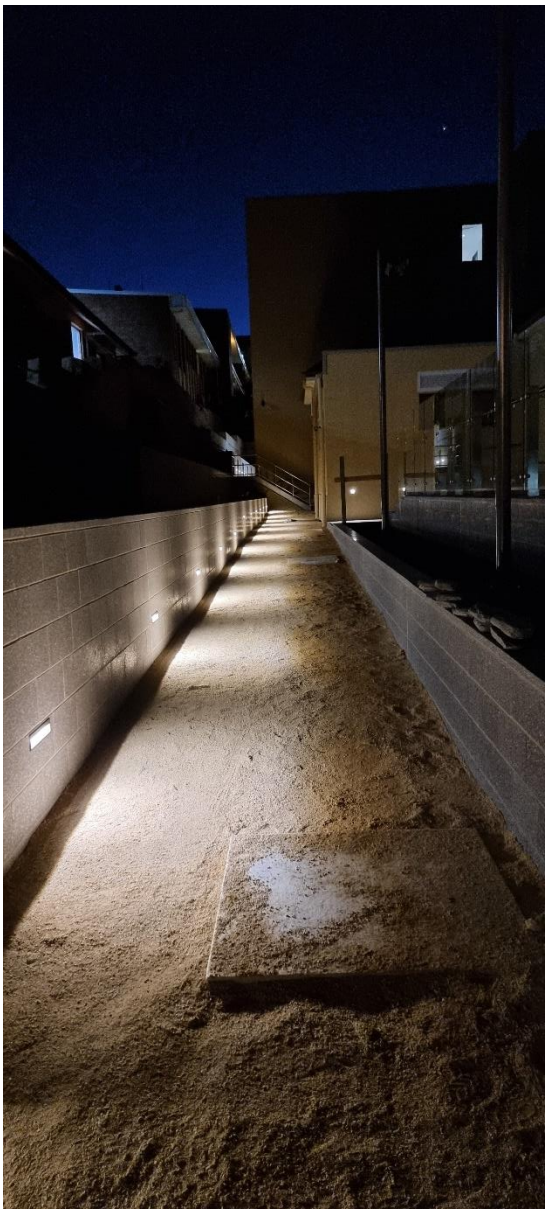


Photo 190



Photo 191

Appendix G – Workflow Status

Workflow Status

Project Name: Nihon University

Date Generated: Jul 30, 2021

On Time

	No. of Workflows
Completed	51
Total	**51**

Overdue

	No. of Workflows
Completed	65
Total	**65**

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000002	Workflow Test	Completed	May 26, 2020	May 28, 2020	Jun 3, 2020	4
WF-000003	Test Consultant Workflow	Completed	May 28, 2020	May 28, 2020	Jun 1, 2020	2
WF-000004	Hydraulic Services Shop Drawings	Completed	Jun 4, 2020	Jun 23, 2020	Jun 10, 2020	-9
WF-000005	Hydraulic Services Shop Drawings	Completed	Jun 10, 2020	Jun 23, 2020	Jun 19, 2020	-2
WF-000006	Formwork Shop Drawing Workflow	Completed	Jun 16, 2020	Jul 1, 2020	Jun 26, 2020	-3
WF-000007	Lift Shop Drawing Workflow 02	Completed	Jun 18, 2020	Jun 29, 2020	Jun 30, 2020	1
WF-000008	Formwork Shop Drawing Workflow 02	Completed	Jun 18, 2020	Jun 19, 2020	Jun 30, 2020	7
WF-000009	Formwork Shop Drawing Workflow - Concrete Profile	Completed	Jun 26, 2020	Jun 29, 2020	Jul 8, 2020	7
WF-000010	Formwork Shop Drawing Workflow	Completed	Jun 29, 2020	Jul 2, 2020	Jul 9, 2020	5
WF-000011	Formwork Shop Drawing Workflow	Completed	Jun 29, 2020	Jul 1, 2020	Jul 9, 2020	6

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000012	Platform Lift Shop Drawing	Completed	Jul 1, 2020	Jul 21, 2020	Jul 13, 2020	-6
WF-000013	Formwork Shop Drawings - Building C	Completed	Jul 2, 2020	Jul 17, 2020	Jul 14, 2020	-3
WF-000014	Formwork Shop Drawings - Building A	Completed	Jul 8, 2020	Jul 20, 2020	Jul 20, 2020	0
WF-000015	Formwork Shop Drawings - Building A	Completed	Jul 8, 2020	Jul 10, 2020	Jul 20, 2020	6
WF-000016	Post Tension Shop Drawings - Building C	Completed	Jul 8, 2020	Jul 29, 2020	Jul 20, 2020	-7
WF-000017	Formwork Shop Drawings - Building A	Completed	Jul 10, 2020	Jul 20, 2020	Jul 22, 2020	2
WF-000018	Formwork Shop Drawings - Building C	Completed	Jul 10, 2020	Jul 22, 2020	Jul 22, 2020	0
WF-000019	Lift Shop Drawing - Building A	Completed	Jul 10, 2020	Jul 14, 2020	Jul 22, 2020	6
WF-000020	Lift Shop Drawing - Building C	Completed	Jul 10, 2020	Jul 23, 2020	Jul 22, 2020	-1
WF-000021	General Formwork Shop Drawings	Completed	Jul 17, 2020	Jul 29, 2020	Jul 29, 2020	0
WF-000022	Platform Lift Shop Drawing	Completed	Jul 21, 2020	Aug 4, 2020	Jul 31, 2020	-2
WF-000023	Formwork Shop Drawings - Building A - Level 2 Concrete Profile Queries	Completed	Jul 21, 2020	Aug 4, 2020	Jul 31, 2020	-2
WF-000024	Formwork Shop Drawings - Building C - Stair C1 (L2 to Roof)	Completed	Jul 23, 2020	Aug 4, 2020	Aug 4, 2020	0
WF-000025	Formwork Shop Drawings - Building C - Stair C1 (L1 to L2)	Completed	Jul 23, 2020	Aug 4, 2020	Aug 4, 2020	0
WF-000026	Formwork Shop Drawings - Building C - Stair C2 (L1 to L2)	Completed	Jul 24, 2020	Aug 4, 2020	Aug 5, 2020	1
WF-000027	Formwork Shop Drawings - Building C - Stair C2 (L2 to Roof)	Completed	Jul 24, 2020	Aug 7, 2020	Aug 5, 2020	-2
WF-000028	Formwork Shop Drawings - Building A - Stair A2 (L1 to Roof)	Completed	Jul 24, 2020	Aug 7, 2020	Aug 5, 2020	-2
WF-000030	Post Tension - Building C - Level 3	Completed	Jul 27, 2020	Aug 13, 2020	Aug 6, 2020	-5

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000032	Formwork Shop Drawings - Building C - L2 & L3 Concrete Profile and Table Layout	Completed	Jul 27, 2020	Aug 10, 2020	Aug 6, 2020	-2
WF-000033	Formwork Shop Drawings [2] - Building A - Level 2 Table Layout	Completed	Jul 27, 2020	Aug 12, 2020	Aug 6, 2020	-4
WF-000034	Formwork Shop Drawings - Building A - Shear Walls (SW1, SW2, SW3)	Completed	Jul 28, 2020	Aug 12, 2020	Aug 7, 2020	-3
WF-000035	Siphonic Shop Drawings	Completed	Jul 30, 2020	Aug 13, 2020	Aug 11, 2020	-2
WF-000036	Lift Shop Drawing - Building A - Lift E1	Completed	Aug 3, 2020	Aug 12, 2020	Aug 13, 2020	1
WF-000037	Hydraulic Shop Drawings - TMV Locations	Completed	Aug 3, 2020	Aug 13, 2020	Aug 13, 2020	0
WF-000038	Platform Lift Shop Drawing - Revision 5	Completed	Aug 4, 2020	Aug 17, 2020	Aug 14, 2020	-1
WF-000039	Electrical Shop Drawings - Building A - Main Switchboard	Completed	Aug 4, 2020	Aug 17, 2020	Aug 14, 2020	-1
WF-000041	Formwork Shop Drawings [2] - Building A	Completed	Aug 6, 2020	Aug 18, 2020	Aug 18, 2020	0
WF-000042	Formwork Shop Drawings - Building C	Completed	Aug 6, 2020	Aug 10, 2020	Aug 18, 2020	6
WF-000043	Fire Sprinkler Shop Drawings	Completed	Aug 6, 2020	Aug 19, 2020	Aug 18, 2020	-1
WF-000044	Post Tension - Building C Level 2 - AFC Review	Completed	Aug 10, 2020	Aug 13, 2020	Aug 17, 2020	2
WF-000046	Post Tension - Building A - Level 2	Completed	Aug 13, 2020	Aug 27, 2020	Aug 25, 2020	-2
WF-000047	Post Tension - Building C Residential - Level 4	Completed	Aug 17, 2020	Aug 18, 2020	Aug 27, 2020	7
WF-000048	Formwork Shop Drawings - Building C Residential - Level 4 & Roof Concrete Profiles	Completed	Aug 17, 2020	Aug 27, 2020	Aug 27, 2020	0
WF-000049	Formwork Shop Drawings - Building A - Level 3 - Concrete Profile	Completed	Aug 17, 2020	Aug 27, 2020	Aug 27, 2020	0
WF-000052	Post Tension - Building A - LEVEL 3 & Typical Punching Shear Detail	Completed	Aug 20, 2020	Sep 8, 2020	Sep 1, 2020	-5
WF-000053	Arcadia Louvre & Screens - Shop Drawings	Completed	Aug 21, 2020	Aug 24, 2020	Sep 2, 2020	7

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000054	Electrical Shop Drawings - MSB & Labelling	Completed	Aug 21, 2020	Sep 8, 2020	Sep 2, 2020	-4
WF-000056	Post Tension - Building C - Roof	Completed	Aug 24, 2020	Aug 25, 2020	Sep 3, 2020	7
WF-000057	Fire Sprinkler Shop Drawings - Level 1 Heritage Courthouse	Completed	Aug 27, 2020	Sep 8, 2020	Sep 8, 2020	0
WF-000058	Dry Fire Shop Drawings	Completed	Aug 27, 2020	Sep 8, 2020	Sep 8, 2020	0
WF-000059	Platform Lift Shop Drawing	Completed	Aug 27, 2020	Sep 8, 2020	Sep 8, 2020	0
WF-000060	Mechanical_Heritage Building Plantrooms	Completed	Sep 3, 2020	Sep 16, 2020	Sep 15, 2020	-1
WF-000061	MSSB-1 Education Building	Completed	Sep 4, 2020	Sep 16, 2020	Sep 16, 2020	0
WF-000063	Formwork Shop Drawings - Building A	Completed	Sep 10, 2020	Sep 21, 2020	Sep 22, 2020	1
WF-000064	Barrisol Lighting	Completed	Sep 11, 2020	Oct 22, 2020	Sep 23, 2020	-21
WF-000066	Fire Sprinkler and Hydrant Shop Drawings	Completed	Sep 11, 2020	Sep 28, 2020	Sep 23, 2020	-3
WF-000067	Post Tension - Building C- Level 4	Completed	Sep 15, 2020	Sep 23, 2020	Sep 25, 2020	2
WF-000068	Formwork Shop Drawings - Building A- Roof Concrete Profile	Completed	Sep 16, 2020	Sep 29, 2020	Sep 28, 2020	-1
WF-000069	Arcadia Louvre & Screens - Shop Drawings_Rev B	Completed	Sep 17, 2020	Oct 2, 2020	Sep 29, 2020	-3
WF-000070	Mechanical Shop Drawings	Completed	Sep 18, 2020	Sep 30, 2020	Sep 30, 2020	0
WF-000071	Kitchen Shop Drawings	Completed	Sep 23, 2020	Oct 9, 2020	Oct 5, 2020	-4
WF-000072	Formwork Shop Drawings - Building A- Level 4 Concrete Profile	Completed	Sep 24, 2020	Oct 7, 2020	Oct 6, 2020	-1
WF-000073	Mechanical Shop Drawings	Completed	Sep 25, 2020	Oct 12, 2020	Oct 7, 2020	-3
WF-000074	Windows and Glazing	Completed	Sep 25, 2020	Oct 7, 2020	Oct 7, 2020	0
WF-000075	Joinery Shop Drawings_Batch 1	Completed	Sep 29, 2020	Nov 9, 2020	Oct 9, 2020	-21

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000076	Post Tension Shop Drawings - Building C- Roof Slab	Completed	Oct 1, 2020	Oct 12, 2020	Oct 13, 2020	1
WF-000077	Electrical Shop Drawings- Main Switch Board	Completed	Oct 1, 2020	Oct 19, 2020	Oct 13, 2020	-4
WF-000078	Windows and Glazing	Completed	Oct 1, 2020	Oct 14, 2020	Oct 13, 2020	-1
WF-000079	Joinery Shop Drawings	Completed	Oct 2, 2020	Oct 19, 2020	Oct 14, 2020	-3
WF-000080	Post Tension - Building A- Level 4	Completed	Oct 6, 2020	Oct 19, 2020	Oct 16, 2020	-1
WF-000081	Post Tension - Building A_Roof	Completed	Oct 7, 2020	Oct 26, 2020	Oct 19, 2020	-5
WF-000082	Mechanical Shop Drawings- Education Building	Completed	Oct 9, 2020	Oct 29, 2020	Oct 21, 2020	-6
WF-000083	Toilet Partitions- All Buildings	Completed	Oct 13, 2020	Oct 29, 2020	Oct 23, 2020	-4
WF-000084	Windows and Glazing- Fire Rated Windows	Completed	Oct 16, 2020	Dec 9, 2020	Oct 28, 2020	-30
WF-000086	Windows and Glazing_Narrow Frameless Glazed Door	Completed	Oct 21, 2020	Oct 29, 2020	Nov 2, 2020	2
WF-000087	Windows and Glazing_Awning Window Detail	Completed	Oct 21, 2020	Oct 29, 2020	Nov 2, 2020	2
WF-000088	Arcadia Louvre & Screens - Shop Drawings	Completed	Oct 23, 2020	Oct 29, 2020	Nov 4, 2020	4
WF-000090	Mechanical Shop Drawings_Grille Schedule	Completed	Oct 28, 2020	Dec 16, 2020	Nov 9, 2020	-27
WF-000091	Joinery Shop Drawings	Completed	Oct 29, 2020	Dec 11, 2020	Nov 10, 2020	-23
WF-000097	Mechanical Shop Drawings	Completed	Nov 30, 2020	Jan 7, 2021	Dec 10, 2020	-20
WF-000098	Windows and Glazing	Completed	Dec 3, 2020	Dec 10, 2020	Dec 15, 2020	3
WF-000099	Structural Steel_Facade Mullions and Lintels_Education Building	Completed	Dec 4, 2020	Dec 14, 2020	Dec 16, 2020	2
WF-000100	Mechanical Shop Drawings_MSSB-2	Completed	Dec 4, 2020	Dec 15, 2020	Dec 16, 2020	1
WF-000101	Structural Steel_Mullions and Lintels_Residential Building	Completed	Dec 4, 2020	Dec 14, 2020	Dec 16, 2020	2
WF-000103	Mechanical Shop Drawings_MSSB 1_Education	Completed	Dec 7, 2020	Jan 7, 2021	Dec 17, 2020	-15

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000104	Structural Steel	Completed	Dec 9, 2020	Feb 1, 2021	Dec 21, 2020	-30
WF-000105	Fire Sprinkler Shop Drawings_RCP_Level 1 and 2 Residential	Completed	Dec 9, 2020	Jan 7, 2021	Dec 21, 2020	-13
WF-000106	Security Shop Drawings	Completed	Dec 10, 2020	Jan 21, 2021	Dec 22, 2020	-22
WF-000107	Electrical Shop Drawings_Distribution Boards	Completed	Dec 11, 2020	Jan 7, 2021	Dec 23, 2020	-11
WF-000108	Windows and Glazing_Window Schedules	Completed	Dec 11, 2020	Jan 7, 2021	Dec 23, 2020	-11
WF-000109	Balustrade and Handrails_BAL 01A	Completed	Dec 11, 2020	Dec 14, 2020	Dec 17, 2020	3
WF-000110	Equitone Shop Drawings_Rev 2	Completed	Dec 14, 2020	Jan 7, 2021	Dec 18, 2020	-14
WF-000111	Access Floors	Completed	Dec 14, 2020	Jan 7, 2021	Dec 18, 2020	-14
WF-000112	Balustrade and Handrails_S03 to S20	Completed	Dec 16, 2020	Jan 7, 2021	Dec 22, 2020	-12
WF-000113	Structural Steel_Education_Stair A3	Completed	Dec 17, 2020	Jan 21, 2021	Dec 29, 2020	-17
WF-000114	Structural Steel_Education Cladding Steel and Stair 06	Completed	Dec 18, 2020	Jan 21, 2021	Dec 30, 2020	-16
WF-000115	Structural Steel_Residential_Cladding Support Steel	Completed	Jan 14, 2021	Feb 12, 2021	Jan 26, 2021	-13
WF-000116	Structural Steel_Residential Atrium	Completed	Jan 21, 2021	Feb 17, 2021	Feb 2, 2021	-11
WF-000117	Alpolic Shop Drawings	Completed	Jan 21, 2021	Feb 17, 2021	Jan 27, 2021	-15
WF-000118	Windows and Glazing	Completed	Feb 2, 2021	Feb 17, 2021	Feb 8, 2021	-7
WF-000119	Toilet Partitions- Bench Seat	Completed	Feb 3, 2021	Feb 22, 2021	Feb 15, 2021	-5
WF-000120	Electrical Shop Drawings_PFC	Completed	Feb 4, 2021	Mar 3, 2021	Feb 16, 2021	-11
WF-000121	Outdure Decking	Completed	Feb 10, 2021	Feb 12, 2021	Feb 22, 2021	6
WF-000124	Operable Walls	Completed	Feb 22, 2021	Feb 24, 2021	Feb 26, 2021	2
WF-000125	Monarch Renlita Doors	Completed	Feb 25, 2021	Mar 11, 2021	Mar 3, 2021	-6

Number	Name	Workflow Status	Start Date	Expected/Actual End Date	Original Due Date	Delay (days)*
WF-000126	Windows and Glazing- Terraces, Cafeteria and Education Building	Completed	Mar 8, 2021	Apr 9, 2021	Mar 18, 2021	-16
WF-000127	Joinery Shop Drawings- Niche Shelving	Completed	Mar 17, 2021	Apr 9, 2021	Mar 29, 2021	-9
WF-000128	Joinery Shop Drawings- Judges Shelving and Plaque Display	Completed	May 10, 2021	May 21, 2021	May 20, 2021	-1
WF-000129	Windows and Glazing_Skylights	Completed	May 21, 2021	Jun 2, 2021	Jun 2, 2021	0
WF-000130	Signage_Braille Signage	Completed	May 24, 2021	Jun 8, 2021	Jun 3, 2021	-3
WF-000131	Signage_Batch 2	Completed	Jun 3, 2021	Jun 18, 2021	Jun 15, 2021	-3
WF-000133	Signage	Completed	Jun 22, 2021	Jun 30, 2021	Jul 2, 2021	2
WF-000134	Signage- Batch 4	Completed	Jun 25, 2021	Jul 5, 2021	Jul 7, 2021	2
WF-000135	Signage_Batch 5	Completed	Jun 30, 2021	Jul 8, 2021	Jul 12, 2021	2
WF-000136	Signage_Batch 6	Completed	Jul 9, 2021	Jul 20, 2021	Jul 21, 2021	1
WF-000137	Signage_Batch 7	Completed	Jul 14, 2021	Jul 23, 2021	Jul 26, 2021	1

*__Delay:__ For In Progress Workflow it is the difference between Expected end date & Original due date. For Completed Workflow it is the difference between Actual end date & Original due date. (Days that are a part of the working week only are considered)

Note: For Delay - Positive is on/before time, Negative is behind time.

Filters: "Workflow Status" equals "Completed".

Appendix H – Statused SSD-9787 Conditions Matrix

	SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX	Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
	PART A - ADMINISTRATIVE CONDITIONS						
	Obligation to Minimise Harm to the Environment						
A1	In addition to meeting the specific performance measures and criteria in this consent, all reasonable and feasbible measures must be implemented to prevent, and, if prevention is not reasonable and feasible, minimise any material harm to the environment that may result from the construction and operation of the development.	Note	Note			✓	Compliant - ongoing
	Terms of Consent						
A2	The development may only be carried out: (a) in compliance with the conditions of this consent; (b) in accordance with all written directions of the Planning Secretary; (c) generally in accordance with the EIS and Response to Submissions; (d) in accordance with the approved plans in the table below:	Note	Note				Non-compliance received from GHD Audit 3 related to n/c with Condition D9
A3	Consistent with the requirements in this consent, the Planning Secretary may make written directions to the Applicant in relation to: (a) the content of any strategy, study, system, plan, program, review, audit, notification, report or correspondence submitted under or otherwise made in relation to this consent, including those that are required to be, and have been, approved by the Planning Secretary; (b) any reports, reviews or audits commissioned by the Planning Secretary regarding compliance with this approval; and (c) the implementation of any actions or measures contained in any such document referred to in (a) above.	Note	Note				Note
A4	The conditions of this consent and directions of the Planning Secretary prevail to the extent of any inconsistency, ambiguity or conflict between them and a document listed in condition A2(c). In the event of an inconsistency, ambiguity or conflict between any of the documents listed in condition A2(c), the most recent document prevails to the extent of the inconsistency, ambiguity or conflict.	Note	Note				Note
	Limits of Consent						
A5	This consent lapses five years after the date of consent unless work is physically commenced.	Note	Note				Note
	Prescribed Conditions						
A6	The Applicant must comply with all relevant prescribed conditions of development consent under Part 6, Division 8A of the EP&A Regulation.	Note	Note				Note
	Planning Secretary as Moderator						
A7	In the event of a dispute between the Applicant and a public authority, in relation to an applicable requirement in this approval or relevant matter relating to the Development, either party may refer the matter to the Planning Secretary for resolution. The Planning Secretary's resolution of the matter must be binding on the parties.	Note	Note				Note
	Evidence of Consultation						
A8	Where conditions of this consent require consultation with an identified party, the Applicant must: (a) consult with the relevant party prior to submitting the subject document for information or approval; and (b) provide details of the consultation undertaken including: (i) the outcome of that consultation, matters resolved and unresolved; and (ii) details of any disagreement remaining between the party consulted and the Applicant and how the Applicant has addressed the matters not resolved.	Note	Note			✓	Compliant - ongoing
	Staging						
A9	The project may be constructed and operated in stages. Where staged construction or operation is proposed, a Staging Report (for either or both construction and operation as the case may be) must be prepared and submitted for the information of the Planning Secretary. The Staging Report must be submitted to the Planning Secretary no later than one month before the commencement of construction of the first of the proposed stages of construction (or if only staged operation is proposed, one month before the commencement of operation of the first of the proposed stages of operation).	Note	Note		23-Jan-20		Closed
A10	A Staging Report prepared in accordance with condition A9 must: (a) if staged construction is proposed, set out how the construction of the whole of the project will be staged, including details of work and other activities to be carried out in each stage and the general timing of when construction of each stage will commence and finish; (b) if staged operation is proposed, set out how the operation of the whole of the project will be staged, including details of work and other activities to be carried out in each stage and the general timing of when operation of each stage will commence and finish (if relevant); (c) specify how compliance with conditions will be achieved across and between each of the stages of the project; and (d) set out mechanisms for managing any cumulative impacts arising from the proposed staging.				24-Jan-20		Closed
A11	Where staging is proposed, the project must be staged in accordance with the Staging Report, as submitted to the Planning Secretary.	Note	Note				Note
A12	Where staging is proposed, the terms of this approval that apply or are relevant to the works or activities to be carried out in a specific stage must be complied with at the relevant time for that stage.	Note	Note				Note
	Staging, Combining and Updating Strategies, Plans or Programs						
A13	With the approval of the Planning Secretary, the Applicant may: (a) prepare and submit any strategy, plan (including management plan, architectural or design plan) or program required by this consent on a staged basis (if a clear description is provided as to the specific stage and scope of the development to which the strategy, plan (including management plan, architectural or design plan) or program applies, the relationship of the stage to any future stages and the trigger for updating the strategy, plan (including management plan, architectural or design plan) or program); (b) combine any strategy, plan (including management plan, architectural or design plan), or program required by this consent (if a clear relationship is demonstrated between the strategies, plans (including management plan, architectural or design plan) or programs that are proposed to be combined); and (c) update any strategy, plan (including management plan, architectural or design plan), or program required by this consent (to ensure the strategies, plans (including management plan, architectural or design plan), or programs required under this consent are updated on a regular basis and incorporate additional measures or amendments to improve the environmental performance of the development).	Note	Note				Not triggered this period.
A14	If the Planning Secretary agrees, a strategy, plan (including management plan, architectural or design plan), or program may be staged or updated without consultation being undertaken with all parties required to be consulted in the relevant condition in this consent.	Note	Note				Note
A15	If approved by the Planning Secretary, updated strategies, plans (including management plan, architectural or design plan), or programs supersede the previous versions of them and must be implemented in accordance with the condition that requires the strategy, plan, program or drawing.	Note	Note				Note
	Structural Adequacy						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
A16	All new buildings and structures, and any alterations or additions to existing buildings and structures, that are part of the development, must be constructed in accordance with the relevant requirements of the BCA and any additional requirements of the Subsidence Advisory NSW where the building or structure is located on land within a declared Mine Subsidence District. Notes: • Part 8 of the EP&A Regulation sets out the requirements for the certification of the development. • Under section 21 of the Coal Mine Subsidence Compensation Act 2017, the Applicant is required to obtain the Chief Executive of Subsidence Advisory NSW's approval before carrying out certain development in a Mine Subsidence District.				23-Jul-20		Closed - CC2b
	[i] Structural adequacy of new buildings engineering certification required to the Certifier		Built	Northrop			Closed
	[ii] Structural adequacy of existing courthouse - certification required for earthquake strengthening + termite repairs - passed to the Certifier	Nihon		Cardno | dwp			Closed
	External Walls and Cladding						
A17	The external walls of all buildings including additions to existing buildings must comply with the relevant requirements of the BCA.				02-Sep-20		Closed - Refer dwp design statement 03 dated 02/09/20
	[i] Design certification of external walls including insulation		Built	dwp | Northrop			
	Site Contamination						
A18	Following the completion of demolition works and prior to the commencement of all other construction, additional site investigations of previously untested or inaccessible areas of the site must be undertaken in accordance with: (a) interim advice dated12 November 2019 and prepared by NSW EPA Accredited Site Auditor Ian Gregson, Principal Environmental Consultant, GHD; (b) the recommendations provided in the Phase 1 Environmental Site Assessment – Technical Note dated 29 April 2019 and prepared by Cardno; (c) NSW EPA Sampling Design Guidelines; (d) Guidelines for the NSW Site Auditor Scheme (3rd edition) 2017 https://www.epa.nsw.gov.au/publications/contaminatedland/17p0269-guidelines-for- thensw-site-auditor-scheme-third-edition; (e) Guidelines for Consultants Reporting on Contaminated Sites, 2011 www.epa.nsw.gov.au/resources/clm/20110650consultantsglines.pdf; (f) The National Environment Protection (assessment of contamination) Measures 2013 as amended; and (g) testing must include assessment of both the soil and groundwater profile.				28-Apr-20		Closed - Douglas Partners DSI Report accepted by GHD.
	[i] Additional site testing and reporting to be undertaken once demolition completed		Built	Douglas Partners			Closed
	[ii] Reviewing and advice on test methods	Nihon		GHD | dwp			Closed
A19	The additional site investigations report must be reviewed by a NSW EPA Accredited Site Auditor and the Conceptual Remediation Action Plan dated 28 May 2019, prepared by Cardno must be updated to reflect the findings of the additional site investigations required by condition A18. The updated remediation action plan must be approved by a NSW EPA Accredited Site Auditor and submitted to the Planning Secretary prior to the commencement of remediation works.				28-Apr-20		Closed - Approved RAP & DSI submitted to DPIE by dwp on 28/04/2020
	[i] Remedial Action Plan required to be updated and to be submitted to site auditor		Built	Douglas Partners			Closed
	[ii] Updated report to be reviewed and approved and forwarded to EPA + planning secretary	Nihon		GHD | dwp			Closed
A20	Remediation works approved as part of this development consent must be carried out in accordance with the remediation action plan approved by a NSW EPA Accredited Site Auditor pursuant to condition A19.					✓	Compliant - ongoing
	[i] Remedial works to be carried out in accordance with the approved RAP - certification required		Built	Douglas Partners			
	[ii] Review of completed remedial works documentation	Nihon		GHD | dwp			
	Applicability of Guidelines						
A21	References in the conditions of this consent to any guideline, protocol, Australian Standard or policy are to such guidelines, protocols, Standards or policies in the form they are in as at the date of this consent.	Note	Note				Note
A22	Consistent with the conditions of this consent and without altering any limits or criteria in this consent, the Planning Secretary may, when issuing directions under this consent in respect of ongoing monitoring and management obligations, require compliance with an updated or revised version of such a guideline, protocol, Standard or policy, or a replacement of them.	Note	Note				Note
	Monitoring and Environmental Audits						
A23	Any condition of this consent that requires the carrying out of monitoring or an environmental audit, whether directly or by way of a plan, strategy or program, is taken to be a condition requiring monitoring or an environmental audit under Division 9.4 of Part 9 of the EP&A Act. This includes conditions in respect of incident notification, reporting and response, noncompliance notification, Site audit report and independent auditing.	Note	Built	GHD | dwp		✓	Compliant - monitoring undertaken in accordance with plans.
	Note: For the purposes of this condition, as set out in the EP&A Act, "monitoring" is monitoring of the development to provide data on compliance with the consent or on the environmental impact of the development, and an "environmental audit" is a periodic or particular documented evaluation of the development to provide information on compliance with the consent or the environmental management or impact of the development.						Note
	Access to Information						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
A24	At least 48 hours before the commencement of construction until the completion of all works under this consent, or such other time as agreed by the Planning Secretary, the Applicant must: (a) make the following information and documents (as they are obtained or approved) publicly available on its website: (i) the documents referred to in condition A2 of this consent; (ii) all current statutory approvals for the development; (iii) all approved strategies, plans and programs required under the conditions of this consent; (iv) regular reporting on the environmental performance of the development in accordance with the reporting arrangements in any plans or programs approved under the conditions of this consent; (v) a comprehensive summary of the monitoring results of the development, reported in accordance with the specifications in any conditions of this consent, or any approved plans and programs; (vi) a summary of the current stage and progress of the development; (vii) contact details to enquire about the development or to make a complaint; (viii) a complaints register, updated monthly; (ix) audit reports prepared as part of any independent audit of the development and the Applicant's response to the recommendations in any audit report; (x) any other matter required by the Planning Secretary; and (b) keep such information up to date, to the satisfaction of the Planning Secretary.				23-Jan-20		Closed
	[i] Information required from contractor to be supplied throughout the construction phase - information website to be displayed on site		**Built**				**Closed**
	[ii] Web site to be established and maintained with current documents - updated with construction inputs - before the commencement of construction	**Nihon**		**Azusa | dwp**			**Closed**
	Compliance						
A25	The Applicant must ensure that all of its employees, contractors (and their sub-contractors) are made aware of, and are instructed to comply with, the conditions of this consent relevant to activities they carry out in respect of the development.	Note	Note			✓	Compliant - provided within contract documents & included within Site Induction
	Incident Notification, Reporting and Response						
A26	The Planning Secretary must be notified in writing to compliance@planning.nsw.gov.au immediately after the Applicant becomes aware of an incident. The notification must identify the development (including the development application number and the name of the development if it has one), and set out the location and nature of the incident.	Note	Note				Note
A27	Subsequent notification must be given and reports submitted in accordance with the requirements set out in **Appendix 2.**	Note	Note				
	Non-Compliance Notification						
A28	The Planning Secretary must be notified in writing to compliance@planning.nsw.gov.au within seven days after the Applicant becomes aware of any non-compliance. The Certifying Authority must also notify the Planning Secretary in writing to compliance@planning.nsw.gov.au within seven days after they identify any non-compliance.	Note	Note				Note
A29	The notification must identify the development and the application number for it, set out the condition of consent that the development is non-compliant with, the way in which it does not comply and the reasons for the non-compliance (if known) and what actions have been, or will be, undertaken to address the non-compliance.	Note	Note				Note
A30	A non-compliance which has been notified as an incident does not need to also be notified as a non-compliance.	Note	Note				
	Revision Strategies, Plans and Programs						
A31	Within three months of: (a) the submission of a compliance report under condition C22; (b) the submission of an incident report under condition A27; (c) the submission of an Independent Audit under condition C32; (d) the approval of any modification of the conditions of this consent; or (e) the issue of a direction of the Planning Secretary under condition A2 which requires a review, the strategies, plans and programs required under this consent must be reviewed, and the Planning Secretary and the Certifier must be notified in writing that a review is being carried out. If necessary to either improve the environmental performance of the development, cater for a modification or comply with a direction, the strategies, plans, programs or drawings required under this consent must be revised, to the satisfaction of the Planning Secretary and/or Certifier (where relevant). Where revisions are required, the revised document must be submitted to the Planning Secretary and/or Certifier for approval and/or information (where relevant) within six weeks of the review. Note: This is to ensure strategies, plans and programs are updated on a regular basis and to incorporate any recommended measures to improve the environmental performance of the development.						Not triggered this period.
	[i] Review and report strategy to be put in place		**Built**				**Closed**
	[ii] Review and report strategy to be put in place	**Nihon**		**Azusa | dwp**			**Closed**
	PART B - PRIOR TO ISSUE OF CONSTRUCTION CERTIFICATE						
	Certified Drawings						
B1	Prior to the issue of the relevant Construction Certificate, the Applicant must submit to the satisfaction of the Certifier structural drawings prepared and signed by a suitably qualified practising Structural Engineer that demonstrates compliance with this development consent.				23-Jul-20		Closed
	[i] Structural certification of compliance of new buildings - issued to the Certifier		**Built**	**Northrop**			**Closed**
	[ii] Structural certification of compliance of existing courthouse building - issued to the Certifier	**Nihon**		**Cardno**			**Closed**
	Development Contributions						
B2	Prior to the issue of any Construction Certificate (not including demolition or site remediation works), a Section 7.12 levy totalling **$288,992**, is to be paid to Council in accordance with Section 7.12 of the EP&A Act and City of Newcastle Section 7.12 Newcastle Local Infrastructure Contributions Plan 2019. Prior to payment Council can provide the value of the indexed levy.				21-Apr-20		Closed CC#1
	[i] Developer contribution to be paid prior to commencement of construction	**Nihon**		**Azusa | dwp**			
	External Walls and Cladding						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
B3	Prior to the issue of any Construction Certificate, the Applicant must provide the Certifier with documented evidence that the products and systems proposed for use or used in the construction of external walls, including finishes and claddings such as synthetic or aluminium composite panels, comply with the requirements of the BCA. The Applicant must provide a copy of the documentation given to the Certifier to the Planning Secretary within seven days after the Certifier accepts it.				02-Sep-20		Closed
	[i] Documented evidence to the Certifier and a copy to the Planning Secretary required	Nihon		dwp | Azusa			Closed
	Protection of Public Infrastructure						
B4	Prior to the issue of the relevant Construction Certificate, the Applicant must: (a) consult with the relevant owner and provider of services that are likely to be affected by the development to make suitable arrangements for access to, diversion, protection and support of the affected infrastructure; (b) prepare a dilapidation report identifying the condition of all public infrastructure in the vicinity of the site (including roads, gutters and footpaths); and (c) submit a copy of the dilapidation report to the Planning Secretary, Certifier and Council.				23-Jan-20		Closed
	[i] Communications strategies and dilapidation survey to be undertaken - copy of dilapidation report to Certifier + Council		Built				Closed
	[ii] Copy of dilapidation report forwarded to Planning Secretary	Nihon		dwp			Closed
	Pre-Construction Dilapidation Report						
B5	Prior to the issue of the relevant Construction Certificate, the Applicant must submit a pre- commencement dilapidation report to Council, NSW Heritage Division and the Certifier. The report must provide an accurate record of the existing condition of adjoining private properties, heritage items and Council assets that are likely to be impacted by the proposed works.				23-Jan-20		Closed
	[i] Dilapidation survey to be undertaken - copy of dilapidation report to Certifier + Council		Built				Closed
	[ii] Copy of dilapidation report forwarded to Planning Secretary	Nihon		dwp			Closed
	Ecologically Sustainable Development						
B6	Prior to the issue of any Construction Certificate, unless otherwise agreed by the Planning Secretary, the Applicant must demonstrate that ESD is being achieved by either: (a) registering for a minimum 4 star Green Star rating with the Green Building Council Australia and submit evidence of registration to the Certifier; or (b) seeking approval from the Planning Secretary for an alternative certification process.				10-Feb-20		Closed
	[i] Management of the green star process - assistance with alternative certification process		Built	dwp|Northrop			Closed
	[ii] Resolution of alternative certification process - notification to Planning Secretary for approval	Nihon		Azusa | dwp	17-Jan-20		Closed
	Operational Waste Storage and Processing						
B7	Prior to the issue of the relevant Construction Certificate, the Applicant must obtain agreement from Council for the design of the operational waste storage area (where waste removal will be undertaken by Council). Where waste removal will be undertaken by a third party, the design of the operational waste storage area must be in accordance with Council's standards. Evidence of the design and Council endorsement (where relevant) must be provided to the Certifier.				16-Apr-20		Closed - dwp Aconex of 6/04/20 ref: dwp AU-GCOR-000296 and dwp design statement 01 dated 16/04/20
	[i] DA approved stormwater drawings to be fowarded to Certifier		Built	dwp|Northrop			Closed
	[ii] Evidence of design and Council endorsement of operational waste storage and processing to be submitted to Certifier	Nihon		Azusa | dwp			Closed
	Rainwater Harvesting						
B8	Prior to the issue of the relevant Construction Certificate, the Applicant must ensure that a rainwater reuse/harvesting system for the development is developed for the site. A rainwater re- use plan must be prepared and certified by an experienced hydraulic engineer.				27-May-20		Closed - Submitted as part of CC#2 documentation
	[i] Rainwater reuse has been designed installation to be finalised + provided to the Certifier		Built	Cardno | Northrop			Closed
	Operational Car Parking and Service Vehicle Layout						
B9	Prior to the issue of the relevant Construction Certificate, compliance with the following requirements must be submitted to the satisfaction of the Certifier: (a) all vehicles must enter and leave the Site in a forward direction; (b) a minimum of 20 on-site car parking spaces for use during operation of the development and designed in accordance with the latest versions of AS 2890.1 and AS 2890.6; (c) the swept path of the longest construction vehicle entering and exiting the Site in association with the new work, as well as manoeuvrability through the Site, must be in accordance with the latest version of AS 2890.2; (d) the safety of vehicles and pedestrians accessing adjoining properties, where shared vehicle and pedestrian access occurs, is to be addressed; and (e) traffic management devices in the form of 'Stop' and 'Give Way to Pedestrian' signs and line marking must be installed at the entry of proposed driveways within the site and constructed in accordance with AS 2890.1:2004: Parking facilities 0 Off-street car parking.				16-Apr-20		Closed - Refer dwp design statement 01 dated 16/04/20
	[i] Final car parking and service layouts to be design certified + provided to the Certifier		Built	dwp | Northrop			Closed
	Bicycle Parking and End of Trip Facilities						
B10	Prior to the issue of the relevant Construction Certificate, compliance with the following requirements for secure bicycle parking and end-of-trip facilities must be submitted to the satisfaction of the Certifier: (a) the provision of a minimum 22 bicycle parking spaces; (b) the layout, design and security of bicycle facilities must comply with the minimum requirements of the latest version of AS 2890.3:2015 Parking facilities - Bicycle parking, and be located in easy to access, well-lit areas that incorporate passive surveillance; (c) the provision of end-of-trip facilities for staff; (d) appropriate pedestrian and cyclist advisory signs are to be provided; and (e) all works/regulatory signposting associated with the proposed developments shall be at no cost to the relevant roads authority				16-Apr-20		Closed - Refer dwp design statement 01 dated 16/04/20
	[i] Final bicycle parking and service facilities to be design certified + provided to the Certifier		Built	Cardno | Northrop			Closed
	PART C - PRIOR TO COMMENCMENT OF CONSTRUCTION						
	Notice of Commencement						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
C1	The Applicant must notify the Planning Secretary in writing of the dates of commencement of physical work and operation at least 48 hours before those dates.	Note	Note		23-Jul-20		Closed - CC2b
	[i] Notification of commencement required to the Planning Secretary		**Built**	**dwp**			**Closed**
C2	If the construction or operation of the development is to be staged, the Planning Secretary must be notified in writing at least 48 hours before the commencement of each stage, of the date of commencement and the development to be carried out in that stage.	Note	Note		23-Jul-20		Closed
	[i] Notification of commencement of each construction stage required to the Planning Secretary		**Built**	**dwp**			**Closed**
	Construction Certificate						
C3	Work must not commence until a Construction Certificate in respect of the work has been issued.				23-Jul-20		Closed
	[i] Construction certification process to be managed		**Built**	**dwp**			**Closed**
	Outdoor Lighting						
C4	Prior to commencement of lighting installation, evidence must be submitted to the satisfaction of the Certifier that all outdoor lighting within the site has been designed to comply with AS 1158.3.1:2005 Lighting for roads and public spaces – Pedestrian area (Category P) lighting – Performance and design requirements and AS 4282-2019 Control of the obtrusive effects of outdoor lighting.				23-Jul-20		Closed - CC2b
	[i] Finalise in outdoor lighting design process and submit to the Certifier		**Built**	**dwp|Northrop**			**Closed**
	Demolition						
C5	Prior to the commencement of construction, demolition work plans required by AS 2601-2001 The demolition of structures (Standards Australia, 2001) must be accompanied by a written statement from a suitably qualified person that the proposals contained in the work plan comply with the safety requirements of the Standard. The work plans and the statement of compliance must be submitted to the Certifier and Planning Secretary.				21-Jan-20		Closed
	[i] Demolition work plans and statement submitted to the certifier		**Built**	**Northrop**	**21-Jan-20**		**Closed**
	[ii] Copy of works plans and statement forwarded to Planning Secretary	**Nihon**		**dwp**	**21-Jan-20**		**Closed**
C6	Prior to the commencement of internal demolition works within the State heritage listed former Newcastle Courthouse, evidence must be submitted to the satisfaction of the Certifier confirming works planned are required to make the existing building compliant with the fire and Life Safety Upgrade Strategy, prepared by Design Confidence, dated 12 June 2019, and that impacts to areas of high significant fabric have been limited.				21-Jan-20		Closed
	[i] Fire and life safety strategy to be confirmed through fire engineering and forwarded to the Certifier		**Built**	**dwp|Northrop**			**Closed**
	Environment Management Plan Requirements						
C7	Management plans required under this consent must be prepared in accordance with relevant guidelines, and include: (a) detailed baseline data; (b) details of: (i) the relevant statutory requirements (including any relevant approval, licence or lease conditions); (ii) any relevant limits or performance measures and criteria; and (iii) the specific performance indicators that are proposed to be used to judge the performance of, or guide the implementation of, the development or any management measures; (c) a description of the measures to be implemented to comply with the relevant statutory requirements, limits, or performance measures and criteria; (d) a program to monitor and report on the: (i) impacts and environmental performance of the development; (ii) effectiveness of the management measures set out pursuant to paragraph (c) above; (e) a contingency plan to manage any unpredicted impacts and their consequences and to ensure that ongoing impacts reduce to levels below relevant impact assessment criteria as quickly as possible; (f) a program to investigate and implement ways to improve the environmental performance of the development over time; (g) a protocol for managing and reporting any: (i) incident and any non-compliance (specifically including any exceedance of the impact assessment criteria and performance criteria); (ii) complaint; (iii) failure to comply with statutory requirements; and (h) a protocol for periodic review / update of the plan and any updates in response to incidents or matters of non-compliance. Note: The Planning Secretary may waive some of these requirements if they are unnecessary or unwarranted for particular management plans				27-Aug-20		Closed
	[i] Plan requirements incorporated in construction works		Built				**Closed**
	[ii] Assessment of plan requirements following on from occupation	**Nihon**		**Azusa | dwp**			**Closed**
	Construction Environmental Management Plan						
C8	Prior to the commencement of construction, the Applicant must submit a Construction Environmental Management Plan (CEMP) to the Certifier and provide a copy to the Planning Secretary. The CEMP must include, but not be limited to, the following: (a) Details of: (i) hours of work; (ii) 24-hour contact details of site manager; (iii) management of dust and odour to protect the amenity of the neighbourhood; (iv) stormwater control and discharge; (v) measures to ensure that sediment and other materials are not tracked onto the roadway by vehicles leaving the site; (vi) groundwater management plan including measures to prevent groundwater contamination; (vii) external lighting in compliance with AS 4282-2019 Control of the obtrusive effects of outdoor lighting; (viii) community consultation and complaints handling; (b) Construction Traffic and Pedestrian Management Sub-Plan (see condition C10); (c) Construction Noise and Vibration Management Sub-Plan (see condition C11); (d) Construction Waste Management Sub-Plan (see condition C11(g)); (e) an unexpected finds protocol for contamination and associated communications procedure; (f) an unexpected finds protocol for non-Aboriginal heritage and associated communications procedure; (g) waste classification (for materials to be removed) and validation (for materials to remain) be undertaken to confirm the contamination status in these areas of the site; and				27-Aug-20		Closed - updated after GHD Audit 02 and submitted to DPIE
	[i] CEMP developed by contractor + submission to the Certifier		**Built**		**22-Jan-20**		**Closed**
	[ii] Copy of CEMP forwarded to Planning Secretary	**Nihon**		**dwp**	**22-Jan-20**		**Closed**

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
C9	The Applicant must not commence construction of the development until the CEMP is submitted to the Certifier and a copy submitted to the Planning Secretary.	Note	Note		27-Aug-20		Closed
C10	The Construction Traffic and Pedestrian Management Sub-Plan (CTPMSP) must address, but not be limited to, the following: (a) be prepared by a suitably qualified and experienced person(s); (b) be prepared in consultation with Council; (c) detail the measures that are to be implemented to ensure road safety and network efficiency during construction in consideration of potential impacts on general traffic, cyclists and pedestrians and bus services; (d) detail heavy vehicle routes, access and parking arrangements; (e) include a Driver Code of Conduct to: (i) minimise the impacts of earthworks and construction on the local and regional road network; (ii) minimise conflicts with other road users; (iii) minimise road traffic noise; and (iv) ensure truck drivers use specified routes; (f) include a program to monitor the effectiveness of these measures; and (g) if necessary, detail procedures for notifying residents and the community (including local schools), of any potential disruptions to routes.				27-Aug-20		Closed - Updated CTPMSP includes additional consultation with Council.
	[i] CTPMSP developed by contractor + submission to Certifier		**Built**				**Closed**
	[ii] Submission to the Planning Secretary required	**Nihon**		**dwp**			**Closed**
C11	The Construction Noise and Vibration Management Sub-Plan must address, but not be limited to, the following: (a) be prepared by a suitably qualified and experienced noise expert; (b) describe procedures for achieving the noise management levels in EPA's Interim Construction Noise Guideline (DECC, 2009); (c) describe the measures to be implemented to manage high noise generating works such as piling, in close proximity to sensitive receivers; (d) include strategies that have been developed with the community for managing high noise generating works; (e) describe the community consultation undertaken to develop the strategies in condition C11(d); (f) include a complaints management system that would be implemented for the duration of the construction; and (g) include a program to monitor and report on the impacts and environmental performance of the development and the effectiveness of the management measures in accordance with condition C7(d). The program should be developed in accordance with the report titled Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting, and included, but not limited: (i) alert triggers where project trigger noise levels are exceeded; and (ii) procedures for respite periods when sensitive receivers become 'highly noise affected' (i.e. noise levels exceed 75 dB(A).				27-Aug-20		Closed
	[i] CNVMS-P developed by contractor + submission to PCA		**Built**	**EMM**	**22-Jan-20**		**Closed**
C12	The Construction Waste Management Sub-Plan (CWMSP) must address, but not be limited to, the following: (a) detail the quantities of each waste type generated during construction and the proposed reuse, recycling and disposal locations; and (b) removal of hazardous materials, particularly the method of containment and control of emission of fibres to the air, and disposal at an approved waste disposal facility in accordance with the requirements of the relevant legislation, codes, standards and guidelines, prior to the commencement of any building works.				27-Aug-20		Closed
	[i] CWPMSP developed by contractor + submission to PCA		**Built**				
	Aboriginal Cultural Heritage Management Plan						
C13	Prior to the commencement of construction (excluding demolition works), an Aboriginal Cultural Heritage Management Plan (ACHMP) must be prepared and address, but not be limited to, the following: (a) be prepared by a suitably qualified and experienced expert in consultation with the Registered Aboriginal Parties; (b) be endorsed by the Planning Secretary prior to construction (excluding demolition works) of any part of the development; (c) describe the measures to protect any Aboriginal cultural deposits or relics uncovered during sub surface archaeological testing in accordance with the relevant legislation.				16-Apr-20		Closed - site works closed out and report issued to PCA. AI # 11 provides confirmation of acceptance from DoP rec'd 16/04/20
	[i] ACHMSP developed by contractor + submission to PCA		**Built**	**AMAC**			**Closed**
	[ii] Submission to and endorsement by the Planning Secretary required	**Nihon**		**dwp**			**Closed**
	Construction Worker Transportation Strategy						
C14	Prior to the commencement of construction, the Applicant must submit a Construction Worker Transportation Strategy to the satisfaction of the Certifier. The Strategy must detail the provision of sufficient parking facilities or other travel arrangements for construction workers in order to minimise demand for parking in nearby public and residential streets or public parking facilities.				23-Jan-20		Closed out
	[i] Strategy developed by contractor + submission to the Certifier		**Built**		**22-Jan-20**		**Closed**
	[ii] Submission to the Planning Secretary required	**Nihon**		**dwp**	**22-Jan-20**		**Closed**
	Stormwater Management System						
C15	Prior to the commencement of construction, the Applicant must design an operational stormwater management system for the development and submit it to the satisfaction of the Certifier. The system must: (a) be designed by a suitably qualified and experienced person(s); (b) be design in consultation with and to the satisfaction of Council; (c) be generally in accordance with the conceptual design in the EIS as amended by the RtS; (d) be in accordance with applicable Australian Standards; (e) ensure that the system capacity has been designed in accordance with Australian Rainfall and Runoff (Engineers Australia, 2019) and Managing Urban Stormwater: Council Handbook (EPA, 1997) guidelines; (f) divert existing clean surface water around operational areas of the site; (g) direct all sediment laden water in overland flow away from the leachate management system; (h) prevent cross-contamination of clean and sediment or leachate laden water; (i) include details of all on-site retention/detention and water quality treatment systems are to be individually signposted in accordance with Council's Stormwater and Water Efficiency for Development Technical Manual.				21-Apr-20		Closed - CC#1
	[i] Stormwater management system developed + submission to the Certifier		**Built**	**Cardno | Northrop**			**Closed**
	Operational Noise – Design of Mechanical Plant and Equipment						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
C16	Prior to installation of mechanical plant and equipment, the Applicant must incorporate the noise mitigation recommendations in the Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting, into the detailed design drawings. The Certifier must verify that all noise mitigation measures have been incorporated into the design to ensure the development will not exceed the recommended operational noise levels identified in the Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting.				23-Jul-20		Closed - CC#2
	[i] Mechanical services design developed for compliance + submission to Certifier		**Built**	**Northrop**			**Closed**
	[ii] The Certifier to verify the submitted design	**Nihon**		**Dix Gardner**			**Closed**
	Archaeological Salvage - Historic Archaeology						
C17	Following the completion of demolition works and prior to the commencement of construction works, all affected historical archaeological deposits are to be subject to professional archaeological excavation and recording. An Archaeological Research Design and Excavation methodology must be prepared to guide the archaeological program. This must be prepared in accordance with Heritage Council of NSW Guidelines and in consultation with Heritage NSW, Department of Premier and Cabinet.				16-Apr-20		Complete for Building A, B & C. Some minor external works remaining. AI # 11 provides formal confirmation of approval from DoP dated 16/04/20
	[i] Methodology developed for compliance - consultation required with Heritage NSW + Premiers Department		**Built**	**AMAC**			**Closed**
C18	The Archaeological program must be directed by a suitably qualified and experienced Archaeologist (Excavation Director). The nominated Excavation Director must be able to demonstrate their ability to undertake this work through a response to the Heritage Council's Excavation Director Criteria (July 2011) for salvage excavation for a site of local heritage significance.		-		15-Apr-20		Closed - issued to PCA via Aconex 14/02/20. AI # 11 provides formal confirmation of approval from DoP dated 16/03/20 and 15/04/20.
	[i] AMAC credentials identified for compliance		**Built**	**AMAC**			**Closed**
	Landscaping						
C19	Prior to the commencement of construction, the Applicant must prepare a revised Landscape Plan that provides a streetscape treatment that does not impede on the understanding of the former Newcastle Courthouse and its relationship to its environment and setting, and submit a copy to the Planning Secretary. The plan must (a) be prepared by a qualified heritage landscape consultant and submitted to the NSW Heritage Council, or its delegate, for endorsement; (b) provide an analysis of the existing site frontage hardstand, fences and gates, colours and finishes and landscape elements within the precinct; (c) demonstrate the retention of the existing heritage cast iron fence along the site frontage, including the iron palisade fence, sandstone plinth and sandstone piers, unless removal of sections is demonstrated to be essential for the functional requirements of the proposal (e.g. clearance required to establish the approved additional driveway crossover); (d) provide for the planting of eight trees that are sympathetic to the heritage values of the item and ensure no planting grow higher than 1.5 m in directly in front of the former Newcastle Courthouse; (e) detail the location, species, maturity and height at maturity of plants to be planted on-site; (f) include species (trees, shrubs and groundcovers) indigenous to the local area; (g) include the planting of trees with a pot container of 100 litres or greater; (h) include the provision of street tree planting. Species and spacing of trees are to be sympathetic to the heritage values of the item and are to be determined in consultation with Council.				27-Apr-20		dwp confirmed condition met and closed out via Aconex on 27/04/20 (NB PCA had previously accepted this as part of the S138 approval and CC#3 submission rather than CC#2). Closed - s.138 approved by CoN
	[i] Landscape requirements to be worked through for resolution with Council + Heritage NSW	**Nihon**		**dwp | Moir**	**09-Oct-20**		**Closed**
	Public Domain Works						
C20	Prior to the commencement of any footpath or public domain works, the Applicant must engage a suitably qualified practicing engineer to design the following public domain works within the Church Street frontage of the site at no cost to Council and in accordance with the Newcastle City Centre Public Domain Manual guideline, design specifications and relevant Australian Standards: (a) new full width footpath and streetscape works and driveway; (b) reconstruct kerb and gutter, including associated road shoulder pavement and any associated drainage works; (c) new street trees and tree planting vaults in accordance with Council's requirement and adjust service pit levels to match new footpath levels; (d) kerb blisters and raised pedestrian crossings at the intersection of Bolton Street and Church Street; (e) upgrade street lighting across the frontage of the site to provide P3 Pedestrian Lighting Category in accordance with Australian Standard 1158.1; (f) upgrade of pedestrian crossing lighting to comply with Australian Standard 1158.4; (g) any necessary adjustments to regulatory signage.				09-Oct-20		dwp confirmed that the PCA will accept this as part of the S138 approval and CC#3 submission rather than CC#2 Closed - s.138 approved by CoN
	[i] Public domain works to be worked through for final resolution	**Nihon**		**dwp | Moir | Cardno**			**Closed**
C21	Prior to the commencement of any footpath or public domain works, the Applicant must consult with Council and demonstrate to the Certifier that the public domain design and treatment, as required by condition C20, meets the Council's requirements, including addressing pedestrian management. The Applicant must submit documentation of approval for each stage from Council to the Certifier.				09-Oct-20		Closed - s.138 approved by CoN
	[i] Public domain works to be worked through for final resolution - approval from Council submitted to the Certifier	**Nihon**		**dwp | Moir | cardno**			**Closed**
	Compliance Reporting						
C22	No later than two weeks before the date notified for the commencement of construction, a Compliance Monitoring and Reporting Program prepared in accordance with the Compliance Reporting Post Approval Requirements (Department 2018) must be submitted to the Planning Secretary and the Certifier.				23-Jan-20		Closed
	[i] Compliance monitoring and reporting program prepared + provided to the Certifier		**Built**	**dwp | Northrop**			**Closed**
	[ii] Submission of report to the Planning Secretary required	**Nihon**		**dwp**	**16-Jan-20**		**Closed**
C23	Compliance Reports of the project must be carried out in accordance with the Compliance Reporting Post Approval Requirements (Department 2018).	Noted	Noted				Note
C24	The Applicant must make each Compliance Report publicly available 60 days after submitting it to the Planning Secretary and notify the Planning Secretary and the Certifying Authority in writing at least seven days before this is done.						Note
	[i] Compliance report made available publically and advise Planning Secretary + Certifier	**Nihon**		**Azusa | dwp**			Not triggered this period.
C25	Notwithstanding the requirements of the Compliance Reporting Post Approval Requirements (Department 2018), the Planning Secretary may approve a request for ongoing annual operational compliance reports to be ceased, where it has been demonstrated to the Planning Secretary's satisfaction that an operational compliance report has demonstrated operational compliance.	Note	Note				Note
	PART D - DURING CONSTRUCTION						
	Site Notice						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
D1	A site notice(s): (a) must be prominently displayed at the boundaries of the site during construction for the purposes of informing the public of project details including, but not limited to the details of the Builder, Certifier and Structural Engineer is to satisfy the following requirements; (b) minimum dimensions of the notice must measure 841 mm x 594 mm (A1) with any text on the notice to be a minimum of 30-point type size; (c) the notice is to be durable and weatherproof and is to be displayed throughout the works period; (d) the approved hours of work, the name of the site/ project manager, the responsible managing company (if any), its address and 24-hour contact phone number for any inquiries, including construction/ noise complaint must be displayed on the site notice; and (e) the notice(s) is to be mounted at eye level on the perimeter hoardings/fencing and is to state that unauthorised entry to the site is not permitted.					✓	Compliant - ongoing through construction
	[i] Site notices developed by contractor + submission to the Certifier		**Built**		**21-Jan-20**		**Closed**
	Operation of Plant and Equipment						
D2	All construction plant and equipment used on site must be maintained in a proper and efficient condition and operated in a proper and efficient manner.					✓	Compliant - ongoing through construction
	[i] Site plant maintained and equipment maintenance by contractor		**Built**			✓	**Compliant - ongoing through construction**
	Demolition						
D3	Demolition work must comply with the demolition work plans required by Australian Standard AS 2601-2001 The demolition of structures (Standards Australia, 2001) and endorsed by a suitably qualified person as required by Condition C5.				21-Jan-20		Closed
	[i] Demolition processes developed by contractor		**Built**				**Closed**
	Construction Hours						
D4	Construction, including the delivery of materials to and from the site, may only be carried out between the following hours: (a) between 7 am and 6 pm, Mondays to Fridays inclusive; and (b) between 8 am and 1 pm, Saturdays. No work may be carried out on Sundays or public holidays.					✓	Compliant - ongoing
	[i] Construction hours factored into construction program		**Built**				**Compliant - ongoing**
D5	Construction activities may be undertaken outside of the hours in condition D4 if required: (a) by the Police or a public authority for the delivery of vehicles, plant or materials; or (b) in an emergency to avoid the loss of life, damage to property or to prevent environmental harm; or (c) where the works are inaudible at the nearest sensitive receivers; or (d) where a variation is approved in advance in writing by the Planning Secretary or his nominee if appropriate justification is provided for the works.	Note	Note			✓	Compliant - ongoing
D6	Notification of such construction activities as referenced in condition D5 must be given to affected residents before undertaking the activities or as soon as is practical afterwards.					✓	Compliant - ongoing
	[i] Notification to affected residents required		**Built**				**Compliant - ongoing**
D7	Rock breaking, rock hammering, sheet piling, pile driving and similar activities may only be carried out between the following hours: (a) 9am to 12pm, Monday to Friday; (b) 2pm to 5pm Monday to Friday; and (c) 9am to 12pm, Saturday.					✓	Compliant - ongoing
	[i] Check advice with the Certifier - demolition processes not considered as rock breaking or rock hammering - to be monitored		**Built**				**Compliant - ongoing**
	Implementation of Management Plans						
D8	The Applicant must carry out the construction of the development in accordance with the most recent version of the approved CEMP (including Sub-Plans) and ACHMP.					✓	Compliant - ongoing
	[i] Monitoring of compliance with management plans		**Built**			✓	**Compliant - ongoing**
	Construction Traffic						
D9	All construction vehicles (excluding site personnel vehicles) are to be contained wholly within the site, except if located in an approved on-street work zone, and vehicles must enter the site before stopping.		**Built**				Non-compliance identified in GHD Audit 3 in relation to extending work zone without approval. Issue resolved with CoN immediately. No further actions.
	Hoarding Requirements						
D10	The following hoarding requirements must be complied with: (a) no third-party advertising is permitted to be displayed on the subject hoarding/ fencing; and (b) the construction site manager must be responsible for the removal of all graffiti from any construction hoardings or the like within the construction area within 48 hours of its application.		**Built**			✓	Compliant - ongoing
	No Obstruction of Public Way						
D11	The public way (outside of any approved construction works zone) must not be obstructed by any materials, vehicles, refuse, skips or the like, under any circumstances.		**Built**			✓	Compliant - ongoing
	Construction Noise Limits						
D12	The development must be constructed to achieve the construction noise management levels detailed in the Interim Construction Noise Guideline (DECC, 2009). All feasible and reasonable noise mitigation measures must be implemented and any activities that could exceed the construction noise management levels must be identified and managed in accordance with the management and mitigation measures identified in the approved Construction Noise and Vibration Management Plan.		**Built**	**EMM \ RAPT**		✓	Compliant - ongoing
D13	The Applicant must ensure construction vehicles (including concrete agitator trucks) do not arrive at the site or surrounding residential precincts outside of the construction hours of work outlined under condition D4.		**Built**			✓	Compliant - ongoing
D14	The Applicant must implement, where practicable and without compromising the safety of construction staff or members of the public, the use of 'quackers' to ensure noise impacts on surrounding noise sensitive receivers are minimised.		**Built**			✓	Compliant - ongoing
	Vibration Criteria						

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
D15	Vibration caused by construction at any residence or structure outside the site must be limited to: (a) for structural damage, the latest version of DIN 4150-3 (1992-02) Structural vibration - Effects of vibration on structures (German Institute for Standardisation, 1999); and (b) for human exposure, the acceptable vibration values set out in the Environmental Noise Management Assessing Vibration: a technical guideline (DEC, 2006) (as may be updated or replaced from time to time).		Built	EMM \ RAPT		✓	Compliant - no vibration causing activities
D16	Vibratory compactors must not be used closer than 30 metres from residential buildings unless vibration monitoring confirms compliance with the vibration criteria specified in condition D15.		Built			✓	Compliant - no compactors onsite
D17	The limits in conditions D15 and D16 apply unless otherwise outlined in a Construction Noise and Vibration Management Plan, approved as part of the CEMP required by condition C11 of this consent.		Built	EMM		✓	Compliant - ongoing
	Tree Protection						
D18	For the duration of the construction works: (a) street trees, with the exception of the one nominated street tree approved for removal to accommodate the new driveway crossover, must not be trimmed or removed unless it forms a part of this development consent or prior written approval from Council is obtained or is required in an emergency to avoid the loss of life or damage to property; (b) all street trees to be retained must be protected at all times during construction. Any tree on the footpath, which is damaged or removed during construction due to an emergency, must be replaced, to the satisfaction of Council; (c) all trees on the site that are not approved for removal must be suitably protected during construction as per recommendations of the Aboricultural Impact Assessment Report dated 17 November 2019 and prepared by Joseph Pidutti Consulting Arborist; and (d) if access to the area within any protective barrier is required during the works, it must be carried out under the supervision of a qualified arborist. Alternative tree protection measures must be installed, as required. The removal of tree protection measures, following completion of the works, must be carried out under the supervision of a qualified arborist and must avoid both direct mechanical injury to the structure of the tree and soil compaction within the canopy or the limit of the former protective fencing, whichever is the greater.		Built		09-Oct-20		Closed - existing street trees approved for removal under Section 138 works and completed by City of Newcastle on 6/11/2020.
	Air Quality						
D19	The Applicant must take all reasonable steps to minimise dust generated during all works authorised by this consent.		Built			✓	Compliant - ongoing
D20	During construction, the Applicant must ensure that: (a) exposed surfaces and stockpiles are suppressed by regular watering; (b) all trucks entering or leaving the site with loads have their loads covered; (c) trucks associated with the development do not track dirt onto the public road network; (d) public roads used by these trucks are kept clean; and (e) land stabilisation works are carried out progressively on site to minimise exposed surfaces.		Built			✓	Compliant - ongoing
	Erosion and Sediment Control						
D21	All erosion and sediment control measures must be effectively implemented and maintained at or above design capacity for the duration of the construction works and until such time as all ground disturbed by the works have been stabilised and rehabilitated so that it no longer acts as a source of sediment. Erosion and sediment control techniques, as a minimum, are to be in accordance with the publication Managing Urban Stormwater: Soils & Construction (4th edition, Landcom, 2004) commonly referred to as the 'Blue Book'.		Built			✓	Compliant - ongoing
	Imported Soil						
D22	The Applicant must: (a) ensure that only VENM, ENM, or other material approved in writing by EPA is brought onto the site; (b) keep accurate records of the volume and type of fill to be used; and (c) make these records available to the Certifier upon request.		Built			✓	Compliant - ongoing
	Disposal of Seepage and Stormwater						
D23	Adequate provisions must be made to collect and discharge stormwater drainage during construction of the building to the satisfaction of the principal Certifier. The prior written approval of Council must be obtained to connect or discharge site stormwater to Council's stormwater drainage system or street gutter.		Built			✓	Compliant - ongoing
	Unexpected Finds Protocol - Aboriginal Heritage						
D24	In the event that surface disturbance identifies a new Aboriginal object, all works must halt in the immediate area to prevent any further impacts to the object(s). A suitably qualified archaeologist and the registered Aboriginal representatives must be contacted to determine the significance of the objects. The site is to be registered in the Aboriginal Heritage Information Management System (AHIMS) which is managed by EES Group and the management outcome for the site included in the information provided to AHIMS. The Applicant must consult with the Aboriginal community representatives, the archaeologists and EES Group to develop and implement management strategies for all objects/sites. Works shall only recommence with the written approval of EES Group.		Built	AMAC		✓	Compliant - not triggered to date
	Unexpected Finds Protocol - Historic Heritage						
D25	If any unexpected archaeological relics are uncovered during the work, then all works must cease immediately in that area and the NSW Heritage Division contacted. Depending on the possible significance of the relics, an archaeological assessment and management strategy may be required before further works can continue in that area. Works may only recommence with the written approval of the NSW Heritage Division.		Built	AMAC		✓	Compliant - not triggered this period
	Waste Storage and Processing						
D26	All waste generated during construction must be secured and maintained within designated waste storage areas at all times and must not leave the site onto neighbouring public or private properties.		Built			✓	Compliant - ongoing
D27	All waste generated during construction must be assess, classified and managed in accordance with the Waste Classification Guidelines Part 1: Classifying Waste (EPA, 2014).		Built			✓	Compliant - ongoing
D28	The Applicant must ensure that concrete waste and rinse water are not disposed of on the site and are prevented from entering any natural or artificial watercourse.		Built			✓	Compliant - ongoing
	Independent Environmental Audit						
D29	Proposed independent auditors must be agreed to in writing by the Planning Secretary prior to the preparation of an Independent Audit Program or commencement of an Independent Audit.						Closed - GHD appointed & endorsed
	[i] Notification of independent auditors to be given to the Planning Secretary and agreed to - relates to environmental aspects of construction	**Nihon**	**Built**	**Azusa | dwp**			**Closed**
D30	Prior to the commencement of construction, an Independent Audit Program prepared in accordance with the Independent Audit Post Approval Requirements (Department 2018) must be submitted to the Planning Secretary and the Certifier.						Closed - dwp issued to DPIE
	[i] Independent audit program prepared and submitted to Planning Secretary and the Certifier	**Nihon**	**Built**	**Azusa | dwp**			**Closed**

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
D31	Table 1 of the Independent Audit Post Approval Requirements (Department 2018) is amended so that the frequency of audits required in the construction phase is: (a) an initial construction Independent Audit must be undertaken within eight weeks of the notified commencement date of construction; (b) a subsequent Independent Audit of construction must be undertaken no later than six months from the date of the initial construction Independent Audit; and In all other respects Table 1 remains the same. The Planning Secretary may require the initial and subsequent Independent Audits to be undertaken at different times to those specified above, upon giving at least 4 weeks notice to the applicant of the date upon which the audit must be commenced.						GHD Audit 01 complete GHD Audit 02 complete GHD Audit 03 complete
	[i] Audit program linked to construction dates	Nihon	Built	Azusa | dwp			Closed
D32	Independent Audits of the development must be submitted to the Planning Secretary and must be carried out in accordance with: (a) the Independent Audit Program submitted to the Planning Secretary and the Certifier under condition D30 of this consent; and (b) the requirements for an Independent Audit Methodology and Independent Audit Report in the Independent Audit Post Approval Requirements (Department 2018).						Note
	[i] Independent audits must be submitted to the Planning Secretary and the Certifier	Nihon	Built	Azusa | dwp			Closed
D33	Requirements (Department 2018), the Applicant must: (a) review and respond to each Independent Audit Report prepared under condition D30 of this consent; (b) submit the response to the Planning Secretary and the Certifier; and (c) make each Independent Audit Report and response to it publicly available 60 days after submission to the Planning Secretary and notify the Planning Secretary and the Certifier in writing at least seven days before this is done.						Note
	[i] Response required to each independent audit - Planning Secretary and the Certifier notified	Nihon	Built	Azusa | dwp			Closed
D34	Notwithstanding the requirements of the Independent Audit Post Approval Requirements (Department 2018), the Planning Secretary may approve a request for ongoing annual operational audits to be ceased, where it has been demonstrated to the Planning Secretary's satisfaction that an audit has demonstrated operational compliance.	Note	Note				Note
	PART E - PRIOR TO ISSUE OF AN OCCUPATION CERTIFICATE OR COMMENCEMENT OF OPERATION						
	Notification of Occupation						
E1	At least one month before commencement of operation, the date of commencement of the operation of the development must be notified to the Planning Secretary in writing. If the operation of the development is to be staged, the Planning Secretary must be notified in writing at least one month before the commencement of each stage, of the date of commencement and the development to be carried out in that stage.					✓	Closed on 13/07/2021
	[i] Notice provided to Planning Secretary	Nihon		Azusa | dwp		✓	Closed - dwp AU-GCOR-001924
	External Walls and Cladding						
E2	Prior to issue of an Occupation Certificate, the Applicant must provide the Certifier with documented evidence that the products and systems used in the construction of external walls including finishes and claddings such as synthetic or aluminium composite panels comply with the requirements of the BCA.						In progress for OC
	[i] Evidence of products used to be issued to the Certifier		Built	Azusa | dwp			In progress for OC
E3	The Applicant must provide a copy of the documentation given to the Certifier to the Planning Secretary within seven days after the Certifier accepts it.						Not triggered
	[i] Copies of the documents sent to the Certifier to be forwarded to Planning Secretary	Nihon		dwp			Not triggered
	Post-construction Dilapidation Report						
E4	Prior to issue of an Occupation Certificate, the Applicant must engage a suitably qualified person to prepare a post-construction dilapidation report at the completion of construction. This report is: a) to ascertain whether the construction created any structural damage to adjoining buildings or infrastructure; b) to be submitted to the Certifier. In ascertaining whether adverse structural damage has occurred to adjoining buildings or infrastructure, the Certifier must: i) compare the post-construction dilapidation report with the pre-construction dilapidation report required by these conditions; and ii) have written confirmation from the relevant authority that there is no adverse structural damage to their infrastructure and roads. c) to be forwarded to Council.						Engineer has commenced dilapidation inspections
	[i] Dilapidation Report forwarded to PCA + Council		Built				Not triggered
	Public Domain Works						
E5	Prior to issue of an Occupation Certificate, the public domain works and footpath works required by condition C20 must be completed to Council's satisfaction.						In progress - CoN regularly inspecting.
	[i] Documented public domain works completed and approved		Built				Not triggered
	Protection of Public Infrastructure						
E6	Unless the Applicant and the applicable authority agree otherwise, the Applicant must: (a) repair, or pay the full costs associated with repairing, any public infrastructure that is damaged by carrying out the development; and (b) relocate, or pay the full costs associated with relocating any infrastructure that needs to be relocated as a result of the development. Note: This condition does not apply to any damage to roads caused as a result of general road usage or otherwise addressed by contributions required by condition B2 of this consent.						Not triggered
	[i] All damage repaired + infrastructure upgraded		Built	Azusa | dwp			Not triggered
	Easements						
E7	Prior to issue of an Occupation Certificate, an easement under section 88A and/or restriction or public positive covenant under section 88E of the *Conveyancing Act 1919* naming the Council as the prescribed authority, which can only be revoked, varied or modified with the consent of the Council, and which provides for the drainage of water must be registered on title of Lot 1 DP 1199904. The easement must be a minimum three metres in width and must be centred over the new stormwater pipeline.						Nihon & CoN negotiating contract.
	[i] Easements to be established	Nihon		Azusa | dwp			Not triggered
	Utilities and Services						
E8	Prior to issue of an Occupation Certificate, a compliance certificate under the section 50 of the *Hunter Water Act 1991* must be obtained from Hunter Water and submitted to the Certifier.						In progress - final survey in progress
	[i] Certificate to be obtained and submitted to the Certifier		Built	Northrop			Not triggered
	Works as Executed Plans						
E9	Prior to issue of an Occupation Certificate, works-as-executed drawings signed by a registered surveyor demonstrating that the stormwater drainage and finished ground levels have been constructed as approved, must be submitted to the Certifier.						Surveys in progress
	[i] As executed plans to be obtained and submitted to the Certifier		Built	Cardno | Northrop			Not triggered
	Green Travel Plan						

X

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status	
		Owner	Contractor					
E10	Prior to issue of an Occupation Certificate, a Green Travel Plan (GTP), must be submitted to the satisfaction of the Planning Secretary to promote the use of active and sustainable transport modes. The plan must: (a) be prepared by a suitably qualified traffic consultant in consultation with Council; (b) include objectives and modes share targets (i.e. Site and land use specific, measurable and achievable and timeframes for implementation) to define the direction and purpose of the GTP; (c) include specific tools and actions to help achieve the objectives and mode share targets; (d) include measures to promote and support the implementation of the plan, including financial and human resource requirements, roles and responsibilities for relevant employees involved in the implementation of the GTP; and (e) include details regarding the methodology and monitoring/review program to measure the effectiveness of the objectives and mode share targets of the GTP, including the frequency of monitoring and the requirement for travel surveys to identify travel behaviours of users of the development.						Under review by DPIE.	
	[i] Green travel plan to be finalised and submitted to the Planning Secretary	**Nihon**		**Azusa | dwp**			**dwp has submitted to DPIE for review.**	X
	Heritage Interpretation Plan							
E11	Prior to issue of an Occupation Certificate, the Applicant must submit a Heritage Interpretation Plan to acknowledge the heritage of the site to the Planning Secretary. The plan must: (a) be prepared by a suitably qualified and experienced expert in consultation with the NSW Heritage Division and Council; (b) outline the Stage 1 heritage interpretation strategy (c) include provision for naming elements within the development that acknowledges the site's heritage; (d) incorporates interpretive information in to the site of the former legal and court functions of the former Newcastle Courthouse.					✓	Closed	
	[i] Heritage Interpretation Plan is required to be completed and submitted to the Planning Secretary - dependent of archaeological findings	**Nihon**		**Azusa | dwp**		✓	**Closed - submitted 07/04/2021**	X
	Operational Management Plan							
E12	Prior to issue of an Occupation Certificate, the Applicant must prepare an Operational Management Plan for the site. The plan must: (a) include measures to ensure all wayfinding signage, security measures, and landscaping is managed to maintain their effectiveness; and (b) include measures to manage the operation and use of rooftop terraces and ground level café terrace; and (c) prohibit use of the rooftop terraces for events or formal teaching; and (d) restrict the use of the rooftop terraces to no later than 9pm daily; and (e) ensure the use of the rooftop terraces does not result in exceedances of the project noise trigger levels in the report titled Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting.						Report complete - pending final review by Nihon University	
	[i] Operational management plan to be finalised	**Nihon**		**Azusa | dwp**			**Pending Nihon review.**	X
E13	The Operational Management Plan must be submitted to the satisfaction of the Certifier and implemented for the life of the approved development.							
	[ii] Operational management plan to be submitted to the Certifier	**Nihon**		**Azusa | dwp**			**Not triggered**	X
	Operational Transport and Access Management Plan [OTAMP]							
E14	Prior to issue of an Occupation Certificate, an OTAMP is to be prepared by a suitably qualified person, in consultation with Council and submitted to the Planning Secretary. The OTAMP must address the following: (a) detailed pedestrian analysis including the identification of safe route options – to identify the need for management measures to ensure students and staff are able to access and leave the Site in a safe and efficient manner at all times; (b) the location of all car parking spaces on the campuses and their allocation (i.e. staff, visitor, accessible, emergency, etc.); (c) delivery and services vehicle management arrangements; (d) use of the services zone limited to: (i) 7am to 8am and 7pm to 8pm Monday to Friday; (ii) 7am to 8am Saturday; (iii) no use on Sundays or Public Holidays; (e) management of approved access arrangements; (f) potential traffic impacts on surrounding road networks and mitigation measures to minimise impacts, including measures to mitigate queuing impacts associated with vehicles accessing the car parking spaces or services zone; (g) a monitoring and review program.					✓	Closed	
	[i] Operational management plan to be finalised and submitted to the Planning Secretary	**Nihon**		**Azusa | dwp**		✓	**Closed - Submitted 14/07/2021**	X
	Mechanical Ventilation							
E15	Prior to issue of an Occupation Certificate, the Applicant must provide evidence to the satisfaction of the Certifier that the installation and performance of the mechanical ventilation systems complies with: (a) *AS 1668.2-2012 The use of air-conditioning in buildings – Mechanical ventilation in buildings* and other relevant codes; and (b) any dispensation granted by Fire and Rescue NSW.						Requested	
	[i] Certification of mechanical installation required and submitted to the Certifier		**Built**	**Northrop**			**Not triggered**	
	Operational Noise - Design of Mechanical Plant and Equipment							
E16	Prior to issue of an Occupation Certificate, the Applicant must submit evidence to the Certifier that the noise mitigation recommendations in the Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting have been incorporated into the design to ensure the development will not exceed the recommended operational noise levels identified in the Environmental Noise Assessment.						Requested	
	[i] Certification of mechanical installation required in relation to noise and vibration mitigation and submitted to the Certifier		**Built**	**Northrop**			**Not triggered**	
	Road Damage							
E17	Prior to the commencement of operation, the cost of repairing any damage caused to Council or other Public Authority's assets in the vicinity of the Subject Site as a result of construction works associated with the approved development must be met in full by the Applicant.						To be reviewed with CoN at completion	
	[i] Damage to public infrastructure caused by construction to be rectified		**Built**				**Not triggered**	
	Fire Safety Certification							
E18	Prior to issue of an Occupation Certificate, a Fire Safety Certificate must be obtained for all the Essential Fire or Other Safety Measures forming part of this consent. A copy of the Fire Safety Certificate must be submitted to the relevant authority and Council. The Fire Safety Certificate must be prominently displayed in the building.						Certificates requested. Nihon to sign FFSC.	
	[i] Fire safety certificate for constructed facility to be submitted to relevant authority		**Built**	**dwp | Northrop**			**Not triggered**	
	Structural Inspection Certificate							

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status	
		Owner	Contractor					
E19	Prior to occupation of the relevant parts of any new or refurbished buildings, a Structural Inspection Certificate or a Compliance Certificate must be submitted to the satisfaction of the Certifier. A copy of the Certificate with an electronic set of final drawings (contact approval authority for specific electronic format) must be submitted to the approval authority and the Council after: (a) the site has been periodically inspected and the Certifier is satisfied that the structural works is deemed to comply with the final design drawings; and (b) the drawings listed on the Inspection Certificate have been checked with those listed on the final Design Certificate/s.						Northrop Certificate accepted by PCA. Cardno Certificate under review by PCA.	
	[i] Structural certification of the works submitted to the Certifier		**Built**	**Cardno | Northrop**			**Partially closed.**	
	Compliance with Food Code							
E20	Prior to issue of an Occupation Certificate, the Applicant is to obtain a certificate from a suitably qualified tradesperson, certifying that the kitchen, food storage and food preparation areas have been fitted in accordance with the AS 4674 Design, construction and fit-out of food premises and provide evidence of receipt of the certificate to the satisfaction of the Certifier.						Requested	
	[i] Certification of the kitchen works submitted to the Certifier		**Built**	**dwp| kitchen sc**			**Not triggered**	
	Stormwater Quality Management Plan							
E21	Prior to issue of an Occupation Certificate, an Operation and Maintenance Plan (OMP) is to be submitted to the satisfaction of the Certifier along with evidence of compliance with the OMP. The OMP must ensure the proposed stormwater quality measures remain effective and contain the following: (a) maintenance schedule of all stormwater quality treatment devices that addresses Council's Technical Manual: Stormwater and Water Efficiency for Development (updated April 2019); (b) record and reporting details; (c) relevant contact information; and (d) Work Health and Safety requirements.						In progress - pending final as-builts	
	[i] OMP prepared and to be submitted to the Certifier		**Built**	**Northrop | Cardno**			**Not triggered**	
	Rainwater Harvesting							
E22	Prior to issue of an Occupation Certificate, signed works-as-executed Rainwater Re-use Plan must be provided to the Planning Secretary and Certifier.						In progress	
	[i] Documentation of the rainwater reuse system to be submitted to the Certifier		**Built**	**Northrop**			**Not triggered**	
	ii] Copy of the documents sent to the Certifier to be forwarded to Planning Secretary	**Nihon**		**dwp**			**Not triggered**	**x**
	Warm Water Systems and Cooling Systems							
E23	The installation of warm water systems and water cooling systems (as defined under the *Public Health Act 2010*) must comply with the *Public Health Act 2010* , Public Health Regulation 2012 and Part 1 (or Part 3 if a Performance-based water cooling system) of *AS/NZS 3666.2:2011 Air handling and water systems of buildings – Microbial control – Operation and maintenance* and the NSW Health Code of Practice for the Control of Legionnaires' Disease.						Closed - PCA accepted Northrop design certificate	
	[i] Certification of the of the warm water and cooling systems to be submitted to the Certifier		**Built**	**Northrop**			**Closed - 12/07/2021**	
	Outdoor Lighting							
E24	. Prior to issue of an Occupation Certificate, the Applicant must submit evidence from a suitably qualified practitioner to the Certifier that demonstrates that installed lighting associated with the development achieves the objective of minimising light spillage to any adjoining or adjacent sensitive receivers and: (a) complies with the latest version of AS 4282-2019 - *Control of the obtrusive effects of outdoor lighting* (Standards Australia, 1997); and (b) has been mounted, screened and directed in such a manner that it does not create a nuisance to surrounding properties or the public road network.						Received on 28/07/2021	
	[i] Certification of the outdoor lighting systems to be submitted to the Certifier		**Built**	**Northrop**			**To be submitted**	
	Archaeological Salvage - Historic Archaeology							
E25	The Applicant must prepare an archaeological report of the salvage excavation undertaken in accordance with condition C17. An interim report of the salvage excavation must be provided for the information of the Heritage Council of NSW and Council within one month of completion of the salvage work and a final report provided within 12 months of completion of the salvage work or within another timeframe agreed with the Planning Secretary. Copies of the report must also be provided to the NSW Heritage Division and Council.						Closed - interim report submitted on 28/07/2021.	
	[i] Submission of archaeological report to Heritage Council and Council - timing to consider		**Built**	**AMAC | dwp**			**Closed**	**x**
	Signage							
E26	Prior to issue of an Occupation Certificate, way-finding signage and signage identifying the location of staff car parking must be installed.						In progress	
	[i] Signage details to be finalised and installed		**Built**	**Azusa | dwp**			**Not triggered**	
E27	Prior to issue of an Occupation Certificate, bicycle way-finding signage must be installed within the site to direct cyclists from footpaths to designated bicycle parking areas.						In progress	
	[i] Signage details to be finalised and installed		**Built**	**Azusa | dwp**			**Not triggered**	
E28	Prior to issue of an Occupation Certificate, 'Do not drink' signage on non-potable water used for toilet flushing and to new hose taps and irrigation systems for landscaped areas must be installed within the site.						In progress	
	[i] Signage details to be finalised and installed		**Built**	**Azusa | dwp**			**Not triggered**	
	Operational Waste Management Plan							
E29	Prior to issue of an Occupation Certificate, the Applicant must prepare a Waste Management Plan for the development and submit it to the Certifier. The Waste Management Plan must: (a) detail the type and quantity of waste to be generated during operation of the development; (b) the location and operational management procedures of the services zone located within the front setback of the Residential Building, including management/traffic controller arrangements; (c) describe the handling, storage and disposal of all waste streams generated on site, consistent with the P*rotection of the Environment Operations Act 1997, Protection of the Environment Operations (Waste) Regulation 2014* and the *Waste Classification Guideline* (Department of Environment, Climate Change and Water, 2009); (d) detail the materials to be reused or recycled, either on or off site; and (e) include the Management and Mitigation Measures included in EIS, as amended by the RtS.						Received from dwp. To be submitted to PCA	**x**
	[i] Operational waste management plan to be prepared and submitted to the Certifier	**Nihon**		**Azusa | dwp**			**To be submitted**	**x**
	Site Contamination							
E30	The Applicant must prepare a Validation Report, where required by the remediation action plan approved by a NSW EPA Accredited Site Auditor pursuant to condition A19, for the development. The Validation Report must: (a) be prepared by a Certified Contaminated Land Consultant; (b) be submitted to the Site Auditor, the Planning Secretary and the Certifier for information within one month after the completion of remediation works; and (c) be prepared in accordance with the remediation action plan approved by a NSW EPA Accredited Site Auditor pursuant to condition A19.						In progress	
	[i] Remedial works to be carried out in accordance with updated RAP and report submitted to site auditor, the Certifier and the Planning Secretary		**Built**	**Douglas Partners**			**Not triggered**	

	SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX	Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status	
		Owner	Contractor					
	Site Audit Statement							
E31	Prior to issue of an Occupation Certificate, the Applicant must submit a Site Audit Report and Section A Site Audit Statement for the relevant part of the site prepared by a NSW EPA accredited Site Auditor. The Site Audit Report and Section A Site Audit Statement must verify the relevant part of the site is suitable for the educational establishment land use and be provided for the information of the Planning Secretary and the Certifier.						In progress	
	[i] Input into site audit statement		**Built**	**Douglas Partners**			**Not triggered**	
	[ii] Site audit statement to be submitted to the Planning Secretary and the Certifier	**Nihon**		**GHD | dwp**			**Not triggered**	X
	Long Term Environmental Management Plan							
E32	The Applicant must prepare a Long Term Environmental Management Plan (LTEMP), where identified as required by the remediation action plan approved by a NSW EPA Accredited Site Auditor pursuant to condition A19, and submit a copy to the Planning Secretary. The plan must: (a) be prepared by a certified Contaminated Land Consultant; (b) be submitted to the Planning Secretary within one month of the completion of remediation works, unless otherwise agreed by the Planning Secretary; and (c) include, but not be limited to: (i) a description of the nature and location of any contamination remaining on site; (ii) provisions to manage and monitor any remaining contamination, including details of any restrictions placed on the land to prevent development over the containment cell; (iii) a description of the procedures for managing any leachate generated from the containment cell, including any requirements for testing, pumping, treatment and/or disposal; (iv) a description of the procedures for monitoring the integrity of the containment cell; (v) a surface and groundwater monitoring program; (vi) mechanisms to report results to relevant agencies; (vii) triggers that would indicate if further remediation is required; and (viii) details of any contingency measures that the Applicant is to carry out to address any ongoing contamination.						In progress	
	[i] Input into long term environmental management plan		**Built**	**Douglas Partners**			**Not triggered**	
	[ii] Long term management plan preparation and submission to the Planning Secretary	**Nihon**		**GHD | dwp**			**Not triggered**	X
E33	The approved LTEMP must be provided to Council within once month for notation of the section 10.7 certificate for the site.						Not triggered	
	[i] Long term management plan preparation provided to Council - timing requirement	**Nihon**		**GHD | dwp**			**Not triggered**	X
E34	Upon completion of remediation works, the Applicant must manage the site in accordance with the LTEMP.						Not triggered	
	[i] Long term management of the site	**Nihon**		**Facility Manager**			**Not triggered**	X
	Landscaping							
E35	Prior to issue of an Occupation Certificate, the Applicant must prepare an Operational Landscape Management Plan to manage the revegetation and landscaping on-site, to the satisfaction of the Certifier. The plan must: (a) describe the ongoing monitoring and maintenance measures to manage revegetation and landscaping; and (b) be consistent with the Applicant's Management and Mitigation Measures at Chapter 10 in the EIS and as updated by the RtS;						In progress	
	[i] Preparation of an operational landscape management plan	**Nihon**		**Moir | Azusa | dwp**			**Not triggered**	X
E36	The Applicant must not commence operation until the Operational Landscape Management Plan is submitted to the Certifier.						Not triggered	
	[i] Submission of an operational landscape management plan	**Nihon**		**Azusa | dwp**			**Not triggered**	X
	PART F - POST OCCUPATION							
	Operation of Plant and Equipment							
F1	All plant and equipment used on site must be maintained in a proper and efficient condition operated in a proper and efficient manner.	**Nihon**		**Facility Manager**			**Not triggered**	
	Warm Water Systems and Cooling Systems							
F2	The operation and maintenance of warm water systems and water cooling systems (as defined under the Public Health Act 2010) must comply with the Public Health Act 2010, Public Health Regulation 2012 and Part 2 (or Part 3 if a Performance-based water cooling system) of AS/NZS 3666.2:2011 Air handling and water systems of buildings – Microbial control – Operation and maintenance and the NSW Health Code of Practice for the Control of Legionnaires' Disease.	**Nihon**		**Facility Manager**			**Not triggered**	
	Community Communication Strategy							
F3	The Community Communication Strategy, as approved by the Planning Secretary, must be implemented for a minimum of 12 months following the completion of construction.	**Nihon**		**Facility Manager**			**Not triggered**	
	Heritage interpretation Plan							
F4	Within three months of the commencement of use, the Applicant must submit an updated Heritage Interpretation Plan to acknowledge the heritage of the site to the Planning Secretary. The plan must: (a) be prepared by a suitably qualified and experienced expert in consultation with the NSW Heritage Division and Council; (b) incorporate the Stage 2 heritage interpretation strategy (c) include provision for naming elements within the development that acknowledges the site's heritage; (d) include a strategy detailing how movable heritage items and any archaeological findings will be interpreted (e) incorporates interpretive information in to the site of the former legal and court functions of the former Newcastle Courthouse.	**Nihon**		**Facility Manager**			**Not triggered**	
F5	The Applicant must implement the most recent version of the Heritage Interpretation Plan approved under conditions E11 and F4.	**Nihon**		**Facility Manager**			**Not triggered**	
	Operational Transport and Access Management Plan (OTAMP)							
F6	The OTAMP(s) approved under condition E14 as revised from time to time) must be implemented by the Applicant for the life of the development.	**Nihon**		**Facility Manager**			**Not triggered**	
	Long Term Environmental Management Plan							
F7	Upon completion of remediation works, the Applicant must manage the site in accordance with the LTEMP approved under condition E32, or an updated version where approved by a NSW EPA Accredited Site Auditor. Any revisions must be submitted to Council within one month of the update.	**Nihon**		**Facility Manager**			**Not triggered**	
	Operational Noise Limits							
F8	The Applicant must ensure that noise generated by operation of the development does not exceed the noise limits in Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting.	**Nihon**		**Facility Manager**			**Not triggered**	

SSD 9787 - FINAL CONDITIONS | SCHEDULE 2 MATRIX		Responsibility		Relevent Consultant/s	Date Addressed	Jul-21	Status
		Owner	Contractor				
F9	The Applicant must undertake short term noise monitoring in accordance with the Noise Policy for Industry within two months following the commencement use. The monitoring program must be carried out by an appropriately qualified person and a monitoring report must be submitted to the Planning Secretary within two months of commencement use of the development to verify that operational noise levels do not exceed the recommended noise levels for mechanical plant identified in the report titled Noise and Vibration Assessment – Operational and Construction report dated May 2019 and prepared by EMM Consulting. Should the noise monitoring program identify any exceedance of the recommended noise levels or internal amenity noise levels for building occupants, the Applicant is required to implement appropriate noise attenuation measures so that operational noise levels do not exceed the recommended noise levels or provide attenuation measures at the affected noise sensitive receivers.	Nihon		Facility Manager			Not triggered
	Unobstructed Driveways and Parking Areas						
F10	All driveways, footways and parking areas must be unobstructed at all times. Driveways, footways and car spaces must not be used for the manufacture, storage or display of goods, materials, refuse, skips or any other equipment and must be used solely for vehicular and/or pedestrian access and for the parking of vehicles associated with the use of the premises.	Nihon		Facility Manager			Not triggered
	Green Travel Plan						
F11	The Green Travel Plan required by condition E10 of this consent must be updated annually and implemented unless otherwise agreed by the Planning Secretary.	Nihon		Facility Manager			Not triggered
	Ecologically Sustainable Development						
F12	Unless otherwise agreed by the Planning Secretary, within six months of commencement of operation, Green Star certification must be obtained demonstrating the development achieves a minimum 4 star Green Star Design & As Built rating. If required to be obtained, evidence of the certification must be provided to the Certifier and the Planning Secretary. If an alternative certification process has been agreed to by the Planning Secretary under Condition B6, evidence of compliance of implementation must be provided to the Planning Secretary and Certifier.						Not triggered
	[i] Resolution of alternative certification process - certification to Planning Secretary and to the Certifier	Nihon		Azusa | dwp			Not triggered
	Outdoor Lighting						
F13	Notwithstanding condition E24, should outdoor lighting result in any residual impacts on the amenity of surrounding sensitive receivers, the Applicant must provide mitigation measures in consultation with affected landowners to reduce the impacts to an acceptable level.	Nihon		Facility Manager			Not triggered
	Landscaping						
F14	The Applicant must maintain the landscaping and vegetation on the site in accordance with the approved Landscape Management Plan required by condition E35 for the duration of occupation of the development.	Nihon		Facility Manager			Not triggered
	Dangerous Goods						
F15	Dangerous goods, as defined by the Australian Dangerous Goods Code, must be stored and handled strictly in accordance with: (a) all relevant Australian Standards; (b) for liquids, a minimum bund volume requirement of 110% of the volume of the largest single stored volume within the bund; and (c) the Environment Protection Manual for *Authorised Officers: Bunding and Spill Management – technical bulletin (EPA, 1997*).	Nihon		Facility Manager			Not triggered
F16	In the event of an inconsistency between the requirements F15(a) to F15(c) , the most stringent requirement must prevail to the extent of the inconsistency.	Nihon		Facility Manager			Not triggered
	Discharge Limits						
F17	The development must comply with section 120 of the POEO Act, which prohibits the pollution of waters.	Nihon		Facility Manager			Not triggered
	Services Zone						
F18	Garbage bins (recyclable and non-recyclable) must be collected and serviced from within the site.	Nihon		Facility Manager			Not triggered
F19	The operation of the services zone located within the front setback of the Residential Building is to only operate between 7am to 8am and 7pm to 8pm Monday to Friday, 7am to 8am Saturday and no service vehicle access permitted on Sunday and public holidays.	Nihon		Facility Manager			Not triggered

Not compliant

Closed

Ongoing / In progress

Not Triggered

Note with no further actions required

Appendix I - Monthly Waste Recovery Reports

CENTRAL WASTE STATION

BUILT

NIHON UNIVERSITY

RESOURCE RECOVERY REPORT

JULY 2021

Towards a Sustainable Future

1800 180 180
centralwaste.com.au
info@centralwaste.com.au
8 Styles Street
Kurri Kurri NSW 2327

BN: 44 604 989 433 |Environmental Protection Licence Number: 13013

AS/NZS 4801 - OHS MANAGEMENT
ISO 9001 - QUALITY MANAGEMENT
ISO 14001 - ENVIRONMENTAL MANAGEMENT

1. OVERVIEW

C&D materials for this month which were placed into bins typically included a mixture of mainly wood/timber, concrete, cardboard etc. processed at our Resource Recovery Facility, offering a very high level of recoverability.


Materials were free of contamination by food or other organic matter which assists in recovery rates, however, non-recoverable/difficult material such as plastics, etc. were found and disposed of as per local regulations.

2. CWS - RECOVERABLE MATERIALS MONTHLY BREAKDOWN

Breakdown of resources recovered, transported and processed at Central Waste Station's Resource Recovery Facility.

MONTHLY BREAKDOWN	
Total Amount Received (Tonnes)	46.76
Total Recovered (Tonnes)	42.36
Total Recovery Percentage	90.59%

RESOURCE TYPE	TONNES RECOVERED	PERCENTAGE
WOOD/TIMBER	24.64	52.69%
BRICK/CONCRETE	7.02	15.01%
METALS	4.50	9.62%
GYPROCK	1.02	2.18%
GREEN WASTE/GSW	0.32	0.68%
CARDBOARD	4.86	10.39%
GENERAL WASTE (NON RECYCLABLE)	3.02	6.46%
PLASTICS	1.38	2.95%

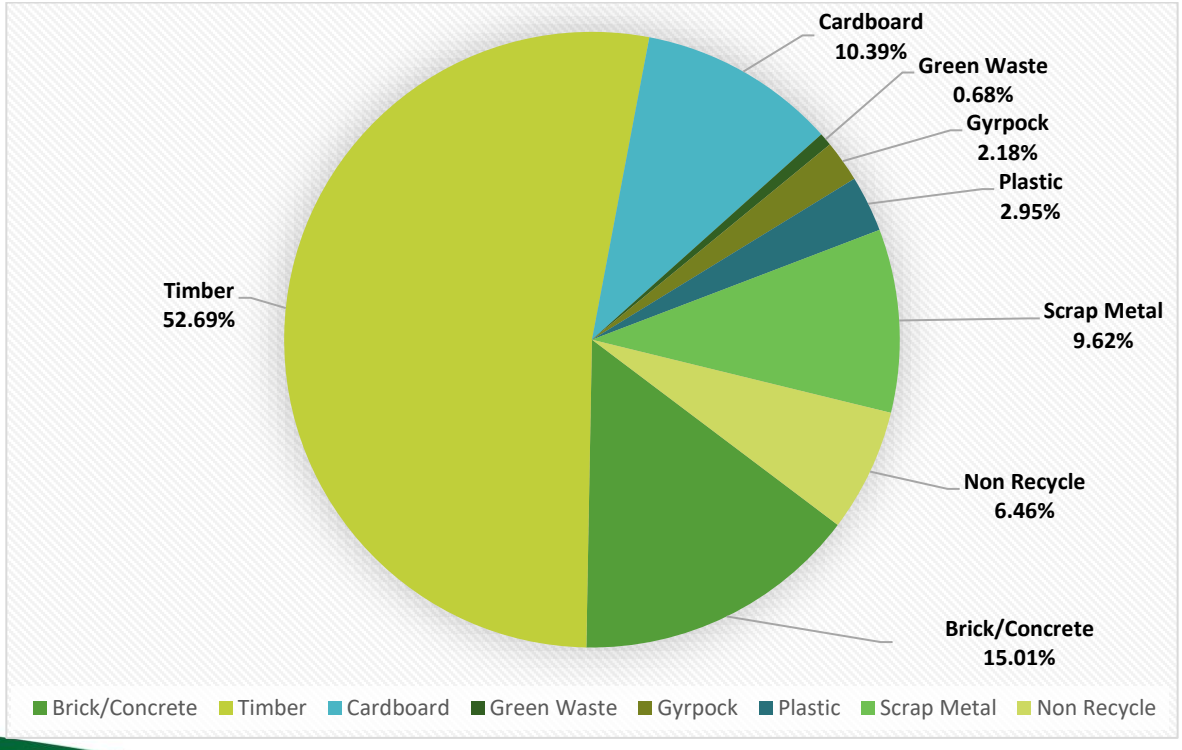

3. RECOVERY SUMMARY)

MONTHLY BREAKDOWN	CWS	OTHER FACILITIES (material specific)	TOTAL
Total Amount Received (Tonnes)	46.76	0	46.76
Total Recovered (Tonnes)	42.36	0	42.36
C&D Non-Recoverable Percentage	9.41%	0%	9.41%
Total Recovery Percentage	90.59%	0%	90.59%
